

कार्यालय अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, सासाराम — 1

पत्रांक:- 1998 3130

सासाराम/दिनांक:- 28.07.20

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, सासाराम-1

सेवा में,

नोडल पदाधिकारी,
3054 एम0आर0 नई अनुरक्षण नीति-2018
ग्रामीण कार्य विभाग
बिहार, पटना।

विषय :-

शीर्ष 3054 एम0आर0 नई अनुरक्षण नीति-2018 के तहत पूर्ण कराये गये पथों के अनुरक्षण कार्य का आवंटन उपलब्ध कराने के संबंध में।

प्रसंग :-

विभागीय पत्रांक मु0अ0-4(मु0)3054-04-229/2021-97 अनु0/पटना दिनांक 07.01.2022

महाशय,

उपर्युक्त विषयक प्रासंगिक पत्र के माध्यम से दिये गये निर्देश के आलोक में कहना है कि जिन पथों का अनुरक्षण कार्य पूर्ण कराया गया है। उन पथों से संबंधित वांछित सुचनाएँ विहित प्रपत्र में तैयार कर आवश्यक कार्यार्थ समर्पित की जाती है।

सुचनार्थ एवं आवश्यक कारवाई हेतु सादर समर्पित।

अनु0 :- यथोक्त।

विश्वासभाजन

N. Kumar
28.07.22

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, सासाराम-1

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

PIU Name:-Sasaram-1

2nd Quarter From(20/07/2021 - 19/10/2021)

1	Name of the Road	Sasaram Chousa Road - Sarodih School		
2	Batch No.	RM/RO/SAS/19/0005		
3	Project ID	10301002211		
4	Total Length of Road (In Km)	2.23 km		
5	Length of Road to Meet Required Service Level [Completed Length] (in Km) [1]	2.23 km		
6	No. of Total Quarter (i.e. 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	10.83484		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	0.54174		
Compliance Criteria	Standard job Description	Non-Compliance		Reduction Payment [6] = [3]/[1] * [2] * [4]
		Length Non- Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGEWAY)	0.00000	60%	0.00000
II	SHOULDERS AND EMBANKMENTS	0.00000	10%	0.00000
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0.00000	15%	0.00000
IV	SIGNAGE AND ROAD SAFETY	0.000000	10%	0.000000
V	VEGATATION	0.00000	5%	0.00000
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh)			[5]	0.00000
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh)			[6]	0.54174

Date of inspection by E/I of his agent

Prepared by Contractor's self Control unit

Name and Designation of person inspection road

(Signature)

Date

Signature of person inspection road

Certify by E/I [signature] Date:-

Name of Road:- Sasaram Chousa Road - Sarodih School

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event
6/7/22	8:59:39	92	0.1	290	10.1	2900	3315	G	25.84045	83.9396629	Normal
6/7/22	9:0:0	92	0.1	310	20.2	3100	3515	G	25.83592	83.940555	Normal
6/7/22	9:0:16	92	0.1	290	10.1	2900	3315	G	25.83897	83.941312	Normal
6/7/22	9:1:0	92	0.1	300	10.1	3000	3415	G	25.84582	83.941935	Normal
6/7/22	9:1:0	92	0.1	270	20.2	2700	3115	G	25.8531	83.942457	Normal
6/7/22	9:1:0	92	0.1	290	30.3	2900	3315	G	25.86192	83.942677	Normal
6/7/22	9:1:26	92	0.1	340	30.3	3400	3815	G	25.8706	83.94276	Normal
6/7/22	9:1:26	92	0.1	310	30.3	3100	3515	G	25.88042	83.942777	Normal
6/7/22	9:1:26	92	0.1	320	30.3	3200	3615	G	25.88907	83.942962	Culvert
6/7/22	9:2:2	92	0.1	310	10.1	3100	3515	G	25.88868	83.943938	Curve
6/7/22	9:2:37	92	0.1	340	10.1	3400	3815	G	25.88888	83.943047	Curve
6/7/22	9:3:0	92	0.1	330	20.2	3300	3715	G	25.88143	83.942793	Normal
6/7/22	9:3:12	92	0.1	300	30.3	3000	3415	G	25.87222	83.942777	Normal
6/7/22	9:3:12	92	0.1	330	30.3	3300	3715	G	25.86328	83.942677	Normal
6/7/22	9:3:12	92	0.1	310	30.3	3100	3515	G	25.8543	83.942525	Curve
6/7/22	9:3:47	92	0.1	210	30.3	2100	2515	G	25.84655	83.94202	Normal
6/7/22	9:4:0	92	0.1	340	10.1	3400	3815	G	25.83997	83.942137	Normal
6/7/22	9:4:22	92	0.1	290	30.3	2900	3315	G	25.83727	83.943113	Normal
6/7/22	9:4:22	92	0.1	290	30.3	2900	3315	G	25.8343	83.94404	Curve
6/7/22	9:4:22	92	0.1	310	20.2	3100	3515	G	25.83965	83.944747	Normal
6/7/22	9:5:0	92	0.1	300	20.2	3000	3415	G	25.84808	83.945318	Speed Breaker
6/7/22	9:7:18	92	0.1	330	10.1	3300	3715	G	25.84758	83.945285	Normal
6/7/22	9:7:18	92	0.1	290	20.2	2900	3315	G	25.84	83.944763	Normal
Average IRI							3458				

$$Y = 0 * X^2 + 1.000 * X + 415.2$$

$$X = 3300$$

$$Y = 3715$$

(R) RURAL ROAD

Good Average Poor

<4000 4001-5000 >5001

17/03/22
25-07-22
D.P

28/07/22
A.E

Executive Engineer
Rural Work's Department
Works Division, Sasaram-1

28.07.22

Name of Customer :	Rinki Devi
Name of Work/ Road :	Chousa Road - Sarodih School
Lab Job number :	92
Date :	7 / 6 / 2022
Section No. :	92


Test Date :	7 / 6 / 2022	Road Name :	Chousa Road - Sarodih School
Machine No. :	391	Road Type :	(R) RURAL ROAD
Start S No. :	96	Side :	Kargahar
Start E No. :	118	Interval :	
Weather :	Normal	UIV Range :	744 To 5000 mm/km
Start Location :	045.83.939662	Dist Range :	0 To 0.7 0.028 * 1000 m
End Location :	584.83.944763	Equation :	$Y = 0 * X^2 + 1.000 * X + 415.2$

Print
Generate Report and Graph

Redraw Graph

Map View

File : F:\Bomp Machine report\06-07-2022\06070957 - Copy XIs, Section No. : 92, Eqn : $Y = 0 * X^2 + 1.000 * X +$
 Name of Customer : Rinki Devi, Name of Work/ Road : Sasaram Chousa Road - Sarodih School, Lab Job number

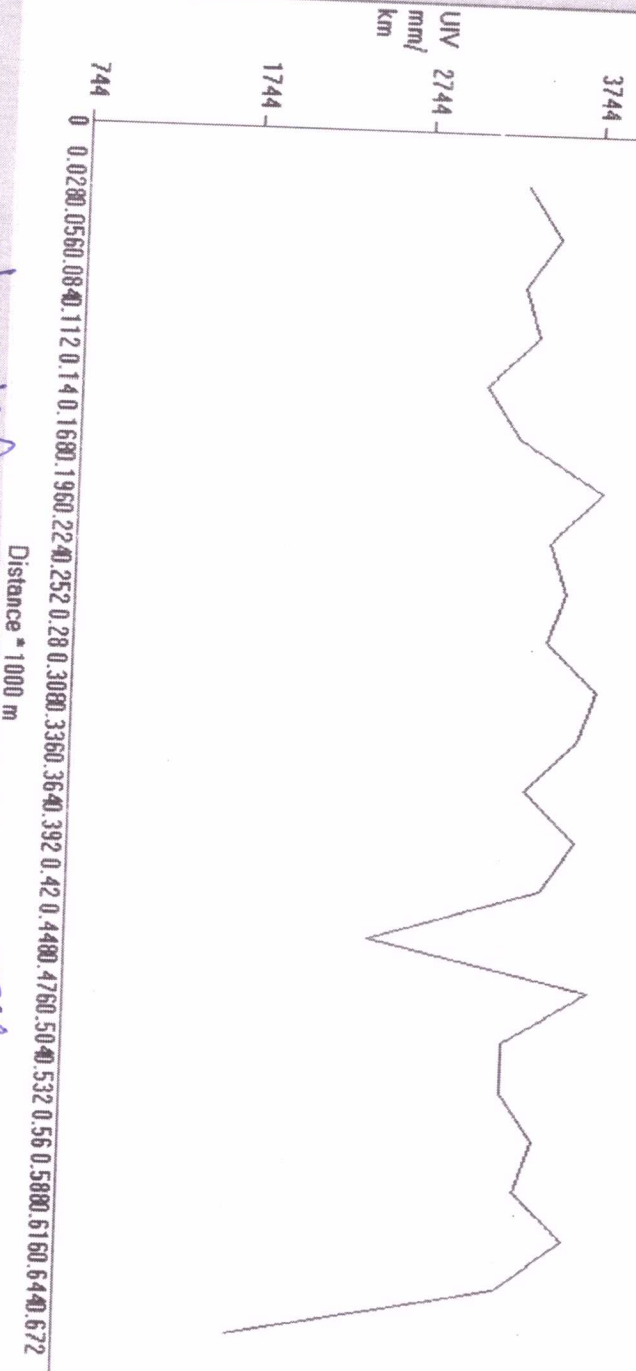

Handwritten notes:
 14022058
 25-07-22
 28/07/22
 AE
 28.07.22
 AE
