

कार्यपालक अभियन्ता का कार्यालय
ग्रामीण कार्य विभाग

कार्य प्रमण्डल गोपालगंज-2

पत्रांक 843 अनु.

दिनांक 09/05/2022

प्रेषक,

कार्यपालक अभियन्ता

ग्रामीण कार्य विभाग

कार्य प्रमण्डल गोपालगंज-2

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी --सह--

सचिव,

ब्राडा,

बिहार, पटना।

विषय:- **MR-3054 (New Maintenance policy 2018)** के अन्तर्गत 5 (पांच) वर्षीय
अनुरक्षण हेतु अधियाचना के संबंध में।

प्रसंग :- अभियन्ता प्रमुख, ग्रामीण कार्य विभाग, बिहार, पटना के पत्रांक-मु0अ0-4 (मु0) 3054
- 04-229/2021-1135 अनु0 पटना, दिनांक-09.03.22।

महाशय,

उपर्युक्त विषयक प्रासंगिक पत्र में दिये गये निर्देश के आलोक में नई अनुरक्षण नीति -
2018 अन्तर्गत पथों के अनुरक्षण की राशि के आवंटन हेतु विहित प्रपत्र में तैयार कर आवश्यक
कार्रवाई हेतु समर्पित की जा रही है।

अतः **MR-3054 (New Maintenance policy 2018)** के अन्तर्गत (MR-N/2019-20
Gopalganj-2/12) 1 झझवा से शाहपुर, 2 कटेया टोला से काशी टेंगराही, 3. विशुनपुरा से
जलालपुर पथ के अनुरक्षण हेतु अधियाचित प्रपत्र में दर्शाये गए राशि उपलब्ध कराने की कृपा
की जाय। कार्य का निरीक्षण किया गया एवं कराया गया कार्य संतोषप्रद है। उक्त पथों में
ए0टी0आर0 लंबित नहीं है।
अनु0- यथोक्त।

विश्वासभाजन


कार्यपालक अभियन्ता

ग्रामीण कार्य विभाग

कार्य प्रमण्डल, गोपालगंज-2

09.5.22

FORM CER 19
(See government of India's Decision) Below Rule-150
Form of utilisation certificate up to Month of May 2022
MR HEAD- 3054 (Initial Rectification with surface Renewal)

SI No.	Name of Scheme	Allotment Received		Expenditure		Balance	
1	Construction of Rural roads under MR Head- 3054 (Initial Rectification with surface Renewal)	By Bank A/C	0.00	By Bank A/C	0.00	In Bank A/C	0.00
		By CFMS	0.00	By CFMS	0.00	In CFMS	0.00
		Total	0.00	Total	0.00	Total	0.00
						Certified that sum of Rs. 0.00 has been utilized for the purpose of MR HEAD- 3054 (Initial Rectification with surface Renewal) as given in the margin for which it was sanction as that the balance of Rs.0.00 remaining unutilized at the end of the period under report	

2. Certified that I have satisfied my self the condition in which the grants aid was sanctioned have been duly full filled are beign fulfilled and that have exercised the following checks to see that the kind of checks exercised:-

- Work have been supervised by executive engineer/Super intending Engineer..... Yes
- Periodical inspection has been conducted by E.E./S.E/E.E. Weekly S.E. quarterly
- Construction materials have been tested-Yes
- Measurement have been recorded in MB as test Check Conducted by Assistant Engineer/ Executive
- All other coda formalities have been observed- Yes

3 Physical Progress achieved:-

- Construction of Road work 11 Nos.
- Construction of CD work 77/2 Nos (77HP CUI/2 No RCC)

09/5/22
 Divisional Accounts Officer
 R.W.D. Works Division
 Gopalganj-2

09/5/22
 Executive Engineer,
 R.W.D. Works Division
 Gopalganj-2
09.5.22

Standrad Format For Roads Quarterly Statement (3rd Quarter)

Name:- R.W.D.(W)Division Gopalganj-2

1	Name of the Road	Vishunpura to Jalalpur		
2	Batch No.			
3	Project ID	314701036977		
4	Total Length of Road(in K.M.)	3.70		
5	Length of Road to Meet Required Service Level (Completed Length)(in K.M.)	3.70		
6	No of Total Quarter(ie 3 Months as a Unit) in 5 Years	20		
7	Ordinary Maintenance Cost as per Schedule (Agreement Amount For Maintenance(in Lakh)	3450216 F D		
8	Quarterly Payment: 1/20 of Ordinary Maintennance Cost as per Schedule (in Lakh)	187510 F D		
Compliance Criteria	Standard Job Description	Non- Compliance		Reduction Payment (6) = (3) / (1)*(2)*(4)
		Length Non Compliant	Weightred Value for Payment Reduction (%)	
	Paved Roads(Carriage Way)	0	60%	0
	Shoulders and Embankments	0	10%	0
	Cross Drainage Including Culverts and Bridges	0	15%	0
	Signage and Road Safety	0	10%	0
	Vegetation	0	5%	0
Total Payment Reduction for the Quarter (in Lakh)				187510 F D
To be Paid for the Quarter/ Demand (in Lakh)				

Date of Inspection by E/I or his agent

Prepared by Contractor's self Control unit

Name and Designation of Person inspecting road

Date:-

Signature of Person inspecting road

(Signature)

Certify by E/I (Signature) Date

RWD, Works Division Gopalganj-2

Government Of Bihar

OM01

Rural Works Department

Road From:- Vishunpura to Jalalpur
(Package No.MR-N/2019-20 Gopalganj-2/12)

Length of Road :- 3.70 Km

Period :- From:- 12.08.21 to 11.11.21

Inspector :- A.E RWD Sub Division : Sidhawalila

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

To:-

Executive Engineer
RWD, Works Division Gopalganj-2

Date:-

Position :- A.E

No	Standard Of Work Item Name	Work Unit	Unit OF Required in each Kilometere										Comments
			1	2	3	4	5	6	7	8	9	10	
OM100	Sealed payment												
OM101	Pothole Patching	m ²	10.3	11.2	12.9	10.6							Defects rectified within stipulated time
OM102	Surface Depression and Rut patching	m ³	0.035	0.04	0.048	0.03							Defects rectified within stipulated time
OM103	Crack Sealing	Lm	510	590	520	250							Defects rectified within stipulated time
	Surface Treatment												
OM104	(a) Loss of Aggregate (Surface Ravelling)	m ²	6.2	5.6	5.9	5.3							Defects rectified within stipulated time
	(b) Bleeding / Flushing	m ²	Nil	Nil	Nil	Nil							Defects rectified within stipulated time
	© Crocodile Cracking	m ²	Nil	Nil	Nil	Nil							No Bleeding/ Flushing Required
105	Edge Repair	m ²	Nil	Nil	Nil	Nil							No Crocodile Cracking Found
106	Digouts	m ²	0.45	0.46	0.48	0.41							No Edge Repair Required
107	Concreate pavement	m ³	N.A	N.A	N.A	N.A							Defects rectified within stipulated time
	Other activities												Not Required
OM200	Shoulder												
	Unsealed Shoulder												
OM201	(a) Edge Drop-off	Lm	Nil	Nil	Nil	Nil							Not Required
	(b) Roughness, Scouring or Potholes	Lm	90.5	88.3	87.6	85.1							Defects rectified within stipulated time
	(c) Holding water	Lm	Nil	Nil	Nil	Nil							Not Required
OM202	Embankment Repair	M ³	8.15	7.95	8.66	3.92							Defects rectified within stipulated time
	Other activities (Rain Cuts)		Nil	Nil	Nil	Nil							Not Required
OM300	Drainage including culverts major												
OM301	Surface Drains & Verge	Lm	N.A	N.A	N.A	N.A							Not Required
OM302	Culvert Cleaning	No	1	Nil	1	Nil							Defects rectified within stipulated time
OM303	Culvert and pit Repair	M ³	Nil	Nil	Nil	Nil							Not Required
	Other activities(Whilw washing)	M ²	20.16	Nil	20.16	Nil							Defects rectified within stipulated time

No	standard Of Work Item Name	Work Unit	1	2	3	4	5	6	7	8	9	10	Comments
OM400	Vegetation												Not Required
	Grass Control												Not Required
OM401	(a) Roadside- General Tidy	Ha	Nil	Nil	Nil	Nil							Not Required
	(b) Clear near Safety signs, kilometer posts and roadside furniture	Ha	Nil	Nil	Nil	Nil							Not Required
	Tree and Shrub Management	No	Nil	Nil	Nil	Nil							Not Required
OM402	Cutting Of Branches Of Trees	No	Nil	Nil	Nil	Nil							Defects rectified within stipulated time
	Cutting Of Shrubs From Road Way	No	510	460	490	430							Defects rectified within stipulated time
	Other activities (Trimming of Grass)	M ²	600	900	720	960							Defects rectified within stipulated time
OM500	Safety Signage and Road		Nil										Not Required
OM501	Signs Maintenance	No	1	Nil	1	Nil							Not Required
OM502	Guard Stones	Lm	N.A	N.A	N.A	N.A							Defects rectified within stipulated time
OM503	Distance Stones	No	1	N.A	1	N.A							Not Required
OM504	Road Marking	M ²	Nil	Nil	Nil	Nil							Defects rectified within stipulated time
	Other activities												

M/S. NANDANI CONSTRUCTION


Bidder

30-4-22
30-4-22
30-4-22

Appendix

Executive Engineer,
RWD, Works Division, Gopalgarh-2

30/4/22

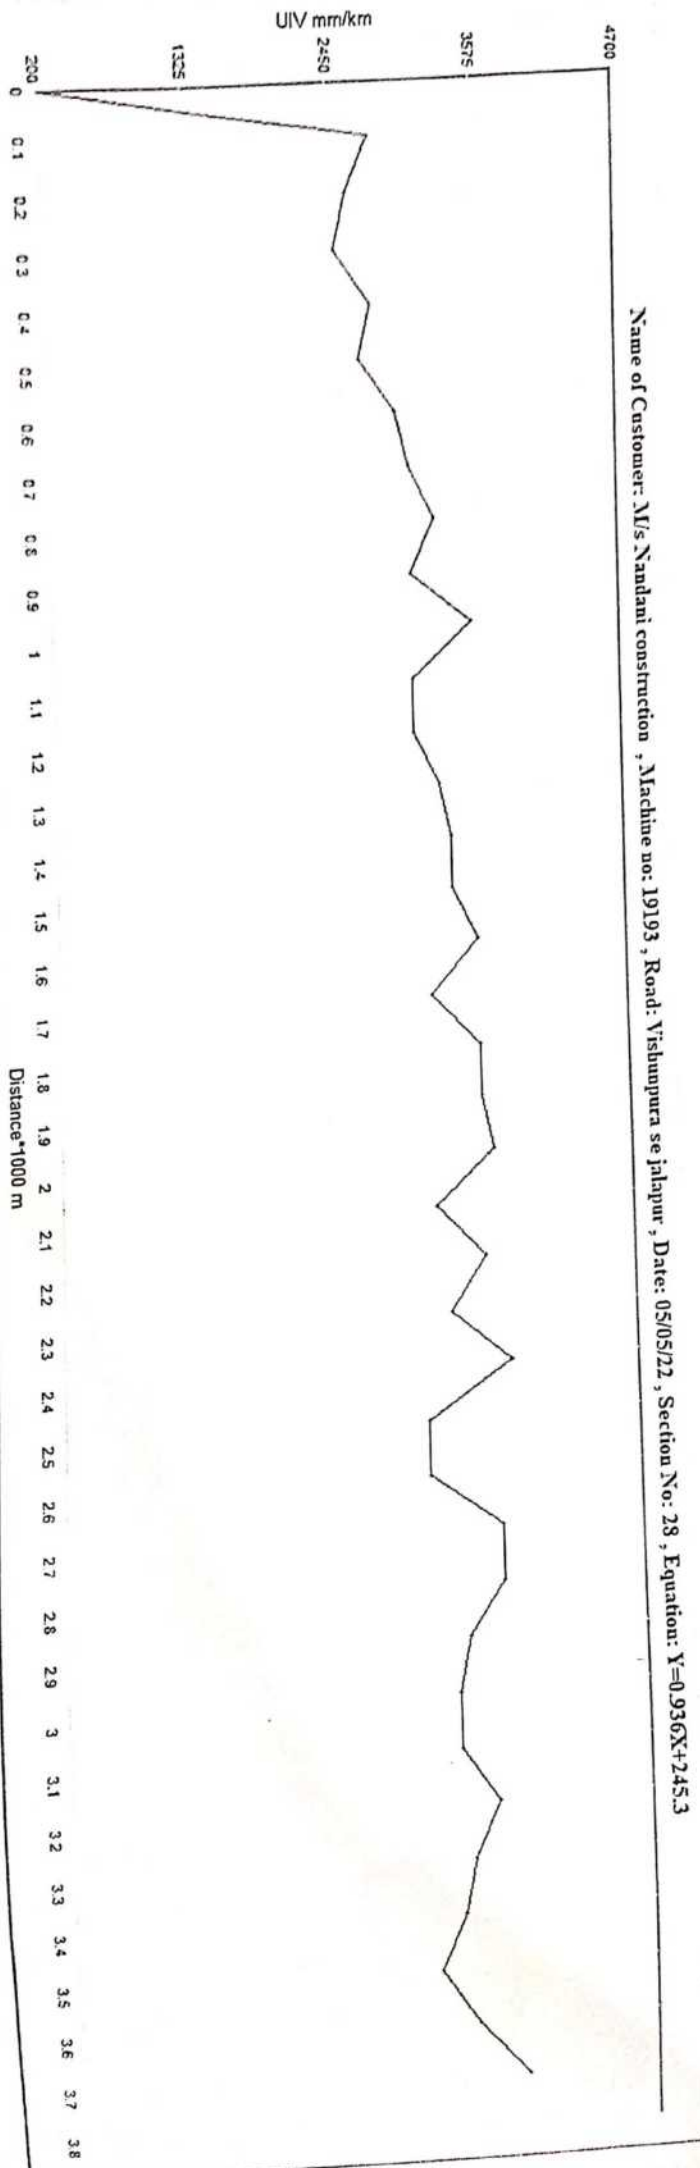

30-4-21
50

30-04-22
50

30/4/22

Name of work : Vishnupura se Jalapur
 Name of customer : M/s Nandani construction

(R) Rural Road		
Good	Average	Poor
< 4000	4001 - 5000	> 5000

Date	Time	Test No	Distance(m)	Total Distance(m)	BUM(cm)	Speed(Km/Hr)	U/m(Km)	Corrected U (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks
30/04/22	10:32:32	25	0	0	0.0 cm	13.3 Km/Hr	0.0 mm/Km	245	0.43	Good	26.4977241	N	83.9338847	E	Normal
30/04/22	12:02:06	26	100	100	27.0 cm	20.1 Km/Hr	2700.0 mm/Km	2773	3.75	Good	26.5001764	N	84.0826654	E	Normal
30/04/22	12:02:19	28	100	200	25.0 cm	25.2 Km/Hr	2500.0 mm/Km	2585	3.53	Good	26.4993658	N	84.0824366	E	Normal
30/04/22	12:02:30	28	100	300	24.0 cm	31.2 Km/Hr	2400.0 mm/Km	2492	3.41	Good	26.4984465	N	84.0821924	E	Normal
30/04/22	12:02:41	28	100	400	27.0 cm	32.4 Km/Hr	2700.0 mm/Km	2773	3.75	Good	26.4975195	N	84.0823069	E	Normal
30/04/22	12:02:52	28	100	500	26.0 cm	34.5 Km/Hr	2600.0 mm/Km	2679	3.64	Good	26.4966478	N	84.0822077	E	Normal
30/04/22	12:03:02	28	100	600	29.0 cm	33.4 Km/Hr	2900.0 mm/Km	2960	3.98	Good	26.4959040	N	84.0820322	E	Normal
30/04/22	12:03:14	26	100	700	30.0 cm	32.0 Km/Hr	3000.0 mm/Km	3053	4.09	Good	26.4952076	N	84.0818338	E	Normal
30/04/22	12:03:27	26	100	800	32.0 cm	27.9 Km/Hr	3200.0 mm/Km	3241	4.32	Good	26.4938574	N	84.0812005	E	Normal
30/04/22	12:03:40	26	100	900	30.0 cm	27.3 Km/Hr	3000.0 mm/Km	3053	4.06	Good	26.4934812	N	84.0810251	E	Normal
30/04/22	12:03:51	28	100	1000	35.0 cm	31.2 Km/Hr	3500.0 mm/Km	3521	4.65	Good	26.4927015	N	84.0804224	E	Normal
30/04/22	12:04:04	28	100	1100	30.0 cm	28.5 Km/Hr	3000.0 mm/Km	3053	4.09	Good	26.4915457	N	84.0801935	E	Normal
30/04/22	12:04:40	28	100	1200	30.0 cm	10.0 Km/Hr	3000.0 mm/Km	3053	4.09	Good	26.4905043	N	84.0802240	E	Normal
30/04/22	12:05:02	26	100	1300	32.0 cm	16.5 Km/Hr	3200.0 mm/Km	3241	4.32	Good	26.4898767	N	84.0799365	E	Normal
30/04/22	12:05:15	28	100	1400	33.0 cm	27.6 Km/Hr	3300.0 mm/Km	3334	4.43	Good	26.4891157	N	84.0798555	E	Normal
30/04/22	12:05:27	28	100	1500	33.0 cm	29.1 Km/Hr	3300.0 mm/Km	3334	4.43	Good	26.4880915	N	84.0799189	E	Normal
30/04/22	12:05:40	28	100	1600	35.0 cm	27.2 Km/Hr	3500.0 mm/Km	3521	4.65	Good	26.4870838	N	84.0799341	E	Normal
30/04/22	12:05:57	28	100	1700	31.0 cm	22.9 Km/Hr	3100.0 mm/Km	3147	4.2	Good	26.4861574	N	84.0799799	E	Normal
30/04/22	12:06:56	28	100	1800	35.0 cm	23.9 Km/Hr	3500.0 mm/Km	3521	4.65	Good	26.4854250	N	84.0802927	E	Normal
30/04/22	12:07:11	28	100	1900	35.0 cm	27.0 Km/Hr	3500.0 mm/Km	3521	4.65	Good	26.4854250	N	84.0802927	E	Normal
30/04/22	12:07:23	28	100	2000	36.0 cm	28.1 Km/Hr	3600.0 mm/Km	3615	4.76	Good	26.4854250	N	84.0802927	E	Normal

30-04-22
 30-5-22

30-04-22
 30-5-22

30/04/22
 30/05/22

Name of work : Vishunpura se Jalalpur
Name of customer : M/s Nandani construction

(R)Rural Road		
Good	Average	Poor
< 4000	4001 - 5000	> 5000

30.04.11	12.12.23	28	100	2100	31.2 cm	34.8 Km/hr	3100.0 mm/Km	3147	4.2	Good	26.4827394	N	84.0804224	E	Normal
30.04.12	12.12.24	28	100	2200	36.0 cm	36.2 Km/hr	3500.0 mm/Km	3621	4.65	Good	26.4816504	N	84.0803080	E	Normal
30.04.13	12.12.25	28	100	2200	32.0 cm	37.0 Km/hr	3200.0 mm/Km	3241	4.32	Good	26.4813604	N	84.0802927	E	Normal
30.04.14	12.12.26	28	100	2400	37.0 cm	30.5 Km/hr	3700.0 mm/Km	3709	4.87	Good	26.4803507	N	84.0802240	E	Normal
30.04.15	12.12.27	28	100	2800	32.0 cm	21.3 Km/hr	3000.0 mm/Km	3053	4.09	Good	26.4792687	N	84.0803690	E	Normal
30.04.16	12.12.28	28	100	2800	36.0 cm	19.6 Km/hr	3500.0 mm/Km	3053	4.09	Good	26.4786024	N	84.0802774	E	Normal
30.04.17	12.12.29	28	100	2700	36.2 cm	22.0 Km/hr	3600.0 mm/Km	3615	4.76	Good	26.4774542	N	84.0802774	E	Normal
30.04.18	12.12.30	28	100	2800	36.0 cm	17.4 Km/hr	3600.0 mm/Km	3615	4.76	Good	26.4767637	N	84.0802726	E	Normal
30.04.19	12.12.31	28	100	2800	33.0 cm	17.4 Km/hr	3300.0 mm/Km	3334	4.43	Good	26.4759485	N	84.0812998	E	Normal
30.04.20	12.12.32	28	100	3000	32.0 cm	20.6 Km/hr	3200.0 mm/Km	3241	4.32	Good	26.4752207	N	84.0811014	E	Normal
30.04.21	12.12.33	28	100	3100	32.0 cm	12.5 Km/hr	3200.0 mm/Km	3241	4.32	Good	26.4743289	N	84.0809412	E	Normal
30.04.22	12.12.34	28	100	3200	36.0 cm	27.3 Km/hr	3500.0 mm/Km	3521	4.85	Good	26.4733973	N	84.0804377	E	Normal
30.04.23	12.12.35	28	100	3300	32.0 cm	17.6 Km/hr	3300.0 mm/Km	3334	4.43	Good	26.4725027	N	84.0803537	E	Normal
30.04.24	12.12.36	28	100	3400	32.0 cm	23.5 Km/hr	3200.0 mm/Km	3241	4.32	Good	26.4719458	N	84.0803537	E	Normal
30.04.25	12.12.37	28	100	3500	36.0 cm	21.8 Km/hr	3000.0 mm/Km	3053	4.09	Good	26.4712419	N	84.0801783	E	Normal
30.04.26	12.12.38	28	100	3600	33.0 cm	23.7 Km/hr	3300.0 mm/Km	3334	4.43	Good	26.4706469	N	84.0799494	E	Normal
30.04.27	12.12.39	28	100	3700	37.0 cm	32.7 Km/hr	3700.0 mm/Km	3709	4.87	Good	26.4690676	N	84.0794611	E	Normal

30-04-22
S-E

20-04-22
AK

Dr. P. A. M.
