

कार्यपालक अभियन्ता का कार्यालय
ग्रामीण कार्य विभाग

कार्य प्रमण्डल गोपालगंज-2

पत्रांक 843 अनु.

दिनांक 09/05/2022

प्रेषक,

कार्यपालक अभियन्ता

ग्रामीण कार्य विभाग

कार्य प्रमण्डल गोपालगंज-2

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी --सह--

सचिव,

ब्राडा,

बिहार, पटना।

विषय:- **MR-3054 (New Maintenance policy 2018)** के अन्तर्गत 5 (पांच) वर्षीय
अनुरक्षण हेतु अधियाचना के संबंध में।

प्रसंग :- अभियन्ता प्रमुख, ग्रामीण कार्य विभाग, बिहार, पटना के पत्रांक-मु0अ0-4 (मु0) 3054
- 04-229/2021-1135 अनु0 पटना, दिनांक-09.03.22।

महाशय,

उपर्युक्त विषयक प्रासंगिक पत्र में दिये गये निर्देश के आलोक में नई अनुरक्षण नीति -
2018 अन्तर्गत पथों के अनुरक्षण की राशि के आवंटन हेतु विहित प्रपत्र में तैयार कर आवश्यक
कार्रवाई हेतु समर्पित की जा रही है।

अतः **MR-3054 (New Maintenance policy 2018)** के अन्तर्गत (MR-N/2019-20
Gopalganj-2/12) 1 झझवा से शाहपुर, 2. कटेया टोला से काशी टेंगराही, 3. विशुनपुरा से
जलालपुर पथ के अनुरक्षण हेतु अधियाचित प्रपत्र में दर्शाये गए राशि उपलब्ध कराने की कृपा
की जाय। कार्य का निरीक्षण किया गया एवं कराया गया कार्य संतोषप्रद है। उक्त पथों में
ए0टी0आर0 लंबित नहीं है।

अनु0- यथोक्त।

विश्वासभाजन


कार्यपालक अभियन्ता

ग्रामीण कार्य विभाग

कार्य प्रमण्डल, गोपालगंज-2

09-5-22

FORM CER 19
(See government of India's Decision) Below Rule-150
Form of utilisation certificate up to Month of May 2022
MR HEAD- 3054 (Initial Rectification with surface Renewal)

SI No.	Name of Scheme	Allotment Received		Expenditure		Balance	
1	Construction of Rural roads under MR Head- 3054 (Initial Rectification with surface Renewal)	By Bank A/C	0.00	By Bank A/C	0.00	In Bank A/C	0.00
		By CFMS	0.00	By CFMS	0.00	In CFMS	0.00
		Total	0.00	Total	0.00	Total	0.00
						Certified that sum of Rs. 0.00 has been utilized for the purpose of MR HEAD- 3054 (Initial Rectification with surface Renewal) as given in the margin for which it was sanction as that the balance of Rs.0.00 remaining unutilized at the end of the period under report	

2. Certified that I have satisfied my self the condition in which the grants aid was sanctioned have been duly full filled are beign fulfilled and that have exercised the following checks to see that the kind of checks exercised:-

- Work have been supervised by executive engineer/Super intending Engineer..... Yes
- Periodical inspection has been conducted by E.E./S.E/E.E. Weekly S.E. quarterly
- Construction materials have been tested-Yes
- Measurement have been recorded in MB as test Check Conducted by Assistant Engineer/ Executive
- All other coda formalities have been observed- Yes

3 Physical Progress achieved:-

- Construction of Road work 11 Nos.
- Construction of CD work 77/2 Nos (77HP CUI/2 No RCC)

09/5/22
 Divisional Accounts Officer
 R.W.D. Works Division
 Gopalganj-2

09/5/22
 Executive Engineer,
 R.W.D. Works Division
 Gopalganj-2
09.5.22

Standrad Format For Roads Quarterly Statement (3rd Quarter)

PU Name:- R.W.D.(W)Division Gopalganj-2

1	Name of the Road	Jhajhawa to Sahpur		
2	Batch No.			
3	Project ID	31407001016		
4	Total Length of Road(in K.M.)	3.30		
5	Length of Road to Meet Required Service Level (Completed Length)(in K.M.)	3.30		
6	No of Total Quarter(ie 3 Months as a Unit) in 5 Years	20		
7	Ordinary Maintenance Cost as per Schedule (Agreement Amount For Maintenance(in Lakh)	348234320		
8	Quarterly Payment: 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh)	17161720		
Compliance Criteria	Standard Job Description	Non- Compliance		Reduction Payment (6) = (3) / (1)*(2)*(4)
		Length Non Compliant	Weightred Value for Payment Reduction (%)	
	Paved Roads(Carriage Way)	0	60%	0
	Shoulders and Embankments	0	10%	0
	Cross Drainage Including Culverts and Bridges	0	15%	0
	Signage and Road Safety	0	10%	0
	Vegetation	0	5%	0
Total Payment Reduction for the Quarter (in Lakh)				17161720
To be Paid for the Quarter/ Demand (in Lakh)				

Date of Inspection by E/I or his agent

Prepared by Contractor's self Control unit

Name and Designation of Person inspecting road

Date:-

5-5-22
S-E

5-5-22
S-E

(Signature)

5/5/22

Signature of Person inspecting road

Certify by E/I (Signature) Date

Requisition Formet for Scheme Head-MR-(3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

1 Year (3rd Quarter)

RWD, Works Division Gopalganj-2

Government Of Bihar

OM101

Rural Works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From:- Jhajhawa to Sahpur
(Package No.MR-N 2019-20 Gopalganj-2 12)

Length of Road :- 3.300 Km

Period :- From:- 12.08.21 to 11.11.21

Inspector :- A.E RWD Sub Division : Sidhawalia

To:-

Executive Engineer
RWD, Works Division Gopalganj-2

Position :- A.E

Date:-

No	Standard Of Work Item Name	Work Unit	Unit Of Required in each Kilometere										Unit Of Required in each Kilometere	
			1	2	3	4	5	6	7	8	9	10		
OM100	Sealed payment													
OM101	Pothole Patching	m ²	2.00	4.00	Nil	2.00							Defects rectified within stipulated time	
OM102	Surface Depression and Rut patching	m ³	0.016	0.015	Nil	0.005							Defects rectified within stipulated time	
OM103	Crack Sealing	Lm	1060.00	950.00	990.00	Nil							Defects rectified within stipulated time	
	Surface Treatment													
OM104	(a) Loss of Aggregate (Surface Ravelling)	m ²	4.50	10.20	10.00	Nil							Defects rectified within stipulated time	
	(b) Bleeding / Flushing	m ²	Nil	Nil	Nil	Nil							No Bleeding Flushing Required	
	© Crocodile Cracking	m ²	Nil	Nil	Nil	Nil							No Crocodile Cracking Found	
105	Edge Repair	m ²	Nil	Nil	Nil	Nil							No Edge Repair Required	
106	Digouts	m ²	0.075	1.25	0.5	0.2							Defects rectified within stipulated time	
107	Concrete pavement	m ³	N.A	N.A	N.A	N.A							N.A	
	Other activities													
OM1200	Shoulder													
	Unsealed Shoulder													
OM1201	(a) Edge Drop-off	Lm	Nil	Nil	Nil	Nil							No Edge Drop-Off Required	
	(b) Roughness, Scouring or Potholes	Lm	9.75	126.00	108.00	Nil							Defects rectified within stipulated time	
	(c) Holding water	Lm	Nil	Nil	Nil	Nil							No Holding Water Found	
OM1202	Embankment Repair	M ³	22.68	13.392	Nil	Nil							Defects rectified within stipulated time	
	Other activities (Rain Cuts)		Nil	Nil	Nil	Nil							Not Required	
OM1300	Drainage including culverts major													
OM1301	Surface Drains & Verge	Lm	N.A	N.A	N.A	N.A							Not Required	
OM1302	Culvert Cleaning	No	2	3	1	1							Defects rectified within stipulated time	
OM1303	Culvert and pit Repair	M ³	Nil	Nil	Nil	Nil							Not Required	
	Other activities (Whitewashing)	M ²	-	-	-	129.6							Defects rectified within stipulated time	
	standard Of Work Item	Work												

No	Name	Unit	1	2	3	4	5	6	7	8	9	10	Comments
OM400	Vegetation												
	Grass Control												
OM401	(a) Roadside- General Tidy	Ha	Nil	Nil	Nil	Nil							Not Required
	(b) Clear near Safety signs, kilometer posts and roadside furniture	Ha	Nil	Nil	Nil	Nil							Not Required
	Tree and Shrub Management	No	Nil	Nil	Nil	Nil							Not Required
	Cutting Of Branches Of Trees	No	Nil	Nil	Nil	Nil							Not Required
OM402	Cutting Of Shrubs From Road Way	No	500	1000	1500	Nil							Defects rectified within stipulated time
	Other activities (Trimming of Grass)	M ²	780.00	900.00	990.00	930.00							Defects rectified within stipulated time
OM500	Safety Signage and Road		Nil										Not Required
OM501	Signs Maintenance	No	0.55	Nil	0.55	Nil							Defects rectified within stipulated time
OM502	Guard Stones	Lm	0.55	N.A	0.55	N.A							Defects rectified within stipulated time
OM503	Distance Stones	No	N.A	N.A	N.A	N.A							Not Required
OM504	Road Marking	M ²	Nil	Nil	Nil	Nil							Not Required
	Other activities												

M/S. NANDANI CONSTRUCTION

1/12/2019 by
PARTNER

Bidder

Appendix

5-5-22
5-5-22

5/5/22

Executive Engineer,
RWD. Works Division, Gopalganj-2

Name of work		Jhaljwa se salpur	
Name of customer		M/s Nandanl construction	
(R) Rural Road			
Good		Average	
< 4000		4001 - 5000	
Poor		> 5000	

Date	Time	Test No	Distance(m)	Total Distance(m)	BUMF(cm)	Speed(Km/Hr)	U/min(Km)	Corrected UI (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks
05-03-22	05:31:45	30	0	0	0.0 cm	32.4 Km/Hr	0.0 mm/Km	245	0.43	Good	26.3349256	N	84.7300272	E	Normal
05-03-22	05:43:27	30	100	100	36.0 cm	10.6 Km/Hr	3600.0 mm/Km	3615	4.76	Good	26.3027253	N	84.686759	E	Normal
05-03-22	05:43:47	30	100	200	33.0 cm	18.7 Km/Hr	3300.0 mm/Km	3334	4.43	Good	26.3028225	N	84.6875010	E	Normal
05-03-22	05:44:00	30	100	300	28.0 cm	27.0 Km/Hr	2800.0 mm/Km	2866	3.87	Good	26.3630209	N	84.6867990	E	Normal
05-03-22	05:44:25	30	100	400	27.0 cm	15.0 Km/Hr	2700.0 mm/Km	2773	3.75	Good	26.3625326	N	84.6854630	E	Normal
05-03-22	05:44:41	30	100	500	28.0 cm	22.2 Km/Hr	2800.0 mm/Km	2866	3.87	Good	26.3622618	N	84.6845407	E	Normal
05-03-22	05:44:53	30	100	600	29.0 cm	29.1 Km/Hr	2900.0 mm/Km	2960	3.98	Good	26.3619890	N	84.6836405	E	Normal
05-03-22	05:45:06	30	100	700	30.0 cm	29.1 Km/Hr	3000.0 mm/Km	3053	4.09	Good	26.3613214	N	84.6825190	E	Normal
05-03-22	05:45:17	30	100	800	22.0 cm	32.4 Km/Hr	2200.0 mm/Km	2305	3.18	Good	26.3606405	N	84.6820612	E	Normal
05-03-22	05:45:30	30	100	900	34.0 cm	26.1 Km/Hr	3400.0 mm/Km	3428	4.54	Good	26.3600721	N	84.6814432	E	Normal
05-03-22	05:45:42	30	100	1000	34.0 cm	29.4 Km/Hr	3400.0 mm/Km	3428	4.54	Good	26.3602190	N	84.6806345	E	Normal
05-03-22	05:46:09	30	100	1100	35.0 cm	14.6 Km/Hr	3500.0 mm/Km	3521	4.85	Good	26.3602095	N	84.6796427	E	Normal
05-03-22	05:46:21	30	100	1200	37.0 cm	25.7 Km/Hr	3700.0 mm/Km	3709	4.87	Good	26.3593149	N	84.6792307	E	Normal
05-03-22	05:46:40	30	100	1300	25.0 cm	19.4 Km/Hr	2500.0 mm/Km	2585	3.53	Good	26.3583879	N	84.6787806	E	Normal
05-03-22	05:46:54	30	100	1400	35.0 cm	29.4 Km/Hr	3500.0 mm/Km	3615	4.76	Good	26.3575525	N	84.6783533	E	Normal
05-03-22	05:47:04	30	100	1500	37.0 cm	29.7 Km/Hr	3700.0 mm/Km	3709	4.87	Good	26.3568487	N	84.6780252	E	Normal
05-03-22	05:47:22	30	100	1600	35.0 cm	21.4 Km/Hr	3500.0 mm/Km	3521	4.65	Good	26.3560476	N	84.6776209	E	Normal
05-03-22	05:47:37	30	100	1700	37.0 cm	23.8 Km/Hr	3700.0 mm/Km	3709	4.87	Good	26.3554125	N	84.6770029	E	Normal
05-03-22	05:47:53	30	100	1800	35.0 cm	21.6 Km/Hr	3500.0 mm/Km	3615	4.76	Good	26.3544359	N	84.6765801	E	Normal
05-03-22	05:48:25	30	100	1900	33.0 cm	31.8 Km/Hr	3300.0 mm/Km	3334	4.43	Good	26.3536272	N	84.6756443	E	Normal
05-03-22	05:48:16	30	100	2000	34.0 cm	30.5 Km/Hr	3400.0 mm/Km	3428	4.54	Good	26.3528242	N	84.6755985	E	Normal

5-5-22
5-5-22

72-5-22
5-5-22

05/05/22

Name of work : [h]ajwa se sahpur
 Name of customer : M/s Nandani construction

(R)Rural Road		
Good	Average	Poor
< 4000	4001 - 5000	> 5000

05/05/22	08.45.29	30	100	2100	33.0 cm	29.3 Km/Hr	3300.0 mm/Km	3334	4.43	Good	26.3516855	N	84.676443	E	Normal
05/05/22	08.48.44	30	100	2200	34.0 cm	23.4 Km/Hr	3400.0 mm/Km	3428	4.54	Good	26.3512869	N	84.6763163	E	Normal
05/05/22	08.49.09	30	100	2300	28.0 cm	15.2 Km/Hr	2800.0 mm/Km	2866	3.87	Good	26.3502092	N	84.6756525	E	Normal
05/05/22	08.49.27	30	100	2400	33.0 cm	20.0 Km/Hr	3300.0 mm/Km	3334	4.43	Good	26.3502452	N	84.6747751	E	Normal
05/05/22	08.49.43	30	100	2500	35.0 cm	22.1 Km/Hr	3500.0 mm/Km	3521	4.65	Good	26.3501548	N	84.6739740	E	Normal
05/05/22	08.49.52	30	100	2600	36.0 cm	23.5 Km/Hr	3600.0 mm/Km	3615	4.76	Good	26.3493738	N	84.6735544	E	Normal
05/05/22	08.50.18	30	100	2700	35.0 cm	24.0 Km/Hr	3500.0 mm/Km	3521	4.65	Good	26.3493745	N	84.6735545	E	Normal
05/05/22	08.50.34	30	100	2800	36.0 cm	25.5 Km/Hr	3600.0 mm/Km	3615	4.76	Good	26.3493731	N	84.6735544	E	Normal
05/05/22	08.50.47	30	100	2900	37.0 cm	25.5 Km/Hr	3700.0 mm/Km	3709	4.87	Good	26.3493735	N	84.6735544	E	Normal
05/05/22	08.50.56	30	100	3000	35.0 cm	26.5 Km/Hr	3500.0 mm/Km	3615	4.76	Good	26.3493738	N	84.6735544	E	Normal
05/05/22	08.51.12	30	100	3100	35.0 cm	26.5 Km/Hr	3500.0 mm/Km	3521	4.65	Good	26.3493737	N	84.6735544	E	Normal
05/05/22	08.51.24	30	100	3200	36.0 cm	25.5 Km/Hr	3600.0 mm/Km	3615	4.76	Good	26.3493738	N	84.6735544	E	Normal
05/05/22	08.51.36	30	100	3300	35.0 cm	24.5 Km/Hr	3500.0 mm/Km	3521	4.65	Good	26.3493734	N	84.6735547	E	Normal

5-5-22
 5-5-22

5-5-22
 5-5-22

5-5-22
 5-5-22


T T

D
 Pr

Dat

Sigr

Name of Customer: Mr. Nandani construction, Machine no: 19193, Road: Jhajhwa se sabpur, Date: 05/05/22, Section No: 30, Equation: $Y=0.916X+245.3$

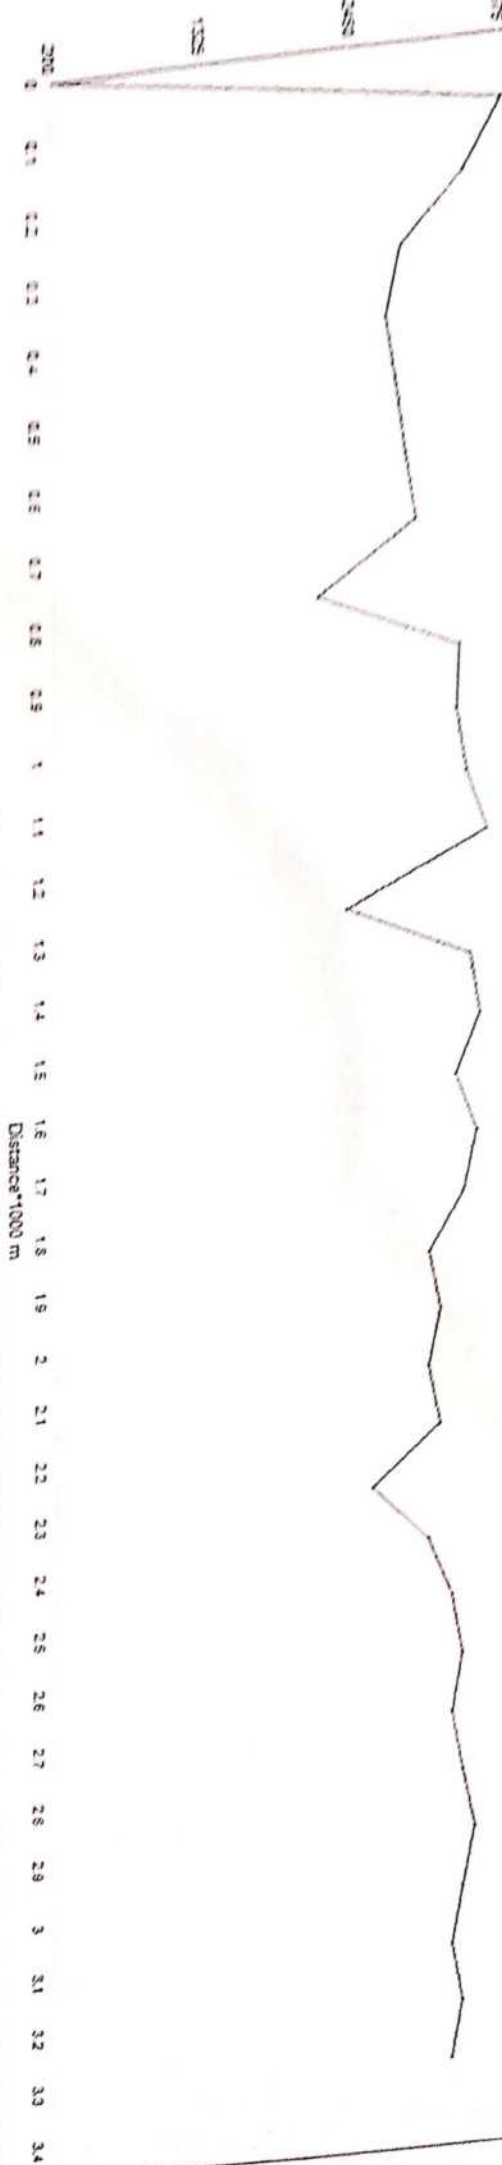

5-5-22
5-5-22
5-5-22

72-50-50
46

05/05/22
