

कार्यपालक अभियन्ता का कार्यालय,

ग्रामीण कार्य विभाग, कार्य प्रमण्डल हथुआ।

पत्रांक- 498 अमृ० / हथुआ।

दिनांक- 05/05/2022

प्रेषक,

कार्यपालक अभियन्ता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, हथुआ।

सेवा में,

सचिव,
बिहार ग्रामीण पथ विकास अभिकरण,
बिहार पटना।

विषय - राशि उपलब्ध कराने के संबंध में।

महाशय,

उपरोक्त विषय के संबंध में कहना है कि बिहार ग्रामीण पथ नई अनुरक्षण नीति-2018 के तहत पंचवर्षीय अनुरक्षण अवधि के अधीन पथों में कराये गये त्रैमासिक अनुरक्षण कार्य हेतु राशि की अधियाचना उपलब्ध कराये गये प्रपत्र में सभी सूचनाओं के साथ अंकित कर समर्पित किया जाता है।

अनु०- यथोक्त।

विश्वासभाजन,



कार्यपालक अभियन्ता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, हथुआ।

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

PIU Name :

1	Name of the Road	NH-80 Itwa Sabayan.		
2	Batch No.	RM/06/HAT/19/0003.		
3	Project ID	31406902081		
	Total Length of Road (in Km)	6.97		
5	Length of Road to Meet Required Service Level [Completed length] (in Km) [1]	6.97		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20.		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	57.01794		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	2.850897		
Compliance Criteria	Standard Job Description	Non- Compliance		Reduction Payments [6] = [3] / [1] * [2] * [4]
		Length Non-Compliant [3]	Weighted value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGEWAY)		60%	00
II	SHOULDERS AND EMBANMENTS		10%	00
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES		15%	00
IV	SIGNAGE AND ROAD SAFETY		10%	00
V	VEGATAION		5%	00
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0
TO BE PAID FOR THE QUARTER / DEMAND (in Lakh) [6]				2.85089

Date of inspection by E/I or his agent

Prepared by Contractor's self Control unit

Name and Designation of person inspecting road

Date

Signature of person inspecting road

Certify by E/I [signature] Date:-

Name of work : NH-80 ITAWA - SABEYAN

Name of customer : GANDHU CHHAPAR CONSTRUCTION PRIVATE LIMITED

(R) Rural Road

Good	Average	Poor
< 4000	4001 - 5000	> 5000

Date	Time	Test No	Distance(m)	Total Distance(m)	BUMP(cm)	Speed(km/hr)	Ull(mm/Km)	Corrected Ull (mm/Km)	RI	Status	Latitude	Direction	Longitude	Direction	Remarks
05/04/22	11:43:31	13	0	0	0.0 cm	29.7 Km/hr	0.0 mm/Km	245	0.43	Good	26.3752413	N	84.3547220	E	Normal
05/04/22	11:47:59	13	100	100	28.0 cm	13.7 Km/hr	2800.0 mm/Km	2866	3.87	Good	26.3860846	N	84.3577967	E	Normal
05/04/22	11:48:14	13	100	200	23.0 cm	23.6 Km/hr	2300.0 mm/Km	2398	3.3	Good	26.3863897	N	84.3564310	E	Normal
05/04/22	11:48:28	13	100	300	23.0 cm	24.6 Km/hr	2300.0 mm/Km	2398	3.3	Good	26.3865576	N	84.3565304	E	Normal
05/04/22	11:48:47	13	100	400	31.0 cm	19.9 Km/hr	3100.0 mm/Km	3147	4.2	Good	26.3867979	N	84.3543634	E	Normal
05/04/22	11:49:21	13	100	500	38.0 cm	10.8 Km/hr	3800.0 mm/Km	3802	4.98	Good	26.3871107	N	84.3536158	E	Normal
05/04/22	11:49:41	13	100	600	36.0 cm	17.6 Km/hr	3600.0 mm/Km	3615	4.76	Good	26.3879480	N	84.3540201	E	Normal
05/04/22	11:50:26	13	100	700	30.0 cm	7.9 Km/hr	3000.0 mm/Km	3053	4.09	Good	26.3884974	N	84.3537760	E	Normal
05/04/22	11:50:58	13	100	800	32.0 cm	11.5 Km/hr	3200.0 mm/Km	3241	4.32	Good	26.3893232	N	84.3536158	E	Normal
05/04/22	11:51:16	13	100	900	34.0 cm	18.0 Km/hr	3400.0 mm/Km	3428	4.54	Good	26.3894911	N	84.3527994	E	Normal
05/04/22	11:51:35	13	100	1000	34.0 cm	19.8 Km/hr	3400.0 mm/Km	3428	4.54	Good	26.3893404	N	84.3516381	E	Normal
05/04/22	11:51:57	13	100	1100	36.0 cm	16.3 Km/hr	3600.0 mm/Km	3615	4.76	Good	26.3897800	N	84.3510599	E	Normal
05/04/22	11:52:24	13	100	1200	30.0 cm	13.7 Km/hr	3000.0 mm/Km	3053	4.09	Good	26.3900442	N	84.3513346	E	Normal
05/04/22	11:52:42	13	100	1300	31.0 cm	19.0 Km/hr	3100.0 mm/Km	3147	4.2	Good	26.3894091	N	84.3497755	E	Normal
05/04/22	11:52:56	13	100	1400	38.0 cm	24.4 Km/hr	3800.0 mm/Km	3802	4.98	Good	26.3895235	N	84.3488321	E	Normal
05/04/22	11:53:10	13	100	1500	33.0 cm	28.2 Km/hr	3300.0 mm/Km	3334	4.43	Good	26.3898287	N	84.3480310	E	Normal
05/04/22	11:53:24	13	100	1600	35.0 cm	25.9 Km/hr	3500.0 mm/Km	3521	4.65	Good	26.3905478	N	84.3473825	E	Normal
05/04/22	11:57:10	13	100	1700	31.0 cm	1.6 Km/hr	3100.0 mm/Km	3147	4.2	Good	26.3914919	N	84.3477411	E	Normal
05/04/22	11:57:48	13	100	1800	35.0 cm	9.3 Km/hr	3500.0 mm/Km	3521	4.65	Good	26.3925467	N	84.3479166	E	Normal
05/04/22	11:58:13	13	100	1900	34.0 cm	14.6 Km/hr	3400.0 mm/Km	3428	4.54	Good	26.3934164	N	84.3483057	E	Normal
05/04/22	11:58:47	13	100	2000	30.0 cm	10.4 Km/hr	3000.0 mm/Km	3053	4.09	Good		N		E	Normal

pkc/13/10/1
13/12/22

13/12/22
13/12/22

Name of work : NH-80 ITAWA - SABEYAN

Name of customer : GANDHU CHAPAR CONSTRUCTION PRIVATE LIMITED

(R) Rural Road		
Good	Average	Poor
< 4000	4001 - 5000	> 5000

05/04/22	11:59:04	13	100	2100	32.0 cm	21.1 Km/Hr	3200.0 mm/Km	3241	4.32	Good	26.3936777	N	84.3478419	E	Normal
05/04/22	11:59:16	13	100	2200	33.0 cm	29.1 Km/Hr	3300.0 mm/Km	3334	4.43	Good	26.3939218	N	84.3468553	E	Normal
05/04/22	11:59:27	13	100	2300	37.0 cm	31.5 Km/Hr	3700.0 mm/Km	3709	4.87	Good	26.3942022	N	84.3460169	E	Normal
05/04/22	11:59:50	13	100	2400	34.0 cm	16.6 Km/Hr	3400.0 mm/Km	3428	4.54	Good	26.3948086	N	84.3445673	E	Normal
05/04/22	12:00:07	13	100	2500	39.0 cm	19.8 Km/Hr	3900.0 mm/Km	3896	5.09	Good	26.3950453	N	84.3439112	E	Normal
05/04/22	12:00:19	13	100	2600	35.0 cm	29.7 Km/Hr	3500.0 mm/Km	3521	4.85	Good	26.3954515	N	84.3428736	E	Normal
05/04/22	12:00:32	13	100	2700	37.0 cm	29.4 Km/Hr	3700.0 mm/Km	3709	4.87	Good	26.3955804	N	84.3418870	E	Normal
05/04/22	12:00:50	13	100	2800	34.0 cm	20.6 Km/Hr	3400.0 mm/Km	3428	4.54	Good	26.3956254	N	84.3409357	E	Normal
05/04/22	12:01:18	13	100	2900	37.0 cm	12.8 Km/Hr	3700.0 mm/Km	3709	4.87	Good	26.3957208	N	84.3403025	E	Normal
05/04/22	12:01:33	13	100	3000	33.0 cm	23.1 Km/Hr	3300.0 mm/Km	3334	4.43	Good	26.3957243	N	84.3384104	E	Normal
05/04/22	12:01:48	13	100	3100	37.0 cm	23.6 Km/Hr	3700.0 mm/Km	3709	4.87	Good	26.3957243	N	84.3384104	E	Normal
05/04/22	12:02:22	13	100	3200	39.0 cm	11.1 Km/Hr	3900.0 mm/Km	3896	5.09	Good	26.3958578	N	84.3374720	E	Normal
05/04/22	12:02:42	13	100	3300	34.0 cm	17.1 Km/Hr	3400.0 mm/Km	3428	4.54	Good	26.3959246	N	84.3365564	E	Normal
05/04/22	12:02:57	13	100	3400	37.0 cm	24.5 Km/Hr	3700.0 mm/Km	3709	4.87	Good	26.3959570	N	84.3360529	E	Normal
05/04/22	12:03:16	13	100	3500	36.0 cm	18.0 Km/Hr	3600.0 mm/Km	3615	4.76	Good	26.3961191	N	84.3342981	E	Normal
05/04/22	12:03:30	13	100	3600	34.0 cm	25.4 Km/Hr	3400.0 mm/Km	3428	4.54	Good	26.3961802	N	84.3332224	E	Normal
05/04/22	12:03:42	13	100	3700	31.0 cm	30.9 Km/Hr	3100.0 mm/Km	3147	4.2	Good	26.3962164	N	84.3327494	E	Normal
05/04/22	12:03:52	13	100	3800	35.0 cm	35.2 Km/Hr	3500.0 mm/Km	3521	4.85	Good	26.3963346	N	84.3315439	E	Normal
05/04/22	12:04:13	13	100	3900	36.0 cm	17.3 Km/Hr	3800.0 mm/Km	3802	4.98	Good	26.3964319	N	84.3306971	E	Normal
05/04/22	12:04:25	13	100	4000	34.0 cm	29.7 Km/Hr	3400.0 mm/Km	3428	4.54	Good	26.3965322	N	84.3293924	E	Normal
05/04/22	12:04:37	13	100	4100	35.0 cm	30.9 Km/Hr	3500.0 mm/Km	3521	4.85	Good	26.3968077	N	84.3281565	E	Normal
05/04/22	12:04:49	13	100	4200	33.0 cm	29.7 Km/Hr	3300.0 mm/Km	3334	4.43	Good	26.3969088	N	84.3275890	E	Normal

20/10/2022

Signature

20/10/2022

Name of work : NH-80 ITAWA - SABEYAN

Name of customer : GANDHU CHHAPAR CONSTRUCTION PRIVATE LIMITED

(R)Rural Road

Good	Average	Poor
< 4000	4001 - 5000	> 5000

05/04/22	12.05.27	13	100	4300	38.0 cm	9.5 Km/Hr	3800.0 mm/Km	3802	4.98	Good	28.3970423	N	84.3202567	E	Normal
05/04/22	12.05.42	13	100	4400	34.0 cm	23.8 Km/Hr	3400.0 mm/Km	3428	4.54	Good	28.3971128	N	84.3255646	E	Normal
05/04/22	12.05.57	13	100	4500	35.0 cm	24.5 Km/Hr	3500.0 mm/Km	3521	4.65	Good	28.3971567	N	84.3243647	E	Normal
05/04/22	12.06.46	13	100	4600	32.0 cm	6.8 Km/Hr	3200.0 mm/Km	3241	4.32	Good	28.3971605	N	84.3233118	E	Normal
05/04/22	12.07.02	13	100	4700	33.0 cm	22.0 Km/Hr	3300.0 mm/Km	3334	4.43	Good	28.3972464	N	84.3224802	E	Normal
05/04/22	12.07.27	13	100	4800	31.0 cm	15.2 Km/Hr	3100.0 mm/Km	3147	4.2	Good	28.3973808	N	84.3211145	E	Normal
05/04/22	12.07.42	13	100	4900	34.0 cm	24.1 Km/Hr	3400.0 mm/Km	3428	4.54	Good	28.3974829	N	84.3204126	E	Normal
05/04/22	12.07.53	13	100	5000	38.0 cm	30.9 Km/Hr	3800.0 mm/Km	3815	4.78	Good	28.3977346	N	84.3192882	E	Normal
05/04/22	12.08.08	13	100	5100	35.0 cm	28.1 Km/Hr	3500.0 mm/Km	3521	4.65	Good	28.3979101	N	84.3181162	E	Normal
05/04/22	12.08.16	13	100	5200	33.8 cm	34.8 Km/Hr	3300.0 mm/Km	3334	4.43	Good	28.3980112	N	84.3174829	E	Normal
05/04/22	12.08.25	13	100	5300	37.0 cm	40.0 Km/Hr	3700.0 mm/Km	3709	4.87	Good	28.3981581	N	84.3161478	E	Normal
05/04/22	12.08.34	13	100	5400	31.0 cm	40.3 Km/Hr	3100.0 mm/Km	3147	4.2	Good	28.3979540	N	84.3151407	E	Normal
05/04/22	12.08.43	13	100	5500	30.0 cm	37.4 Km/Hr	3000.0 mm/Km	3053	4.09	Good	28.3979818	N	84.3143549	E	Normal
05/04/22	12.08.54	13	100	5600	28.0 cm	33.4 Km/Hr	2800.0 mm/Km	2866	3.87	Good	28.3983278	N	84.3130579	E	Normal
05/04/22	12.09.05	13	100	5700	29.0 cm	33.0 Km/Hr	2900.0 mm/Km	2960	3.98	Good	28.3984594	N	84.3124704	E	Normal
05/04/22	12.09.15	13	100	5800	29.0 cm	36.7 Km/Hr	2900.0 mm/Km	2960	3.98	Good	28.3986788	N	84.3110666	E	Normal
05/04/22	12.09.25	13	100	5900	28.0 cm	36.3 Km/Hr	2800.0 mm/Km	2860	3.88	Good	28.3987551	N	84.3105478	E	Normal
05/04/22	12.09.39	13	100	6000	30.0 cm	25.7 Km/Hr	3000.0 mm/Km	3053	4.09	Good	28.3989592	N	84.3092966	E	Normal
05/04/22	12.09.57	13	100	6100	37.0 cm	19.8 Km/Hr	3700.0 mm/Km	3709	4.87	Good	28.3991137	N	84.3088446	E	Normal
05/04/22	12.10.09	13	100	6200	30.0 cm	28.7 Km/Hr	3000.0 mm/Km	3053	4.09	Good	28.3991137	N	84.3088446	E	Normal
05/04/22	12.10.22	13	100	6300	36.0 cm	27.2 Km/Hr	3600.0 mm/Km	3615	4.78	Good	28.3991137	N	84.3088446	E	Normal
05/04/22	12.10.35	13	100	6400	37.0 cm	27.3 Km/Hr	3700.0 mm/Km	3709	4.87	Good	28.3991137	N	84.3088446	E	Normal

12/10/22

12/10/22

12/10/22

Name of work : NH-80 ITAWA - SABEYAN

Name of customer : GANDHU CHHAPAR CONSTRUCTION PRIVATE LIMITED

(R) Rural Road


Good	Average	Poor
< 4000	4001 - 5000	> 5000

05/04/22	12:10:47	13	100	6500	35.0 cm	30.9 Km/Hr	3500.0 mm/Km	3521	4.55	Good	26,399.137	N	B4,3088846	E	Normal
05/04/22	12:11:04	13	100	6600	28.0 cm	22.0 Km/Hr	2800.0 mm/Km	2866	3.87	Good	26,399.137	N	B4,3088846	E	Normal
05/04/22	12:11:16	13	100	6700	26.0 cm	27.6 Km/Hr	2600.0 mm/Km	2679	3.64	Good	26,399.137	N	B4,3088846	E	Normal
05/04/22	12:11:27	13	100	6800	32.0 cm	33.8 Km/Hr	3200.0 mm/Km	3241	4.32	Good	26,399.137	N	B4,3088846	E	Normal
05/04/22	12:11:44	13	100	6900	38.0 cm	23.2 Km/Hr	3800.0 mm/Km	3802	4.98	Good	26,399.137	N	B4,3088846	E	Normal
05/04/22	12:12:30	13	100	7000	35.0 cm	7.7 Km/Hr	3500.0 mm/Km	3521	4.55	Good	26,399.137	N	B4,3088846	E	Normal

Refined 12/03/22
12/03/22
AZ

12/03/22

Name of Customer: GANDHU CHHAPAR CONSTRUCTION PRIVATE LIMITED, Machine no: 19193, Road: NH-80 ITAWA, SAREVAN, Date: 05/04/22, Section No: 13, Equation: $Y=0.936X-245.3$

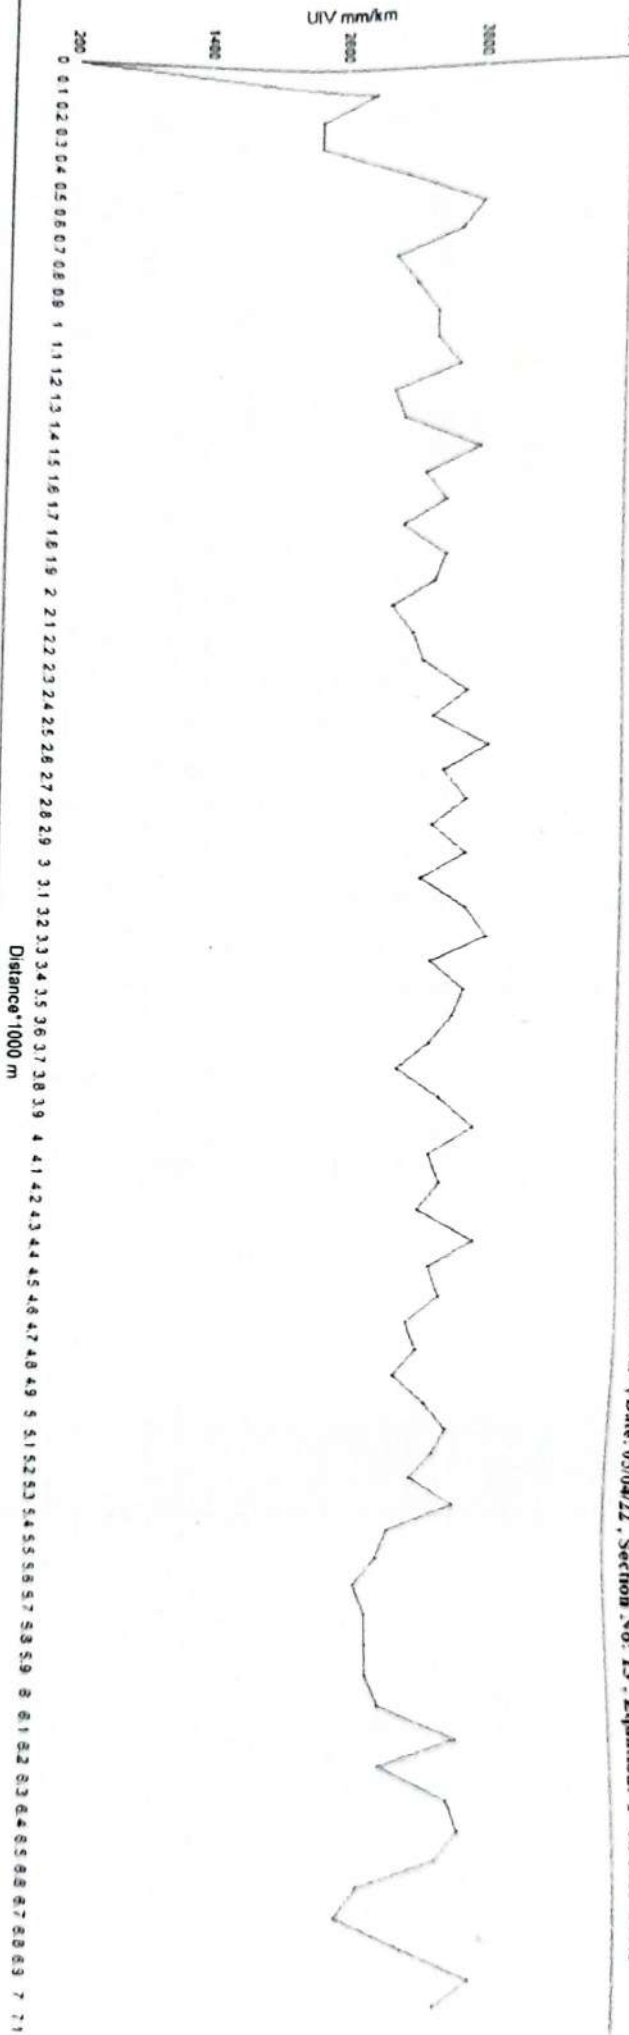

R. P. Singh

12/12/22

24/12/22

Requisition Formet for Scheme Head-MR-(3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

1 Year (1st Quarter)

RWD, Works Division Hathua

Government Of Bihar

OM01

Rural Works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From:- NH-80 ITWA to Shabeya
Length of Road :- 6.970 Km
Inspector :- J.E RWD Sub Division : uchkagaon

To:-
Executive Engineer
RWD, Works Division Hathua

Position :- J.E

Date:-

No	standard Of Work Item	Work Unit	Unit Of Required in each Kilometer										Comments
	Name		1	2	3	4	5	6	7	8	9	10	
OM100	Sealed payment												No Pot Hole Found.
OM101	Pothole Patching	m ²	Nil	Nil	Nil	Nil							Not Surface Depression & Rut Patching Found
OM102	Surface Depression and Rut patching	m ³	Nil	Nil	Nil	Nil							No Crack sealing Found
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil							No loss Of Aggregates (Surface Ravelling) Found
	Surface Treatment												No Bleeding/ Flushing Required
OM104	(a) Loss of Aggregate (Surface Ravelling)	m ²	Nil	Nil	Nil	Nil							No Crocodile Cracking Found
	(b) Bleeding / Flushing	m ²	Nil	Nil	Nil	Nil							No Edge Repair Required
	(c) Crocodile Cracking	m ²	Nil	Nil	Nil	Nil							
105	Edge Repair	m ²	Nil	Nil	Nil	Nil							
106	Digouts	m ²	N.A	N.A	N.A	N.A							
107	Concrete pavement	m ³	N.A	N.A	N.A	N.A							
	Other activities												
OM200	Shoulder												
	(a) Edge Drop-off	Lm	Nil	Nil	Nil	Nil							No Edge Drop-Off Required
OM201	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil	Nil	Nil							Not Required
	(c) Holding water	Lm	Nil	Nil	Nil	Nil							No Holding Water Found
OM202	Embankment Repair	M ³	Nil	Nil	Nil	Nil							Not Required
	Other activities (Rain Cuts)												
OM300	Drainage including culverts major	Lm	N.A	N.A	N.A	N.A							Not Required
OM301	Surface Drains & Verge	No	Nil	Nil	Nil	Nil							Not Required
OM302	Culvert Cleaning	M ³	Nil	Nil	Nil	Nil							Not Required
OM303	Culvert and pit Repair	M ²	Nil	Nil	Nil	Nil							Not Required
	Other activities(Whitw washing)	M ²	Nil	Nil	Nil	Nil							Not Required

15/11/2018

Inspector

Signature

No	standard Of Work Item	Work Unit	1	2	3	4	5	6	7	8	9	10	Comments
OMA00	Vegetation												Not Required
	Grass Control												Not Required
	(a) Roadside- General Tidy	Ha	Nil	Nil	Nil	Nil							Not Required
OMA01	(b) Clear near Safety signs, kilometer posts and roadside furniture	Ha	Nil	Nil	Nil	Nil							Not Required
	Tree and Shrub Management	No	Nil	Nil	Nil	Nil							Not Required
	Cutting Of Branches Of Trees	No	Nil	Nil	Nil	Nil							Not Required
OMA02	Cutting Of Shrubs From Road Way	No	Nil	Nil	Nil	Nil							Not Required
	Other activities (Trimming of Grass)	M ²	Nil	Nil	Nil	Nil							Not Required
OMS00	Safety Signage and Road		Nil										Not Required
OMS01	Signs Maintenance	No	Nil	Nil	Nil	Nil							Not Required
OMS02	Guard Stones	Lm	N/A	N/A	N/A	N/A							Not Required
OMS03	Distance Stones	No	N/A	N/A	N/A	N/A							Not Required
OMS04	Road Marking	M ²	Nil	Nil	Nil	Nil							Not Required
	Other activities												Not Required

Rhino 11/05/10/12

12/5/12

12/5/12
