

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मुजफ्फरपुर पूर्वी-1

पत्रांक.....1153

दिनांक.....10/06/2022

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मुजफ्फरपुर पूर्वी-1

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव
बिहार ग्रामीण पथ विकास अभिकरण,
बिहार पटना।


विषय: नई अनुरक्षण नीति 2018 अंतर्गत वित्तीय वर्ष 2022-23 में अनुरक्षण मद में व्यय हेतु आवंटन की मांग।

महाशय,

उपर्युक्त विषय के संबंध में नई अनुरक्षण नीति 2018 अंतर्गत वित्तीय वर्ष 2022-23 में अनुरक्षण मद में व्यय हेतु संलग्न विवरणी के अनुसार 22.02865 (बाईस लाख दो हजार आठ सौ पैसठ) रुपये का आवंटन उपलब्ध कराने की कृपा की जाये ताकि किये गये कार्यों का भुगतान किया जा सके।

अनुलग्नक:- यथोक्त।

विश्वासभाजन



10.06.22

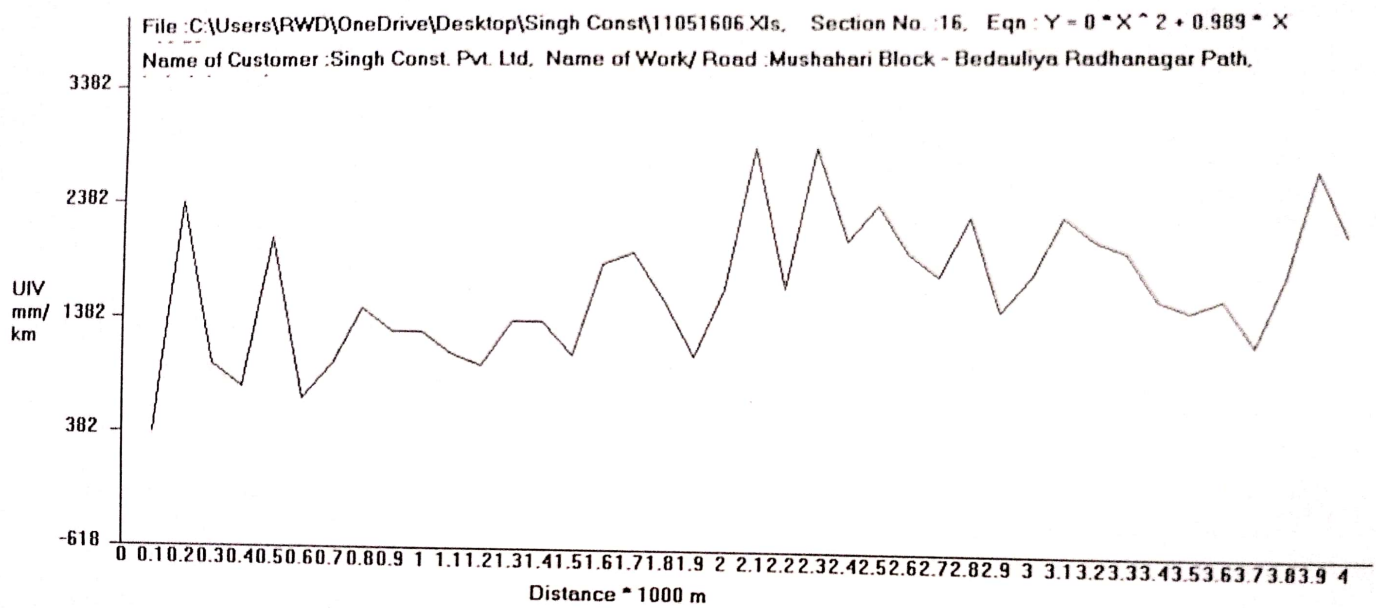
कार्यपालक अभियंता,
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मुजफ्फरपुर पूर्वी-1

Maintenance Requisition Formate for Scheme Head- MR (3054) Under Bihar Rural Road Maintenance Policy-2018

Name of Works Division:- Muzaffarpur East-1

Road Details				Actual Date of Completion	AA Details		Agreement							Actual Maintenance Expenditure							Length as per Bump Report	IRI As per bump Report	Current Maintenance Demand						Remarks
SL No.	Name of Raods	Batch No.	Project ID		Main Work Amount (in Lakh)	Maintenance Amount (in lakh)	Main Work Amount (in Lakh)	Agreement-1	Agreement-2	Agreement-3	Agreement-4	Agreement-5	Total Maintenance	Length (in KM)	1st. Year Maintenance	2nd. Year Maintenance	3rd. Year Maintenance	4th Year Maintenance	5th Year Maintenance	Total Maintenance Expenditure			1st QTR Maintenance	2nd QTR Maintenance	3rd QTR Maintenance	4th QTR Maintenance	5th QTR Maintenance	Total	
1	SHERPUR CHOWK NH-28 SHERPUR VIA SHERPUR MIDDLE SCHOOL	RM/MUMUZ/19/0019	1010357	20/08/2020	42.429	19.83000	38.03500	0.50787	1.32786	4.71510	1.25903	4.75608	12.56614	2.300	0.000	0.000	0.000	0.000	0.000	0.000	2.30	1930.000	0.62831	0.62831	0.62831	0.62831	0.62831	3.14154	
2	Construction of Patahi Chowk se Madhubani Chowk hote huw Chousuma School Pakari Parmanadpur Dubetol hote hue sakri road mai towards sadak Nirman Karya	RM/MUMUZ/19/0019	310701018	20/04/2021	76.750	30.28000	68.98400	1.62533	3.05954	7.81190	3.67769	8.58930	24.78376	3.000	0.000	0.000	0.000	0.000	0.000	0.000	3.00	2211.230	1.23919	1.23919				2.47838	
3	MUSHARI BLOCK - BEDAULIAR ADHANAGAR PATH	RM/MUMUZ/19/0019	NEA22002568	20/08/2020	79.000	41.65000	71.05500	2.21353	4.15898	10.60720	5.00471	11.64645	33.63087	4.050	0.000	0.000	0.000	0.000	0.000	0.000	4.05	1647.000	1.68154	1.68154	1.68154	1.68154	1.68154	8.40772	
4	NH-77 Bikanpur - Bakhari NH57 path	RM/MUMUZ/19/0019	NEA22002569	20/08/2020	109.275	39.66900	61.42600	2.11142	3.96033	10.09008	4.76425	11.07800	32.00408	3.850	0.000	0.000	0.000	0.000	0.000	0.000	3.85	1881.000	1.60020	1.60020	1.60020	1.60020	1.60020	8.00102	
Total																												22.02865	


 Executive Engineer
 R.W.D. Works Division
 Muzaffarpur East-1



[Signature]
 10.06.22
 J.E

[Signature]
 10/06/22
 A.E

[Signature]
 10.06.22

Name Of Road:- Mushahari Block - Bedauliya Radhnagar

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI In MM/Km	CATEG ORY ROAD	Latitude	Longitu de	Event	Y = 0 * X ^ 2 + 0.989 * X - 13.58	
25/ 5/ 22	14: 24: 25	16	0.1	40	0	400	382	G	26.93748	85.44675	Normal	X = 2143	
25/ 5/ 22	14: 24: 25	16	0.1	240	20.2	2400	2360	G	26.94602	85.44689	Normal	Y = 2106	
25/ 5/ 22	14: 25: 0	16	0.1	100	20.2	1000	975	G	26.95538	85.44685	Normal		
25/ 5/ 22	14: 25: 0	16	0.1	80	20.2	800	778	G	26.96473	85.44685	Normal		
25/ 5/ 22	14: 25: 36	16	0.1	210	10.1	2100	2063	G	26.96798	85.44758	Normal	(R) RURAL ROAD	
25/ 5/ 22	14: 26: 0	16	0.1	70	20.2	700	679	G	26.96792	85.44867	Normal	Good	Average Poor
25/ 5/ 22	14: 26: 11	16	0.1	100	20.2	1000	975	G	26.96748	85.44965	Normal	<4000	4001-5000 >5001
25/ 5/ 22	14: 26: 11	16	0.1	150	30.3	1500	1470	G	26.96803	85.45071	Normal		
25/ 5/ 22	14: 26: 11	16	0.1	130	20.2	1300	1272	G	26.96935	85.452	Normal		
25/ 5/ 22	14: 26: 46	16	0.1	130	20.2	1300	1272	G	26.97155	85.45266	Normal		
25/ 5/ 22	14: 27: 0	16	0.1	110	30.3	1100	1074	G	26.9718	85.45369	Normal		
25/ 5/ 22	14: 27: 21	16	0.1	100	20.2	1000	975	G	26.9703	85.4547	Normal		
25/ 5/ 22	14: 27: 21	16	0.1	140	10.1	1400	1371	G	26.96663	85.45551	Normal		
25/ 5/ 22	14: 27: 21	16	0.1	140	30.3	1400	1371	G	26.96638	85.45652	Normal		
25/ 5/ 22	14: 28: 0	16	0.1	110	10.1	1100	1074	G	26.96138	85.45715	Normal		
25/ 5/ 22	14: 28: 31	16	0.1	190	20.2	1900	1866	G	26.95342	85.45746	Normal		
25/ 5/ 22	14: 28: 31	16	0.1	200	20.2	2000	1964	G	26.94518	85.45763	Normal		
25/ 5/ 22	14: 29: 6	16	0.1	160	20.2	1600	1569	G	26.94235	85.45855	Normal		
25/ 5/ 22	14: 30: 17	16	0.1	110	0	1100	1074	G	26.93902	85.45955	Normal		
25/ 5/ 22	14: 30: 52	16	0.1	170	10.1	1700	1668	G	26.93942	85.46052	Normal		
25/ 5/ 22	14: 31: 0	16	0.1	290	20.2	2900	2855	G	26.93805	85.46153	Normal		
25/ 5/ 22	14: 31: 27	16	0.1	170	10.1	1700	1668	G	26.93658	85.46246	Normal		
25/ 5/ 22	14: 31: 27	16	0.1	290	10.1	2900	2855	G	26.94585	85.46263	Normal		
25/ 5/ 22	14: 32: 3	16	0.1	210	10.1	2100	2063	G	26.95508	85.46269	Normal		
25/ 5/ 22	14: 32: 3	16	0.1	240	20.2	2400	2360	G	26.96408	85.46259	Normal		
25/ 5/ 22	14: 32: 38	16	0.1	200	20.2	2000	1964	G	26.97257	85.46254	Normal		
25/ 5/ 22	14: 33: 0	16	0.1	180	20.2	1800	1767	G	26.98213	85.46224	Normal		
25/ 5/ 22	14: 33: 13	16	0.1	230	20.2	2300	2261	G	26.99123	85.462	Normal		
25/ 5/ 22	14: 33: 13	16	0.1	150	20.2	1500	1470	G	26.10003	85.46173	Normal		
25/ 5/ 22	14: 33: 49	16	0.1	180	20.2	1800	1767	G	26.10096	85.46155	Normal		
25/ 5/ 22	14: 34: 0	16	0.1	230	10.1	2300	2261	G	26.10183	85.46145	Normal		
25/ 5/ 22	14: 34: 24	16	0.1	210	20.2	2100	2063	G	26.10273	85.46113	Normal		
25/ 5/ 22	14: 34: 24	16	0.1	200	20.2	2000	1964	G	26.10361	85.46093	Culvert		
25/ 5/ 22	14: 35: 0	16	0.1	160	30.3	1600	1569	G	26.10456	85.46074	Normal		

25/5/22 14:35:0	16	0.1	150	30.3	1500	1470	G	26.1054	85.46052	Normal
25/5/22 14:35:0	16	0.1	160	20.2	1600	1569	G	26.10586	85.4599	Normal
25/5/22 14:35:34	16	0.1	120	20.2	1200	1173	G	26.10579	85.45884	Normal
25/5/22 14:35:34	16	0.1	180	20.2	1800	1767	G	26.1057	85.45785	Normal
25/5/22 14:36:10	16	0.1	270	20.2	2700	2657	G	26.1054	85.45687	Normal
25/5/22 14:36:10	16	0.014	30	90.9	2143	2106	G	26.10533	85.45665	Normal
					Avg	1647				

[Signature]
10.06.22
J.E

[Signature]
10/06/22
A.C

[Signature]
10.06.22

Requisition Format for Scheme Head - MR (3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division :- Muzaffarpur East-I

Government of Bihar
OM01
Rural works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From- MUSHARI BLOCK -
BEDAULIARADHANAGAR PATH
Length of Road: 4.05 KM

Period : From.....
Inspector: A.E RWD Sub Division, Mushari

To: Executive Engineer
RWD Works Division Muzaffarpur East-I

Date:

Position: A.E

Standard Work item		Work	Units of work required in each kilometre										Comments
S No	Name	Units	1	2	3	4	5	6	7	8	9	10	
OM100 Sealed Pavement													
OM101	Pothole Patching	m2	Nil	Nil	Nil	Nil							No. Pothole found.
OM102	Surface Depression and Rut Patching	m2	Nil	Nil	Nil	Nil							No Surface Depression and Rut Patching found
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil							No Crack Sealing found
OM104	Surface Treatment												
	(a) Loss of Aggregate (Surface Ravelling)	m2	Nil	Nil	Nil	Nil							No Loss of Aggregate (Surface Ravelling) found
	(b) Bleeding/Flushing	m2	Nil	Nil	Nil	Nil							No Bleeding/Flushing Required
	(c) Crocodile Cracking	m2	Nil	Nil	Nil	Nil							No Crocodile Cracking found
OM105	Edge Repair	m2	Nil	Nil	Nil	Nil							No Edge Repair Required
OM106	Digouts	m2	N/A	N/A	N/A	N/A							
OM107	Concrete Pavement	m3	N/A	N/A	N/A	N/A							
	Other activities	Lm											
OM200 Shoulder													
OM201	Unsealed Shoulder	No											
	(a) Edge Drop off	Lm	Nil	Nil	Nil	Nil							No Edge Drop off Required
	(b) Roughness, Scouring or Potholes	Lm	Nil	3%	2%	Nil							Defects rectified within stipulated time.
	(c) Holding Water	Lm	Nil	Nil	Nil	Nil							No Holding water found
OM202	Embankment Repair	No	Nil	Nil	Nil	Nil							No Embankment Repair Required
	Other Activite (Raincut)		3%	1%	2%								Defects rectified within stipulated time.
OM 300 Drainage including culverts major													
OM301	Surface Drains & Verge	Lm	N/A	N/A	N/A	N/A							Not Required
OM302	Culvert Cleaning	Lm											Culvert maintain within stipulated time
OM303	Culvert and Pit repair	m2	Nil	Nil	Nil	Nil							Not Required

	Other activities (White Washing)	m2	Nil	Nil	Nil	Nil							Not Required
OM 400 Vegetation													
OM401	Grass Contorol												
	a) Roadside-General Tidy	Ha	Nil	Nil	Nil	Nil							Not Required
	b) Clear near Safety signs, kilometre posts and roadside furniture	Ha	Nil	Nil	Nil	Nil							Not Required
OM402	Tree and shrub management	No	Nil	Nil	Nil	Nil							Not Required
	Cutting trees	No	Nil	Nil	Nil	Nil							Not Required
	Cutting Shrubs	No	Nil	Nil	Nil	Nil							Not Required
	Other activities (Trimming of Grass)	M2	Nil	Nil	Nil	Nil							Not Required
OM500	Safety Signage and Road												Not Required
OM501	Signs Maintenance	No	Nil	Nil	Nil	Nil							Not Required
OM502	Guard Stones	Lm	N/A	N/A	N/A	N/A							Not Applicable
OM503	Distance Stones	No	N/A	N/A	N/A	N/A							Not Applicable
OM504	Road Marking	m2	Nil	Nil	Nil	Nil							Not Required
Other activities													

SINGH CONSTRUCTION PVT. LTD.

Satish Kumar
Managing Director
Bidder

10.6.22
Appendix
10/6/22
A.C

10.6.22
Executive Engineer, Rural Work Department, Work
Division, Muzaffarpur East I

STANDRAD FORMAT FOR ROADS QUARTERLY STATEMENT

1	Name of the Road	MUSHARI BLOCK - BEDAULIARADHANAGAR PATH
2	Batch No.	
3	Project ID	RM/MU/MUZ/19/0019
4	Total Length of Road (in Km)	NEA220002668
5	Length of Road to Meet Required Service Level [Completed length] (in Km)	4.05
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	4.05
7	Ordinary Maintenance Cost as per Schedule (Agreement Amount for Maintenance) (in Lakh)	20
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh)	33.63087
	(2)	1.68154

Compliance Criteria	Standard Job Description	Non-Compliant		Reduction Payment (6) = (3) / (1) * (2) * (4)
		Length Non Compliant (3)	Weighted Value for Payment Reduction (%) (4)	
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0.00000
II	SHOULDERS AND EMBANMENTS	0	10%	0.00000
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0	15%	0.00000
IV	SIGNAGE AND ROAD SAFETY	0	10%	0.00000
V	VEGATAION		5%	0.00000
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0.00000
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh) [6]				0.00000
				1.68154

Date of inspection by E/I or his agent Prepared by
Contractor's self Control unit

Date

Signature of person inspecting road

Name and Designation of person inspecting road
(Signature)

Certify by E/I (signature) Date
