

**कार्यपालक अभियंता का कार्यालय, ग्रामीण कार्य विभाग,
कार्य प्रमंडल पकड़ीदयाल, पूर्वी चम्पारण।**

पत्रांक.....690 अफ्फ

पकड़ीदयाल,

दिनांक 3.6.22

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल पकड़ीदयाल।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी,
-सह-सचिव BRRDA,
बिहार, पटना।

**विषय :- MR-3054 (New Maintenance Policy 2018) के अन्तर्गत 5 (पॉच) वर्षीय
अनुरक्षण हेतु अधियाचना के संबंध में।**

प्रसंग :- अभियंता प्रमुख, ग्रामीण कार्य विभाग, बिहार, पटना के पत्रांक-मु0अ0-4 (मु0)
3054-04-229/2021-2021-1135 अनु0 पटना दिनांक-09.03.2022

महाशय,

उपरोक्त विषयक एवं प्रासंगिक पत्र में दिये गये निर्देश के आलोक में नई अनुरक्षण नीति-2018 अन्तर्गत पथों के अनुरक्षण की राशि के आवंटन हेतु विहित प्रपत्र में तैयार कर आवश्यक कार्रवाई हेतु समर्पित की जा रही है।

अतः MR-3054 (New Maintenance Policy 2018) के अन्तर्गत MR-N/19-20 Pakridayal/-10 (1). Khutauna Avdhesh Singh House To Bharam Asthan. (2). Sikarganj Patahi Pitch Road At Dumari To Mahamadi Siwan Via Mahamada. (3) Bokane To Mishra Tola Path High Level RCC Pull. (4) Kodariya Pitch Road To Betauna Parti Tola. (5) Bakhari To Bhitgharwa. (6) Champapur Jai Mangal Rai House To Mirjaupr Siwan. (7) Gamhariya To Gonahi Road. (8) Bara Sankar Bhaya Karmohana Pakki Road To Mahamadi. (9) Narkatiya To Chainpur Road. (10) Narkatiya Sanskrit School To Betauna. (11) Betauna Hanuman Mandir To Parti Tola. (12) Sikarganj Pitch Road To Balua Primary School. पथ के अनुरक्षण हेतु अधियाचित प्रपत्र में दर्शाये गए राशि उपलब्ध कराने की कृपा की जाए। कार्य का निरीक्षण किया गया एवं कराया गया कार्य संतोषप्रद है। उक्त पथों में ए0टी0आर0 लंबित नहीं है।

अनु0 :- यथोक्त।

विश्वासभाजन

K. Singh
36/22
कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, पकड़ीदयाल।

Division Pakridayal
of Bihar

Rural Works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From:- Betauna Hanuman Mandir To Parti Tola.
(Package No. MR-N/19-20 Pakridayal/-10)

To:-

**Executive Engineer
RWD, Works Division Pakridayal**

Date:-

Length of Road :- 0.950 Km

Period :- From:- 12-08-2021 To 11-11-2021

Inspector :- A.E RWD Sub Division : Patahi

Position :- A.E

Standard Of Work Item										Work	Unit Of Required in each Kilometer										Comments
No	Name	Unit	1	2	3	4	5	6	7	8	9	10									
OM100	Sealed payment												Defects Rectified within stipulated time								
OM101	Pothole Patching	m ²	8.91										Defects Rectified within stipulated time								
OM102	Surface Depression and Rut patching	m3	0.03										Defects Rectified within stipulated time								
OM103	Crack Sealing	Lm	380.00																		
OM104	Surface Treatment												Defects Rectified within stipulated time								
	(a) Loss of Agreegate (SurfaceRavelling)	m ²	8.91										No Bleeding/ Flushing Required								
	(b) Bleeding / Flushing	m ²	Nil										No Crocodile Cracking Found								
	© Crocodile Cracking	m ²	Nil										No Edge Repair Required								
105	Edge Repair	m ²	Nil										Defects Rectified within stipulated time								
106	Digous	m ²	0.67																		
	Digous	m ³	N.A																		
107	Concrate pavement																				
	Other activities																				
OM200	Shoulder																				
	Unsealed Shoulder												No Edge Drop-Off Required								
OM201	(a) Edge Drop-off	Lm	Nil										Defects Rectified within stipulated time								
	(b) Roughness, Scouring or Potholes	Lm	90.25										No Holding Water Found								
	(c) Holding water	Lm	Nil										Defects Rectified within stipulated time								
OM202	Embankment Repair	M ³	13.54										Defects Rectified within stipulated time								
	Other activities (Rain Cuts)		Nil										Not Required								
OM300	Drainage including culverts major												Not Required								
OM301	Surface Drains & Verge	Lm	N.A										Defects Rectified within stipulated time								
OM302	Culvert Cleaning	No	2										Not Required								
OM303	Culvert and pit Repair	M ³	Nil										Defects Rectified within stipulated time								
	Other activities(Whilw washing)	M ²	42										Defects Rectified within stipulated time								

Work Item Name	Work Unit	Unit OF Required in each Kilometere										Comments
		1	2	3	4	5	6	7	8	9	10	
Vegetation												
Grass Control												Not Required
OM401 (a) Roadside- General Tidy	Ha	Nil										Not Required
(b) Clear near Safety signs, kilometer posts and roadside furniture	Ha	Nil										Not Required
Tree and Shrub Management	No	Nil										Not Required
OM402 Cutting Of Branches Of Trees	No	Nil										Defects Rectified within stipuleted time
Cutting Of Shrubs From Road Way	No	380.00										Defects Rectified within stipuleted time
Other activities (Trimming of Grass)	M ²	722.00										Not Required
OM500 Safety Signage and Road		Nil										Defects Rectified within stipuleted time
OM501 Signs Maintenance	No	0.475										Not Required
OM502 Guard Stones	Lm	Nil										Defects Rectified within stipuleted time
OM503 Distance Stones	No	0.475										Not Required
OM504 Road Marking	M ²	Nil										
Other activities												

S. E
3/6/22
S.E

Ref
3/6/22

Vor digap
3/6/22
Executive Engineer,
RWD. Works Division, Pakridayal.

Standrad Format For Roads Quarterly Statement (3 rd Quarter)

PIU Name:- R.W.D.(W) Division, Pakridayal

1	Name of the Road	Betauna Hanuman Mandir To Parti Tola.		
2	Batch No.	RM/EA/PAK/19/0010		
3	Project ID	31708607009		
4	Total Length of Road(in K.M.)	0.95		
5	Length of Road to Meet Required Service Level (Completed Length)(in K.M.)	0.95		
6	No of Total Quarter(ie 3 Months as a Unit) in 5 Years	20		
7	Ordinary Maintenance Cost as per Schedule (Agreement Amount For Maintenance(in Lakh)	9.81341		
8	Quarterly Payment: 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh)	0.49067		
Compliance Criteria	Standard Job Description	Non- Compliance		Reduction Payment (6) = (3) / (1)*(2)*(4)
		Length Non Compliant	Weightred Value for Payment Reduction (%)	
	Paved Roads(Carriage Way)	0	60%	0
	Shoulders and Embankments	0	10%	0
	Cross Drainage Including Culverts and Bridges	0	15%	0
	Signage and Road Safety	0	10%	0
	Vegetation	0	5%	0
Total Payment Reduction for the Quarter (in Lakh)				0
To be Paid for the Quarter/ Demand (in Lakh)				0.49067

Date of Inspection by E/I or his agent

Prepared by Contractor's self Control unit

Name and Designation of Person inspecting road

Date:-

Signature of Person inspecting road

[Signature]
(Signature) 3/6/22

Certify by E/I (Signature) Date

[Signature]
3/6/22
S.E

Contractor Name:- M/S.S. K. BUILDERS

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event	
12/5/22	12:43:5	17	0.1	390	0	3900	3855 G		26.58538	85.196328	Normal	$Y = 0 * X^2 + 0.954 * X + 134.5$
12/5/22	12:43:5	17	0.1	370	30.3	3700	3664 G		26.586303	85.196413	Normal	$X = 11695$
12/5/22	12:43:5	17	0.1	350	30.3	3500	3473 G		26.587232	85.196582	Normal	$Y = 11291$
12/5/22	12:43:41	17	0.1	380	30.3	3800	3759 G		26.588075	85.196918	Normal	
12/5/22	12:44:0	17	0.1	390	20.2	3900	3855 G		26.588185	85.197793	Normal	(R) RURAL ROAD
12/5/22	12:44:16	17	0.1	360	30.3	3600	3568 G		26.588382	85.198602	Normal	Good
12/5/22	12:45:0	17	0.1	370	30.3	3700	3664 G		26.588893	85.19936	Curve	Average
12/5/22	12:45:0	17	0.1	320	20.2	3200	3187 G		26.589155	85.200185	Normal	Poor
12/5/22	12:45:26	17	0.1	360	20.2	3600	3568 G		26.589743	85.200487	Normal	
12/5/22	12:45:38	17	0.05	90	10.1	3600	3568 G		26.58999	85.200353	Normal	
Total:-							36161					
Avg IRI :-							3616					

Scheme:- MR New Policy
Division:- Pakridayal

31/6/22
S.E

31/6/22
S.E

31/6/22
S.E

Name of Customer : M/S. S. K BUILDERS
 Name of Work/ Road : Betauna Hanuman Mandir to Partola
 Lab Job number :
 Date : 12-05-2022
 Section No. : 17


Test Date : 12-05-2022
 Machine No : 437
 Start S No :
 Start E No :
 Weather : Normal
 Start Location :
 End Location :
 Road Name : a Hanuman Mandir to Partola
 Road Type : (R) RURAL ROAD
 Side :
 UIV Range : 2187 To 5000 Interval 1000 mm/km
 Dist Range : 0 To 1.1 0.1 * 1000 m
 Equation : $Y = 0 * X^2 + 0.954 * X + 134.5$

Print Generate Report and Graph

Redraw Graph

Map View

File : D:\2022 PAKDL (Feb 22 se)\Bump Integrator 2022\Pakridayal Div Rd Bump\Bump Read SK Builder 12.5.22\Bump
 Name of Customer : M/S. S. K. BUILDERS, Name of Work/ Road : Betauna Hanuman Mandir to Partola, Lab Job

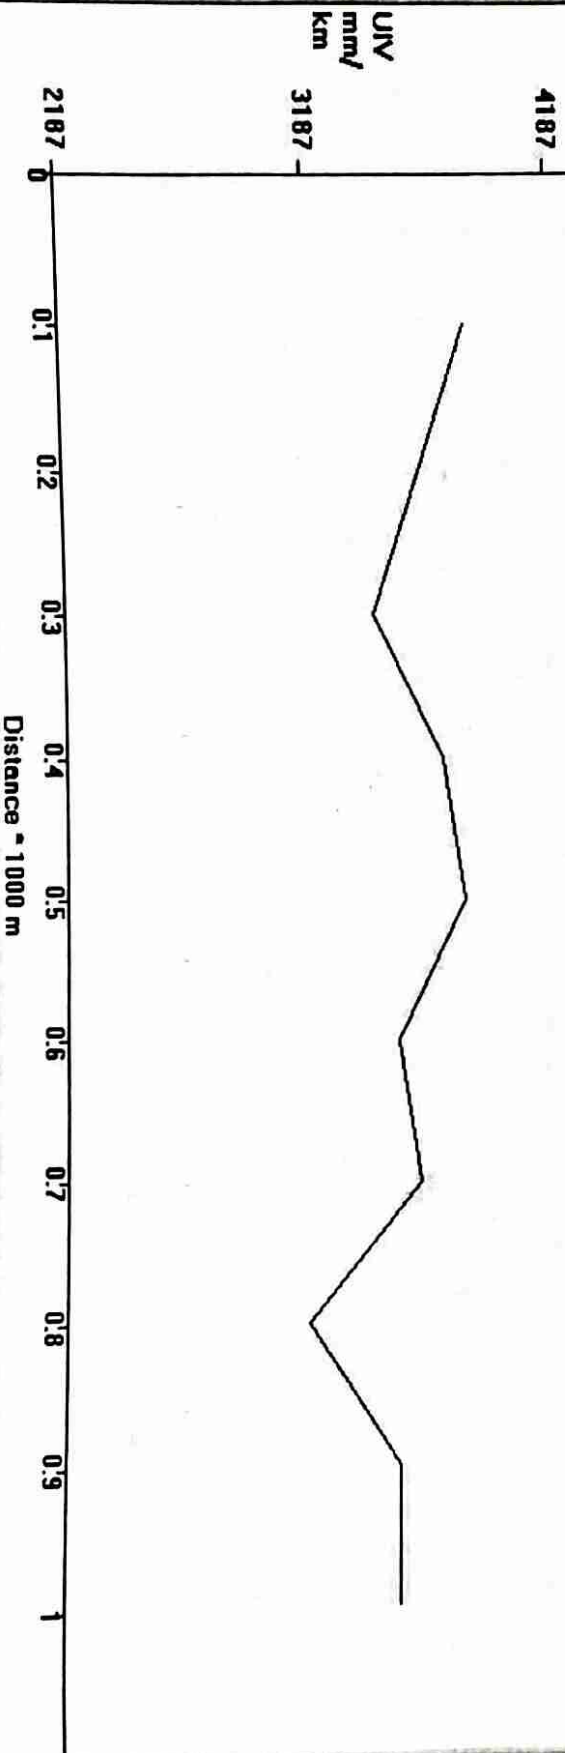

3/6/2022
 3/6/2022
 3/6/2022
