

**कार्यपालक अभियंता का कार्यालय, ग्रामीण कार्य विभाग,
कार्य प्रमंडल पकड़ीदयाल, पूर्वी चम्पारण।**

पत्रांक.....6903/मु0

पकड़ीदयाल,

दिनांक 3.6.22

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल पकड़ीदयाल।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी,
-सह-सचिव BRRDA,
बिहार, पटना।

**विषय :- MR-3054 (New Maintenance Policy 2018) के अन्तर्गत 5 (पॉच) वर्षीय
अनुरक्षण हेतु अधियाचना के संबंध में।**

प्रसंग :- अभियंता प्रमुख, ग्रामीण कार्य विभाग, बिहार, पटना के पत्रांक-मु0अ0-4 (मु0)
3054-04-229/2021-2021-1135 अनु0 पटना दिनांक-09.03.2022

महाशय,

उपरोक्त विषयक एवं प्रासंगिक पत्र में दिये गये निर्देश के आलोक में नई अनुरक्षण नीति-2018 अन्तर्गत पथों के अनुरक्षण की राशि के आवंटन हेतु विहित प्रपत्र में तैयार कर आवश्यक कार्रवाई हेतु समर्पित की जा रही है।

अतः MR-3054 (New Maintenance Policy 2018) के अन्तर्गत MR-N/19-20 Pakridayal/-10 (1). Khutauna Avdhesh Singh House To Bharam Asthan. (2). Sikarganj Patahi Pitch Road At Dumari To Mahamadi Siwan Via Mahamada. (3) Bokane To Mishra Tola Path High Level RCC Pull. (4) Kodariya Pitch Road To Betauna Parti Tola. (5) Bakhari To Bhitgharwa. (6) Champapur Jai Mangal Rai House To Mirjaupr Siwan. (7) Gamhariya To Gonahi Road. (8) Bara Sankar Bhaya Karmohana Pakki Road To Mahamadi. (9) Narkatiya To Chainpur Road. (10) Narkatiya Sanskrit School To Betauna. (11) Betauna Hanuman Mandir To Parti Tola. (12) Sikarganj Pitch Road To Balua Primary School. पथ के अनुरक्षण हेतु अधियाचित प्रपत्र में दर्शाये गए राशि उपलब्ध कराने की कृपा की जाए। कार्य का निरीक्षण किया गया एवं कराया गया कार्य संतोषप्रद है। उक्त पथों में ए0टी0आर0 लंबित नहीं है।

अनु0 :- यथोक्त।

विश्वासभाजन

K. Singh
36/22
कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, पकड़ीदयाल।

Division Pakridayal

1 Year (4th Quarter)

Rural Works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From:- Sikarganj Pith Road To Balua Primary School.
(Package No. MR-N/19-20 Pakridayal/-10)

Length of Road :- 1.100 Km

Period :- From:- 23-08-2021 To 22-11-2021

Inspector :- A.E RWD Sub Division : Patahi

To:-

Executive Engineer
RWD, Works Division Pakridayal

Position :- A.E

Date:-

[illegible]

Work Item Name	Work Unit	Unit Of Required in each Kilometer										Comments
		1	2	3	4	5	6	7	8	9	10	
OM401 Vegetation Grass Control												Not Required
(a) Roadside- General Tidy	Ha	Nil	Nil									Not Required
(b) Clear near Safety signs, kilometer posts and roadside furniture	Ha	Nil	Nil									Not Required
Tree and Shrub Management	No	Nil	Nil									Not Required
Cutting Of Branches Of Trees	No	Nil	Nil									Not Required
Cutting Of Shrubs From Road Way	No	396.00	264.00									Defects Rectified within stipulated time
Other activities (Trimming of Grass)	M ²	831.60	554.40									Defects Rectified within stipulated time
OM402 Safety Signage and Road		Nil	Nil									Not Required
OM501 Signs Maintenance	No	0.55	Nil									Defects Rectified within stipulated time
OM502 Guard Stones	Lm	Nil	Nil									Not Required
OM503 Distance Stones	No	0.55	Nil									Defects Rectified within stipulated time
OM504 Road Marking	M ²	Nil	Nil									Not Required
Other activities												

Sharon
31/6/22
S.E

Sharon
31/6/22
AK

Michael
31/6/22
Executive Engineer,
RWD. Works Division, Pakridayal.

Standrad Format For Roads Quarterly Statement (4 th Quarter)

PIU Name:- R.W.D.(W) Division, Pakridayal

1	Name of the Road	Sikarganj Pitch Road To Balua Primary School.		
2	Batch No.	RM/EA/PAK/19/0010		
3	Project ID	31708607040		
4	Total Length of Road(in K.M.)	1.1		
5	Length of Road to Meet Required Service Level (Completed Length)(in K.M.)	1.1		
6	No of Total Quarter(ie 3 Months as a Unit) in 5 Years	20		
7	Ordinary Maintenance Cost as per Schedule (Agreement Amount For Maintenance(in Lakh)	10.71078		
8	Quarterly Payment: 1/20 of Ordinary Maintennance Cost as per Schedule (in Lakh)	0.53554		
Compliance Criteria	Standard Job Description	Non- Compliance		Reduction Payment (6) = (3) / (1)*(2)*(4)
		Length Non Compliant	Weightred Value for Payment Reduction (%)	
	Paved Roads(Carriage Way)	0	60%	0
	Shoulders and Embankments	0	10%	0
	Cross Drainage Including Culverts and Bridges	0	15%	0
	Signage and Road Safety	0	10%	0
	Vegetation	0	5%	0
Total Payment Reduction for the Quarter (in Lakh)				0
To be Paid for the Quarter/ Demand (in Lakh)				0.53554

Date of Inspection by E/I or his agent

Prepared by Contractor's self Control unit

Name and Designation of Person inspecting road

Date:-

Signature of Person inspecting road

(Signature)

Certify by E/I (Signature) Date

of Road :- Sikaragani Pitch road to Balua Primary School
Contractor Name:- M/S S. K. BUILDERS

Date	Time	Section	No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km ROAD	CATEGORY	Latitude	Longitude	Event	
12/5/22	16: 16: 0	29	0.1	350	0	3500	3473 G	26.594615	85.152357 Normal				
12/5/22	16: 16: 0	29	0.1	310	10.1	3100	3091 G	26.59471	85.151347 Normal				$Y = 0 * X^2 + 0.954 * X + 134.5$
12/5/22	16: 16: 0	29	0.1	300	30.3	3000	2996 G	26.594673	85.150318 Normal				$X = 11695$
12/5/22	16: 17: 4	29	0.1	250	30.3	2500	2519 G	26.5948	85.14936 Normal				$Y = 11291$
12/5/22	16: 18: 50	29	0.1	330	30.3	3300	3282 G	26.594972	85.14837 Normal				
12/5/22	16: 19: 0	29	0.1	350	20.2	3500	3473 G	26.594812	85.14739 Curve				(R) RURAL ROAD
12/5/22	16: 19: 24	29	0.1	360	20.2	3600	3568 G	26.59461	85.14648 Normal				Good
12/5/22	16: 19: 24	29	0.1	400	20.2	4000	3950 G	26.594273	85.145605 Normal				Average
12/5/22	16: 19: 24	29	0.1	320	20.2	3200	3187 G	26.593573	85.144998 Normal				Poor
12/5/22	16: 20: 0	29	0.1	370	30.3	3700	3664 G	26.593325	85.144023 Normal				
12/5/22	16: 20: 3	29	0.1	330	30.3	3300	3282 G	26.593112	85.143113 Normal				
				Total:-			36485						
				Avg IRI :-			3317						

Scheme:- MR New Policy
Division:- Pakridayal

$$Y = 0 * X^2 + 0.954 * X + 134.5$$

$$X = 11695$$

$$Y = 11291$$

(R) RURAL ROAD
Good Average Poor
<4000 4001-5000 >5001

Signature
31/6/22
S.E

Signature
31/6/22
AD

Signature
31/6/22
AD

Name of Customer : M/S S. K. BUILDERS
Name of Work/ Road : In road to Balua Primary School
Lab Job number :
Date : 12-05-2022
Section No. : 29


Test Date : 12-05-2022
Machine No. : 437
Start S No. :
Start E No. :
Weather : Normal
Start Location :
End Location :
Road Name : In road to Balua Primary School
Road Type : (R) RURAL ROAD
Side :
Interval :
UV Range : 1519 To 5000 mm/km
Dist Range : 0 To 12 0.1 - 1000 m
Equation : $Y = 0 * X^2 + 0.954 * X + 1345$

Print Generate Report and Graph

Redraw Graph

Map View

File : D:\2022 PAKDL (Fb 22 se)\Bump Integrator 2022\Pakridayal Div Rd Bump\Bump Read SK Builder 12.5.22\Bump
 Name of Customer : M/S S. K. BUILDERS. Name of Work/ Road : Sikaraganj Pitch road to Balua Primary School.

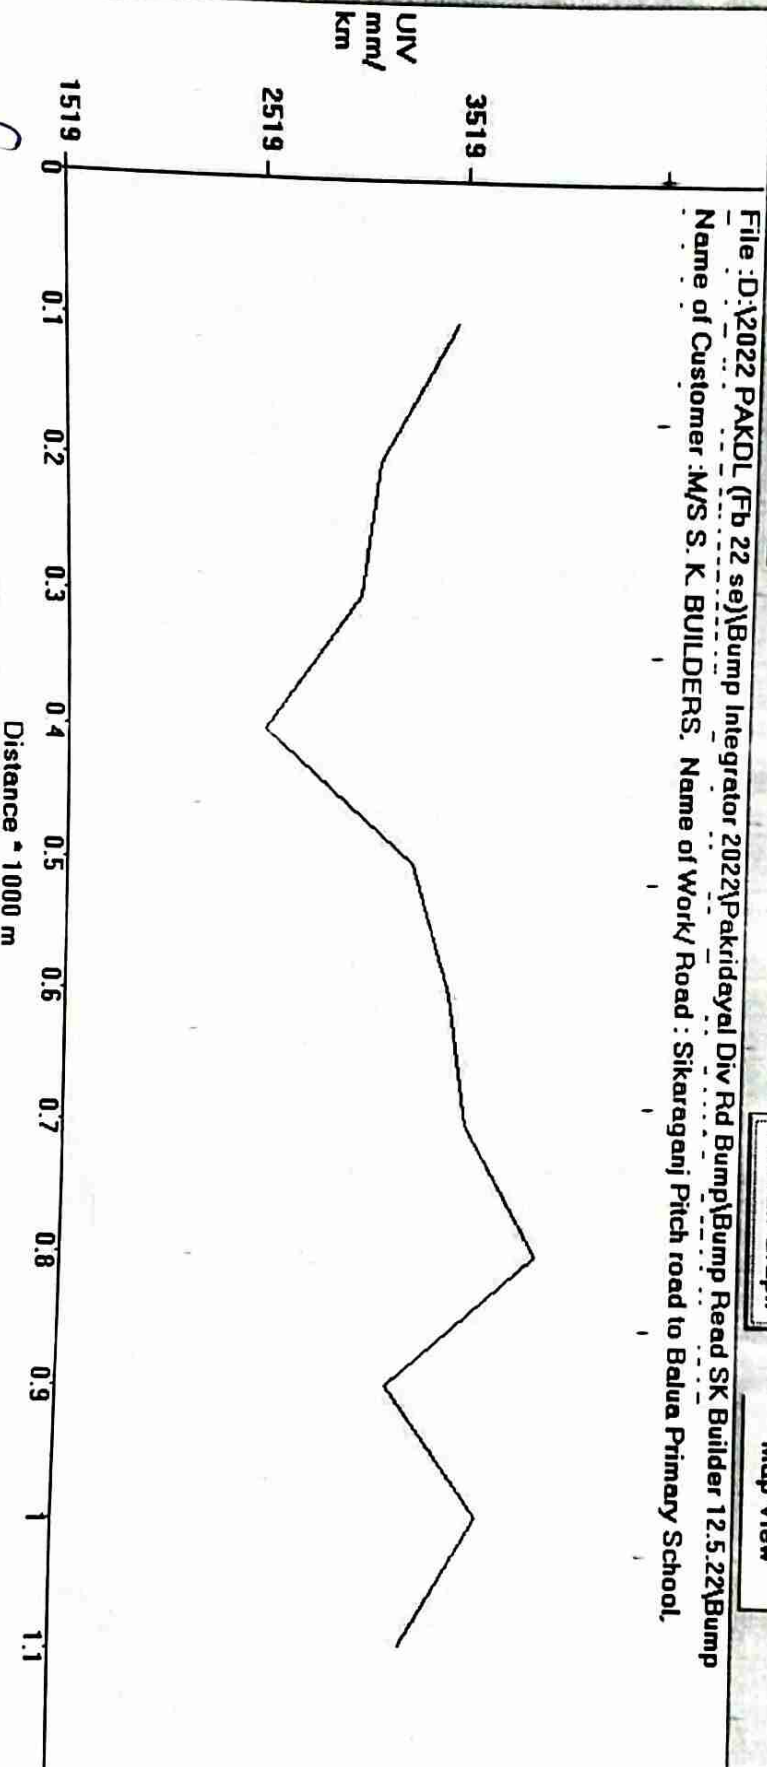

SKB
 3/6/22
 G-E

Bump
 3/6/22
 G-E
