

पत्रांक.....817 (मिनू)

मंडौल-बखरी, दिनांक...12.6.22

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल मंडौल-बखरी।

सेवा में,

नोडल पदाधिकारी,
3054 कोषांग,
ग्रामीण कार्य विभाग,
बिहार, पटना।

विषय:- शीर्ष नई अनुसंधान नीति 2018 के अंतर्गत स्वीकृत योजनाओं में किये जा रहे कार्यों के विरुद्ध
अधियाचना के संबंध में।


महाशय,

उपर्युक्त विषय के संबंध में सूचित करना है कि ग्रामीण कार्य विभाग, कार्य प्रमंडल मंडौल-बखरी
अंतर्गत कार्यान्वित कराये जा रहे नई अनुसंधान नीति 2018 के अंतर्गत Bakhri Khagaria Road to Babhin पथ
की अधियाचना (विहित प्रपत्र) में अंकित राशि रुपये 85,25,560.00 (पचासी लाख पच्चीस हजार पाँच सौ साठ)
मात्र विमुक्ति हेतु भेजी जा रही है।

अतः अनुरोध है कि उक्त संवेदक का नाम आवंटन में जोड़ने एवं उक्त अंकित राशि विमुक्त करने की
कृपा की जाए।

अनु०:-विहित प्रपत्र।

विश्वासभाजन


13/6/22

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल मंडौल-बखरी

FORM 19-A

Form of Utilisation Certificate upto 13th June 2022
MR-3054 (New Maintenance Policy 2018)

PIU : E.E. RWD, (W) Division, Manjhaul-Bakhri

Sl. No.	Name of Scheme	Sanction No. & Date with Amount (In Rs. Lacs)	Amount Received (In Rs. Lacs)	Particulars
1	Construction of Rural roads under MR-3054 (New Maintenance Policy 2018)	Vide Letter No. 17 dt 26.02.2021	29.30900	Certified that out of Rs 1556.87547 Lac received in favour of Executive Engineer, RWD, Works Division, Manjhaul-Bakhri; a sum of Rs 1556.87527 has been utilized for the purpose of MR-3054 (New Maintenance Policy 2018) Schemes as given in the margin for which it was sanctioned and that the balance Fund Rs 0.00020
		Vide Letter No. 20 dt 19.03.2021	29.30900	
		Vide Letter No. 52(Encl) dt 24.08.2021	44.80488	
		Vide Letter No. 58(Encl) dt 27.10.2021	423.51826	
		Vide Letter No. 60(Encl) dt 09.11.2021	66.75987	
		Vide Letter No. 02(Encl) dt 03.01.2022	227.65333	
		Vide Letter No. 05(Encl) dt 25.01.2022	381.46495	
		Vide Letter No. 12 (Encl) dt 28.02.2022	110.77364	
		Vide Letter No. 31 (Encl) dt 24.03.2022	102.40516	
		Vide Letter No. 43 (Encl) dt 08.04.2022	-0.01973	
		Vide Letter No. 46 (Encl) dt 13.04.2022	32.35712	
		Vide Letter No. 01 (Encl) dt 20.05.2022	108.53999	
	Total		1556.87547	

2 Certified that I have satisfied myself that the condons on which the grants-in-aid was sanctioed have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.

Kind of Cheeks exercised :-

- Works have been supervised by Executive Engineer/Superintending Engineer.
- Periodical inspection has been conducted by Executive Engineer/Superintending Engineer.
- Construction material have been tested.
- Measurements have been recorded in the MBs and test check conducted by the Assistant.
- All other / codal formalities have been observed.

3 Physical Progress achieved :-

- Construction of Road Works.
- Construction of CD Works.

alrev
13/06/22
D.A.O. II

RWD, Works Division,
Manjhaul-Bakhri

Paesin
13/6/22

Executive Engineer
RWD, Works Division,
Manjhaul-Bakhri


Requisition Format for Scheme Head - MR (3054) Under Bihar Rural Road maintenance Policy 2018 (Initial Rectification and Surface Renewal)

Name of Division : Manjhaul-Bakhri

Sl. No	Package no.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (in Lac)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in percentage	Previous Total Allotted Amount (Lac)	up to date expenditure as per MIS (in Lac)	Requisition Against work done (in lac)	Remarks
					Length (in Km)	Amount (in Lac)	Initial Rectification with Surface Renewal (in lac)	5 years Routine Maintenance (in lac)										
1	ME-N/19-20-MANJHAUL-BAKHRI/12	Bakhri Khagaria Road to Babhin	32010501004	5460/dt 16.10.19	4.200	146.54700	94.71587	41.71705	04/MBD/M R-3054/2021-22 Dt- 07.09.2021	06.06.2022	30.05.2022	Attached	25	5	0.00000	0.00000	85.25560	Completed

(Rs. Eighty Five Lac Twenty Five Thousand Five Hundred Sixty Only)

85.25560


13/6/22
Executive Engineer

RWD Works Division Manjhaul-Bakhri.

1.

No. and date of agreement.
(These four lines should be repeated at the commencement
of the measurements relating to each work).

Date of completion + 06.06.22

Agreement Rate 5.16%

Name of Agency 1 + M/S Brothers Builders

Executed
RWD W
Manjha

Scanned with CamScanner

... ..

Particulars	Debit	Credit	Balance
1. To Balance b/d			1000
2. To Cash	500		1500
3. To Bank	300		1800
4. To Sales		2000	3800
5. To Purchases	1000		2800
6. To Salaries	500		2300
7. To Rent	200		2100
8. To Interest	100		2000
9. To Dividend	100		1900
10. To Profit		1000	2900
11. To Balance c/d			2900
Total	2900	2900	

Executive Engineer
New Works Division
Bombay District

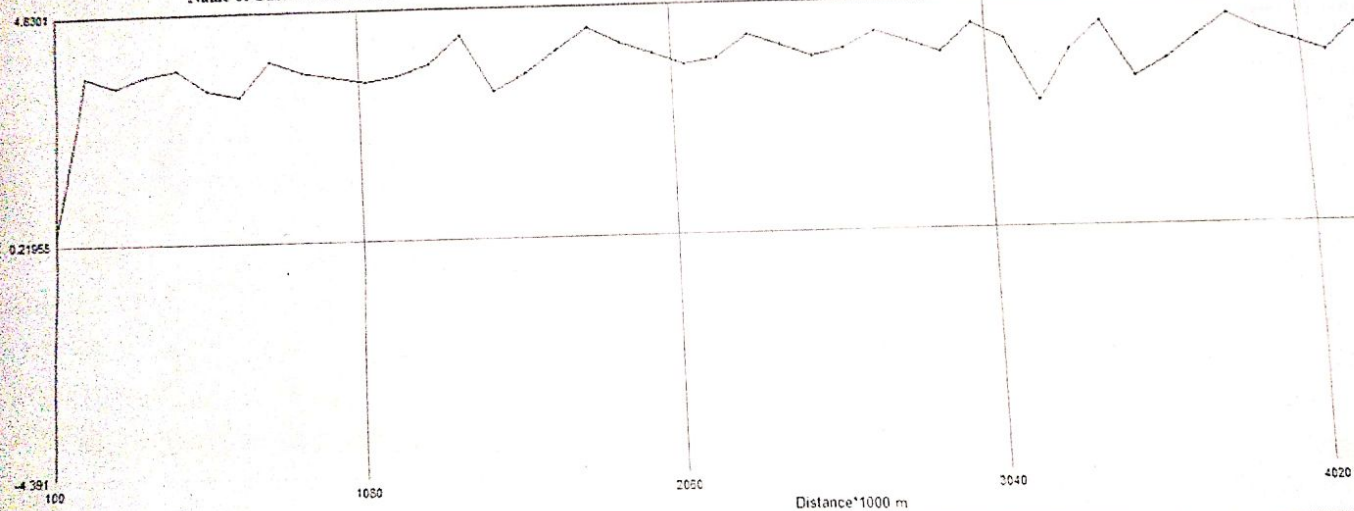
Name of Customer: M/S Brothers Builders
 Name of Work/Road: Bakhri Khagaria Road to Babhin
 Lab Job Number: 26
 Date: 25 May 2022
 Section No: 26

Test Date: 25 May 2022
 Machine no: 19204
 Start S No: 0.000
 Start E No: 4.200
 Weather:
 Start Location:
 End Location:

Road Name: Bakhri Khagaria Road to Babhin
 Road Type: (P) OG PREMIX CARPET
 Side:
 Interval:
 UIV Range: To mm/km
 Dist Range: 0.000 To 4.200 1 *1000 m
 Equations: $Y=0.929X+237.9$

Corrected IRI v/s distance Data

Name of Customer: M/S Brothers Builders, Machine no: 19204, Road: Bakhri Khagaria Road to Babhin, Date: 25-05-22, Section No: 26, Equation: $Y=0.929X+237.9$



Sanjay Kumar
 25/05/22
 26

Pradeep
 25/5/22
 AC

Pravin
 13/6/22
 EE

Name of the work: Bakhti Khagaria Road to Babbu

Date	Time	Test No	Distance (meter)	Total Distance (meter)	BUNIP (cm)	Speed (Km/Hr)	UI (mm/Km)	Corrected UI (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction	Remarks
25-05-2022	15:09:06	26	100	100	0.0 cm	5.9 Km/Hr	0.0 mm/Km	237.9	0.419	Good	25.5568226 N		86.2645193 E		Normal
25-05-2022	15:09:46	26	100	200	26.0 cm	13.6 Km/Hr	2600.0 mm/Km	2653.3	3.61	Good	25.5568907 N		86.2646005 E		Normal
25-05-2022	15:10:11	26	100	300	24.0 cm	19.0 Km/Hr	2400.0 mm/Km	2467.5	3.384	Good	25.5577758 N		86.2620499 E		Normal
25-05-2022	15:10:39	26	100	400	26.0 cm	17.6 Km/Hr	2600.0 mm/Km	2653.3	3.61	Good	25.5584412 N		86.2654429 E		Normal
25-05-2022	15:11:04	26	100	500	27.0 cm	17.8 Km/Hr	2700.0 mm/Km	2746.2	3.723	Good	25.5592714 N		86.2657357 E		Curve
25-05-2022	15:11:33	26	100	600	23.0 cm	17.6 Km/Hr	2300.0 mm/Km	2374.6	3.27	Good	25.559623 N		86.2665915 E		Normal
25-05-2022	15:11:59	26	100	700	22.0 cm	17.8 Km/Hr	2200.0 mm/Km	2281.7	3.155	Good	25.5595492 N		86.2675639 E		Normal
25-05-2022	15:12:29	26	100	800	28.0 cm	18.0 Km/Hr	2800.0 mm/Km	2839.1	3.835	Good	25.5593931 N		86.2684287 E		Normal
25-05-2022	15:12:58	26	100	900	26.0 cm	17.5 Km/Hr	2600.0 mm/Km	2653.3	3.61	Good	25.5596602 N		86.2692022 E		Normal
25-05-2022	15:13:21	26	100	1000	25.0 cm	17.0 Km/Hr	2500.0 mm/Km	2560.4	3.497	Good	25.5598511 N		86.2700458 E		Normal
25-05-2022	15:13:46	26	100	1100	24.0 cm	17.3 Km/Hr	2400.0 mm/Km	2467.5	3.384	Good	25.5598332 N		86.2708393 E		Normal
25-05-2022	15:14:08	26	100	1200	25.0 cm	18.2 Km/Hr	2500.0 mm/Km	2560.4	3.497	Good	25.5607481 N		86.2709708 E		Normal
25-05-2022	15:14:31	26	100	1300	27.0 cm	18.4 Km/Hr	2700.0 mm/Km	2746.2	3.723	Good	25.5620663 N		86.2714686 E		Normal
25-05-2022	15:14:55	26	100	1400	32.0 cm	19.7 Km/Hr	3200.0 mm/Km	3210.7	4.28	Good	25.5670371 N		86.2725705 E		Normal
25-05-2022	15:15:22	26	100	1500	22.0 cm	19.2 Km/Hr	2200.0 mm/Km	2281.7	3.155	Good	25.5610311 N		86.2728832 E		Normal
25-05-2022	15:15:47	26	100	1600	25.0 cm	19.7 Km/Hr	2500.0 mm/Km	2560.4	3.497	Good	25.560157 N		86.2728452 E		Normal
25-05-2022	15:16:11	26	100	1700	29.0 cm	21.4 Km/Hr	2900.0 mm/Km	2932	3.947	Good	25.5594542 N		86.2747569 E		Normal
25-05-2022	15:16:44	26	100	1800	33.0 cm	17.5 Km/Hr	3300.0 mm/Km	3303.6	4.391	Good	25.5597246 N		86.2737239 E		Normal
25-05-2022	15:17:10	26	100	1900	30.0 cm	18.4 Km/Hr	3000.0 mm/Km	3024.9	4.059	Good	25.5580014 N		86.2709299 E		Normal
25-05-2022	15:17:32	26	100	2000	28.0 cm	18.8 Km/Hr	2800.0 mm/Km	2839.1	3.835	Good	25.5600159 N		86.2761525 E		Normal
25-05-2022	15:17:57	26	100	2100	26.0 cm	18.1 Km/Hr	2600.0 mm/Km	2653.3	3.61	Good	25.5608909 N		86.2764968 E		Normal
25-05-2022	15:18:20	26	100	2200	27.0 cm	18.8 Km/Hr	2700.0 mm/Km	2746.2	3.723	Good	25.5618116 N		86.2768228 E		Normal
25-05-2022	15:18:42	26	100	2300	31.0 cm	18.8 Km/Hr	3100.0 mm/Km	3117.8	4.17	Good	25.5625704 N		86.277153 E		Normal

Y=0.929X+237.9
 @ RURAL ROAD
 Good 4001-
 <4000 5000
 Poor >5000

Bakhti
 25/5/22

Rudra
 25/5/22

Babbar
 13/6/22

Date	Time	Test No	Distance (meter)	Total Distance (meter)	BUMP (cm)	Speed (Km/Hr)	UI (mm/Km)	Corrected UI (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction	Remarks
25-05-2022	15:19:03	26	100	2400	29.0 cm	19.6 Km/Hr	2900.0 mm/Km	2932	3.947	Good	25.5631514	N	86.2778206	E	Normal
25-05-2022	15:19:26	26	100	2500	27.0 cm	19.6 Km/Hr	2700.0 mm/Km	2746.2	3.723	Good	25.5637801	N	86.278569	E	Normal
25-05-2022	15:19:49	26	100	2600	28.0 cm	19.2 Km/Hr	2800.0 mm/Km	2839.1	3.835	Good	25.5644371	N	86.279105	E	Normal
25-05-2022	15:20:13	26	100	2700	31.0 cm	18.9 Km/Hr	3100.0 mm/Km	3117.8	4.17	Good	25.5651666	N	86.2796596	E	Normal
25-05-2022	15:20:37	26	100	2800	29.0 cm	18.8 Km/Hr	2900.0 mm/Km	2932	3.947	Good	25.5658511	N	86.280125	E	Curve
25-05-2022	15:20:59	26	100	2900	27.0 cm	18.9 Km/Hr	2700.0 mm/Km	2746.2	3.723	Good	25.5667148	N	86.2800642	E	Normal
25-05-2022	15:21:19	26	100	3000	32.0 cm	19.9 Km/Hr	3200.0 mm/Km	3210.7	4.28	Good	25.5674222	N	86.2803267	E	Normal
25-05-2022	15:21:39	26	100	3100	29.0 cm	19.8 Km/Hr	2900.0 mm/Km	2932	3.947	Good	25.567439	N	86.2812881	E	Curve
25-05-2022	15:21:59	26	100	3200	18.0 cm	19.2 Km/Hr	1800.0 mm/Km	1910.1	2.692	Good	25.5675632	N	86.2822753	E	Normal
25-05-2022	15:22:01	26	100	3200	18.0 cm	19.2 Km/Hr	1800.0 mm/Km	1910.1	2.692	Good	25.5675632	N	86.2822753	E	Normal
25-05-2022	15:22:25	26	100	3300	27.0 cm	18.4 Km/Hr	2700.0 mm/Km	2746.2	3.723	Good	25.5680348	N	86.2830212	E	Normal
25-05-2022	15:22:25	26	100	3300	27.0 cm	18.4 Km/Hr	2700.0 mm/Km	2746.2	3.723	Good	25.5687427	N	86.2835008	E	Curve
25-05-2022	15:22:51	26	100	3400	32.0 cm	19.7 Km/Hr	3200.0 mm/Km	3210.7	4.28	Good	25.5687427	N	86.2835008	E	Curve
25-05-2022	15:22:51	26	100	3400	32.0 cm	19.7 Km/Hr	3200.0 mm/Km	3210.7	4.28	Good	25.5695249	N	86.283286	E	Normal
25-05-2022	15:23:12	26	100	3500	22.0 cm	19.2 Km/Hr	2200.0 mm/Km	2281.7	3.155	Good	25.5702555	N	86.2826441	E	Curve
25-05-2022	15:23:35	26	100	3600	25.0 cm	19.7 Km/Hr	2500.0 mm/Km	2560.4	3.497	Good	25.5702555	N	86.2826441	E	Normal
25-05-2022	15:23:35	26	100	3600	25.0 cm	19.7 Km/Hr	2500.0 mm/Km	2560.4	3.497	Good	25.5706354	N	86.2817821	E	Normal
25-05-2022	15:23:57	26	100	3700	29.0 cm	21.3 Km/Hr	2900.0 mm/Km	2932	3.947	Good	25.5708997	N	86.2808374	E	Normal
25-05-2022	15:24:21	26	100	3800	33.0 cm	17.4 Km/Hr	3300.0 mm/Km	3303.6	4.391	Good	25.5712617	N	86.2800504	E	Normal
25-05-2022	15:24:43	26	100	3900	30.0 cm	18.3 Km/Hr	3000.0 mm/Km	3024.9	4.059	Good	25.5712617	N	86.2800504	E	Normal
25-05-2022	15:24:43	26	100	3900	30.0 cm	18.3 Km/Hr	3000.0 mm/Km	3024.9	4.059	Good	25.5717844	N	86.2795654	E	Normal
25-05-2022	15:25:05	26	100	4000	28.0 cm	18.7 Km/Hr	2800.0 mm/Km	2839.1	3.835	Good	25.5717844	N	86.2795654	E	Normal
25-05-2022	15:25:05	26	100	4000	28.0 cm	18.7 Km/Hr	2800.0 mm/Km	2839.1	3.835	Good	25.5724096	N	86.2802623	E	Curve
25-05-2022	15:25:29	26	100	4100	26.0 cm	18.2 Km/Hr	2600.0 mm/Km	2653.3	3.61	Good	25.5724096	N	86.2802623	E	Normal
25-05-2022	15:25:52	26	100	4200	31.0 cm	18.7 Km/Hr	3100.0 mm/Km	3117.8	4.17	Good	25.5741529	N	86.2807577	E	Normal

Sandip
25/5/22

Ravi
25/5/22
AC

Ravi
13/6/22
EXECUTIVE ENGINEER
RURAL WORKS DEPARTMENT
WORKS DIVISION- MANJHAUL-BAKHRI
