

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल, रक्सौल।

पत्रांक :- 587 उफु

रक्सौल, /दिनांक :- 06/06/2022

प्रेषक :-

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, रक्सौल।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव,
बिहार ग्रामीण पथ विकास अभिकरण,
ग्रामीण कार्य विभाग, बिहार, पटना।


विषय :- बिहार ग्रामीण पथ अनुसंधान नीति-2018 अन्तर्गत पाँच वर्षीय रूटीन अनुसंधान कार्य मद
योजना अन्तर्गत आवंटन निर्गत करने हेतु अध्याचना के संबंध में।
महाशय,

उपर्युक्त विषयक बिहार ग्रामीण पथ अनुसंधान नीति-2018 अन्तर्गत पाँच वर्षीय रूटीन अनुसंधान
कार्य मद में संलग्न सूची के अनुसार आवंटन अध्याचना संबंधित प्रपत्र में भरकर आवश्यक कार्रवाई हेतु
समर्पित किया जाता है।


अनुलग्नक :- संलग्न सूची

1. पथों का आवंटन अध्याचना प्रपत्र।
2. Bump Integrator Report

विश्वासभाजन,



कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, रक्सौल।


05/06/22

Standard Format For Roads Quarterly Statement (3rd Quarter)

PIU Name:- Rural Works Department, (Works) Division, Raxaul

1	Name of the Road	NII-28A to Bishambarpur		
2	Batch No.	RM/EA/RAX/20/0007		
3	Project ID	31708202154		
4	Total Length of Road (In Km)	2.520		
5	Length of Road to Meet Required Service Level [Completed Length] (In Km) [1]	2.520		
6	No. of Total Quarter (i.e. 3 Months as a unit) in 5 Years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	26.61827		
8	Quarterly Payment: 1/20 of ordinary Maintenance Cost as per Schedule (in Lakh) [2]	1.33091		
Compliance Criteria	Standard Job Description	Non Compliance		Reduction Payment [6] = [3]/[1]*[2]*[4]
		Length Non Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	Paved Roads (Carriageway)	0	60%	0
II	Shoulders and Embanments	0	10%	0
III	Cross Drainage Including Culverts and Bridge	0	15%	0
IV	Signage and Road Safety	1	10%	0.05281
V	Vegataion	0	5%	0
Total Payment Reduction For the Quarterly (In Lakh) [5]				0.05281
To be Paid for the Quarter / Demand (In Lakh) [6]				1.27810

Date of Inspection by E/I or his agent 03/06/22

Prepared by Contractor's self Control Unit

Sanjay Kumar A.E
Name and Designation of person inspecting road

Date: 03.06.2022

Signature of person inspecting road
[Signature]

(Signature)

Certify by E/I [Signature] Date

Rural Works Department, Works Division, Raxaul
Government of Bihar
OM01Q

Rural Works Department

Road From: **NH-28A**

(Package No. RM/EA/RAX/20/0007)

Length of Road. 2.52 Km

Period: From 06.07.2021 to 05.10.2021

Inspector: A.E., RWD, Works Sub Division, Ramgarhwa

Position Good

Comments

Date 03/06/22

[illegible]

Standard Work Item		Work	Unit of work required in each Kilometre										Comments
No	Name	Units	1	2	3	4	5	6	7	8	9	10	
OM300 Drainage including culverts major and minor bridges													
OM301	Surface Drains & Verge	Lm	NA	NA	NA								Not Required
OM302	Culvert Cleaning	Lm	3	Nil	Nil								Defects Rectified within stipulated time
OM303	Culvert and Pit Repair	m ³	Nil	Nil	Nil								Not Required
	Other activities (White Washing)	m ²	63	Nil	Nil								Defects Rectified within stipulated time
OM400 Vegetation													
	Grass Control												Not Required
OM401	(a) Roadside General Tidy	Ha	Nil	Nil	Nil								Not Required
	(b) Clear near safety signs, kilometer posts and roadside furniture	Ha	Nil	Nil	Nil								Not Required
OM402	Tree and Shrub Management	Ha	Nil	Nil	Nil								Not Required
	Other activities												
OM500 Signage and Road Safety													
OM501	Signs Maintenance	No	Nil	Nil	Nil								Not Required
OM502	Guard stones	Lm	NA	NA	NA								Not Required
OM503	Distance Stones	No	NA	NA	NA								Not Required
OM504	Road Markings	No	Nil	Nil	Nil								Not Required
	Other activities												

Ramkrishna Kumar
Bidder

Appendix

3/6/22
A.E

8/16/22
Executive Engineer,
RWD, Works Division, Raxaul

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate mm/km	OR mm/km	IRI, TEGORY ROAD	Latitude	ongitude	Event
10/5/22	18:21:0	24	0.1	260	20.2	2600	2492 G	26.90267	84.81933	Normal
10/5/22	18:21:25	24	0.1	280	20.2	2800	2666 G	26.90225	84.82027	Normal
10/5/22	18:22:1	24	0.1	280	20.2	2800	2666 G	26.90204	84.8212	Normal
10/5/22	18:22:1	24	0.1	310	20.2	3100	2966 G	26.90187	84.82219	Normal
10/5/22	18:22:36	24	0.1	270	20.2	2700	2579 G	26.90193	84.82318	Normal
10/5/22	18:22:36	24	0.1	290	20.2	2900	2752 G	26.90266	84.82375	Normal
10/5/22	18:23:0	24	0.1	260	20.2	2600	2492 G	26.90244	84.82471	Normal
10/5/22	18:23:11	24	0.1	210	20.2	2100	2057 G	26.90231	84.82566	Normal
10/5/22	18:23:11	24	0.1	290	20.2	2900	2752 G	26.90226	84.82662	Normal
10/5/22	18:23:11	24	0.1	260	20.2	2600	2492 G	26.90247	84.82766	Normal
10/5/22	18:23:47	24	0.1	250	20.2	2500	2405 G	26.90277	84.82864	Normal
10/5/22	18:23:47	24	0.1	240	20.2	2400	2318 G	26.90305	84.8296	Normal
10/5/22	18:24:0	24	0.1	310	20.2	3100	2926 G	26.90351	84.83042	Normal
10/5/22	18:24:0	24	0.1	330	30.3	3300	3100 G	26.90412	84.83106	Normal
10/5/22	18:24:0	24	0.1	300	20.2	3000	2839 G	26.9048	84.83185	Normal
10/5/22	18:24:22	24	0.1	280	20.2	2800	2666 G	26.90558	84.83219	Normal
10/5/22	18:24:22	24	0.1	280	20.2	2800	2666 G	26.9064	84.83271	Normal
10/5/22	18:25:0	24	0.1	310	20.2	3100	2926 G	26.90668	84.83359	Normal
10/5/22	18:25:0	24	0.1	270	20.2	2700	2579 G	26.90701	84.83453	Normal
10/5/22	18:25:32	24	0.1	290	20.2	2900	2752 G	26.90645	84.83522	Normal
10/5/22	18:26:8	24	0.1	260	20.2	2600	2492 G	26.90563	84.83574	Normal
10/5/22	18:27:0	24	0.1	210	20.2	2100	2057 G	26.90608	84.83621	Normal
10/5/22	18:27:18	24	0.1	350	10.1	3500	3274 G	26.90602	84.83719	Normal
TOTAL				60874						

$$Y = 0 * X^2 + 0.869 * X + 232.9$$

X = 2111
Y = 2067

(R) RURAL ROAD
Good Average Poor
<4000 4001-5000 >5001

Handwritten signature
3/6/22
AE

AVERAGE 2640.25
3/6/22
AE

Handwritten signature
5/10/22

Name of Customer : PA CONSTRUCTION PVT LTD
 Name of Work : NH 28 SE BISHMARA PUR
 Road :
 Lab Job number :
 Date : 10-05-2022
 Section No. : 24


Test Date : 10-05-2022
 Road Name : NH 28 SE BISHMARA PUR
 Machine No : 406
 Road Type : (A) ASPHALTIC
 Start S No :
 Side :
 Start E No :
 Interval :
 Weather :
 UV Range : 1057 To 4000 1000 mm/km
 Dial Range : 0 To 23 01 ~ 1000 m
 Start Location : NH 28 SE
 End Location : SHIMBAPUR
 Equation : test

Print Generate Report and Graph

Redraw Graph

Map View


File : C:\Users\BRADAI26\Desktop\BUMP INTRE GRETOR REPORT\Bump 2nd phase\date -11-05-1\PARMABA
 Name of Customer : PARMABA CONSTRUCTION PVT LTD, Name of Work/ Road : NH 28 SE BISHMARA PUR, Lab

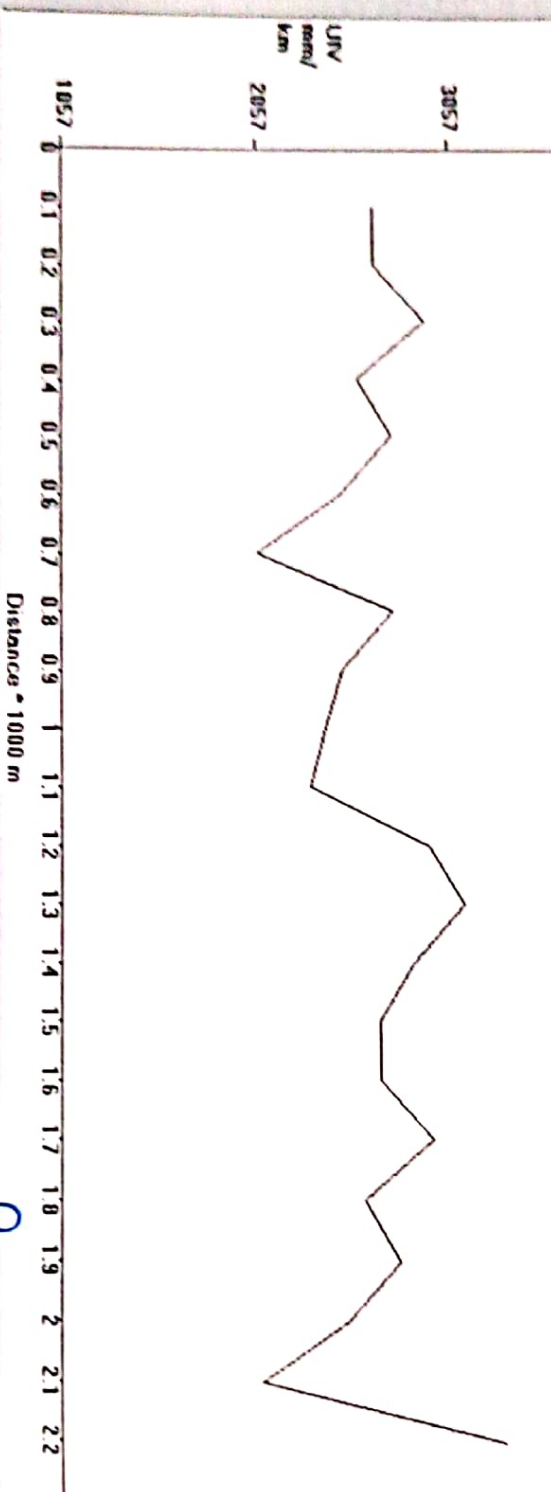

Handwritten signature
 3/6/22

Handwritten signature
 3/6/22
 AE

Handwritten signature
 5/12

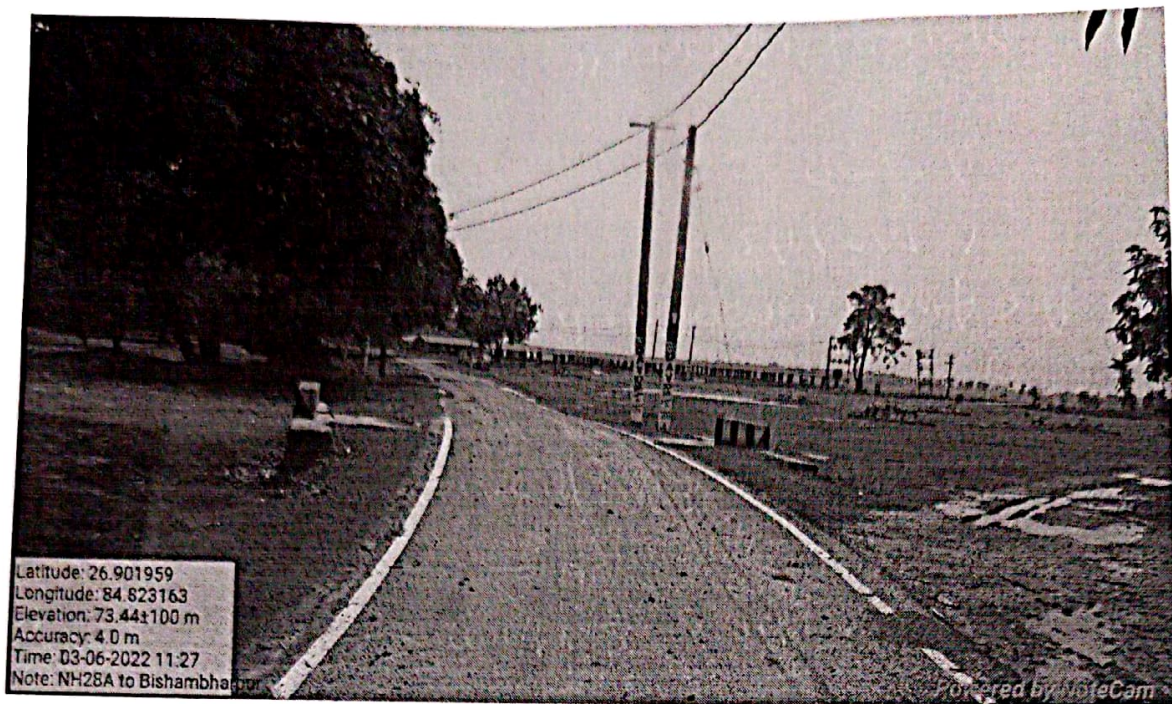





Latitude: 26.902473
Longitude: 84.8275
Elevation: 72.44±100 m
Accuracy: 3.9 m
Time: 03-06-2022 11:28
Note: NH28A to Bishambha

Powered by NoteCam
