

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल, रक्सौल।

पत्रांक :- 581 JK

रक्सौल, / दिनांक :- 06/06/2022

प्रेषक :-

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, रक्सौल।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव,
बिहार ग्रामीण पथ विकास अभिकरण,
ग्रामीण कार्य विभाग, बिहार, पटना।

विषय :- बिहार ग्रामीण पथ अनुरक्षण नीति-2018 अन्तर्गत पाँच वर्षीय रूटीन अनुरक्षण कार्य मद
योजना अन्तर्गत आवंटन निर्गत करने हेतु अधियाचना के संबंध में।


महाशय,

उपर्युक्त विषयक बिहार ग्रामीण पथ अनुरक्षण नीति-2018 अन्तर्गत पाँच वर्षीय रूटीन अनुरक्षण
कार्य मद में संलग्न सूची के अनुसार आवंटन अधियाचना संबंधित प्रपत्र में भरकर आवश्यक कार्रवाई हेतु
समर्पित किया जाता है।


अनुलग्नक :- संलग्न सूची

1. पथों का आवंटन अधियाचना प्रपत्र।
2. Bump Integrator Report

विश्वासभाजन,



कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, रक्सौल।


05/06/22

Standard Format For Roads Quarterly Statement (1st Quarter)
PIU Name:- Rural Works Department, (Works) Division, Raxaul

1	Name of the Road	Palanwa thana to Dhangar toli hote hue Bahuara		
2	Batch No.	PMGSY Road Tak		
3	Project ID	RM/EA/RAX/20/0012		
4	Total Length of Road (In Km)	31708508009		
5	Length of Road to Meet Required Service Level [Completed Length] (In Km) [1]	1.570		
6	No. of Total Quarter (i.e. 3 Months as a unit) in 5 Years	1.570		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	20		
8	Quarterly Payment: 1/20 of ordinary Maintenance Cost as per Schedule (in Lakh) [2]	15.70012		
Compliance Criteria	Standard Job Description	Non Compliance		Reduction Payment [6] = [3]/[1]*[2]*[4]
		Length Non Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	Paved Roads (Carriageway)	0	60%	0.00000
II	Shoulders and Embanments	0	10%	0
III	Cross Drainage Including Culverts and Bridge	0	15%	0
IV	Signage and Road Safety	0	10%	0
V	Vegetaion	1	5%	0.02500
Total Payment Reduction For the Quarterly (In Lakh) [5]				0.02500
To be Paid for the Quarter / Demand (In Lakh) [6]				0.76001

Date of Inspection by E/I or his agent 04/06/22

Prepared by Contractor's self Control Unit

Sayam Kumar A.E
 Name and Designation of person inspecting road

Date: 4/6/22

Signature of person inspecting road
SEL Roy.

SEL
 (Signature) 4/6/22

Certify by E/I [Signature] Date
SEL Roy.

[illegible]

Standard Work Item		Work	Unit of work required in each kilometre										Comments
No	Name	Units	1	2	3	4	5	6	7	8	9	10	
OM300 Drainage including culverts major and minor bridges													
OM301	Surface Drains & Verge	Lm	NA	NA									Not Required
OM302	Culvert Cleaning	Lm	Nil	Nil									Not Required
OM303	Culvert and Pit Repair	m ³	Nil	Nil									Not Required
	Other activities												Not Required
OM400 Vegetation													
	Grass Control												Not Required
OM401	(a) Roadside General Tidy	Ha	Nil	Nil									Not Required
	(b) Clear near safety signs, kilometer posts and roadside furniture	Ha	Nil	Nil									Not Required
OM402	Tree and Shrub Management	Ha	Nil	Nil									Not Required
	Other activities												
OM500 Signage and Road Safety													
OM501	Signs Maintenance	No	Nil	Nil									Not Required
OM502	Guard stones	Lm	NA	NA									Not Required
OM503	Distance Stones	No	NA	NA									Not Required
OM504	Road Markings	No	Nil	Nil									Not Required
	Other activities												

Pankaj Kumar Pandey
Bidder

Appendix

del 21/6/22
A.E

AWD/22
Executive Engineer,
RWD, Works Division, Raigarh

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate mm/km	OR mm/km	IRI, CATEGORY ROAD	Latitude	ongitude	Event
ROAD NAME: PALNWA THANA SE DHANGER TOLI HOTE BAHURWA PMGSY PATH TK										
10/5/22	17:25:0	21	0.1	240	20.2	2400	2318 G	26.9236	84.75859	Normal
10/5/22	17:25:0	21	0.1	310	20.2	3100	2926 G	26.9236	84.75956	Normal
10/5/22	17:25:23	21	0.1	330	30.3	3300	3100 G	26.92346	84.76051	Normal
10/5/22	17:25:23	21	0.1	300	20.2	3000	2839 G	26.92336	84.76158	Normal
10/5/22	17:25:23	21	0.1	280	20.2	2800	2666 G	26.92322	84.76258	Normal
10/5/22	17:25:23	21	0.1	280	20.2	2800	2666 G	26.92305	84.76355	Normal
10/5/22	17:26:0	21	0.1	310	20.2	3100	2926 G	26.92275	84.76451	Normal
10/5/22	17:26:0	21	0.1	270	20.2	2700	2579 G	26.92225	84.76534	Normal
10/5/22	17:26:34	21	0.1	290	20.2	2900	2752 G	26.9214	84.76505	Normal
10/5/22	17:26:34	21	0.1	260	20.2	2600	2492 G	26.92055	84.76502	Normal
10/5/22	17:27:0	21	0.1	210	20.2	2100	2057 G	26.91969	84.76505	Normal
10/5/22	17:27:8	21	0.1	290	20.2	2900	2752 G	26.91879	84.76534	Normal
10/5/22	17:27:8	21	0.1	260	20.2	2600	2492 G	26.91794	84.76534	Normal
10/5/22	17:27:8	21	0.1	250	20.2	2500	2405 G	26.91698	84.76532	Normal
10/5/22	17:27:43	21	0.1	240	20.2	2400	2318 G	26.91616	84.76519	Normal
10/5/22	17:27:43	21	0.1	310	20.2	3100	2926 G	26.91539	84.7647	Normal
		TOTAL					42214			
		AVERAGE					2638.37			

$$Y = 0 * X^2 + 0.869 * X + 232.9$$

$$X = 2111$$

$$Y = 2067$$

(R) RURAL ROAD
Good Average Poor
<4000 4001-5000 >5001

4/16/22
A.E.

4/16/22
A.E.

Name of Customer : BA CONSTRUCTION PVT LTD
 Name of Work : PALNWA THANA SE DHANGI
 Road :
 Lab Job number :
 Date : 10-05-2022
 Section No. : 21


Print Generate Report and Graph

File : C:\Users\BPRDAI26\Desktop\BUMP INTIRE GREYTOR REPORT\Bump 2nd phase\date -11-05-19\PARNABA
 Name of Customer : PARMBA CONSTRUCTION PVT LTD, Name of Work/Road : PALNWA THANA SE DHANGER

Redraw Graph

Map View

Test Date : 10-05-2022
 Machine No : 406
 Start S No :
 Start E No :
 Weather :
 Start Location : A THANA SE
 End Location : I HOTE HIDE
 Road Name : BAHURWA FMGSY PATH TK
 Road Type : (A) ASPHALTIC
 Side :
 UV Range : 1057 To 4000 Interval 1000 mm/km
 Dist Range : 0 To 15 01
 Equation : best

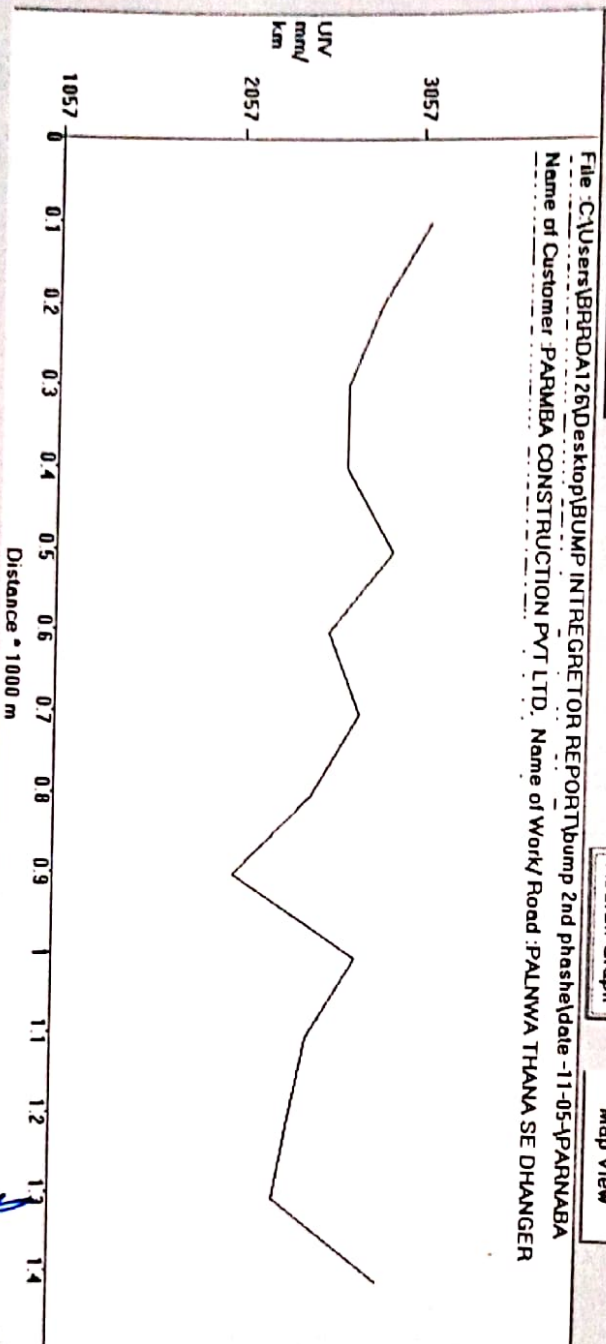

4/12/2020

21/6/22 A.E

5/1/22



Latitude: 26.923103
Longitude: 84.763125
Elevation: 72.49±100 m
Accuracy: 3.9 m
Time: 04-06-2022 16:38
Note: Palanwa Thana to Dh

Powered by NoteCam



Latitude: 26.921598
Longitude: 84.765001
Elevation: 67.49±100 m
Accuracy: 4.6 m
Time: 04-06-2022 16:37
Note: Palanwa Thana to Dhammar Toli Bahujarwa PMGSY

Powered by NoteCam





Latitude: 26.916027
Longitude: 84.765096
Elevation: 62.49±100 m
Accuracy: 3.9 m
Time: 04-06-2022 16:36
Note: Palanwa Thana to Dhamra, Odisha, India

Powered by NoteCam

