

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल, रक्सौल।

पत्रांक :- 588 34

रक्सौल, / दिनांक :- 05/06/2022

प्रेषक :-

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, रक्सौल।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव,
बिहार ग्रामीण पथ विकास अभिकरण,
ग्रामीण कार्य विभाग, बिहार, पटना।

विषय :- बिहार ग्रामीण पथ अनुरक्षण नीति-2018 अन्तर्गत पाँच वर्षीय रूटीन अनुरक्षण कार्य मद योजना अन्तर्गत आवंटन निर्गत करने हेतु अधियाचना के संबंध में।

महाशय,

उपर्युक्त विषयक बिहार ग्रामीण पथ अनुरक्षण नीति-2018 अन्तर्गत पाँच वर्षीय रूटीन अनुरक्षण कार्य मद में संलग्न सूची के अनुसार आवंटन अधियाचना संबंधित प्रपत्र में भरकर आवश्यक कार्रवाई हेतु समर्पित किया जाता है।


अनुलग्नक :- संलग्न सूची

1. पथों का आवंटन अधियाचना प्रपत्र।
2. Bump Integrator Report

विश्वासभाजन,


5/6/22

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, रक्सौल।



Standard Format For Roads Quarterly Statement (1st Quarter)

PIU Name:- Rural Works Department, (Works) Division, Raxaul

1	Name of the Road	Shekhawa Tola to Beldarwa		
2	Batch No.	RM/EA/RAX/20/0001		
3	Project ID	317851032002		
4	Total Length of Road (In Km)	2.450		
5	Length of Road to Meet Required Service Level [Completed Length] (In Km) [1]	2.405		
6	No. of Total Quarter (i.e. 3 Months as a unit) in 5 Years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	24.56310		
8	Quarterly Payment: 1/20 of ordinary Maintenance Cost as per Schedule (in Lakh) [2]	1.22816		
Compliance Criteria	Standard Job Description	Non Compliance		Reduction Payment [6] = [3]/[1]*[2]*[4]
		Length Non Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	Paved Roads (Carriageway)	0	60%	0.00000
II	Shoulders and Embanments	0	10%	0.00000
III	Cross Drainage Including Culverts and Bridge	0	15%	0
IV	Signage and Road Safety	0	10%	0.00000
V	Vegataion	1	5%	0.02553
Total Payment Reduction For the Quarterly (In Lakh) [5]				0.02553
To be Paid for the Quarter / Demand (In Lakh) [6]				1.20262

Date of Inspection by E/I or his agent 05/06/22

Prepared by Contractor's self Control Unit

Sanjay Kumar A.E
Name and Designation of person inspecting road

Date: 5/6/22

Signature of person inspecting road

(Signature)

Certify by E/I [Signature] Date

Standard Work Item		Work	Unit of work required in each Kilometre										Comments
No	Name	Units	1	2	3	4	5	6	7	8	9	10	
OM300 Drainage including culverts major and minor bridges													
OM301	Surface Drains & Verge	Lm	NA	NA	NA								Not Required
OM302	Culvert Cleaning	Lm	Nil	Nil	Nil								Not Required
OM303	Culvert and Pit Repair	m ³	Nil	Nil	Nil								Not Required
	Other activities												Not Required
OM400 Vegetation													
	Grass Control												Not Required
	(a) Roadside General Tidy	Ha	Nil	Nil	Nil								Not Required
OM401	(b) Clear near safety signs, kilometer posts and roadside furniture	Ha	Nil	Nil	Nil								Not Required
OM402	Tree and Shrub Management	Ha	Nil	Nil	Nil								Not Required
	Other activities												
OM500 Signage and Road Safety													
OM501	Signs Maintenance	No	Nil	Nil	Nil								Not Required
OM502	Guard stones	Lm	NA	NA	NA								Not Required
OM503	Distance Stones	No	NA	NA	NA								Not Required
OM504	Road Markings	No	Nil	Nil	Nil								Not Required
	Other activities												

M/S ANSAR CONSTRUCTION

Abdul Hafeez Mageri
Managing Partner

Bidder

Appendix

for 5/6/22
A-E

ANM
5/6/22
Executive Engineer,
RWD, Works Division, Raxaul

Name of Road:-Shekha Toila To Beldarwa
Name of Contractor:-M/S Ansar Construction

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR	CATEGORY	Latitude	ongitude	Event
9/3/22	17:34:0	64	0.1	280	0	2800	ROAD	26.94252	84.94498	Normal
9/3/22	17:34:21	64	0.1	270	20.2	2700		26.94334	84.9453	Curve
9/3/22	17:34:51	64	0.1	290	20.2	2900		26.94405	84.9449	Culvert
9/3/22	17:35:10	64	0.1	300	20.2	3000		26.94477	84.94542	Normal
9/3/22	17:35:41	64	0.1	260	20.2	2600		26.94521	84.94636	Normal
9/3/22	17:36:22	64	0.1	270	20.2	2700		26.94574	84.94712	Normal
9/3/22	17:36:55	64	0.1	270	20.2	2700		26.94632	84.94798	Normal
9/3/22	17:37:27	64	0.1	340	10.1	3400		26.9467	84.94887	Normal
9/3/22	17:37:57	64	0.1	300	10.1	3000		26.94704	84.94944	Normal
9/3/22	17:38:22	64	0.1	270	20.2	2700		26.94777	84.94998	Normal
9/3/22	17:38:50	64	0.1	280	20.2	2800		26.94857	84.95049	Normal
9/3/22	17:39:18	64	0.1	250	20.2	2500		26.94939	84.95096	Normal
9/3/22	17:39:58	64	0.1	300	20.2	3000		26.95016	84.95153	Normal
9/3/22	17:40:28	64	0.1	300	10.1	3000		26.95085	84.95209	Normal
9/3/22	17:40:55	64	0.1	310	10.1	3100		26.95168	84.95241	Normal
9/3/22	17:41:30	64	0.1	340	20.2	3400		26.95247	84.9529	Normal
9/3/22	17:41:58	64	0.1	320	20.2	3200		26.95328	84.95323	Normal
9/3/22	17:42:28	64	0.1	320	10.1	3200		26.95417	84.95348	Curve
9/3/22	17:42:55	64	0.1	300	20.2	3000		26.95486	84.95411	Normal
9/3/22	17:43:25	64	0.1	320	10.1	3200		26.95573	84.95431	Normal
9/3/22	17:43:53	64	0.1	220	20.2	2200		26.95662	84.95426	Normal
9/3/22	17:44:19	64	0.1	260	10.1	2600		26.95747	84.95431	Normal
9/3/22	17:44:49	64	0.1	270	20.2	2700		26.95835	84.95456	Normal
9/3/22	17:45:14	64	0.1	320	20.2	3200		26.95927	84.9547	Normal
9/3/22	17:45:44	64	0.1	320	20.2	3200		26.95945	84.95475	Normal

Total IRI	75383
Average IRI	3015.32

$$Y = 0 \cdot X^2 + 0.998 \cdot X + 109.5$$

$$X = 13889$$

$$Y = 13970$$

(R) RURAL ROAD
Good Average Poor
<4000 4001-5000 >5001

9/13/22
J.E.

09/13/22
A.E.

09/13/22

over analyzer

Name of Customer: M/S Ansar Construction
Name of Work: Shekha Tola To Beldarwa
Road:
Lab Job number: 24
Date: 09-03-2022
Section No: 64


Test Date: 09-03-2022
Machine No: 378
Road Name: Shekha Tola To Beldarwa
Road Type: (R) RUPAL ROAD
Start S No: 0.00km
Start E No: 2.450km
Side:
Weather: Normal
Interval:
UIV Range: 1305 To 5000 1000 mm/km
Start Location: Shekha Tola
Dist Range: 0 To 26 0.1 * 1000 m
End Location: Beldarwa
Equation: $Y = 0 * X^2 + 0.398 * X + 103.5$

Print Generate Report and Graph

Redraw Graph

Map View

File : C:\Users\RW\Desktop\Bump Mothari\Excel 09.03.2022\Shekha Tola To Beldarwa\09031736.xls.
Name of Customer : M/S Ansar Construction. Name of Work/ Road : Shekha Tola To Beldarwa. Lab Job number

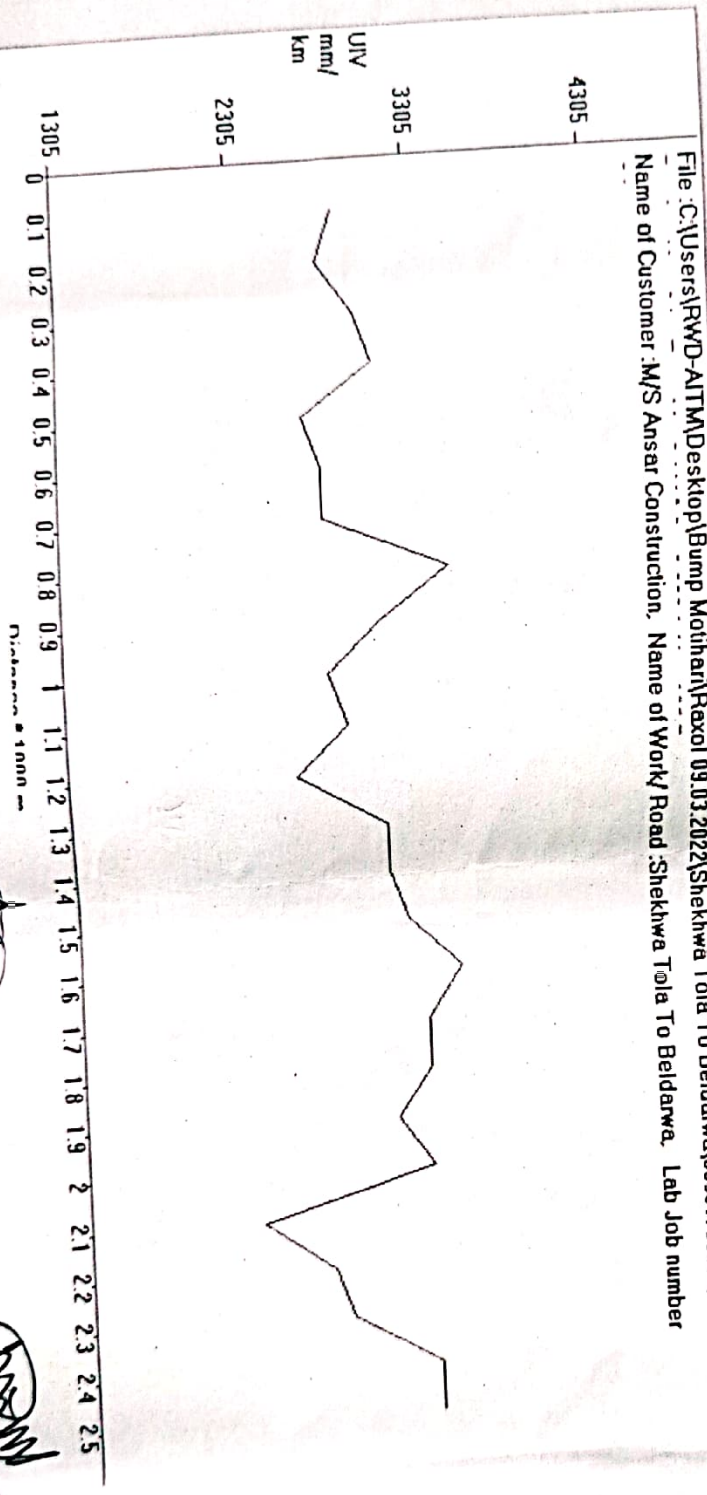


Shm
9/3/22
J.E

Shm
09/03/22
A.E.

Shm
19/4/22




Latitude: 26.957241
Longitude: 84.954306
Altitude: 13.0±146 m
Accuracy: 73.0 m
Time: 18-06-2022 16:04
Note: shekhwatola to beldarwa road

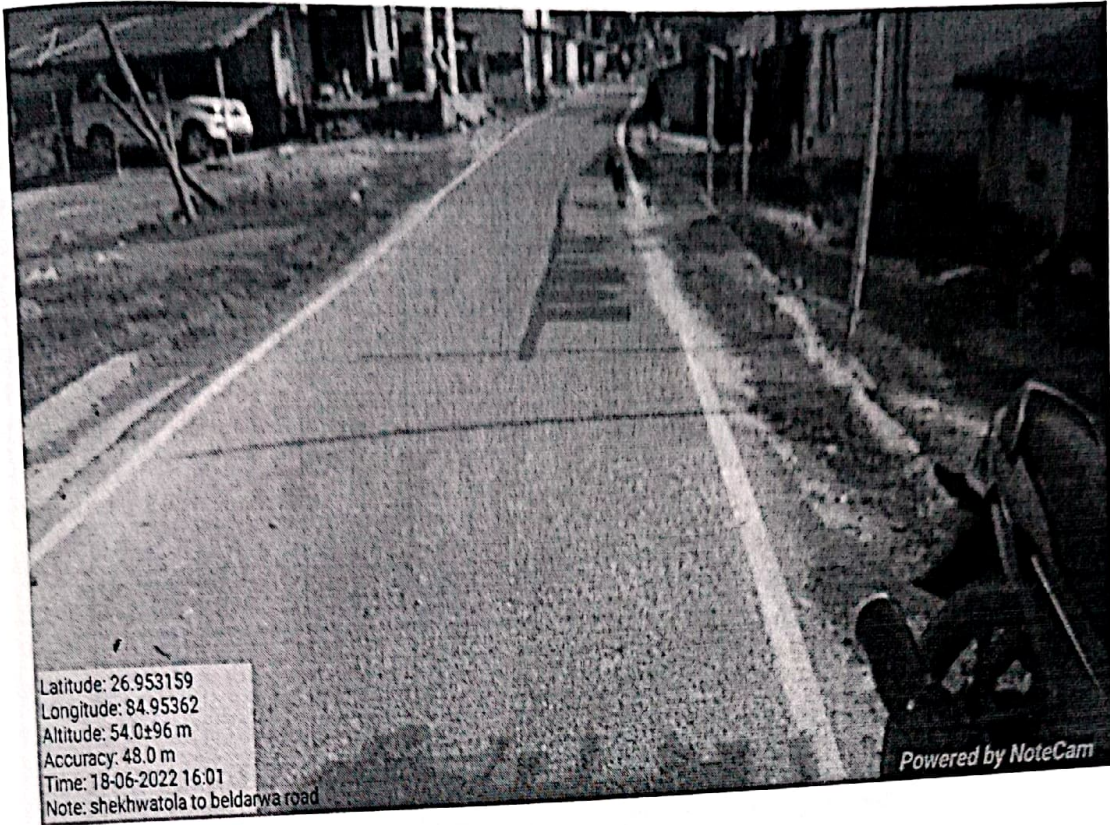

Latitude: 26.953159
Longitude: 84.95362
Altitude: 54.0±96 m
Accuracy: 48.0 m
Time: 18-06-2022 16:01
Note: shekhwatola to beldarwa road


Powered by NoteCam

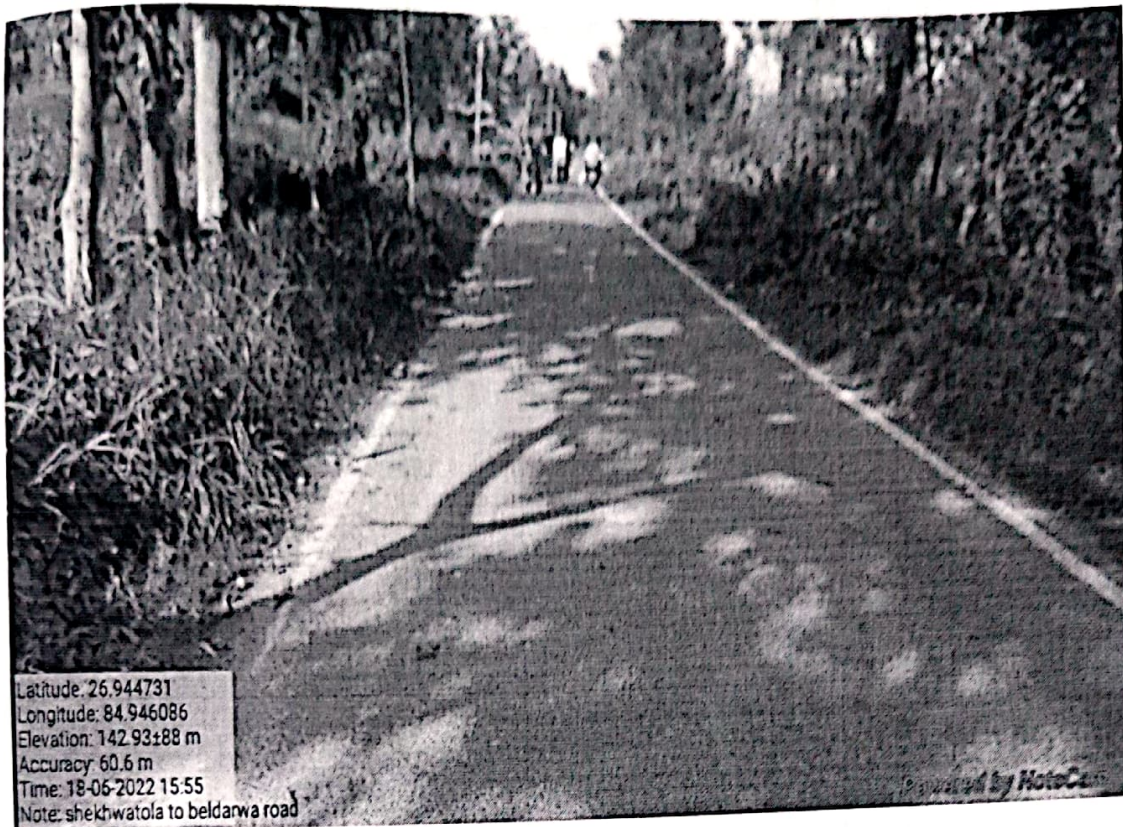

Latitude: 26.944731
Longitude: 84.946086
Elevation: 142.93±88 m
Accuracy: 60.6 m
Time: 18-06-2022 15:55
Note: shekhwatola to beldarwa road

Powered by HotoCam



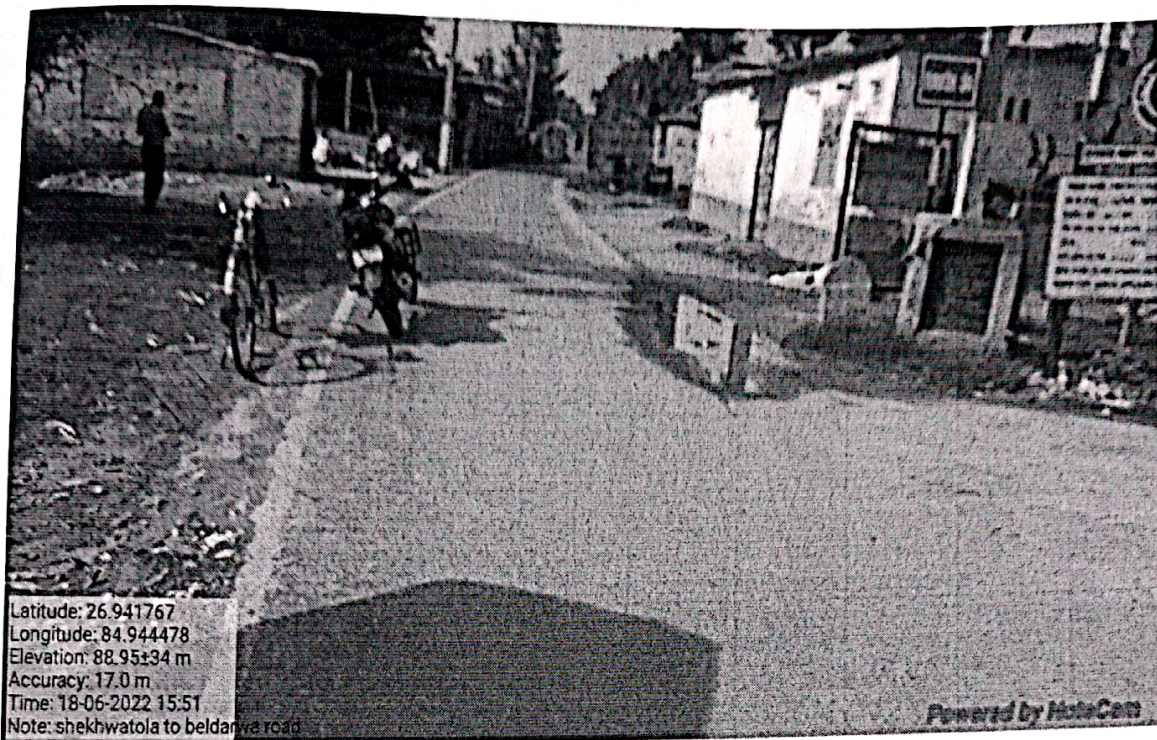

Latitude: 26.941767
Longitude: 84.944478
Elevation: 88.95±34 m
Accuracy: 17.0 m
Time: 18-06-2022 15:51
Note: shekhwatola to beldanwa road

Powered by HoloCam
