

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, छपरा-2।

पत्रांक.....1160.....

छपरा / दिनांक.....17-06-2022

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, छपरा।

सेवा में,

नोडल पदाधिकारी (MR 3054)
ग्रामीण कार्य विभाग
पटना, बिहार

विषय :-


नई अनुरक्षण नीति-2018MR (3054) योजना के अंतर्गत पथ में कराये गये कार्य के विरुद्ध
आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपरोक्त विषय के संबंध में सूचित करना है कि नई अनुरक्षण नीति-2018 MR (3054) योजना के अंतर्गत पथ में कराये गये कार्य के लिए संवेदक को भुगतान करने हेतु अधियाचना विहित प्रपत्र में भरकर आवश्यक कार्यवाही हेतु समर्पित की जाती है।

अनु :- यथोक्त।

विष्वासभाजन



कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, छपरा -2।

17/6/22

(परिषद्- 'H')

FORM GFR 19-A

(See Government of India's Decision (1) below Rule-150)

Form of utilization Certificate up to month of June-2022

NEW MAINTAINANCE POLICY 2018(MR3054)MAINTAINANCE

PIU:EXECUTIVE ENGINEER,RWD WORKS DIVISION,CHAPRA-2

S.No.	Name of Scheme	Sanction No.& Date with Amount (in Rs.lacs)	Amount Received (in Rs. lacs)	Particulars
1.	Construction of Road Under New Maintainance Policy 2018(MR 3054) Maintainance	NIL	NIL	Certified that out of Rs. 0.00 lacs received till Date in favour of Ex.Engineer,RWD Works Division, Chapra-2 . A sum of Rs. NIL has been utilized for the purpose of New Maintainance Policy 2018(MR 3054) Maintainance Schemes as given in the margin for which it was sanctioned and that the balance of Rs. NIL remaining unutilized at the end of the period under the time of completion.
	Total	NIL	NIL	

2. Certified that I have satisfied myself that the conditions on which the grants-in-aid was sanctioned have been duly fulfilled / are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.

Kind of Checks exercised :

- Works have been supervised Executive Engineer / Superintending e Engineer.
- Periodical inspection has been conducted by Executive Engineer/Superintending Engineer.
- Construction material have been tested.
- Measurements have been recorded in the MBs and test check conducted by the Assistant .
- All other codal formalities have been observed.

Physical Progress achieved:

- Construction of Road Works.
- Construction of CD works.

Executive Engineer
RWD Works Division
Chapra-2

AS
17/6/22

Maintenance Requisition Formate for Scheme Head- MR (3054) Under Bihar Rural Road Maintenance Policy-2018
Name of Works Division:- Chapra-2

Road Details					AA Details				Agreement						
Sl. No.	Name of Raods	Batch No.	Project ID	Actual Date of Completion	Main Work Amount (in Lakh)	Maintenance Amount (in lakh)	Main Work Amount (in Lakh)	Agreement-1	Agreement-2	Agreement-3	Agreement-4	Agreement-5	Total Maintenance	Length (in Km)	
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	
1	Hansrajpur Khurd - Harharpur	RM/SA/CHA/19/0001	31306302036	08-05-2021	84.708	41.084	84.652	3.99393	4.71073	12.14982	6.29346	13.16478	40.31272	3.97	
2	T-08 - KARAH	RM/SA/CHA/19/0001	31306302083	21-01-2021	56.015	24.003	55.771	1.98476	2.90931	5.63854	3.67387	9.73007	23.93655	3.3	
3	T08 - Bhatwalya	RM/SA/CHA/19/0001	31306302102	08-05-2021	75.317	36.476	75.29	3.57258	4.20319	10.70947	5.59519	11.60111	35.68154	3.47	
4	T08 - EBRAHIMPUR HARPUR	RM/SA/CHA/19/0001	31306302104	08-05-2021	65.371	29.328	65.328	2.11309	3.79838	7.00008	5.24146	11.1262	29.27941	3.4	
5	L-036 TEKNIVAS JALALPUR ROAD - PIRARI	RM/SA/CHA/19/0017	31306402034	08-05-2021	60.115	30.36	59.993	2.97799	3.47719	8.64529	5.01025	10.20268	30.3134	3	
6	T03 - KANUN	RM/SA/CHA/19/0017	31306402093	18-04-2021	49.686	24.012	49.654	2.61523	3.05107	5.06458	4.37488	8.87498	23.98074	2.6	
7	T05 - BANGARA	RM/SA/CHA/19/0017	31306402095	08-05-2021	25.123	11.785	25.089	1.12615	1.55437	3.32005	1.9358	3.83968	11.77605	1.1	
8	TARWA - PATILA	RM/SA/CHA/19/0017	31306402099	08-05-2021	117.592	62.293	117.523	6.08824	8.46038	16.04169	10.55744	21.11538	62.26313	6.1	
Total					533.927	259.341	533.3	24.47197	32.16482	68.56952	42.68235	89.65488	257.54354	26.94	

Executive Engineer
 RWD Works Division
 Chapra-2
 02/11/22
 17/11/22

Maintenance Requisition Formate for Scheme Head- MR (3054) Under Bihar Rural Road Maintenance Policy-2018

Actual Maintenance Expenditure						Current Maintenance Demand										Remarks
1st. Year Maintenance	2nd. Year Maintenance	3rd. Year Maintenance	4th Year Maintenance	5th Year Maintenance	Total Maintenance Expenditure	Length as per Bump Report	IRI As per bump Report	1st QTR Maintenance	2nd QTR Maintenance	3rd QTR Maintenance	4th QTR Maintenance	5th QTR Maintenance	6th QTR Maintenance	7th QTR Maintenance	Total(In Lac)	
16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	32
0.000	0.000	0.000	0.000	0.000	0.000	3.97	2768.47	2.01563	2.01563	2.01563					6.04689	
0.000	0.000	0.000	0.000	0.000	0.000	3.3	2796.42	1.19682	1.19682	1.19682	1.19682	1.19682			5.9841	
0.000	0.000	0.000	0.000	0.000	0.000	3.47	2614.77	1.78407	1.78407	1.78407					5.35221	
0.000	0.000	0.000	0.000	0.000	0.000	3.4	2684.5	1.46397	1.46397	1.46397					4.39191	
0.000	0.000	0.000	0.000	0.000	0.000	3	279.4	1.51567	1.51567	1.51567					4.54701	
0.000	0.000	0.000	0.000	0.000	0.000	2.6	2593.96	1.19903	1.19903	1.19903					3.59709	
0.000	0.000	0.000	0.000	0.000	0.000	1.1	2899.72	0.58880	0.58880	0.58880					1.76640	
0.000	0.000	0.000	0.000	0.000	0.000	6.1	2649.22	3.11315	3.11315	3.11315					9.33945	
0.000	0.000	0.000	0.000	0.000	0.000			12.87714	12.87714	12.87714	1.19682	1.19682			41.02506	

Executive Engineer
RWD Works Division

Chapra-2

12/6/22

STANDRAD FORMAT FOR ROADS QUARTERLY STATEMENT

1	Name of the Road	L-036 TEKNIWAS JALALPUR ROAD - PIRARI		
2	Batch No.	RM/SA/CHA/19/0017		
3	Project ID	31306402034		
4	Total Length of Road (in Km)	3		
5	Length of Road to Meet Required Service Level [Completed length] (in Km) (1)	3		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule (Agreement Amount for Maintenance) (in Lakh)	30.31340		
8	Quarterly Payment :1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) (2)	1.51567		
Compliance Criteria	Standard Job Description	Non-Compliant		Reduction Payment (6) = (3) / (1) * (2) * (4)
		Length Non Compliant (3)	Weighted Value for Payment Reduction (%) (4)	
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0.00000
II	SHOULDERS AND EMBANMENTS	0	10%	0.00000
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0	15%	0.00000
IV	SIGNAGE AND ROAD SAFETY	0	10%	0.00000
V	VEGATAION		5%	0.00000
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0.00000
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh) [6]				1.51567

Date of inspection by E/I or his agent Prepared by
Contractor's self Control unit

Name and Designation of person inspecting road
(Signature)

Date

Signature of person inspecting road

Certify by E/I (signature) Date

Requisition Format for Scheme Head - MR (3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division :- Chapra-2

Government of Bihar

OM01

Rural works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

To: Executive Engineer

RWD Works Division Chapra-2

Date:

Road From-L-036 TEKNIWAS JALALPUR ROAD - PIRARI

Length of Road: 3.0 KM

Periode : From.....

Position: A.E

Inspector: A.E RWD Sub Division, Jalalpur

Standard Work item		Work	1	2	3	4	5	6	7	8	9	10	Comments
S No	Name	Units											
OM100 Sealed Pavement													
OM101	Pothole Patching	m2	Nil	Nil	Nil	Nil							No. Pothole found.
OM102	Surface Depression and Rut Patching	m2	Nil	Nil	Nil	Nil							No Surface Depression and Rut Patching found
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil							No Crack Sealing found
Surface Treatment													
(a) Loss of Aggregate (Surface Ravelling)													
OM104	(b) Bleeding/Flushing	m2	Nil	Nil	Nil	Nil							No Loss of Aggregate (Surface Ravelling) found
	(c) Crocodile Cracking	m2	Nil	Nil	Nil	Nil							No Bleeding/Flushing Required
													No Crocodile Cracking found
OM105	Edge Repair	m2	Nil	Nil	Nil	Nil							No Edge Repair Required
OM106	Digouts	m2	N/A	N/A	N/A	N/A							
OM107	Concrete Pavement	m3	N/A	N/A	N/A	N/A							
Other activities													
OM200 Shoulder													
Unsealed Shoulder													
(a) Edge Drop off													
OM201	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil	Nil	Nil							No Edge Drop off Required
	(c) Holding Water	Lm	Nil	Nil	Nil	Nil							Defects rectified within stipulated time.
Embankment Repair													
OM202	Other Activite (Raincut)	No	Nil	Nil	Nil	Nil							No Holding water found
		3%	1%	2%	Nil								No Embankment Repair Required
													Defects rectified within stipulated time.

MM
17/06/22
(S/E)

Signature
17/06/22

Signature
17/06/22

OM 300 Drainage including culverts major												
OM301	Surface Drains & Verge	Lm	N/A	N/A	N/A	N/A	N/A					Not Required
OM302	Culvert Cleaning	Lm										Culvert maintain within stipulated time
OM303	Culvert and Pit repair	m2	Nil	Nil	Nil	Nil	Nil					Not Required
	Other activities (White Washing)	m2	Nil	Nil	Nil	Nil	Nil					Not Required
OM 400 Vegetation												
OM401	Grass Contorol											
	a) Roadside-General Tidy	Ha	Nil	Nil	Nil	Nil	Nil					Not Required
	b) Clear near Safety signs, kilometre posts and roadside furniture	Ha	Nil	Nil	Nil	Nil	Nil					Not Required
OM402	Tree and shrub management	No	Nil	Nil	Nil	Nil	Nil					Not Required
	Cutting trees	No	Nil	Nil	Nil	Nil	Nil					Not Required
	Cutting Shrubs	No	Nil	Nil	Nil	Nil	Nil					Not Required
	Other activities (Trimming of Grass)	M2	Nil	Nil	Nil	Nil	Nil					Not Required
OM500	Safety Signage and Road											Not Required
OM501	Signs Maintenance	No	Nil	Nil	Nil	Nil	Nil					Not Required
OM502	Guard Stones	Lm	N/A	N/A	N/A	N/A	N/A					Not Applicable
OM503	Distance Stones	No	N/A	N/A	N/A	N/A	N/A					Not Applicable
OM504	Road Marking	m2	Nil	Nil	Nil	Nil	Nil					Not Required
	Other activities											

Bidder

Appendix

Executive Engineer, Rural Work Department, Work Division, Chapra-2

Mmm
17/06/22
(S.E.)

Signature

Signature

Signature

CONT. NAME:- RAJESHWAR SINGH
ROAD NAME:- L-036 TEKNIWAS JALALPUR ROAD - PIRARI


Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event
16/6/22	8:24:0	34	0.1	240	10.1	2400	2858 G		25.853543	84.678680	Normal
16/6/22	8:24:33	34	0.1	230	10.1	2300	2745 G		25.853580	84.678263	Normal
16/6/22	8:24:33	34	0.1	250	10.1	2500	2972 G		25.853604	84.678538	Normal
16/6/22	8:25:8	34	0.1	230	10.1	2300	2745 G		25.853260	84.680565	Normal
16/6/22	8:25:44	34	0.1	250	10.1	2500	2972 G		25.853826	84.680918	Normal
16/6/22	8:26:0	34	0.1	270	0	2700	3199 G		25.854425	84.681188	Normal
16/6/22	8:26:19	34	0.1	250	10.1	2500	2972 G		25.855216	84.681327	Normal
16/6/22	8:27:0	34	0.1	180	10.1	1800	2177 G		25.856055	84.681666	Normal
16/6/22	8:27:30	34	0.1	230	10.1	2300	2745 G		25.857064	84.682813	Speed Breaker
16/6/22	8:27:30	34	0.1	310	0	3100	3654 G		25.857098	84.683837	Normal
16/6/22	8:28:5	34	0.1	240	10.1	2400	2858 G		25.857155	84.685451	Normal
16/6/22	8:28:40	34	0.1	230	10.1	2300	2745 G		25.857312	84.685822	Normal
16/6/22	8:29:0	34	0.1	250	10.1	2500	2972 G		25.857622	84.687139	Normal
16/6/22	8:29:15	34	0.1	230	10.1	2300	2745 G		25.857552	84.688564	Normal
16/6/22	8:29:15	34	0.1	200	20.2	2000	2404 G		25.856595	84.689521	Normal
16/6/22	8:29:51	34	0.1	240	10.1	2400	2858 G		25.856320	84.691183	Normal
16/6/22	8:30:0	34	0.1	230	10.1	2300	2745 G		25.856385	84.693357	Normal
16/6/22	8:30:0	34	0.1	250	10.1	2500	2972 G		25.856421	84.693585	Normal
16/6/22	8:30:26	34	0.1	230	10.1	2300	2745 G		25.856198	84.695378	Normal
16/6/22	8:30:26	34	0.1	250	10.1	2500	2972 G		25.856198	84.695378	Normal
16/6/22	8:30:26	34	0.1	240	10.1	2400	2858 G		25.855750	84.696862	Normal
16/6/22	8:31:1	34	0.1	230	10.1	2300	2745 G		25.855757	84.696863	Speed Breaker
16/6/22	8:31:1	34	0.1	250	10.1	2500	2972 G		25.854323	84.697911	Normal
16/6/22	8:31:37	34	0.1	230	10.1	2300	2745 G		25.854325	84.697951	Normal
16/6/22	8:32:0	34	0.1	190	20.2	1900	2290 G		25.853703	84.699992	Normal
16/6/22	8:32:12	34	0.1	230	10.1	2300	2745 G		25.853690	84.700159	Normal
16/6/22	8:32:47	34	0.1	170	20.2	1700	2063 G		25.853547	84.701438	Normal
16/6/22	8:33:0	34	0.1	240	10.1	2400	2858 G		25.853588	84.701510	Normal
16/6/22	8:33:22	34	0.1	220	10.1	2200	2631 G		25.853606	84.701537	Normal
16/6/22	8:34:0	34	0.1	240	10.1	2400	2858 G		25.853606	84.701537	Normal
AVERAGE									2794		

M. M. Singh
11/06/22
(JTE)

Signature

Signature

File : C:\Users\Devi\Desktop\RAJESHWAR SINGH\pipari.Xls. Section No. : 34. Eqn : test
Name of Customer : RAJESHWAR SINGH, Name of Work/ Road : L-036 TEKNIWAS JALALPUR ROAD-PIPARI, Lab

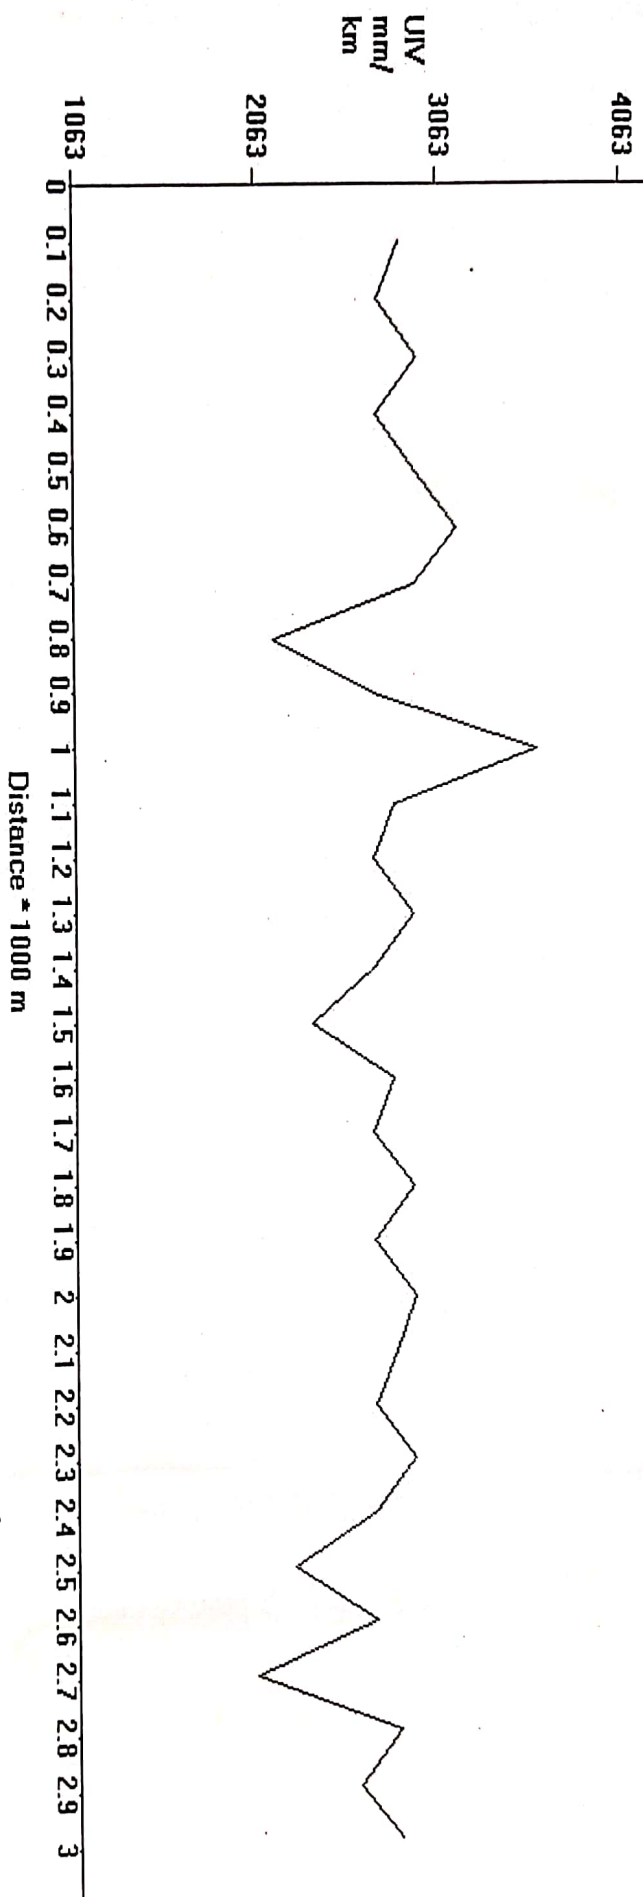

M. K. Singh
19/06/22
(J.E)

Singh
19/06/22
J.E

27/10/22
(J.E)
