



ग्रामीण कार्य विभाग

Rural Works Department, Govt of Bihar

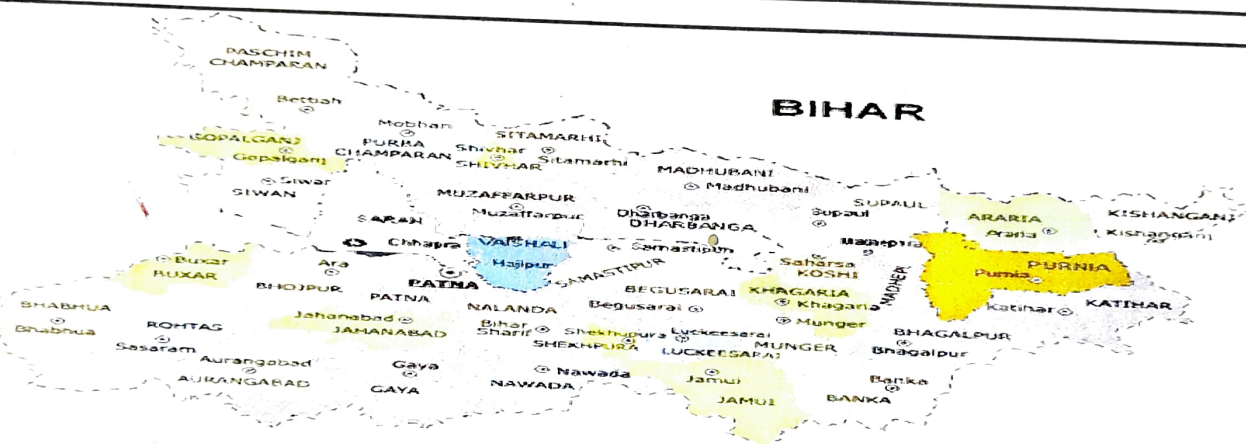


BIHAR RURAL ROADS PROJECT

Bihar Rural Road Development Agency (BRRDA)

Govt. of Bihar

EMERGENT REPAIR OF ROAD FROM NH-30 GYASPUR- RUPAS MAHAJI UNDER FDR



Name of the Road :-

EMERGENT REPAIR OF ROAD FROM NH-30 GYASPUR- RUPAS MAHAJI UNDER FDR

DISTRICT	:	Patna	
DIVISION	:	Patna	
BLOCK	:	BAKHTIARPUR	
Total Damaged length of Road	:	2.170 1.665	km
TOTAL COST OF CONSTRUCTION	:	9.334	Lacs
TOTAL COST OF PROJECT	:	9.334	Lacs

Executive Engineer
Rural Works Division,
Patna

SUMMARY OF COST ESTIMATE FOR THE PROJECT

NAME OF ROAD :	EMERGENT REPAIR OF ROAD FROM NH-30 GYASPUR- RUPAS MAHAJI UNDER FDR	
DISTRICT	PATNA	
BLOCK	BAKHTIARPUR	
DIVISION	PATNA	
Total Damaged length of Road	0.170 Km 4.68 km	
Sl. No.	DESCRIPTION	AMOUNT (LAKHS)
1	COST OF ITEM	807165.00 ₹ 9,33,432.33
	TOTAL COST IN LACS =	9.334 8.072

[Signature]
JE
RWD

[Signature]
AE
RWD

[Signature]
EE
RWD

Technically sanctioned for Rs. 8,07,200/- (Rupees Eight Lakh.
Seven thousand and Two hundred only)
including five year Maintenance Cost

[Signature]
14/12/2021

Superintending Engineer
R.W.D. WORKS CIRCLE, PATNA

[Signature] *[Signature]*
सहायक सलाहकार Superintending Engineer
ग्रामीण कार्य विभाग R.W.D. WORKS CIRCLE, PATNA
क्षेत्र अंचल, पटना

प्रतिवेदन

कार्य का नाम :

एन०एच०-30 ग्यासपुर-रूपस महाजी पथ की आपातकालीन मरम्मत ।

पथ की लम्बाई :

0.170
4.68 कि०मी०


प्राक्कलित राशि :


रू० 9.334 लाख

मद :

एफ० डी० आर०

प्रस्तुत प्राक्कलन बख्तियारपुर प्रखण्ड अंतर्गत एन०एच०-30 ग्यासपुर-रूपस महाजी पथ की आपातकालीन मरम्मत हेतु एकरारनामित दर पर रू० 9.334 लाख (नौ लाख तैंतीस हजार चार सौ रूपये) मात्र का तैयार किया गया है । विगत पिछले माह में बाढ़ एवं अतिवृष्टि के कारण पथ में बड़े-बड़े गड्ढे बन गये हैं । विभागीय निर्देशानुसार पथ को यातायात योग्य बनाना है, जिसके लिए पहले से ही संवेदक चयनित है । पथ के क्षतिग्रस्त पथांश में ब्रीक्स वैट एवं स्थानीय बालू से भरा सीमेंट बैग से भर दिया गया है । वर्तमान में आवागमन चालू है । अतः कार्यहित में प्राक्कलन की स्वीकृति अति आवश्यक है ।


कनीय अभियंता
बख्तियारपुर


सहायक अभियंता
बख्तियारपुर


कार्यपालक अभियंता
(ग्रामीण कार्य विभाग)
कार्य प्रमंडल, पटना

Inspection Report for Flood Damage Work

D,

Date :- 03/12/2021

1. Name of PIUs :- E.E. RWD(W) Division Patna
2. Name of Block / Road :- Babhtigaspur NH-30 G. gaspur to Rupas Mahaji
- A. For Road
 1. Damage Location / Chainage :- between Ch. 0.350 to 3.500 Km
 2. Damage Length :- 170 m
 3. Nature of Damage :- Scour in the road and Flank
 - i. Material being used in Restoration works :- Brick bats and sand bag
 - ii. Equipments / Tools being used in Restoration works : J.C.B, tractor, Roller
 - iii. Procedure taken up in Restoration works : By Filling brick bats & sand bags provided at the edge of the road.
 - iv. Restored Length : 170 m

B. For Road Bridge


1. Damage Location / Chainage :-] NIL
2. Damage Length :-] NIL
3. Nature of Damage :-] NIL

4. Details of Restoration Works :-

- i. Material being used in Restoration works :- Brick bats and sand bag
- ii. Equipments / Tools being used in Restoration works : J.C.B, tractor, Roller
- iii. Procedure taken up in Restoration works : By Filling brick bats & sand bags provided at the edge of the road
- iv. Restored Length : 170 m

Work is satisfactory.


06/12/21
RB


Name of Inspector
Executive Engineer
R.W.D. Works Division, Masaurhi

F6	
NAME OF ROAD	EMERGENT REPAIR OF ROAD FROM NH-30 GYASPUR - RUPAS MAHAJI UNDER FDR

807164.00

EE (RWD)
WORK DIVISION
PATNA

25/10/21, J.E. 25/10/21
92

2)	Laying Cement bag filled with local sand									
	1	x	28.00	x	1.00	x	1.00			400.00
	2	x	33.00	x	5.00	x	2.00			660.00
	3	x	28.00	x	4.00	x	2.00			400.00
					Total Qty					1460.00

SEIGNORANCE

S.no.	Item	Unit	Qty	Basic Rate	Amount	10 % seig
1	Brick Bats	m3	422.21 ^{422.26}	1062.00	448140.12 ^{448140.12} 522722.02	11889.01 ^{11889.01} 52272.70
2	Local Sand	m3	49.64	141.85	7041.43	704.14
					Total =	52976.85

~~15518.15~~

[Signature]
25/10/21
JE

[Signature]
25.10.21
AE

[Signature]
25/10/21
EE
RWD

73 +
373
446
