

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल, छपरा - 1

राजेन्द्र सरोवर, श्री नन्दन पथ,
छपरा (सारण) 841301

मो० - 8986915253

पत्रांक 885330
प्रेषक,

दिनांक 27.06.22

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, छपरा - 1

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी,
ग्रामीण कार्य विभाग, बिहार, पटना।

विषय :- नई अनुरक्षण नीति 2018 शीर्ष 3054 (अनुरक्षण मद) में व्यय हेतु आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपर्युक्त विषयक संबंध में कहना है कि नई अनुरक्षण नीति 2018 शीर्ष 3054 (अनुरक्षण मद) में कराए गए कार्य के विरुद्ध उचित प्रपत्र में अधियाचना प्रपत्र समर्पित की जा रही है। अधियाचित राशि शीघ्र उपलब्ध कराने की कृपा की जाय ताकि भुगतान संभव हो।

अनु० - यथोक्त।

विश्वासभाजन,

कार्यपालक अभियंता

ग्रा०का०वि०, का० प्रमंडल, छपरा - 1
27.06.22

MR-3054 New Maintenance Policy-2018 के अंतर्गत पंचवर्षीय रुटीन अनुरक्षण मद में आवंटन योग से संबंधित अधियाचना प्रपत्र।

कार्य प्रमंडल का नाम:-ग्रामीण कार्य विभाग, कार्य प्रमंडल, छपरा - 1

क्र० सं०	Project ID	पथ का नाम (अंग्रेजी में)	संवेदक का नाम (अंग्रेजी में)	पथ की लंबाई (कि०मी० में)	कार्य पूर्ण होने की वार्षिक तिथि	पंचवर्षीय रूटीन अनुरक्षण की राशि-वर्षवार (लाख में)							अनुरक्षण मद में कुल व्यय (MIS पर) (लाख में)	वर्तमान अधियाचित राशि Quarter Wise (लाख में)						कुल अधियाचना की राशि (लाख में)
						प्रथम वर्ष (लाख में)	द्वितीय वर्ष (लाख में)	तृतीय वर्ष (लाख में)	चतुर्थ वर्ष (लाख में)	पंचम वर्ष (लाख में)	कुल पंचवर्षीय एकसहित राशि (लाख में)	1st Quarter (लाख में)		2nd Quarter (लाख में)	3rd Quarter (लाख में)	4th Quarter (लाख में)	5th Quarter (लाख में)	6th Quarter (लाख में)		
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	
		Meserawalia Sidhwalia	Mukesh Singh	6.48	07-05-21	5.44716	8.17242	19.08027	9.86266	20.98314	63.54565	0.000000	3.17728	3.17728	3.17728	3.17728	0.00000	0.00000	12.70912	
2		Semaria NH - 10 Mainpura	Mukesh Singh	5.50	27-12-20	2.81445	5.29245	14.23888	5.94796	15.19698	43.49072	0.000000	2.17454	2.17454	2.17454	2.17454	2.17454	2.17454	13.04724	
3		Bhadapa Semaria Khurd	Mukesh Singh	5.70	31.12.20	4.82906	7.19425	16.85656	8.79942	18.60441	56.28370	0.000000	2.81419	2.81419	2.81419	2.81419	2.81419	2.81419	16.88514	
Total:-												0.00000	5.35182	5.35182	5.35182	5.35182	2.17454	2.17454	42.64150	

प्रमाणित किया जाता है कि :-

प्रमाणित किया जाता है कि :-

- (1) उपरोक्त पथों का मूल कार्य पूर्ण कराया जा चुका है।
- (2) संवेदक के द्वारा किये गये अनुरक्षण कार्य की जाँच कर ली गई है (जाँच प्रतिवेदन संलग्न)

ग्रामीण कार्य विभाग, कार्य प्रमंडल, छपरा - 1
 कार्यालय छपरा
 08.06.24

STANDRAD FORMAT FOR ROADS QUARTERLY STATEMENT

PIU Name :- R.W.D. (W) Division, Charpa - I

1	Name of the Road	Meserawalia Sidhwalia		
2	Batch No.	RM/SA/CHA/19/0012		
3	Project ID	31306202062		
4	Total Length of Road (in Km)	6.48		
5	Length of road to Meet Required Service Level [Completed length] (in Km) [1]	6.48		
6	No. of Totla Quarter (ie 3 Months as a unit) in 5 Years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenacne] (in Lakh)	63.54565		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	3.17728		
Compliance Criteria	Standard Job Description	Non-Comliance		Reduction Payment [6] = [3]/[1]*[2]*[4]
		Length Non- Complaint [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0
II	SHOULEDRS AND EMBANMENTS	0	10%	0
III	CROSS DRAINAGE INCLUDING CULERTS AND BRIDGES	0	15%	0
IV	SIGNANCE AND ROAD SAFETY	0	10%	0
V	VEGATAION	0	5%	0
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh) [6]				3.17728

Date of inpection by E/I or his agent
Prepared by Contractor's self Control unit

Name and Designation of Person Inspecting road

Date

(Signature)

Signature of Person inspecting road

Certify by E/I [signature] Date :-

(Signature)
Executive Engineer
R.W.D. (W) Division,
Charpa-I

Road Works Department

Road From : - Meserawaia Sidhwaia

To : Executive Engineer, R.W.D., (W) Division, Chapra - I

Length of Road : 6.48

Date

Inspector : - A.E., RWD, Work Sub Division, Sadar

Position : - A.E.

No.	Standard work item	Work Units	Units of work required in each kilometre										Comments
			1	2	3	4	5	6	7	8	9	10	
OM100	Scaled Pavement												
OM101	Pothole Patching	m2	Nil	Nil	Nil	Nil	Nil	Nil	Nil				No Pot Hole Found
OM102	Surface Depression and Rut Patching	m2	Nil	Nil	Nil	Nil	Nil	Nil	Nil				Not Surface Depression & Pot Patching Found
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil	Nil	Nil	Nil				No Crack Sealing Found
OM104	Surface Treatment												
	(a) Loss of Aggregate (Surface Ravelling)	m2	Nil	Nil	Nil	Nil	Nil	Nil	Nil				No Loss of Aggregates (Surface Ravelling) found
	(b) Bleeding/Flushing	m2	Nil	Nil	Nil	Nil	Nil	Nil	Nil				No Bleeding/Flushing Required
	(c) Crocodile Cracking	m2	Nil	Nil	Nil	Nil	Nil	Nil	Nil				No Crocodile Cracking found
OM105	Edge Repair	m2	Nil	Nil	Nil	Nil	Nil	Nil	Nil				No Edge repair Required
OM106	Digouts	m2	Nil	Nil	Nil	Nil	Nil	Nil	Nil				
OM107	Concrete Pavement	m3	Nil	Nil	Nil	Nil	Nil	Nil	Nil				
	Other activities												
OM200	Shoulder												
OM201	Unsealed Shoulder												
	(a) Edge Drop off	Lm	Nil	Nil	Nil	Nil	Nil	Nil	Nil				No Edge Drop off required
	(b) Roughness, Scouring of Potholes	Lm	Nil	Nil	Nil	Nil	Nil	Nil	Nil				No roughness
	(c) Holding Water	Lm	Nil	Nil	Nil	Nil	Nil	Nil	Nil				No holding water found
OM202	Embankment Repair	No	Nil	Nil	Nil	Nil	Nil	Nil	Nil				No Embankment Repair required
	Other activities												
OM300 Drainage including culverts major and minor bridges													
OM301	Surface Drains & Verge	Lm	Nil	Nil	Nil	Nil	Nil	Nil	Nil				No Required
OM302	Culvert Cleaning	Lm	Nil	Nil	Nil	Nil	Nil	Nil	Nil				No Required
OM303	Culvert and pit Repair		Nil	Nil	Nil	Nil	Nil	Nil	Nil				No Required
	Other activities		Nil	Nil	Nil	Nil	Nil	Nil	Nil				No Required

Standard work item	Work	Units of work required in each kilometre										Comments
Name	Units	1	2	3	4	5	6	7	8	9	10	
OM400 Vegetation												
Grass Control												
a) Roadside-General Tidy	Ha	Nil	Nil	Nil	Nil	Nil	Nil	Nil				No Required
b) Clear near Safety signs, kilometre posts and roadside furniture	Ha	Nil	Nil	Nil	Nil	Nil	Nil	Nil				No Required
OM402 Tree and Shrub Management	No	Nil	Nil	Nil	Nil	Nil	Nil	Nil				No Required
(Cutting of Branches of Trees)	No	Nil	Nil	Nil	Nil	Nil	Nil	Nil				No Required
(Cutting of Shrubs from Road Way)	No	Nil	Nil	Nil	Nil	Nil	Nil	Nil				No Required
Other activities (Trimming of Grass)	M2	Nil	Nil	Nil	Nil	Nil	Nil	Nil				No Required
OM500 Signage and Road Safety												
OM501 Signs Maintenance	No	Nil	Nil	Nil	Nil	Nil	Nil	Nil				No Required
OM502 Guard Stones	Lm	N.A	N.A	N.A	N.A	N.A	N.A	N.A				No Required
OM503 Distance Stones	No	N.A	N.A	N.A	N.A	N.A	N.A	N.A				No Required
OM504 Road Markings	M2	Nil	Nil	Nil	Nil	Nil	Nil	Nil				No Required
Other activities												

[Signature of Contractor/Authorized representative]

Date

Time

Place

[Handwritten Signature]
25/6/22

[Handwritten Signature]
25.6.22

[Handwritten Signature]
R. D. (IV) Division,
Chapra-1

File: C:\Users\DELL\Downloads\16011557.xls


Name of Customer: Mukesh Singh

Name of Work/ Road: Meserwalya to Sidhwalya

Section No.: 82

Eqn. $Y = 0 - X^2 + 0.816 - X + 249$

Lab Job number :

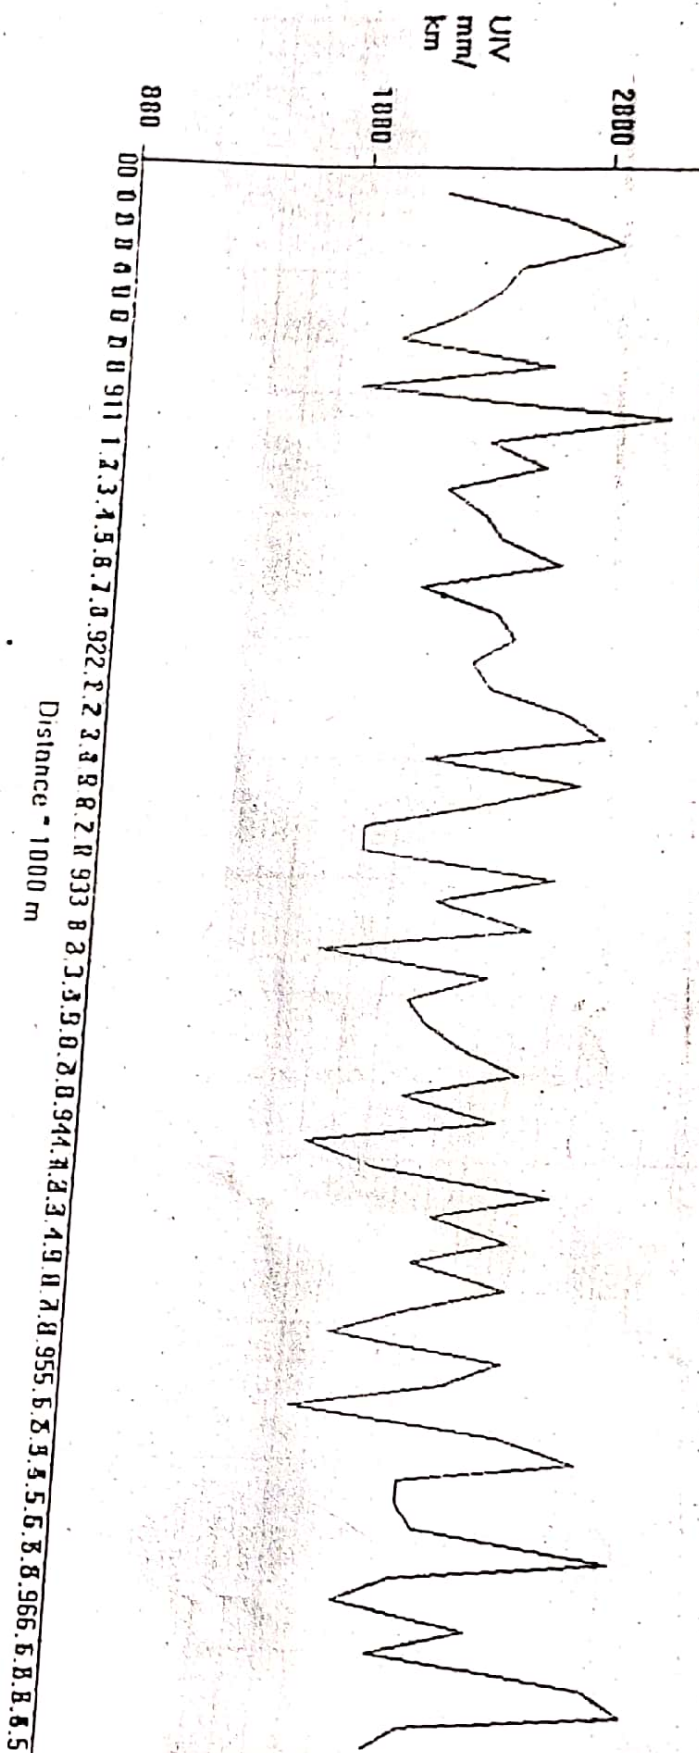

[Signature]
20.6.22

[Signature]
20.6.22

[Signature]
R. W. S. (IV) Division,
Chapra-I

Scheme-NEW MR
Road Name-Mesarwalliya to Sidwalliya
Contractor-Mukesh Singh

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event	Good	Average	Poor
16/1/22	14:0:41	82	0.1	240	0	2400	2207	ROAD	25.860593	84.714343	Normal	Y = 0 * X ^ 2 + 0.816 * X + 249		
16/1/22	14:1:0	82	0.1	300	20.2	3000	2696	G	25.860513	84.715268	Normal	X = 3200		
16/1/22	14:1:16	82	0.1	330	20.2	3300	2941	G	25.860313	84.716312	Normal	Y = 2860		
16/1/22	14:1:52	82	0.1	280	20.2	2800	2533	G	25.861032	84.71672	Normal			
16/1/22	14:2:27	82	0.1	250	10.1	2500	2288	G	25.861932	84.716952	Normal			
16/1/22	14:3:2	82	0.1	300	10.1	3000	2044	G	25.862458	84.717608	Normal			
16/1/22	14:3:37	82	0.1	200	10.1	2000	2696	G	25.862452	84.718618	Normal			
16/1/22	14:4:0	82	0.1	360	10.1	3600	3186	G	25.862503	84.720673	Normal			
16/1/22	14:4:13	82	0.1	270	10.1	2700	2452	G	25.862258	84.721548	Normal			
16/1/22	14:5:0	82	0.1	300	20.2	3000	2696	G	25.861652	84.722087	Normal			
16/1/22	14:5:23	82	0.1	250	10.1	2500	2288	G	25.861052	84.722457	Normal			
16/1/22	14:5:23	82	0.1	270	10.1	2700	2452	G	25.860107	84.722272	Normal			
16/1/22	14:6:0	82	0.1	280	10.1	2800	2533	G	25.859798	84.723013	Normal			
16/1/22	14:6:34	82	0.1	310	10.1	3100	2778	G	25.859447	84.724965	Normal			
16/1/22	14:7:9	82	0.1	240	10.1	2400	2207	G	25.859198	84.725992	Normal			
16/1/22	14:8:0	82	0.1	290	10.1	2900	2615	G	25.859047	84.726952	Normal			
16/1/22	14:8:20	82	0.1	270	10.1	2700	2452	G	25.858862	84.727862	Normal			
16/1/22	14:9:0	82	0.1	280	10.1	2800	2533	G	25.858657	84.728855	Normal			
16/1/22	14:9:30	82	0.1	320	20.2	3200	2860	G	25.85841	84.729747	Normal			
16/1/22	14:9:30	82	0.1	340	20.2	3400	3023	G	25.857643	84.729308	Normal			
16/1/22	14:10:0	82	0.1	250	20.2	2500	2288	G	25.856795	84.729023	Normal			
16/1/22	14:10:5	82	0.1	330	20.2	3300	2941	G	25.855875	84.728803	Normal			
16/1/22	14:10:5	82	0.1	280	20.2	2800	2533	G	25.855013	84.72842	Normal			
16/1/22	14:10:41	82	0.1	220	20.2	2200	2044	G	25.854187	84.728215	Normal			
16/1/22	14:11:0	82	0.1	220	20.2	2200	2044	G	25.853327	84.727827	Normal			
16/1/22	14:11:16	82	0.1	320	20.2	3200	2860	G	25.8525	84.727473	Normal			
16/1/22	14:11:16	82	0.1	260	20.2	2600	2370	G	25.8515	84.727153	Normal			
16/1/22	14:11:51	82	0.1	310	20.2	3100	2778	G	25.850743	84.72673	Normal			
16/1/22	14:12:0	82	0.1	200	10.1	2000	1880	G	25.849918	84.726397	Normal			
16/1/22	14:12:0	82	0.1	200	10.1	2000	1880	G	25.84898	84.72643	Normal			

16/1/22	14-12:27	82	0.1	290	10.1	2900	2615	G	25.848103	84.72643	Speed Breaker
16/1/22	14-13:2	82	0.1	250	10.1	2500	2288	G	25.847328	84.726127	Normal
16/1/22	14-13:2	82	0.1	260	10.1	2600	2370	G	25.846463	84.72601	Curve
16/1/22	14-13:37	82	0.1	280	20.2	2800	2533	G	25.845642	84.725892	Normal
16/1/22	14-14:12	82	0.1	310	10.1	3100	2778	G	25.844802	84.725555	Normal
16/1/22	14-14:12	82	0.1	250	20.2	2500	2288	G	25.843963	84.725572	Normal
16/1/22	14-14:48	82	0.1	300	20.2	3000	2696	G	25.843158	84.725185	Normal
16/1/22	14-15:0	82	0.1	200	10.1	2000	1880	G	25.842355	84.72478	Normal
16/1/22	14-15:23	82	0.1	240	10.1	2400	2207	G	25.84147	84.724612	Normal
16/1/22	14-16:0	82	0.1	330	10.1	3300	2941	G	25.84059	84.724427	Curve
16/1/22	14-16:0	82	0.1	270	10.1	2700	2452	G	25.839802	84.724057	Normal
16/1/22	14-16:34	82	0.1	310	20.2	3100	2778	G	25.83898	84.723652	Normal
16/1/22	14-17:9	82	0.1	460	10.1	2600	2370	G	25.838042	84.723298	Speed Breaker
16/1/22	14-17:44	82	0.1	310	10.1	3100	2778	G	25.837222	84.722912	Speed Breaker
16/1/22	14-18:19	82	0.1	260	10.1	2600	2370	G	25.836625	84.722928	Curve
16/1/22	14-19:0	82	0.1	220	10.1	2200	2044	G	25.836297	84.723888	Normal
16/1/22	14-19:0	82	0.1	310	10.1	3100	2778	G	25.835905	84.72483	Normal
16/1/22	14-19:30	82	0.1	280	20.2	2800	2533	G	25.835602	84.725707	Normal
16/1/22	14-19:30	82	0.1	200	20.2	2000	1880	G	25.835553	84.72672	Normal
16/1/22	14-20:5	82	0.1	310	20.2	3100	2778	G	25.835507	84.727693	Normal
16/1/22	14-20:5	82	0.1	350	20.2	3500	3104	G	25.835423	84.72867	Normal
16/1/22	14-21:0	82	0.1	260	10.1	2600	2370	G	25.835187	84.729713	Normal
16/1/22	14-22:0	82	0.1	260	10.1	2600	2370	G	25.834825	84.729662	Normal
16/1/22	14-22:26	82	0.1	270	10.1	2700	2452	G	25.835343	84.729192	Normal
16/1/22	14-23:2	82	0.1	370	20.2	3700	3268	G	25.835462	84.728265	Normal
16/1/22	14-23:2	82	0.1	260	20.3	2600	2370	G	25.83553	84.727305	Normal
16/1/22	14-23:2	82	0.1	230	20.3	2300	2125	G	25.835568	84.726278	Normal
16/1/22	14-23:37	82	0.1	300	20.3	3000	2696	G	25.835718	84.725235	Normal
16/1/22	14-24:0	82	0.1	250	20.2	2500	2288	G	25.836173	84.724325	Normal
16/1/22	14-24:11	82	0.1	360	10.1	3600	3186	G	25.836487	84.7234	Normal
16/1/22	14-24:47	82	0.1	380	10.1	3800	3349	G	25.836847	84.722658	Curve
16/1/22	14-25:22	82	0.1	270	10.1	2700	2452	G	25.837658	84.723147	Speed Breaker
16/1/22	14-26:0	82	0.1	250	10.1	2500	2288	G	25.838495	84.723502	Speed Breaker
				Total-		163758					
				IRI Value-		2519					
