

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, मोतिहारी।

पत्रांक 793 अनु / दिनांक 28.4.2022

प्रेषक

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल मोतिहारी।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी,
—सह—सचिव BRRDA,
बिहार, पटना।

विषय — MR-3054(New Maintenance Policy 2018) के अन्तर्गत 5 (पाँच) वर्षीय
अनुरक्षण हेतु अध्याचना के संबंध में।

प्रसंग:— अभियंता प्रमुख, ग्रामीण कार्य विभाग, बिहार पटना के पत्रांक मु0अ0-4 (मु0)
3054-04-229 / 2021- 2021 -1135 अनु0 पटना दिनांक 09.03.2022

महाशय,

उपर्युक्त विषयक प्रासंगिक पत्र में दिये गये निर्देश के आलोक में गई
अनुरक्षण नीति-2018 अन्तर्गत पथों के अनुरक्षण की राशि के आवंटन हेतु विहित प्रपत्र में
तैयार कर आवश्यक कार्रवाई हेतु समर्पित की जा रही है।

अतः MR-3054(New Maintenance Policy 2018) के अन्तर्गत (MR-
N/19-20 Motihari-07) 1. NH28 To Chijhapati 2. NH 28 A Banshakti Mai Sthan
to Sapha Chamar Toli 3. Bhargawa To Baudha Kurbaini 4. T04 To Dharampur
पथ के अनुरक्षण हेतु अध्याचित प्रपत्र में दर्शाये गए राशि उपलब्ध कराने की कृपा की
जाए। कार्य का निरीक्षण किया गया एवं कराया गया कार्य संतोषप्रद है। उक्त पथों में
ए0टी0आर0 लंबित नहीं है।

अनु0:— यथोक्त।

विश्वासभाजन,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, मोतिहारी।

Standrad Format For Roads Quarterly Statement (2 nd Quarter)

PTU Name:- R.W.D.(W) Division, Motihari

1	Name of the Road	T04 To Dharampur		
2	Batch No.			
3	Project ID	31708202250		
4	Total Length of Road(in K.M.)	1.402		
5	Length of Road to Meet Required Service Level (Completed Length)(in K.M.)	1.402		
6	No of Total Quarter(ie 3 Months as a Unit) in 5 Years	20		
7	Ordinary Maintenance Cost as per Schedule (Agreement Amount For Maintenance(in Lakh)	14.25252		
8	Quarterly Payment: 1/20 of Ordinary Maintennance Cost as per Schedule (in Lakh)	0.71263		
Compliance Criteria	Standard Job Description	Non- Compliance		Reduction Payment (6) = (3) / (1)*(2)*(4)
		Length Non Compliant	Weightred Value for Payment Reduction (%)	
	Paved Roads(Carriage Way)	0	60%	0
	Shoulders and Embankments	0	10%	0
	Cross Drainage Including Culverts and Bridges	0	15%	0
	Signage and Road Safety	0	10%	0
	Vegetation	0	5%	0
Total Payment Reduction for the Quarter (in Lakh)				0
To be Paid for the Quarter/ Demand (in Lakh)				0.71263

Date of Inspection by E/I or his agent

Prepared by Contractor's self Control unit

Name and Designation of Person inspecting road

(Signature)

Date:-

Signature of Person inspecting road

Certify by E/I (Signature) Date

Requisition Formlet for Scheme Head-MR-(3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

1 Year (2 nd Quarter)

D. Works Division Motihari

Government Of Bihar

OM101

Rural Works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From:- 104 To Dharampur
(Package No.MR-N/19-20 Motihari/13)

To:-

Executive Engineer
RWD, Works Division Motihari

Date:-

Length of Road :- 1.40 Km

Period :- From:- 16-07-2021 To 15-10-2021

Inspector :- A.E.RWD Sub Division : Sugauli

Position :- A.E

No	Standard Of Work Item Name	Work Unit	Unit Of Required in each Kilometer	1	2	3	4	5	6	7	8	9	10	Comments
OM100	Scaled payment													
OM101	Pothole Patching	m ²	Nil	Nil	Nil	Nil	Nil							No Pot Hole Found.
OM102	Surface Depression and Rut patching	m ³	Nil	Nil	Nil	Nil	Nil							Not Surface Depression & Rut Patching Found
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil	Nil							No Crack sealing Found
	Surface Treatment													
OM104	(a) Loss of Aggregate (Surface Ravelling)	m ²	Nil	Nil	Nil	Nil	Nil							No Loss Of Aggregates (Surface Ravelling) Found
	(b) Bleeding / Flushing	m ²	Nil	Nil	Nil	Nil	Nil							No Bleeding/ Flushing Required
	© Crocodile Cracking	m ²	Nil	Nil	Nil	Nil	Nil							No Crocodile Cracking Found
105	Edge Repair	m ²	Nil	Nil	Nil	Nil	Nil							No Edge Repair Required
106	Digouts	m ²	N.A	N.A	N.A	N.A	N.A							
107	Concrete pavement	m ³	N.A	N.A	N.A	N.A	N.A							
	Other activities													
OM200	Shoulder													
	Unsealed Shoulder													
OM201	(a) Edge Drop-off	Lm	Nil	Nil	Nil	Nil	Nil							No Edge Drop-Off Required
	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil	Nil	Nil	Nil							Not Required
	(c) Holding water	Lm	Nil	Nil	Nil	Nil	Nil							No Holding Water Found
OM202	Embankment Repair	M ³	Nil	Nil	Nil	Nil	Nil							Not Required
	Other activities (Rain Cuts)		Nil	Nil	Nil	Nil	Nil							Not Required
OM300	Drainage including culverts major													
OM301	Surface Drains & Verge	Lm	N.A	N.A	N.A	N.A	N.A							Not Required
OM302	Culvert Cleaning	No	Nil	Nil	Nil	Nil	Nil							Not Required

Signature

Name of Road:- T04 to Dharampur

Name of Contractor:- M/S Jyoji Vandana Construction

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR	IRI	CATEGORY	Latitude	Longitude	Event
27/4/22	8:51:0	10	0.1	390	0	3900	3431 G	26.72926	84.79209	Normal	Y = 0 * X ^ 2 + 0.816 * X + 249
27/4/22	8:51:0	10	0.1	370	10.1	3700	3268 G	26.72961	84.79176	Normal	X = 3300
27/4/22	8:51:33	10	0.1	350	10.1	3500	3104 G	26.72961	84.79177	Normal	Y = 2941
27/4/22	8:51:33	10	0.1	310	20.2	3100	2778 G	26.7319	84.79405	Normal	
27/4/22	8:52:9	10	0.1	310	20.2	3100	2778 G	26.72244	84.81246	Normal	(R) RURAL ROAD
27/4/22	8:52:9	10	0.1	310	10.1	3100	2778 G	26.7319	84.79405	Normal	Good
27/4/22	8:52:44	10	0.1	380	10.1	3800	3349 G	26.7318	84.79405	Normal	Average
27/4/22	8:53:0	10	0.1	300	10.1	3000	2696 G	26.7319	84.79405	Speed Breaker	Poor
27/4/22	8:53:19	10	0.1	270	10.1	2700	2452 G	26.7319	84.7940	Normal	
27/4/22	8:53:19	10	0.1	280	20.2	2800	2533 G	26.73068	84.79079	Normal	
27/4/22	8:54:0	10	0.1	370	20.2	3700	3268 G	26.73902	84.78785	Normal	
27/4/22	8:54:0	10	0.1	340	20.2	3400	3023 G	26.73394	84.77969	Normal	
27/4/22	8:54:30	10	0.1	310	10.1	3100	2778 G	26.7339	84.77969	Normal	
27/4/22	8:55:5	10	0.1	320	20.2	3200	2860 G	26.73394	84.77969	Normal	
27/4/22	8:55:5	10	0.1	260	20.2	2600	2370 G	26.73394	84.77969	Normal	

Total IRI	43466
Average IRI	2897.733

27/4/22

27/4/22

Name of Customer : M/S Jyoti Vandana Construction
 Name of Work : T04 to Dharmpur
 Road :
 Lab Job number : 10
 Date : 4/27/2022
 Section No : 10


Print Generate Report and Graph

Test Date :	4/27/2022	Road Name :	T04 to Dharmpur
Machine No :	378	Road Type :	(R) RURAL ROAD
Start S No :		Side :	
Start E No :		Interval :	
Weather :		UV Range :	1370 To 4000 mm/km
Start Location :		Dist Range :	0 To 16 01 - 1000 m
End Location :		Equation :	$Y = 0 \cdot X^2 + 0.816 \cdot X + 2.43$

Redraw Graph

Map View

File : D:\PUMPTMOTILARI DIM\Jyoti Vandana 6 Roads\T04 To Dharmpur\05040906 Xls. Section No : 10. Egn : Y =
 Name of Customer : M/S Jyoti Vandana Construction. Name of Work : Road : T04 to Dharmpur. Lab Job number : 10

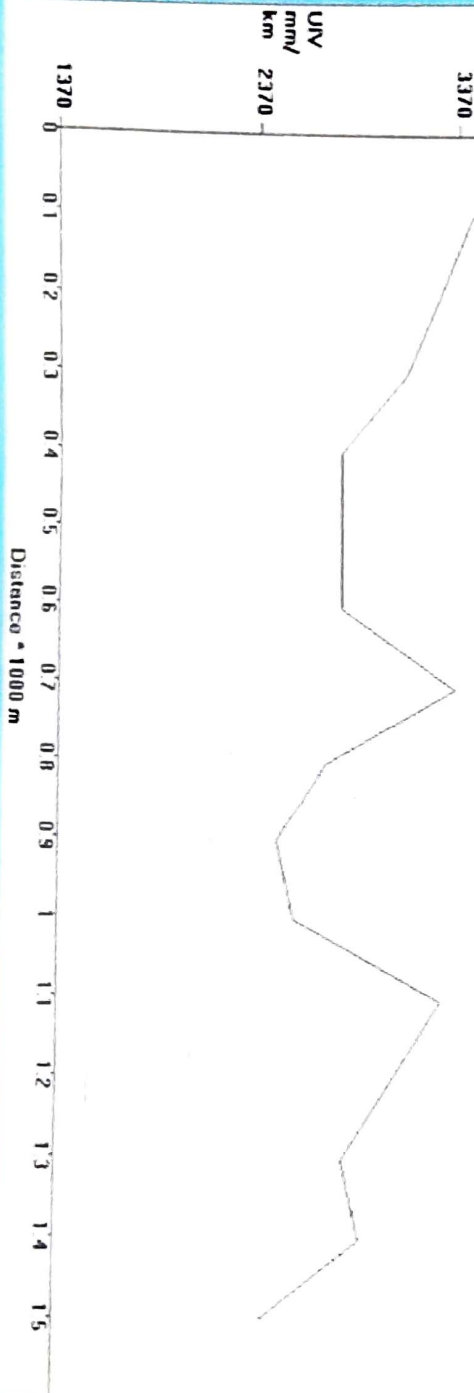

24/04/22
J.E.

28/4/22
BE
