

कार्यालय अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, सासाराम — 1

पत्रांक:- ९६० अउ०

सासाराम/दिनांक:- 16.6.22

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, सासाराम-1

सेवा में,

नोडल पदाधिकारी,
3054 एम0आर0 नई अनुस्क्षण नीति-2018
ग्रामीण कार्य विभाग
बिहार, पटना।

विषय :- शीर्ष 3054 एम0आर0 नई अनुस्क्षण नीति-2018 के तहत पूर्ण कराये गये पथों के अनुस्क्षण कार्य का आवंटन उपलब्ध कराने के संबंध में।

प्रसंग :- विभागीय पत्रांक मु0अ0-4(मु0)3054-04-229/2021-97 अनु0/पटना दिनांक 07.01.2022


महाशय,

उपर्युक्त विषयक प्रासंगिक पत्र के माध्यम से दिये गये निर्देश के आलोक में कहना है कि जिन पथों का अनुस्क्षण कार्य पूर्ण कराया गया है। उन पथों से संबंधित वांछित सुचनाएँ विहित प्रपत्र में तैयार कर आवश्यक कार्यार्थ समर्पित की जाती है।

सुचनार्थ एवं आवश्यक कारवाई हेतु सादर समर्पित।

अनु0 :- यथोक्त।

विश्वासभाजन


कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, सासाराम-1

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

PIU Name:- ER PARWEZ ALAM

1st Quarter - 31/07/2021 - 30/10/2021

1	Name of the Road	Seo Sagar - Chenari Rd. - Semari		
2	Batch No.	RM/RO/SAS/20/0002		
3	Project ID	NEA 22 0001049		
4	Total Length of Road (In Km)	2 KM		
5	Length of Road to Meet Required Service Level [Completed Length] (in Km) [1]	2 KM		
6	No. of Total Quarter (i.e. 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	17.32142 lakh		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	0.866071 lakh		
Compliance Criteria	Standard job Description	Non-Compliance		Reduction Payment [6] = [3]/[1] * [2] * [4]
		Length Non-Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGEWAY)	0.00	60%	0.00
II	SHOULDERS AND EMBANKMENTS	0.00	10%	0.00
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0.00	15%	0.00
IV	SIGNAGE AND ROAD SAFETY	0.00	10%	0.00
V	VEGETATION	0.00	5%	0.00
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh)			[5]	0.00
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh)			[6]	0.86607 lakh

Date of inspection by E/I of his agent

Prepared by Contractor's self Control unit

Puneshwar. yadav

Name and Designation of person inspection road

06/06/22

(Signature)

Date 06/06/22

Signature of person inspection road

AE

Certify by E/I [signature] Date:-

06/06/22

Name of Road : SHEOSAGAR CHENARI PATH SE SEMRI

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event
4/6/22	7:37:0	18	0.1	290	20.2	2900	3426 G		24.913527	83.822862	Normal
4/6/22	7:37:36	18	0.1	320	20.2	3200	3767 G		24.914413	83.823063	Normal
4/6/22	7:38:0	18	0.1	330	20.2	3300	3881 G		24.915302	83.823163	Normal
4/6/22	7:38:11	18	0.1	320	30.3	3200	3767 G		24.916137	83.82337	Normal
4/6/22	7:38:11	18	0.1	310	30.3	3100	3654 G		24.91702	83.823535	Normal
4/6/22	7:38:11	18	0.1	270	30.3	2700	3199 G		24.917947	83.823687	Normal
4/6/22	7:38:11	18	0.1	300	20.2	3000	3540 G		24.918807	83.823838	Normal
4/6/22	7:38:46	18	0.1	310	20.2	3100	3654 G		24.919658	83.824057	Normal
4/6/22	7:39:0	18	0.1	340	20.2	3400	3994 G		24.920658	83.82414	Normal
4/6/22	7:39:0	18	0.1	290	20.2	2900	3426 G		24.921527	83.824275	Normal
4/6/22	7:39:21	18	0.1	330	20.2	3300	3881 G		24.922472	83.824393	Normal
4/6/22	7:40:0	18	0.1	290	20.2	2900	3426 G		24.923355	83.824545	Curve
4/6/22	7:40:0	18	0.1	270	30.3	2700	3199 G		24.923505	83.825453	Normal
4/6/22	7:40:0	18	0.1	280	30.3	2800	3313 G		24.92348	83.82648	Normal
4/6/22	7:40:32	18	0.1	340	30.3	3400	3994 G		24.92367	83.827457	Normal
4/6/22	7:40:32	18	0.1	340	30.3	3400	3994 G		24.923682	83.82842	Normal
4/6/22	7:41:0	18	0.1	320	20.2	3200	3767 G		24.924272	83.82904	Normal
4/6/22	7:41:7	18	0.1	320	20.2	3200	3767 G		24.925092	83.829477	Speed Breaker
4/6/22	7:41:7	18	0.1	290	20.2	2900	3426 G		24.9258	83.83003	Normal
4/6/22	7:45:13	18	0.1	340	20.2	3400	3994 G		24.926073	83.83003	Normal
Average IRI							3653				

$$Y = 0 * X^2 + 1.136 * X + 132.5$$

$$X = 3000$$

$$Y = 3540$$

(R) RURAL ROAD
Good
<4000
Average
4001-5000
Poor
>5001

[Signature]
06.06.22
JL

[Signature]
06/06/2022
AC

[Signature]
Executive Engineer
Rural Work's Department
Work Division, Sasaram-1

Name of Customer : SHARDA BHAWANI INFRAST
Name of Work/ Road : SHEOSAGAR CHENARI PATH
Lab Job number : 18
Date : 4/6/2022
Section No. : 18

Test Date : 4/6/2022
Road Name : SHEOSAGAR CHENARI PATH
Machine No. : 391
Road Type : (P) RURAL ROAD
Start S No. : 116
Side : CHENARI
Start E No. : 135
Weather : NORMAL
Interval :
U/V Range : 2199 To 5000
Dist Range : 0 To 0.588
Equation : test
Start Location : 24.913527
End Location : 24.926073
U/V mm/km : 1000
mm/km : 1000 m

Print


Generate Report and Graph

Redraw Graph

Map View

File : E:\BUM INDICATOR REPORT\2022-23\JUN-22\4-6-2022.Xls, Section No. : 18, Eqn : test

Name of Customer : SHARDA BHAWANI INFRASTRUCTURE, Name of Work/ Road : SHEOSAGAR CHENARI PATH

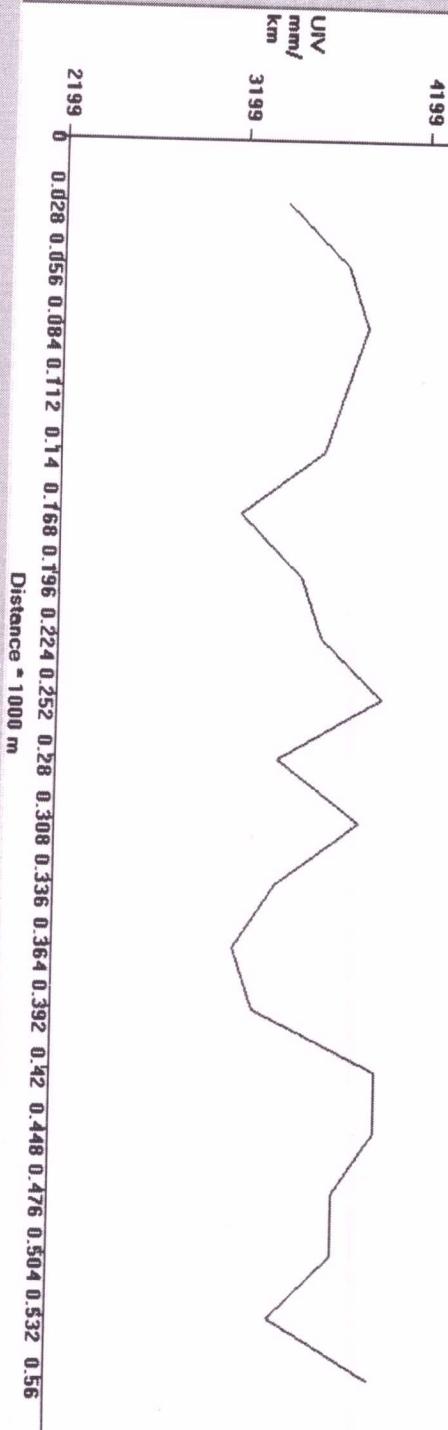

Shy 06.06.22

AE 06/06/2022

WB 16/09/22
