

कार्यालय अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, सासाराम - 1

पत्रांक:- 964 अ३०

सासाराम/दिनांक:- 16.6.22

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, सासाराम-1

सेवा में,

नोडल पदाधिकारी,
3054 एम0आर0 नई अनुरक्षण नीति-2018
ग्रामीण कार्य विभाग
बिहार, पटना।

विषय :- शीर्ष 3054 एम0आर0 नई अनुरक्षण नीति-2018 के तहत पूर्ण कराये गये पथों के अनुरक्षण कार्य का आवंटन उपलब्ध कराने के संबंध में।


प्रसंग :- विभागीय पत्रांक मु0अ0-4(मु0)3054-04-229/2021-97 अनु0/पटना दिनांक 07.01.2022

महाशय,

उपर्युक्त विषयक प्रासंगिक पत्र के माध्यम से दिये गये निर्देश के आलोक में कहना है कि जिन पथों का अनुरक्षण कार्य पूर्ण कराया गया है। उन पथों से संबंधित वांछित सुचनाएँ विहित प्रपत्र में तैयार कर आवश्यक कार्यार्थ समर्पित की जाती है।
सुचनार्थ एवं आवश्यक कारवाई हेतु सादर समर्पित।

अनु0 :- यथोक्त।

विश्वासभाजन


कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, सासाराम-1

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

PIU Name:- **ER. PARWEZ ALAM**

1st Quarter - 27/08/2021 - 26/11/2021

1	Name of the Road	Chenari Malhibur Rd. - Primary Uda School Via Pevandi		
2	Batch No.	RM/RO/SA/20/0002		
3	Project ID	NEA22000758		
4	Total Length of Road (In Km)	4.55 KM		
5	Length of Road to Meet Required Service Level [Completed Length] (in Km) [1]	4.55 KM		
6	No. of Total Quarter (i.e. 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	39.29137 lakh		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	1.96457 lakh		
Compliance Criteria	Standard job Description	Non-Compliance		Reduction Payment [6] = [3]/[1] * [2] * [4]
		Length Non-Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGEWAY)	0.00	60%	0.00
II	SHOULDERS AND EMBANKMENTS	0.00	10%	0.00
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0.00	15%	0.00
IV	SIGNAGE AND ROAD SAFETY	0.00	10%	0.00
V	VEGETATION	0.00	5%	0.00
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh)		[5]		0.00
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh)		[6]		1.96457 lakh

Date of inspection by E/I of his agent

Prepared by Contractor's self Control unit

Puneshwar Yadav
Name and Designation of person inspection road

06.06.22
(Signature)

Date 06/06/22

AE
Signature of person inspection road

06/06/22
Certify by E/I [signature] Date:-

Name of Road : CHENARI MALHIPUR PATH SE PRATHMIK URDU VIDYALAY VIA PEVANDI

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD			
4/6/22	8: 24: 6	20	0.1	310	10.1	3100	3654	G	24.911492	83.785673	Normal
4/6/22	8: 24: 41	20	0.1	330	20.2	3300	3881	G	24.910577	83.785723	Speed Breaker
4/6/22	8: 25: 0	20	0.1	320	10.1	3200	3767	G	24.909698	83.785908	Normal
4/6/22	8: 25: 17	20	0.1	320	20.2	3200	3767	G	24.908825	83.785823	Speed Breaker
4/6/22	8: 26: 0	20	0.1	330	10.1	3300	3881	G	24.907943	83.785622	Normal
4/6/22	8: 26: 27	20	0.1	300	10.1	3000	3540	G	24.907748	83.786143	Normal
4/6/22	8: 26: 27	20	0.1	270	10.1	2700	3199	G	24.907575	83.787153	Curve
4/6/22	8: 27: 3	20	0.1	270	10.1	2700	3199	G	24.90673	83.787087	Normal
4/6/22	8: 27: 38	20	0.1	280	10.1	2800	3313	G	24.905857	83.787037	Normal
4/6/22	8: 28: 0	20	0.1	340	10.1	3400	3994	G	24.905488	83.787945	Speed Breaker
4/6/22	8: 29: 24	20	0.1	280	10.1	2800	3313	G	24.905415	83.78882	Speed Breaker
4/6/22	8: 30: 0	20	0.1	270	20.2	2700	3199	G	24.90537	83.789628	Normal
4/6/22	8: 30: 34	20	0.1	270	20.2	2700	3199	G	24.905405	83.788687	Normal
4/6/22	8: 31: 0	20	0.1	330	10.1	3300	3881	G	24.905547	83.787793	Normal
4/6/22	8: 31: 10	20	0.1	320	10.1	3200	3767	G	24.905905	83.786918	Normal
4/6/22	8: 31: 45	20	0.1	290	10.1	2900	3426	G	24.906192	83.785908	Normal
4/6/22	8: 32: 0	20	0.1	300	10.1	3000	3540	G	24.906463	83.784965	Normal
4/6/22	8: 32: 19	20	0.1	270	10.1	2700	3199	G	24.906632	83.784007	Normal
4/6/22	8: 32: 19	20	0.1	290	20.2	2900	3426	G	24.906735	83.783147	Normal
4/6/22	8: 32: 19	20	0.1	320	40.4	3200	3767	G	24.906885	83.78212	Normal
4/6/22	8: 32: 19	20	0.1	340	30.3	3400	3994	G	24.90716	83.781178	Normal
4/6/22	8: 33: 0	20	0.1	330	20.2	3300	3881	G	24.907338	83.7801	Normal
4/6/22	8: 34: 5	20	0.1	320	20.2	3200	3767	G	24.907888	83.78005	Normal
4/6/22	8: 34: 5	20	0.1	300	30.3	3000	3540	G	24.908498	83.78079	Normal
4/6/22	8: 34: 5	20	0.1	330	30.3	3300	3881	G	24.909028	83.781515	Normal
4/6/22	8: 34: 5	20	0.1	310	40.4	3100	3654	G	24.909635	83.782272	Normal
4/6/22	8: 34: 40	20	0.1	280	40.4	2800	3313	G	24.91027	83.78303	Normal
4/6/22	8: 34: 40	20	0.1	290	40.4	2900	3426	G	24.9109	83.783703	Normal
4/6/22	8: 35: 0	20	0.1	300	40.4	3000	3540	G	24.911588	83.784443	Normal
4/6/22	8: 35: 0	20	0.1	290	40.4	2900	3426	G	24.912177	83.78508	Normal
4/6/22	8: 35: 16	20	0.1	300	40.4	3000	3540	G	24.91287	83.785858	Normal
4/6/22	8: 35: 16	20	0.1	330	30.3	3300	3881	G	24.913497	83.786548	Normal
4/6/22	8: 35: 16	20	0.1	330	20.2	3300	3881	G	24.91413	83.787272	Normal
4/6/22	8: 36: 0	20	0.1	340	20.2	3400	3994	G	24.914808	83.787945	Normal
4/6/22	8: 36: 0	20	0.1	300	30.3	3000	3540	G	24.915473	83.788602	Normal

$$Y = 0 * X^2 + 1.136 * X + 132.5$$

$$X = 3000$$

$$Y = 3540$$

(R) RURAL ROAD

Average Poor
4001-5000 >5001

249

4/6/22	8:36:26	20	0.1	320	20.2	3200	3767	G	24.91616	83.789325	Normal
4/6/22	8:36:26	20	0.1	310	20.2	3100	3654	G	24.916858	83.789932	Normal
4/6/22	8:37:1	20	0.1	320	10.1	3200	3767	G	24.917632	83.790487	Normal
4/6/22	8:37:37	20	0.1	320	20.2	3200	3767	G	24.918387	83.790875	Normal
4/6/22	8:37:37	20	0.1	300	20.2	3000	3540	G	24.919258	83.791212	Normal
4/6/22	8:38:0	20	0.1	310	20.2	3100	3654	G	24.9201	83.79148	Normal
4/6/22	8:38:12	20	0.1	310	20.2	3100	3654	G	24.921013	83.7918	Normal
4/6/22	8:38:12	20	0.1	320	20.2	3200	3767	G	24.921873	83.792087	Normal
4/6/22	8:38:47	20	0.1	310	20.2	3100	3654	G	24.92273	83.792373	Normal
4/6/22	8:39:0	20	0.1	330	30.3	3300	3881	G	24.923565	83.792642	Normal
Average IRI									3628		

Shy
06.06.22
JE

Nur
06/06/2022
AE

28/6/22
Executive Engineer
Rural Work's Department
Work Division, Sasaram-1


Name of Customer : SHARDA BHAWANI INFRAST
Name of Work/ Road : CHENARI MALHIPUR PATH S
Lab Job number : 20
Date : 4 / 6 / 2022
Section No. : 20

Print Generate Report and Graph

Test Date : 4 / 6 / 2022
Machine No. : 391
Start S No. : 171
Start E No. : 215
Weather : NORMAL
Start Location : 24.911492
End Location : 24.923565
Road Name : CHENARI MALHIPUR PATH S
Road Type : (R) RURAL ROAD
Side : CHENARI
Interval :
U/V Range : 2199 To 5000
Dist Range : 0 To 1.288
Equation : test
U/V mm/km

Redraw Graph

Map View

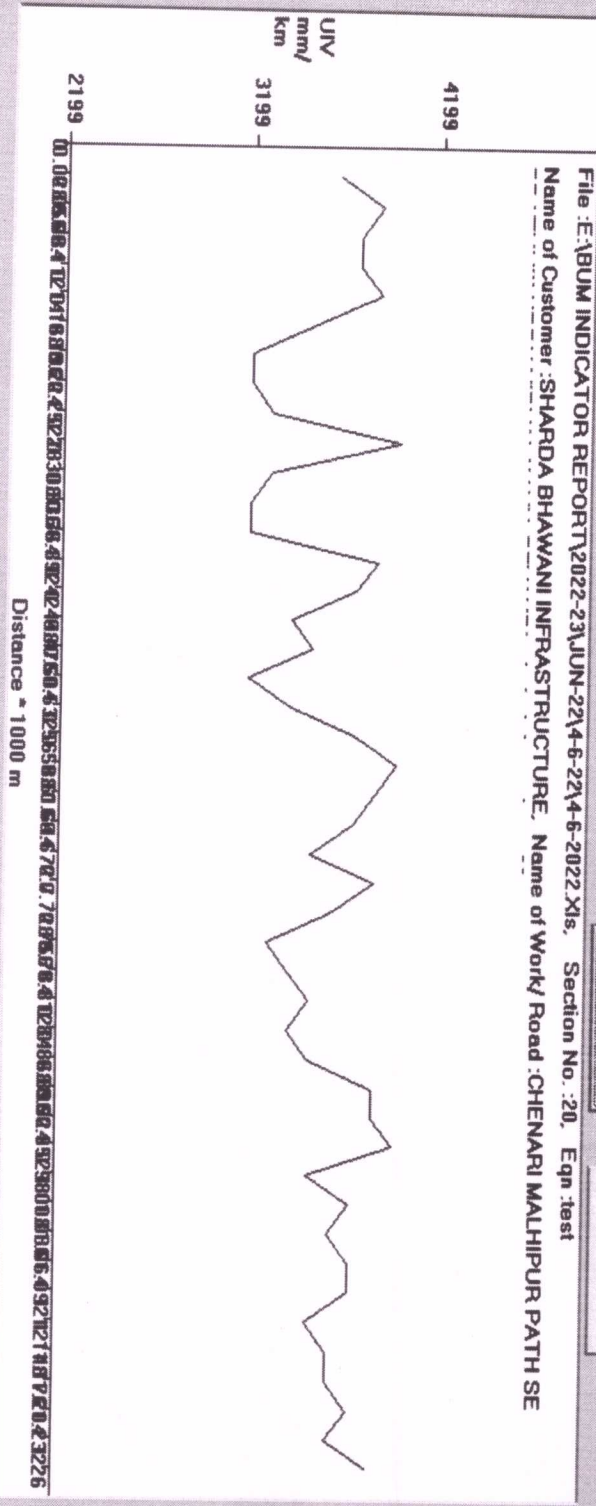

06.04.22
 06/06/22
 16/6/22
