

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, हाजीपुर

पत्रांक:- 484

/दिनांक:- 10.03.2022

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
हाजीपुर।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-
सचिव, बिहार, ग्रामीण पथ विकास अभिकरण,
पटना।

विषय:- शीर्ष 3054 नई अनुरक्षण नीति 2018 मद का अधियाचना के सम्बन्ध में।

महाशय,

उपर्युक्त विषयक संबंध में कहना है कि शीर्ष 3054 नई अनुरक्षण नीति 2018 मद योजनान्तर्गत इस प्रमंडल अंतर्गत चल रहे पथों के निर्माण कार्यों हेतु कुल 43.250 लाख रुपये आवंटन की आवश्यकता है।

अतः अनुरोध है कि उक्त मांग की गयी राशि उपलब्ध कराने की कृपा की जाए।

अनु: - अधियाचना विहित प्रपत्र में

विश्वासभाजन


10/3/22

कार्यपालक अभियंता
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
हाजीपुर।

Requisition Format for Scheme Head - MR (3054) Under Bihar Rural Road Maintenance Policy - 2018 (Initial Rectification and Surface Renewal)

Name of Works Division : - RWD, Works Division, Hajipur.

Sl NO	Package No	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date)	Administrative Approval (AA)		Agreement Amount (In Lakh)		Agreement No/ Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness Bitumen Layer(in mm	Value of Bitumen Content in Percentage	Previous Total Alloted Amount (In Lakh)	up-to-date Expenditure as per MIS (In Lakh)	Requisition against work done (In Lakh)	Remarks
					Length (in KM)	Amount (In Lakh)	Initial Rectification With Surface Renewal (In Lakh)	5 Year Routine Maintenance (In Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
I	RM/VA/HAJ /19/0004	Kansara - Sapha	31507502071	3352/01.08.19	2.39	73.48752	43.28500	19.19500	49/MBD/2020-21 dt- 07.12.2020	08.06.2020		2070.000	25.00	5.010	0.000000	0.000000	43.25000	Surface Completed.

1 Signed Hard Copy and Soft Copy (In excel) of recorded IRI is enclosed.

2 Up-to-date Physical Progress has been Uploaded in MIS.


 Executive Engineer
 RWD, Works Division,
 Hajipur.

Name of the work: KANSARA - SAPHA

Date	Time	Test No	Distance (meter)	Total Distance (meter)	BUMP (cm)	Speed(Km/Hr)	UI(mm/Km)	Corrected UI (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction 1	Remarks
9/3/2022	19:25:51	12	100	100	17.0 cm	4.8 Km/Hr	1700.0 mm/Km	1670.3	2.39	Good	25.6704435	N	85.2515955	E	Normal
9/3/2022	19:26:20	12	100	200	11.0 cm	12.4 Km/Hr	1100.0 mm/Km	1124.9	1.68	Good	25.6704435	N	85.2515955	E	Normal
9/3/2022	19:26:42	12	100	300	28.0 cm	16.3 Km/Hr	2800.0 mm/Km	2670.2	3.63	Good	25.6704435	N	85.2515955	E	Normal
9/3/2022	19:27:04	12	100	400	14.0 cm	16.0 Km/Hr	1400.0 mm/Km	1397.6	2.04	Good	25.6704435	N	85.2515955	E	Normal
9/3/2022	19:29:34	12	100	500	19.0 cm	2.4 Km/Hr	1900.0 mm/Km	1852.1	2.62	Good	25.7164888	N	85.3096018	E	Normal
9/3/2022	19:29:55	12	100	600	16.0 cm	16.3 Km/Hr	1600.0 mm/Km	1579.4	2.27	Good	25.7164888	N	85.3096018	E	Normal
9/3/2022	19:29:55	12	100	700	16.0 cm	17.6 Km/Hr	1600.0 mm/Km	1579.4	2.27	Good	25.7164888	N	85.3096018	E	Normal
9/3/2022	19:30:15	12	100	800	17.0 cm	18.8 Km/Hr	1700.0 mm/Km	1670.3	2.39	Good	25.7164888	N	85.3096018	E	Normal
9/3/2022	19:30:35	12	100	900	23.0 cm	21.2 Km/Hr	2300.0 mm/Km	2215.7	3.07	Good	25.7127199	N	85.3100748	E	Normal
9/3/2022	19:30:52	12	100	1000	13.0 cm	8.8 Km/Hr	1300.0 mm/Km	1306.7	1.92	Good	25.7127199	N	85.3100748	E	Normal
9/3/2022	19:31:32	12	100	1100	15.0 cm	9.1 Km/Hr	1500.0 mm/Km	1488.5	2.16	Good	25.7105398	N	85.3093958	E	Normal
9/3/2022	19:32:12	12	100	1200	17.0 cm	9.0 Km/Hr	1700.0 mm/Km	1670.3	2.39	Good	25.7105398	N	85.3093958	E	Normal
9/3/2022	19:32:52	12	100	1300	15.0 cm	17.4 Km/Hr	1500.0 mm/Km	1488.5	2.16	Good	25.7105398	N	85.3093958	E	Normal
9/3/2022	19:33:12	12	100	1400	16.0 cm	19.0 Km/Hr	1600.0 mm/Km	1579.4	2.27	Good	25.7105398	N	85.3093958	E	Normal
9/3/2022	19:33:31	12	100	1500	11.0 cm	18.6 Km/Hr	1100.0 mm/Km	1124.9	1.68	Good	25.7071543	N	85.307992	E	Normal
9/3/2022	19:33:50	12	100	1600	12.0 cm	19.2 Km/Hr	1200.0 mm/Km	1215.8	1.8	Good	25.7071543	N	85.307992	E	Normal
9/3/2022	19:34:09	12	100	1700	15.0 cm	17.6 Km/Hr	1500.0 mm/Km	1488.5	2.16	Good	25.7071543	N	85.307992	E	Normal
9/3/2022	19:34:29	12	100	1800	19.0 cm	13.7 Km/Hr	1900.0 mm/Km	1852.1	2.62	Good	25.7071543	N	85.307992	E	Normal
9/3/2022	19:34:56	12	100	1900	10.0 cm	14.7 Km/Hr	1000.0 mm/Km	1034	1.56	Good	25.7071543	N	85.307992	E	Normal
9/3/2022	19:35:20	12	100	2000	7.0 cm	11.8 Km/Hr	700.0 mm/Km	761.3	1.18	Good	25.7044649	N	85.3046045	E	Normal
9/3/2022	19:35:51	12	100	2100	9.0 cm	9.8 Km/Hr	900.0 mm/Km	943.1	1.43	Good	25.7045908	N	85.3036127	E	Normal
9/3/2022	19:36:27	12	100	2200	3.0 cm	15.6 Km/Hr	300.0 mm/Km	397.7	0.66	Good	25.7049322	N	85.3028955	E	Normal
9/3/2022	19:36:52	12	100	2300	13.0 cm	11.5 Km/Hr	1300.0 mm/Km	1306.7	1.92	Good	25.705287	N	85.302331	E	Normal
9/3/2022	19:37:21	12	100	2400	9.0 cm	12.1 Km/Hr	900.0 mm/Km	943.1	1.43	Good					

IRI Value 2070
Machine No 19190


10.03.22
JE

Sanjay 10.03.22

9/3/22

ms 10/3/22

Name of Contractor: M/S NARAINI CONSTRUCTION, Machine no: 19190, Road: KANSARA - SAPHA, Date: 09/03/22, Section No: 12, Equation: $Y=0.908X+125.0$

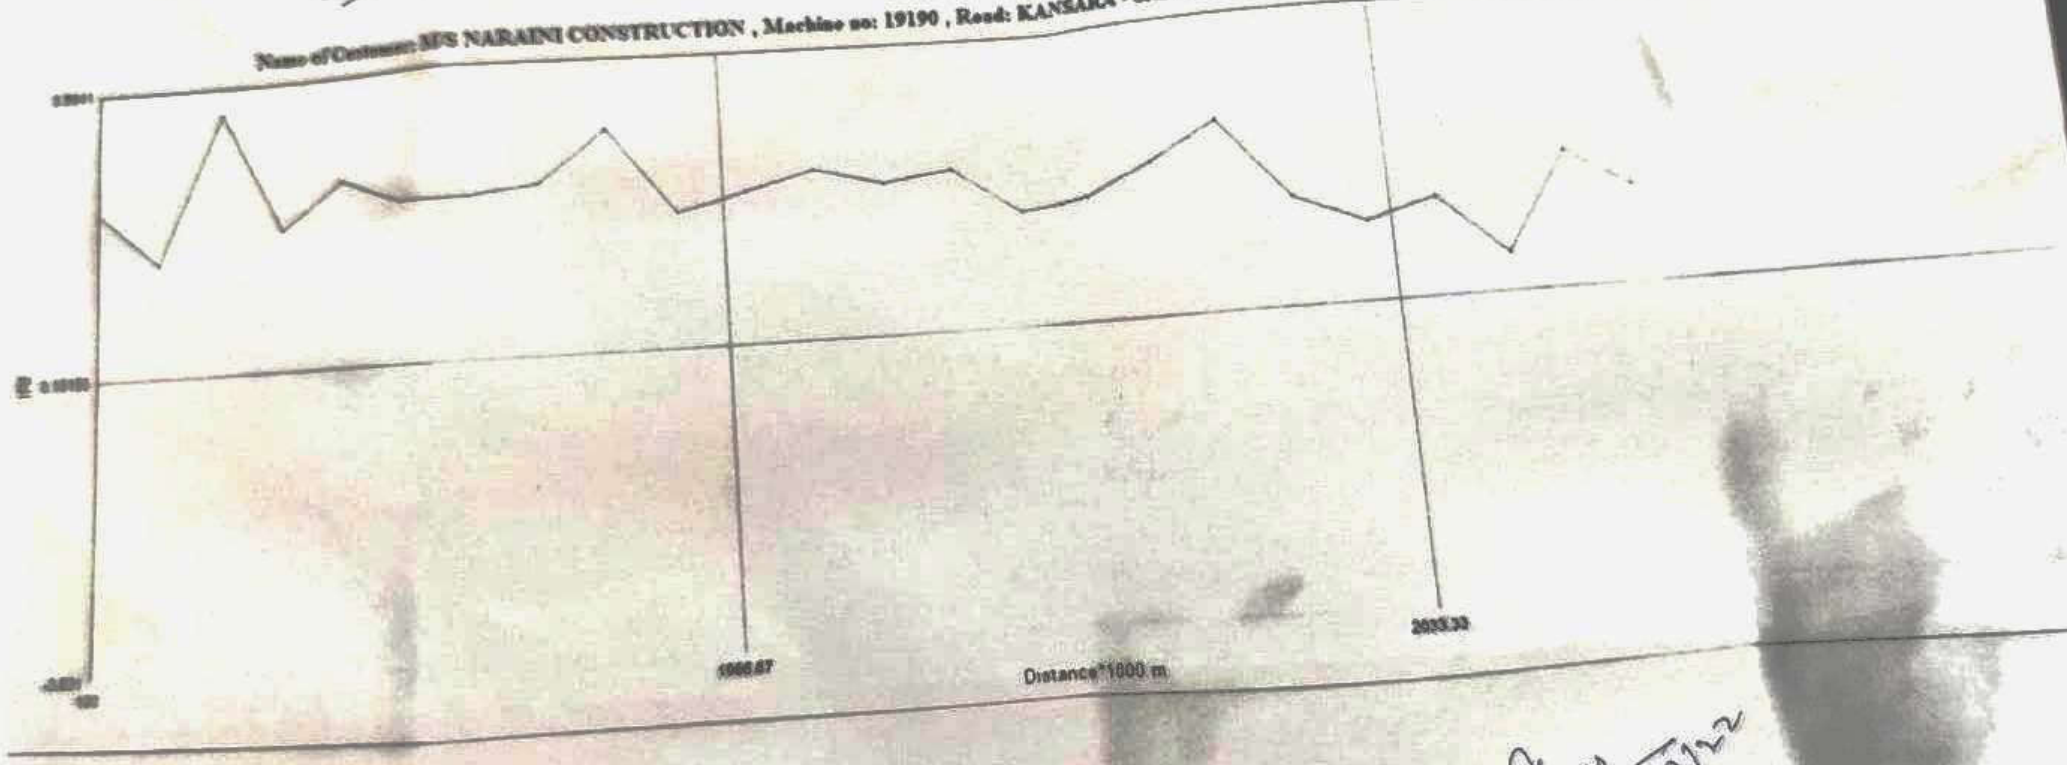

K
10.03.22
JE

Sanjay
10.03.22

Jas
10/3/22
JL

Direction

1
E
E
E
E
E
E
E

3
8
18
58
158
358

958
392
992

99
199
79
16
3
1

Sanjay
10.03.22

Assistant Engineer
RWD, Works Sub Division, Hajipur
Works Division, Hajipur

Executive Engineer
RWD Works Division
Hajipur
