

**कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल, कटिहार।**

पत्रांक :- 533

/कटिहार, दिनांक-14-03-2022

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, कटिहार।

सेवा में,

अपर-मुख्य-कार्यपालक-पदाधिकारी,
BRRDA, 3री मंजिल, भूमि विकास बैंक भवन,
बिहार, पटना।

विषय :- शीर्ष New Maintenance Policy-2018 योजनान्तर्गत निर्माण हेतु आवंटन की अधियाचना के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि शीर्ष New Maintenance Policy-2018 योजनान्तर्गत ग्रा0का0वि0, कार्य प्रमंडल, कटिहार द्वारा विहित प्रपत्र में अधियाचना तैयार कर आपके अग्रेतर कार्रवाई हेतु समर्पित की जाती है।

अनु0:-यथोक्त।

विश्वासभाजन,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, कटिहार।

ज्ञापांक:- 533

/कटिहार, दिनांक:- 14-03-2022

प्रतिलिपि:- नोडल पदाधिकारी, 3054 MR, ग्रामीण कार्य विभाग, बिहार, पटना को सूचनार्थ एवं आवश्यक कार्रवाई हेतु समर्पित।

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, कटिहार।

Requisition Format for Scheme Head - MR (3054) Under Bihar Rural Road maintenance Policy 2018 (Initial Rectification and Surface Renewal)

Name of Division : Katihar

[Signature]
Executive Engineer
RWD, Work Division, Kathihar

[Signature]
14/13/22
Divisional Accounts Officer
RWD, Works Division, Kathihar

(See Government of India's Decision (1) below Rule-150)
Form of Utilisation Certificate upto the month of March, 2022

Sl. No.	Name of Scheme	Sanction No. & Date with Amount (in Rs. Lacs)	Amount Received (in Rs. Lacs)	Particulars
I	New Maintenance Policy-2018	Lt, No.- 017 Dt - 26.02.21	80 03702	Certified that out of Rs. 3069.61029 lacs received upto the year-2021-22 in favour of Ex. Engineer, RWD, Katihar a sum of Rs. 2703.62776 lacs has been utilized for the purpose of NMP-2018 rural roads Schemes as given in the margin for which it was sanctioned and that the balance of Rs. 365.98253 lacs remaining unutilized at the end of the period under.
		Lt, No.- 027 Dt - 04.05.21	70 40501	
		Lt, No.- 040 Dt - 14.06.21	368 10325	
		Lt, No.- 052 Dt - 24.08.21	273 38928	
		Lt, No.- 058 Dt - 27.10.21	161 36000	
		Lt, No.- 060 Dt - 09.11.21	357 44478	
		Lt, No.- 064 Dt - 06.12.21	765 74778	
		Lt, No.- 068 Dt - 23.12.21	98 70000	
		Lt, No.- 002 Dt - 03.01.22	4 80697	
		Lt, No.- 005 Dt - 25.01.22	358 67297	
		Lt, No.- 010 Dt - 21.02.22	145 54793	
		Lt, No.- 016 Dt - 08.03.22	87 69809	
		Lt, No.- 018 Dt - 11.03.22	297 69721	
		Total :-	3069.61029	

- Executive Engineer,
RWD (W) Division, Katihar.

Lab Job number :62

Date :13-03-2022

Name of Customer :Anwar Hussain

Name of Work/ Road :Hasanganj Satami PWD Road To Rampur Koshpali

Sr.no	Location of test(in km)	Corrected U.I value(mm/km)	Road catagory
1	0.100	2593	G
2	0.200	2690	G
3	0.300	2400	G
4	0.400	2981	G
5	0.500	3369	G
6	0.600	2787	G
7	0.700	2012	G
8	0.800	3272	G
9	0.900	3175	G
10	1.000	2884	G
11	1.100	2593	G
12	1.200	2690	G
13	1.300	2787	G
14	1.400	2981	G
15	1.500	3369	G
16	1.600	2884	G
17	1.700	2593	G
18	1.800	3175	G
19	1.900	3369	G
20	2.000	2884	G
21	2.100	3078	G
22	2.200	3272	G
23	2.300	2690	G
24	2.400	2497	G
25	2.500	2884	G
26	2.600	2400	G
27	2.700	2690	G
28	2.800	2400	G
29	2.900	2254	G
Average IRI value		2815.62	

Signature
13.3.2022
JE

Signature
19/3/2022
Executive Engineer
R.W.D. (W) Division
Kathihar

Lab Job number :62
Date :13-03-2022

Name of Customer :Anwar Hussain

Name of Work/ Road :Hasanganj Satami PWD Road To Rampur Koshpali

Date	Section No.	Time	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event
13/3/22	62	8:34:39	0.100	260	0	2600	2593	G	25.669920	87.593130	Normal
13/3/22	62	8:35:0	0.100	270	10.1	2700	2690	G	25.670815	87.593130	Normal
13/3/22	62	8:35:14	0.100	240	20.2	2400	2400	G	25.671660	87.593430	Normal
13/3/22	62	8:35:14	0.100	300	20.2	3000	2981	G	25.672403	87.593938	Normal
13/3/22	62	8:35:49	0.100	340	20.2	3400	3369	G	25.673275	87.594107	Normal
13/3/22	62	8:36:0	0.100	280	20.2	2800	2787	G	25.674180	87.594107	Normal
13/3/22	62	8:36:0	0.100	200	20.2	2000	2012	G	25.675058	87.594512	Normal
13/3/22	62	8:36:24	0.100	330	20.2	3300	3272	G	25.675850	87.594915	Normal
13/3/22	62	8:36:24	0.100	320	20.2	3200	3175	G	25.676622	87.595453	Normal
13/3/22	62	8:37:0	0.100	290	20.2	2900	2884	G	25.677423	87.595908	Normal
13/3/22	62	8:37:0	0.100	260	20.2	2600	2593	G	25.678195	87.596347	Normal
13/3/22	62	8:37:35	0.100	270	20.2	2700	2690	G	25.679027	87.596648	Curve
13/3/22	62	8:37:35	0.100	280	20.2	2800	2787	G	25.679627	87.597407	Normal
13/3/22	62	8:38:0	0.100	300	20.2	3000	2981	G	25.680482	87.597390	Curve
13/3/22	62	8:38:10	0.100	340	20.2	3400	3369	G	25.681362	87.597222	Curve
13/3/22	62	8:38:10	0.100	290	20.2	2900	2884	G	25.682260	87.597222	Normal
13/3/22	62	8:38:46	0.100	260	20.2	2600	2593	G	25.683143	87.597153	Normal
13/3/22	62	8:39:0	0.100	320	20.2	3200	3175	G	25.684025	87.597070	Normal
13/3/22	62	8:39:21	0.100	340	20.2	3400	3369	G	25.684857	87.596885	Curve
13/3/22	62	8:39:21	0.100	290	20.2	2900	2884	G	25.685723	87.596868	Culvert
13/3/22	62	8:39:21	0.100	310	20.2	3100	3078	G	25.686158	87.596110	Curve
13/3/22	62	8:40:0	0.100	330	20.2	3300	3272	G	25.687057	87.596127	Normal
13/3/22	62	8:40:0	0.100	270	30.3	2700	2690	G	25.687978	87.596178	Normal
13/3/22	62	8:40:31	0.100	250	20.2	2500	2497	G	25.688895	87.596010	Curve
13/3/22	62	8:40:31	0.100	290	20.2	2900	2884	G	25.689470	87.595387	Curve
13/3/22	62	8:41:0	0.100	240	20.2	2400	2400	G	25.689987	87.594595	Curve
13/3/22	62	8:41:7	0.100	270	20.2	2700	2690	G	25.690872	87.594612	Normal
13/3/22	62	8:41:7	0.100	240	20.2	2400	2400	G	25.691842	87.594713	Normal
13/3/22	62	8:41:7	0.040	90	30.3	2250	2254	G	25.692092	87.594763	Normal


Y = 0 * X ^ 2 + 0.969 * X + 74.60
X = 2250
Y = 2254

(R) RURAL ROAD
Good <4000
Average 4001-5000
Poor >5001

13.3.2022
76

Anwar Hussain
Executive Engineer
R.W.D. (W) Division
Katihar

File : C:\RAM KUMAR\MISC Files\Bump integrator\{Hasanganj\Rampur Kospali\13030842.Xls, Section No. : 62, Eqn
 Name of Customer : Anwar Hussain, Name of Work/ Road : Hasanganj Satami PWD Road To Rampur Koshpali, Lab

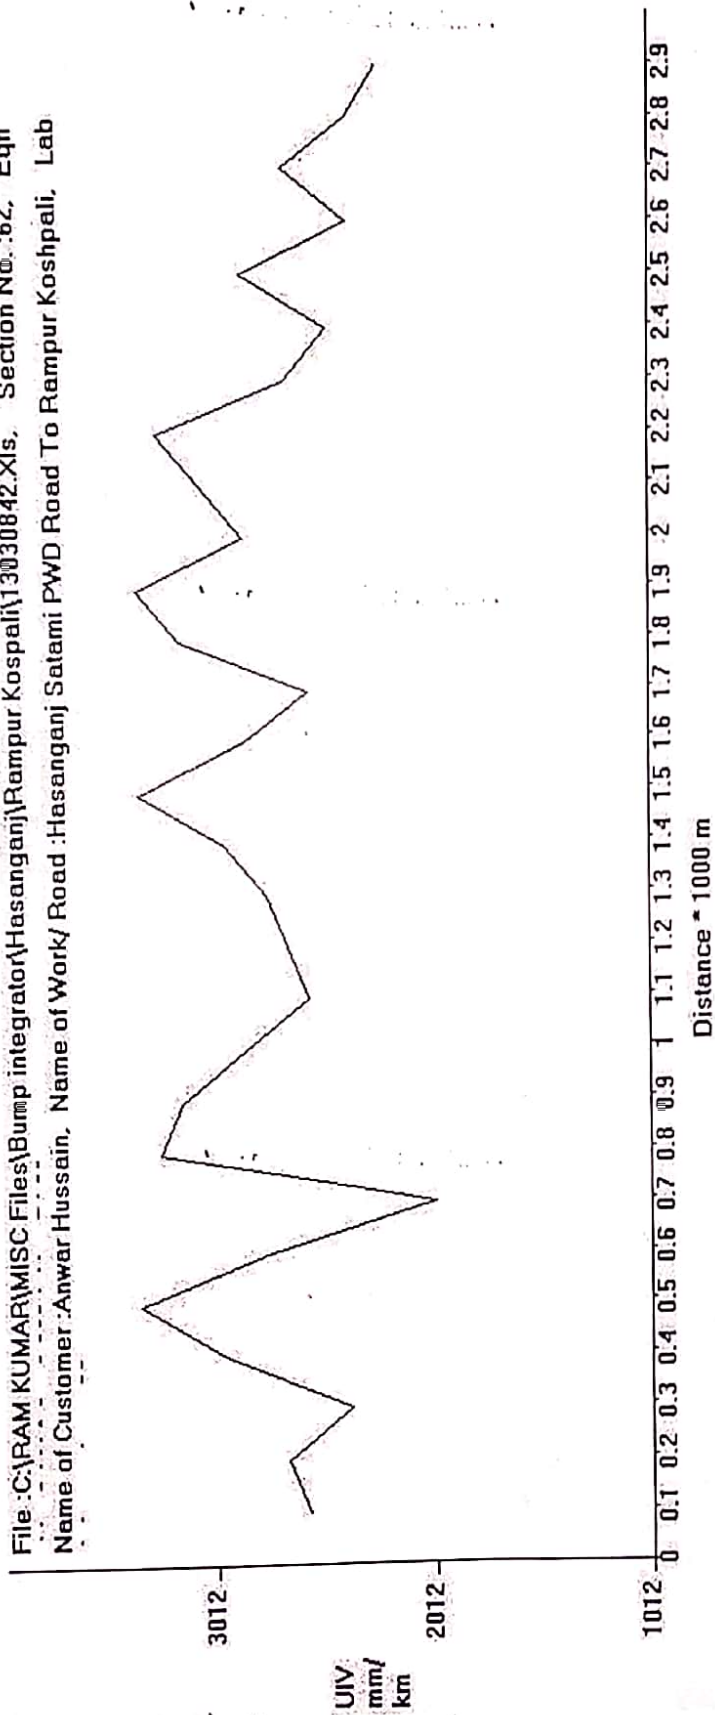

ful
 13.3.2022
 TL

Anwar Hussain
 Executive Engineer
 R.W.D. (W) Division
 Katihar

MR-N/19-20

Schedule XLV-Form No. 134
HASANIGANS SATAM PWD ROAD To
RAMPUR KOSHAPALI.

R.W.D. KATHAR- DIVISION

HASANIGANS-SUB-DIVISION

(NO-2038-)

MEASUREMENT BOOK

Istan A/C Bill

Sch. XLV—Form No. 134

11

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
ABSTRACT OF COST					
Name of work:—Hasanganj P.W.D					
To Rambar Kestali					
Agency: Anwar Hussain AT					
Officers colony mirchaibon					
Keshibon					
Agreement no 08/MDD 2020-2021					
Dated/commencement 8.8.2020					
Date of Completion 7.5.2021					
Re: constantly					
① cleaning 18000 bbs					
of road land					

0.568 Hec @ 4 TMBP-1

0.568 Hec @ 53232.50/H = 302362

② PV & fixing 18000 bbs

2 NO @ 4 TMBP-1

2 NO @ 9463.01/NO = 189262

③ PV laying & Compaction

Co. S.D. with well

graded Stonemeter

113.07 m³ @ 4 TMBP-3

113.07 m³ @ 199550/m³ = 2256652

④ limit 109.34 PV laying & Compaction 218220=20

with m.c. II

111.58 m³ @ 4 TMBP-5

Continuation

Total C.O. = 2798272

B = 2673822

Sch. XLV—Form No. 134

$$B = 45,729312 \infty$$

Stingh
13/3/2023
A.E.

Executive Engineer
R.W.D. (W) Division
Katihar
