

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग कार्य प्रमंडल अररिया

पत्रांक 982 अनु0 / अररिया,

दिनांक 12-03-22

प्रेषक,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमण्डल, अररिया।

सेवा में,

सचिव सह शक्ति प्रदत्त पदाधिकारी
ब्राडा (BRRDA)
बिहार पटना।

विषय:- M/R (3054) Bihar Rural Road Maintenance Policy - 2018 में कराए गए
कार्य का भुगतान हेतु अधियाचना के संबंध में।

महाशय

उपर्युक्त विषय के संबंध में कहना है कि इस प्रमंडल के कार्य क्षेत्रान्तर्गत कार्यान्वित
हो रहे M/R (3054) Bihar Rural Road Maintenance Policy - 2018 में संवेदक के विपत्र का
भुगतान हेतु संलग्न विवरणीनुसार आवंटन उपलब्ध कराने की कृपा की जाय।

अनु0-

1. विवरणी

विश्वासभाजन

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, अररिया।

09.3.22

Requisition Format for Scheme Head MR (3054) under Bihar Rural Road Maintenance Policy - 2018 (Initial Rectification and Surface Renwal)

Division - Araria

Si. No.	Package no.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (in Lakh)		Agreement No. & Date	Date of Completion as per Agreement	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in percentage	Previous Total Allowed Amount (in Lakh)	Up to date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (in Km.)	Amount (in Lakh)	Initial Rectification and Surface Renwal	5 Year Routine Maintenance									
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18
1	MR-N/19-20/AR/ARLA/04	NH-57 Pactola Kusiyargawan part-B	NEA2200022	Letter no. 2066 Date - 24.07.2019	6.00	200.755	273.54611	118.2724	128 MBD MR 3054 2020-21	03.12.2021	2906	25mm	5.01%	110.99865	110.99865	17.82951	

- 1 Signed Hard Copy and Soft Copy (In excel) of Recorde IRI is enclosed.
- 2 Up - to date Physical Progress has been uploaded in MIS


 Executive Engineer
 RWD Araria Works Division, Araria
 14.9.22

Lab Job number :37
Date :22-01-2021

Name of Customer :Gray stone Inf.pvt

Name of Work/ Road :REO ROAD RAMPUR KUDARKATTI

Sr no Location of Corrected U.I Road catagory
test(in km) value(mm/km)

76	0.1	3272 G
77	0.2	2981 G
78	0.3	3369 G
79	0.4	2400 G
80	0.5	3874 G
81	0.6	2787 G
82	0.7	2206 G
83	0.8	3369 G
84	0.9	3272 G
85	1	4135 A
86	1.1	3369 G
87	1.2	2690 G
88	1.3	2981 G
89	1.4	2012 G
90	1.5	3078 G
91	1.6	3369 G
92	1.7	4397 A
93	1.8	2787 G
94	1.9	1721 G
95	2	2109 G
96	2.1	2690 G
97	2.2	2400 G
98	2.3	3369 G
99	2.4	2787 G
100	2.5	3562 G
101	2.6	2497 G
102	2.7	2497 G
103	2.8	2109 G
104	2.9	1624 G
105	3	3369 G
106	3.1	2206 G
107	3.2	2884 G
108	3.3	3874 G
109	3.4	3078 G
110	3.5	3369 G
111	3.6	4157 A
112	3.7	3562 G
113	3.8	2884 G
114	3.9	3175 G
115	4	3853 G

22/01/21
AL

Executive Engineer
R.M.D. Works Division
Anand

116	4.1
117	4.2
118	4.3
119	4.4
120	4.5
121	4.6
122	4.7
123	4.8
124	4.9
125	5
126	5.1
127	5.2
128	5.3
129	5.4
130	5.5
131	5.6
132	5.7
133	5.8

3466 G
3789 G
2981 G
3466 G
3756 G
3369 G
3466 G
3272 G
3562 G
2206 G
3272 G
3659 G
3466 G
2787 G
3369 G
2593 G
2787 G
2690 G

AS
22/01/24
AZ

by
Zambory

Executive Engineer
R.W.D. Works Division
Araria

Date	Time	Section No	Length		Bumps	Speed	OR		IRI CATEGORY	Latitude	Longitude	Event
			in km	in mm		Rate	mm/km	mm/km				
22/1/21	13 18 34	37	0.1		330	0	3300		3272 G	26 7826	87 48276	Normal
22/1/21	13 19 0	37	0.1		300	30.3	3000		2981 G	26 7802	87 48187	Normal
22/1/21	13 19 11	37	0.1		340	20.2	3400		3369 G	26 77752	87 48084	Normal
22/1/21	13 19 11	37	0.1		240	20.2	2400		2400 G	26 777	87 47988	Normal
22/1/21	13 19 46	37	0.1		410	20.2	3400		3874 G	26 77438	87 47886	Normal
22/1/21	13 20 0	37	0.1		280	30.3	2800		2787 G	26 77493	87 47788	Normal
22/1/21	13 20 0	37	0.1		220	30.3	2200		2206 G	26 77627	87 47692	Normal
22/1/21	13 20 22	37	0.1		340	20.2	3400		3369 G	26 77748	87 47591	Curve
22/1/21	13 20 22	37	0.1		330	20.2	3300		3272 G	26 76878	87 47594	Normal
22/1/21	13 21 0	37	0.1		450	20.2	4100		4135 A	26 75987	87 47599	Curve
22/1/21	13 21 0	37	0.1		340	20.2	3400		3469 G	26 75613	87 47508	Normal
22/1/21	13 21 0	37	0.1		270	30.3	2700		2690 G	26 75473	87 47406	Normal
22/1/21	13 21 31	37	0.1		300	20.2	3000		2981 G	26 75377	87 47308	Normal
22/1/21	13 22 0	37	0.1		200	20.2	2000		2012 G	26 74595	87 47269	Normal
22/1/21	13 22 6	37	0.1		310	10.1	3100		3078 G	26 74102	87 47194	Curve
22/1/21	13 22 42	37	0.1		340	10.1	3400		3469 G	26 73377	87 47148	Normal
22/1/21	13 23 17	37	0.1		570	10.1	4300		4197 A	26 72653	87 47101	Speed Brea
22/1/21	13 23 17	37	0.1		280	10.1	2800		2787 G	26 72107	87 47032	Normal
22/1/21	13 23 17	37	0.1		170	20.2	1700		1721 G	26 7209	87 46931	Normal
22/1/21	13 24 0	37	0.1		210	20.2	2100		2109 G	26 722	87 46835	Normal
22/1/21	13 24 0	37	0.1		270	20.2	2700		2690 G	26 72262	87 46732	Normal
22/1/21	13 24 28	37	0.1		240	20.2	2400		2400 G	26 72378	87 46631	Normal
22/1/21	13 24 15	37	0.1		340	20.2	3400		3400 G	26 72318	87 4653	Normal
22/1/21	13 26 15	37	0.1		280	0	2800		2787 G	26 72322	87 46535	Normal
22/1/21	13 26 15	37	0.1		360	20.2	3600		3562 G	26 72375	87 46638	Normal
22/1/21	13 26 49	37	0.1		250	20.2	2500		2497 G	26 72252	87 46736	Normal
22/1/21	13 27 0	37	0.1		250	30.3	2500		2497 G	26 72162	87 46813	Normal
22/1/21	13 27 0	37	0.1		210	30.3	2100		2109 G	26 72085	87 46938	Normal
22/1/21	13 29 45	37	0.1		160	20.2	1600		1624 G	26 72118	87 47039	Normal
22/1/21	13 30 0	37	0.1		340	10.1	3400		3339 G	26 75197	87 47631	Normal
22/1/21	13 30 0	37	0.1		220	20.2	2200		2206 G	26 74313	87 47662	Normal
22/1/21	13 30 0	37	0.1		290	20.2	2900		2884 G	26 7346	87 47695	Normal
22/1/21	13 30 0	37	0.1		450	10.1	3600		3874 G	26 72672	87 47739	Normal
22/1/21	13 31 0	37	0.1		310	20.2	3100		3078 G	26 72675	87 47702	Normal
22/1/21	13 31 0	37	0.1		340	20.2	3400		3400 G	26 71044	87 47611	Normal
22/1/21	13 31:41	37	0.1		460	10.1	3800		4157 A	26 7014	87 47859	Normal
22/1/21	13 32 6	37	0.1		360	10.1	3600		3562 G	26 691	87 47882	Normal
22/1/21	13 32 45	37	0.1		290	10.1	2900		2884 G	26 68427	87 47916	Normal
22/1/21	13 33 0	37	0.1		320	10.1	3200		3175 G	26 67613	87 47958	Normal
22/1/21	13 33 17	37	0.1		390	20.2	3900		3851 G	26 6675	87 47991	Normal
22/1/21	13 33 17	37	0.1		350	20.2	3500		3466 G	26 65878	87 4802	Normal
22/1/21	13 34 0	37	0.1		500	10.1	3540		3789 G	26 65023	87 48047	Normal
22/1/21	13 34 27	37	0.1		300	10.1	3000		2981 G	26 64137	87 48079	Normal
22/1/21	13 34 27	37	0.1		350	20.2	3500		3466 G	26 63328	87 48116	Speed Brea
22/1/21	13 35 3	37	0.1		380	20.2	3800		3756 G	26 62492	87 48153	Normal
22/1/21	13 35 3	37	0.1		340	20.2	3400		3369 G	26 6162	87 48185	Normal
22/1/21	13 35 38	37	0.1		350	10.1	3500		3466 G	26 60753	87 48212	Normal
22/1/21	13 35 38	37	0.1		330	20.2	3300		3272 G	26 59873	87 48234	Normal
22/1/21	13 36 0	37	0.1		360	20.2	3600		3562 G	26 58953	87 48253	Normal
22/1/21	13 36 13	37	0.1		220	20.2	2200		2206 G	26 58028	87 48268	Normal
22/1/21	13 37 0	37	0.1		330	0	3300		3272 G	26 57165	87 48291	Normal
22/1/21	13 37 24	37	0.1		370	10.1	3700		3659 G	26 56355	87 48322	Normal
22/1/21	13 37 24	37	0.1		350	20.2	3500		3466 G	26 55518	87 48359	Normal
22/1/21	13 38 0	37	0.1		290	20.2	2900		2884 G	26 54642	87 48391	Normal
22/1/21	13 38 0	37	0.1		340	10.1	3400		3400 G	26 53797	87 48426	Normal
22/1/21	13 38 34	37	0.1		260	20.2	2600		2595 G	26 52973	87 48461	Normal
22/1/21	13 38 34	37	0.1		280	20.2	2800		2787 G	26 52105	87 48498	Normal
22/1/21	13 39 10	37	0.1		270	20.2	2700		2690 G	26 5124	87 48535	Normal


Rev
22/1/21

AR
22/01/21
AC

22/1/21

Executive Engineer

Name of Customer : Gray stone inf.pvt. Name of Work Road : RED ROAD RAMPUR KUDARKATTI, Lab Job

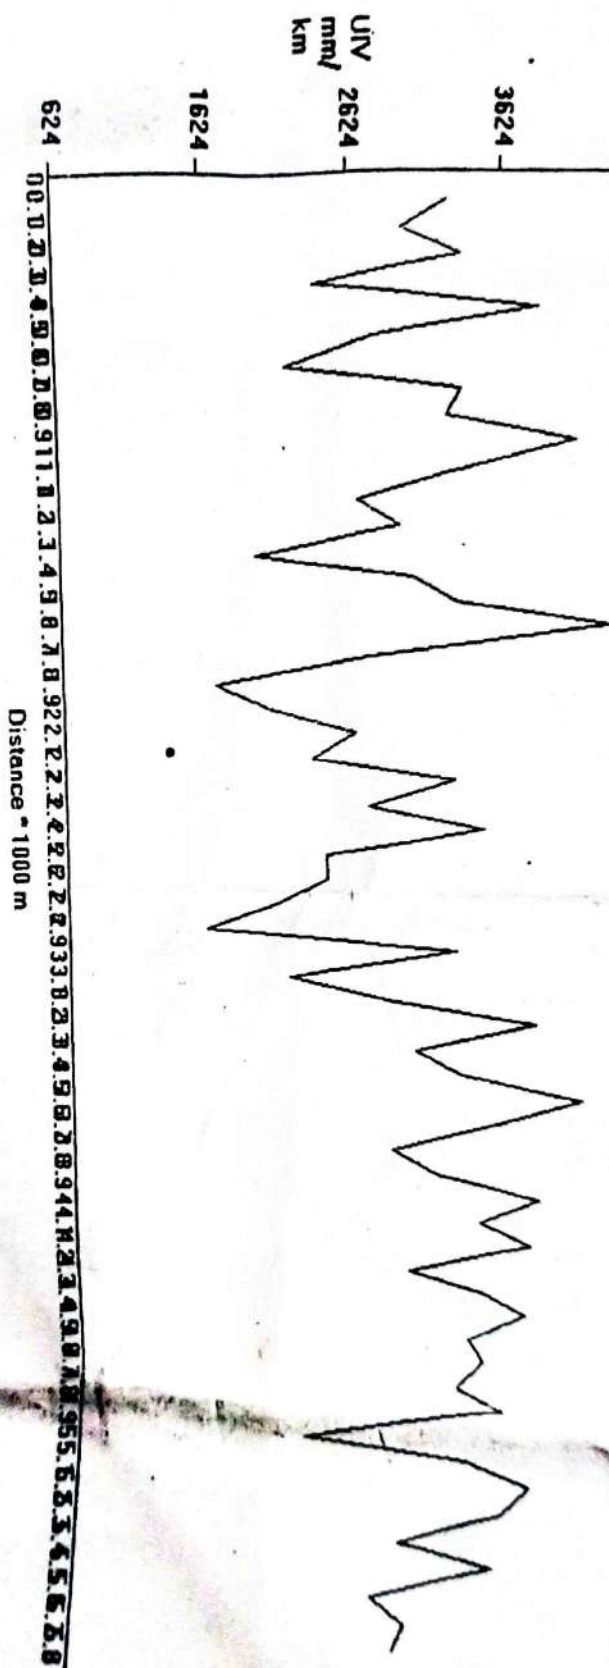

Distance = 1000 m

22.01.24

2012/21

20.12.19

Engine
Division
Arata

3054. 51051A Const. of Road from
1-57 Pakfola to Kushiyatgan
Part - B (Package NO-1412-N/11-3 14-04
Agreement NO-128/M13D/M16-3054-20-21
Schedule XLV-Form No. 134

Name of Const. Gya Stone for Pvt. Ltd

Const. Cost - 27354611=

Maint. Cost - 11827294=

Total - 39181855=

DIVISION

Date of Commence:- 04/12/2020

SUB-DIVISION

Date of Completion:- 03/12/2021

MEASUREMENT BOOK

2209

Sch. XLV-Form No. 134

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
Name of Road:- Comp. of Road from NH 51 to Park side to Kumbhgarh Amt B.					
Package no:- MR-N/19-20/104.					
Agency:- Graystone Infra Pvt Ltd.					
At:- Ashram Mohalla, 12/11-10, Amritsar.					
Agmt no:- 128/MBD/MR-3054 dt/2020-21					
Date of start:- 04/12/2020					
Date of Comp:- 03/12/2021					
Actual Date of start:- 03/12/2021					
Measurement:-					
1) Constr. of Subgrade (Earth) shoulder do E1					
For plank ^{1st} =	2x6x	30.00x	0.70x	0.30 =	75.60 m ³
	2x13x	10.00x	0.70x	0.30 =	54.60 ..
	2x4x	6.00x	0.45x	0.25 =	5.40 ..
	2x8x	8.00x	0.30x	0.30 =	11.52 ..
	2x5x	20.00x	0.70x	0.30 =	42.00 ..
	2x7x	15.00x	0.70x	0.30 =	56.60 ..
	2x11x	30.00x	0.70x	0.30 =	138.60 ..
	2x12x	16.50x	0.70x	0.30 =	15.54 ..
				Tot =	399.88 m ³
					(A)
2nd Km =	2x14x	15.00x	0.70x	0.30 =	88.20 m ³
	2x7x	30.00x	0.70x	0.30 =	113.40 ..
	2x8x	6.00x	0.60x	0.25 =	14.40 ..
	2x5x	30.00x	0.60x	0.30 =	54.00 ..
	2x5x	20.00x	0.70x	0.30 =	42.00 ..
	2x10x	15.00x	0.70x	0.30 =	63.00 ..

Continuation
