



ग्रामीण कार्य विभाग



(बिहार सरकार)

क्षतिग्रस्त पथ का नाम

Middle Schoole Belha to

Belha Bajrang Chowk

(Estimated Cost: ^{0.80275 L.} ~~1.71585~~ Lakh)

ग्रामीण कार्य विभाग,
कार्य प्रमंडल- फुलपरास।

प्रकल्प - फुलपरास

Inspection Report for Flood Damaged Work in the year 2021-22


Date of Inspection :- 28.4.22 Name Of PIU:-RWD, Works Division, Benipatti
Name of Block :- Phulparas
Name of Road :- Middle school Belha To Belha Barrang
Chouk.
For Road . :-

1. Damage Location/ Chainage :- 270, 278, 55
2. Damage Length :- 58.50 mtr
3. Nature of Damage :- ~~35.542~~ Flank damaged.


4. Details of Restoration Works :-

- i. Material being used in Restoration Works Brick bats
ii. Equipment's/ Tools being used in Restoration Works Tractors
iii. Procedure taken up in Restoration Works Brick bats Filling.
iv. Restored Length - 58.50 mtr Restored Qty = 35.542 m³

Remarks :-


28.04.22
S.E. Chak
JE
Signature of JE/AE


28.04.22
A.E.


28.04.22
Signature of E.E.

Detailed estimate For restoration of road From - Middle School belha
Belha Bagrang chowk.
Under FDR 2021.

Abstract Of Cost.

1. Restoration of Road embankment using Brick Bats.....etc....

35-542
~~75.97~~ ²⁴² m3 @ Rs. 1907/m3 = Rs. - 677.94.00
 Add GST 12% = Rs. 1,44,907.00
 Add LC 1% = Rs. 17,389.00
 Fee ³⁵⁻⁵⁴² ~~75.97~~ m3 @ 1032m3 x 10% = Rs. 678.00
 1449.00
 3668.00
 78,902.00
Total = Rs. 1,71,585.00

Rs. 80,275.00

1000
 2.11.21

2.11.21

21/11/21

R2

कार्य प्रालोकन अभिलेख जारी किया जा रहा है। कार्य प्रमाणित लेनी पड़ेगी।
 जांचोपरान्त, पत्रांक - 855 (अगु) दिनांक:- 29/04/2022

Technically sanctioned for Rs- 80,275.00 (Rupees -
 Eighty thousand two hundred seventy five) only.

Superintending Engineer
 RWD Work Circle, Darbhanga

Abhinav
 05/05/22

Detailed estimate For restoration of road From Middle School Belh to Belha Bazar chowk. FDR 2021.

Restoration of road embankment using brick bats.....etc.

CH. 270 M to 295 M -

$$1 \times 25.10 \times \frac{1.0 + 2.0}{2} \times \frac{0.3 + 0.500}{2} = 15.00 \text{ M}^3$$

$$34.88 \text{ M}^3$$

Link Road

CH. 55 M to 68.50 M.

$$11.50 \text{ M} \times \frac{1.90 + 2.30}{2} \times \frac{0.3 + 0.800}{2} = 13.282 \text{ M}^3$$

$$22.94$$

CH. 278 M to 300 M

$$1 \times 22.1 \text{ M} \times \frac{1.00 + 1.20}{2} \times \frac{0.15 + 0.45}{2} = 7.26 \text{ M}^3$$

$$18.15$$

58.50 M

75.97 M³

35.542 M³

Sub
2.11.21
JE

Sum
2.11.21
B

3005
2.11.21

Chanel
28.04.22
A.E

chuka & venkatesh
28.04.22
OE

28.04.22
I.E

28.04.22
A.E

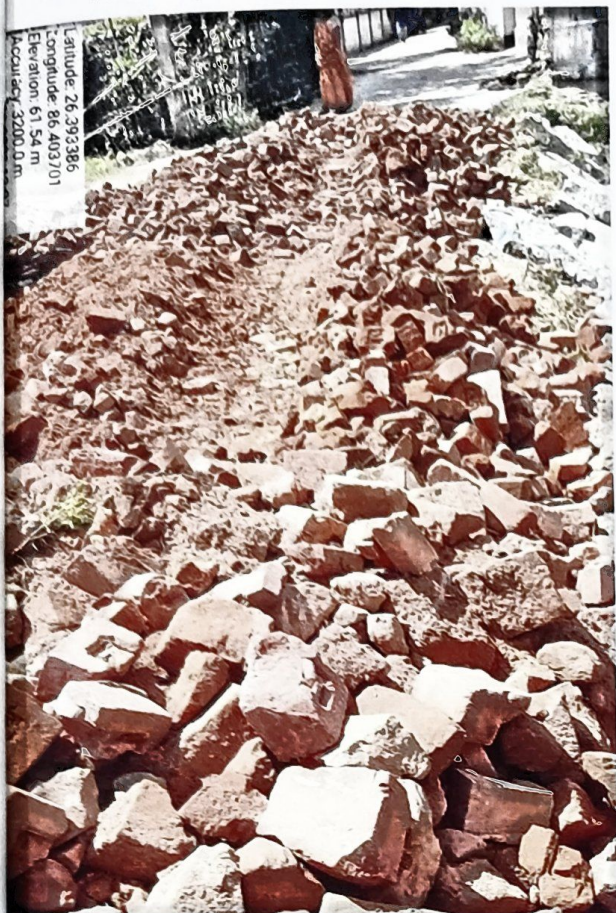
29.04.22
EE
Banipatti

MIDDEL SCHOOL BELHA TO BAJRANG CHAUK



Redon
2.11.21 JE
2.11.21 JE

MIDDLE SCHOOL BELHA TO BAJRANG CHAUK



Ldoo
2.11.21/02

2.11.21
82

Particulars	Details of actual measurement				Contents of area
	No.	L ₁	D ₁	D ₂	
(1) Name of Work: Restoration of Road					
from Middle School Bldg to Bldg.					
Surveying done under C.D.R.					
Authority: C.L. Road (w/ Dir's Phulpur)					
Agency: Departmental					
Date of Measurements: 29.7.21					
Date of entry: 30.7.22					
(2) Restoration of road					
embankment using					
brick bats					
At charge 270 M to 295 M					
1 x 2.5.0 x 1.0 + 2.0 x 0.30 + 0.80 = 15.0 M ³					
Link Road					
or 55 M to 68.50 M					
1 x 1.50 M x 1.90 + 2.30 x 0.30 + 0.80 = 13.88					
or 278 M to 300 M					
1 x 22.0 x 1.0 + 1.20 x 0.150 + 0.450 = 7.25					
Total 30.7.22					35.542 M ³
Sum 30.4.22					
Abstract of cost					
(1) Restoration of road					
embankment using brick					
bats					
35.542 x 3 @ 2 1907.42 / 113 R					67794.00
477 G.S. 12% - 8					8135.00
Adm L.C. - 1% - 8					678.00
3. Free R					3668.00

Continuation

9 80,275 = 00
