

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमण्डल हथुआ।

पत्रांक:- 498 3190 / हथुआ।

दिनांक:- 05/05/2022

प्रेषक,

कार्यपालक अभियन्ता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, हथुआ।

सेवा में,

सचिव,
बिहार ग्रामीण पथ विकास अभिकरण,
बिहार पटना।


विषय :- राशि उपलब्ध कराने के संबंध में।

महाशय,

उपरोक्त विषय के संबंध में कहना है कि बिहार ग्रामीण पथ नई अनुरक्षण नीति-2018 के तहत पंचवर्षीय अनुरक्षण अवधि के अधीन पथों में कराये गये त्रैमासिक अनुरक्षण कार्य हेतु राशि की अधियाचना उपलब्ध कराये गये प्रपत्र में सभी सूचनाओं के साथ अंकित कर समर्पित किया जाता है।

अनु0- यथोक्त।

विश्वासभाजन,


कार्यपालक अभियन्ता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, हथुआ।

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT *1st Quarter*

PIU Name :

1	Name of the Road	<i>Bukit Buzor To Sawang Li Bajar</i>		
2	Batch No.	<i>RM/60/HAT/20/0003</i>		
3	Project ID	<i>314711031757</i>		
	Total Length of Road (in Km)	<i>3.70 Km</i>		
5	Length of Road to Meet Required Service Level [Completed length] (in Km) [1]	<i>3.70 Km</i>		
6	No. of Total Quarter (ic 3 Months as a unit) in 5 years	<i>20</i>		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	<i>34.8896</i>		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	<i>1.74448</i>		
Compliance Criteria	Standard Job Description	Non-Compliance		Reduction Payments [6] = [3] / [1] * [2] * [4]
		Length Non-Compliant [3]	Weighted value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGEWAY)	<i>00</i>	<i>60%</i>	<i>00</i>
II	SHOULDERS AND EMBANMENTS	<i>00</i>	<i>10%</i>	<i>00</i>
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	<i>00</i>	<i>15%</i>	<i>00</i>
IV	SIGNAGE AND ROAD SAFETY	<i>00</i>	<i>10%</i>	<i>00</i>
V	VEGATAION	<i>00</i>	<i>5%</i>	<i>00</i>
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				<i>00</i>
TO HE PAID FOR THE QUARTER / DEMAND (in Lakh) [6]				<i>1.74448</i>

Date of inspection by E/I or his agent
Prepared by Contractor's self Control unit

OH
28/3/22
Name and Designation of person inspecting road

Date

Signature of person inspecting road

(Signature)

Certify by E/I [signature] Date:-

Name of work : bathua bajar to sawanahi bajar

Name of customer : Hathuva Construction Private Limited

(R)Rural Road	
Good	Average
< 4000	4001 - 5000
	Poor
	> 5000

Date	Time	Test No	Distance(m)	Total Distance(m)	BUI(P/cm)	Speed(Km/Hr)	U/I(mm/Km)	Corrected U/I (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks
Z7/03/22	20:34:34	8	0	0	0.0 cm	36.3 Km/Hr	0.0 mm/Km	245	0.43	Good	26.3949671	N	84.2267923	E	Normal
Z7/03/22	21:17:40	8	100	100	22.0 cm	5.0 Km/Hr	2200.0 mm/Km	2305	3.18	Good	26.4805231	N	84.2345514	E	Normal
Z7/03/22	21:17:53	8	100	200	31.0 cm	26.4 Km/Hr	3100.0 mm/Km	3147	4.2	Good	26.4809828	N	84.2346898	E	Normal
Z7/03/22	21:18:05	8	100	300	33.0 cm	29.1 Km/Hr	3300.0 mm/Km	3334	4.43	Good	26.4822683	N	84.2346787	E	Normal
Z7/03/22	21:18:17	8	100	400	30.0 cm	30.9 Km/Hr	3000.0 mm/Km	3053	4.09	Good	26.4822883	N	84.2349787	E	Normal
Z7/03/22	21:18:27	8	100	500	36.0 cm	33.8 Km/Hr	3600.0 mm/Km	3615	4.76	Good	26.4836874	N	84.2352381	E	Normal
Z7/03/22	21:18:37	8	100	600	39.0 cm	36.7 Km/Hr	3900.0 mm/Km	3896	5.09	Good	26.4849901	N	84.2354517	E	Normal
Z7/03/22	21:18:47	8	100	700	33.0 cm	36.3 Km/Hr	3300.0 mm/Km	3334	4.43	Good	26.4859228	N	84.2356424	E	Normal
Z7/03/22	21:18:58	8	100	800	28.0 cm	33.0 Km/Hr	2800.0 mm/Km	2886	3.87	Good	26.4868422	N	84.2358103	E	Normal
Z7/03/22	21:18:11	8	100	900	36.0 cm	28.8 Km/Hr	3600.0 mm/Km	3615	4.76	Good	26.4875536	N	84.2360010	E	Normal
Z7/03/22	21:18:22	8	100	1000	34.0 cm	32.0 Km/Hr	3400.0 mm/Km	3428	4.54	Good	26.4886484	N	84.2362299	E	Normal
Z7/03/22	21:18:32	8	100	1100	32.0 cm	34.5 Km/Hr	3200.0 mm/Km	3241	4.32	Good	26.4895239	N	84.2364283	E	Normal
Z7/03/22	21:18:43	8	100	1200	37.0 cm	36.0 Km/Hr	3700.0 mm/Km	3709	4.87	Good	26.4905157	N	84.2366037	E	Normal
Z7/03/22	21:20:09	8	100	1300	31.0 cm	14.4 Km/Hr	3100.0 mm/Km	3147	4.2	Good	26.4911547	N	84.2367334	E	Normal
Z7/03/22	21:20:41	8	100	1400	38.0 cm	10.2 Km/Hr	3800.0 mm/Km	3802	4.98	Good	26.4922743	N	84.2369471	E	Normal
Z7/03/22	21:20:53	8	100	1500	38.0 cm	30.3 Km/Hr	3800.0 mm/Km	3802	4.98	Good	26.4928160	N	84.2370815	E	Normal
Z7/03/22	21:21:05	8	100	1600	33.0 cm	28.8 Km/Hr	3300.0 mm/Km	3334	4.43	Good	26.4932909	N	84.2371454	E	Normal
Z7/03/22	21:21:17	8	100	1700	34.0 cm	32.4 Km/Hr	3400.0 mm/Km	3428	4.54	Good	26.4944906	N	84.2374048	E	Normal
Z7/03/22	21:21:29	8	100	1800	32.0 cm	28.8 Km/Hr	3200.0 mm/Km	3241	4.32	Good	26.4956789	N	84.2375956	E	Normal
Z7/03/22	21:21:38	8	100	1900	32.0 cm	36.7 Km/Hr	3200.0 mm/Km	3241	4.32	Good	26.4966726	N	84.2377939	E	Normal
Z7/03/22	21:21:48	8	100	2000	32.0 cm	37.0 Km/Hr	3200.0 mm/Km	3241	4.32	Good	26.4976377	N	84.2379923	E	Normal

Name of work : bathua bajar to sawanahi bajar
 Name of customer : Hathuwa Construction Private Limited

(R)Rural Road


		Good		Average		Poor									
		< 4000		4001 - 5000		> 5000									
27/03/22	21:21:58	8	100	2100	36.0 cm	37.8 Km/Hr	3600.0 mm/Km	3615	4.76	Good	26.4965857	N	84.2381678	E	Normal
27/03/22	21:22:11	8	100	2200	36.0 cm	28.2 Km/Hr	3600.0 mm/Km	3615	4.76	Good	26.4994802	N	84.2383280	E	Normal
27/03/22	21:22:23	8	100	2300	34.0 cm	28.2 Km/Hr	3400.0 mm/Km	3428	4.54	Good	26.5003920	N	84.2384577	E	Normal
27/03/22	21:22:37	8	100	2400	30.0 cm	26.2 Km/Hr	3000.0 mm/Km	3053	4.09	Good	26.5013227	N	84.2385599	E	Normal
27/03/22	21:22:49	8	100	2500	35.0 cm	30.3 Km/Hr	3500.0 mm/Km	3521	4.85	Good	26.5022306	N	84.2386408	E	Normal
27/03/22	21:23:03	8	100	2600	32.0 cm	25.9 Km/Hr	3200.0 mm/Km	3241	4.32	Good	26.5031347	N	84.2387247	E	Normal
27/03/22	21:23:17	8	100	2700	31.0 cm	25.7 Km/Hr	3100.0 mm/Km	3147	4.2	Good	26.5040541	N	84.2387552	E	Normal
27/03/22	21:30:08	8	100	2800	34.0 cm	0.9 Km/Hr	3400.0 mm/Km	3428	4.54	Good	26.5045748	N	84.2382282	E	Normal
27/03/22	21:30:41	8	100	2900	30.0 cm	11.0 Km/Hr	3000.0 mm/Km	3053	4.09	Good	26.5044680	N	84.2402811	E	Normal
27/03/22	21:31:12	8	100	3000	32.0 cm	11.3 Km/Hr	3200.0 mm/Km	3241	4.32	Good	26.5040293	N	84.2403040	E	Normal
27/03/22	21:31:24	8	100	3100	19.0 cm	29.1 Km/Hr	1900.0 mm/Km	2024	2.83	Good	26.5029268	N	84.2401667	E	Normal
27/03/22	21:31:36	8	100	3200	29.0 cm	30.9 Km/Hr	2900.0 mm/Km	2950	3.98	Good	26.5009268	N	84.2401667	E	Normal
27/03/22	21:31:47	8	100	3300	33.0 cm	32.4 Km/Hr	3300.0 mm/Km	3334	4.43	Good	26.5009985	N	84.2386920	E	Normal
27/03/22	21:31:56	8	100	3400	36.0 cm	36.5 Km/Hr	3600.0 mm/Km	3615	4.76	Good	26.5003462	N	84.2389157	E	Normal
27/03/22	21:32:05	8	100	3500	27.0 cm	40.0 Km/Hr	2700.0 mm/Km	2773	3.75	Good	26.4996271	N	84.2397013	E	Normal
27/03/22	21:32:13	8	100	3600	29.0 cm	43.2 Km/Hr	2900.0 mm/Km	2960	3.98	Good	26.4989023	N	84.2396173	E	Normal
27/03/22	21:32:21	8	100	3700	34.0 cm	45.9 Km/Hr	3400.0 mm/Km	3428	4.54	Good	26.4973040	N	84.2393579	E	Normal

Handwritten signature and date: 27/03/22, 15/5

Handwritten signature and date: 27/03/22, 15/5

Handwritten signature and date: 27/03/22, 15/5

Name of Customer: Hathwa Construction Private Limited, Machine no: 19193, Road: bathua bajar to saranahi bajar, Date: 27/03/22, Section No: 09, Equation: $y=0.936x+245.3$

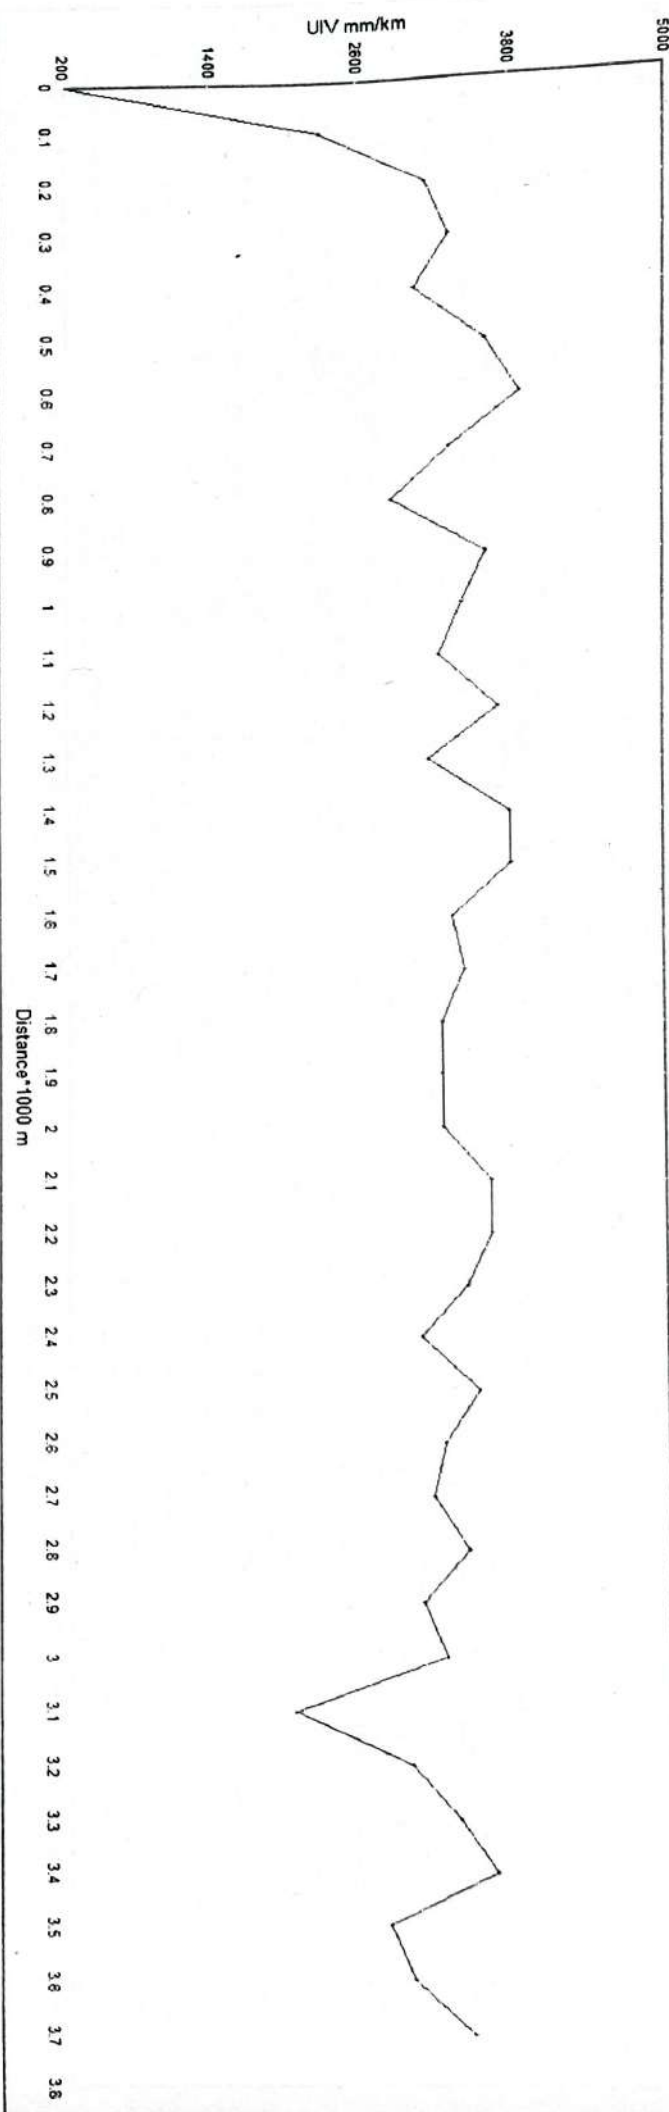

[Handwritten signature]
27/3/22
S.E.

[Handwritten signature]
27/3/22
K.R.

[Handwritten signature]
27/3/22
P.B.

