

कार्यपालक अभियन्ता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमण्डल हथुआ।

पत्रांक:- 498 अगु / हथुआ।

दिनांक:- 05/05/2022

प्रेषक,

कार्यपालक अभियन्ता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, हथुआ।

सेवा में,

सचिव,
बिहार ग्रामीण पथ विकास अभिकरण,
बिहार पटना।

विषय :- राशि उपलब्ध कराने के संबंध में।

महाशय,

उपरोक्त विषय के संबंध में कहना है कि बिहार ग्रामीण पथ नई अनुरक्षण नीति-2018 के तहत पंचवर्षीय अनुरक्षण अवधि के अधीन पथों में कराये गये त्रैमासिक अनुरक्षण कार्य हेतु राशि की अधियाचना उपलब्ध कराये गये प्रपत्र में सभी सूचनाओं के साथ अंकित कर समर्पित किया जाता है।

अनु0- यथोक्त।

विश्वासभाजन,



कार्यपालक अभियन्ता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, हथुआ।

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

PIU Name : **EE RND WORKS DIVISION - HATHUA**

1st Quarter.

1	Name of the Road	Const. of a road from house of Biswadev Banarjee in Sital Hattuan to Sital Kala chaper road road to Sital middle school pitah road via Hattuan to road house of Chandranali Banarjee.		
2	Batch No.	RM/60/HAT/19/0006		
3	Project ID	31407103001		
	Total Length of Road (in Km)	1.100		
5	Length of Road to Meet Required Service Level [Completed length] (in Km) [1]	1.075		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20.		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	9.39210.		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	0.46960		
Compliance Criteria	Standard Job Description	Non- Compliance		Reduction Payments [6] = [3] / [1] * [2] * [4]
		Length Non-Compliant [3]	Weighted value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGEWAY)	00	60%	00
II	SHOULDERS AND EMBANMENTS	00	10%	00
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	00	15%	00
IV	SIGNAGE AND ROAD SAFETY	00	10%	00
V	VEGATAION	00	5%	00
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				00
TO BE PAID FOR THE QUARTER / DEMAND (in Lakh) [6]				0.46960

Date of inspection by E/I or his agent

Prepared by Contractor's self Control unit

Rishi Raj (AE)
15/03/22
Name and Designation of person inspecting road

Date 13.03.2022.

Signature of person inspecting road

(Signature)
[Signature]
13/03/22
Certify by E/I [signature] Date:-

Name of work : Construction of Road from House of Bisundeo Bhagat in Sesai
Harijan Tola

Name of customer : M/S Vishvas Infrastructure

(R) Rural Road


Good															Average															Poor														
< 4000															4001 - 5000															> 5000														
Date	Time	Test No	Distance(m)	Total Distance(m)	BUMPI(cm)	Speed(Km/Hr)	Ulimm(Km)	Corrected UI (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks																													
09/03/22	17:28:43	18	100	100	30.0 cm	9.3 Km/Hr	3000.0 mm/Km	3053	4.09	Good	26.4056578	N	84.0978174	E	Normal																													
09/03/22	17:28:57	18	100	200	26.0 cm	27.0 Km/Hr	2600.0 mm/Km	2679	3.64	Good	26.4059992	N	84.0982599	E	Normal																													
09/03/22	17:29:08	18	100	300	32.0 cm	32.7 Km/Hr	3200.0 mm/Km	3241	4.32	Good	26.4056234	N	84.0997095	E	Normal																													
09/03/22	17:29:21	18	100	400	25.0 cm	28.0 Km/Hr	2500.0 mm/Km	2585	3.53	Good	26.4055681	N	84.1005869	E	Normal																													
09/03/22	17:29:32	18	100	500	22.0 cm	33.1 Km/Hr	2200.0 mm/Km	2305	3.18	Good	26.4061041	N	84.1014185	E	Normal																													
09/03/22	17:29:50	18	100	600	39.0 cm	20.8 Km/Hr	3900.0 mm/Km	3896	5.09	Good	26.4068613	N	84.1021357	E	Normal																													
09/03/22	17:30:06	18	100	700	29.0 cm	21.6 Km/Hr	2900.0 mm/Km	2960	3.98	Good	26.4075155	N	84.1027384	E	Normal																													
09/03/22	17:30:20	18	100	800	28.0 cm	25.9 Km/Hr	2800.0 mm/Km	2866	3.87	Good	26.4080133	N	84.1035852	E	Normal																													
09/03/22	17:30:43	18	100	900	35.0 cm	18.0 Km/Hr	3500.0 mm/Km	3521	4.65	Good	26.4086313	N	84.1042948	E	Normal																													
09/03/22	17:31:01	18	100	1000	23.0 cm	19.0 Km/Hr	2300.0 mm/Km	2398	3.3	Good	26.4092092	N	84.1036310	E	Normal																													
09/03/22	17:31:26	18	100	1100	40.0 cm	15.0 Km/Hr	4000.0 mm/Km	3989	5.2	Good	26.4098234	N	84.1027984	E	Normal																													

9/3/22
16/3/22

linked
9/3/22

26/03/22
26/03/22

Machine no: 19193, Road: Construction of Road from House of Bisundeo Bhagat in Sesai Harijan Tola, Sesai Lala Chapar pitch road to Sisra Middle School pitch road via Harijan Tola and house of Chandrabali Nourya, Date: 09

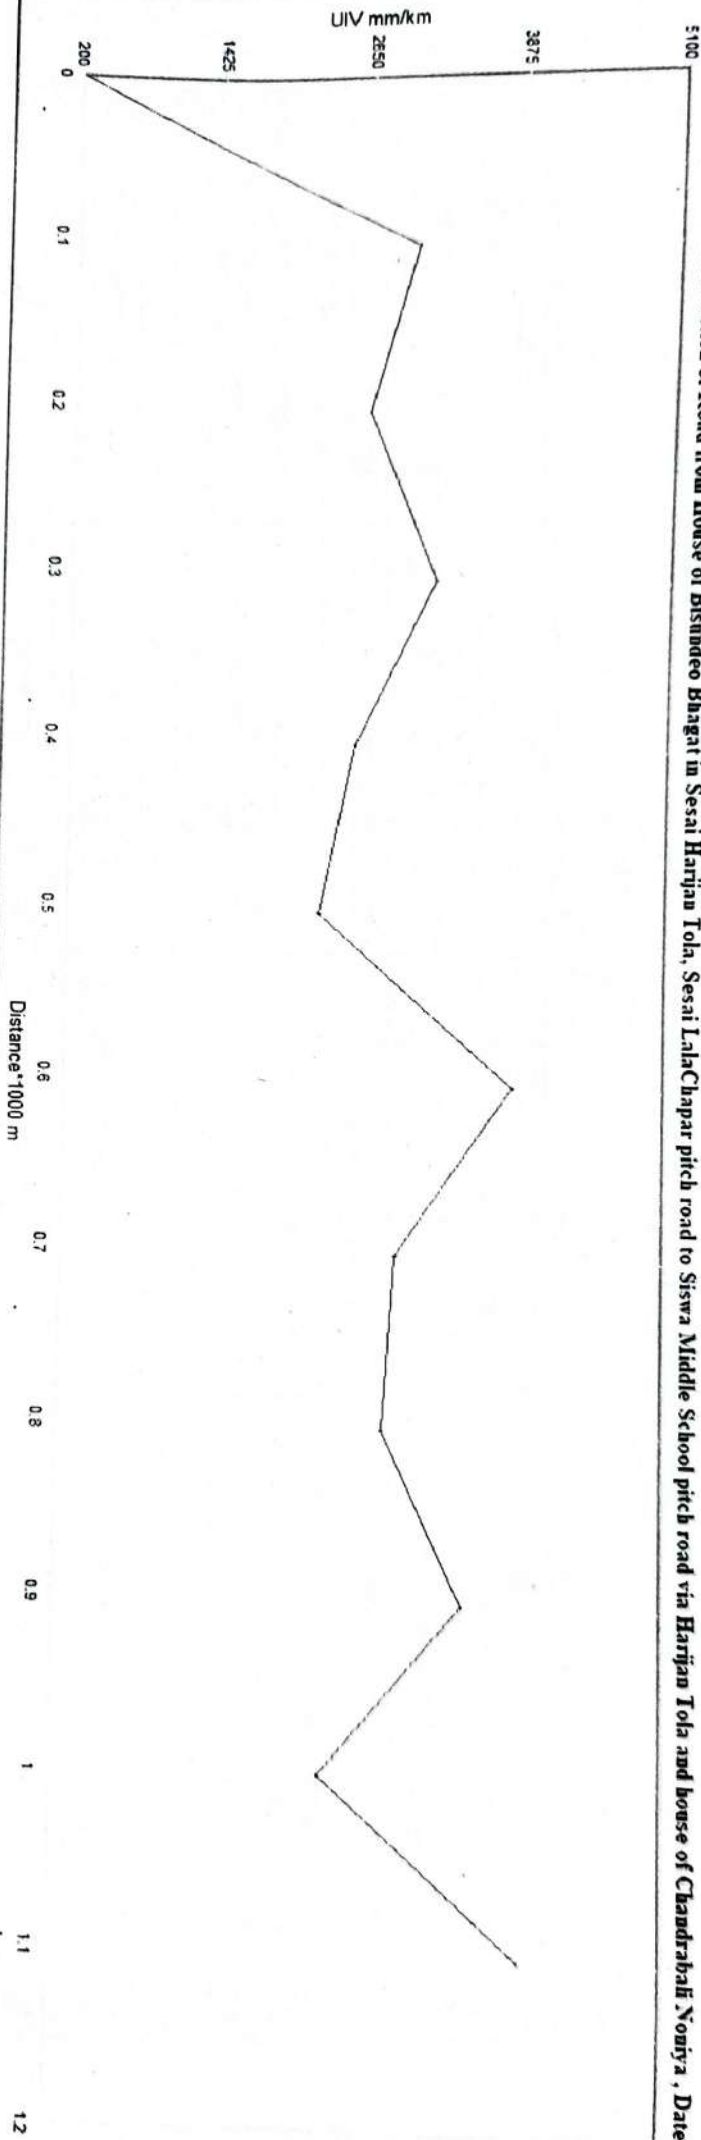

✓
9/13/22

✓
9/13/22
(A/E)

✓
01/03/22
B/B

RWD, Works Division Hathua

Government Of Bihar

OM01

Rural Works Department

Requisition Formet for Scheme Head -MR-(3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

1 Year (1st Quarter)

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From:- Construction of Road from House of Bisundeo Bhagat in Sesai Harijan Tola, Sesai
LalaChapar pitch road to Siswa Middle School pitch road via Harijan Tola and house of Chandrabali
Noniyaa
(Package No.RM/SO/HAT/19/0006)
Length of Road :- 1.1 Km
Inspector :- J.E RWD Sub Division : Bhore

To:-
Executive Engineer
RWD, Works Division Hathua

Date:-

Position :- J.E

No	standard Of Work Item Name	Work Unit	Unit Of Required in each Kilometer										Comments
			1	2	3	4	5	6	7	8	9	10	
OM100	Sealed payment												No Pot Hole Found.
OM101	Pothole Patching	m ²	Nil	Nil	Nil	Nil							Not Surface Depression & Rut Patching Found
OM102	Surface Depression and Rut patching	m ³	Nil	Nil	Nil	Nil							No Crack sealing Found
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil							No Loss Of Aggregates (Surface Ravelling) Found
	Surface Treatment												No Bleeding/ Flushing Required
OM104	(a) Loss of Aggregate (Surface Ravelling)	m ²	Nil	Nil	Nil	Nil							No Crocodile Cracking Found
	(b) Bleeding / Flushing	m ²	Nil	Nil	Nil	Nil							No Edge Repair Required
	(c) Crocodile Cracking	m ²	Nil	Nil	Nil	Nil							
105	Edge Repair	m ²	Nil	Nil	Nil	Nil							
106	Digouts	m ²	N.A	N.A	N.A	N.A							
107	Concrete pavement	m ³	N.A	N.A	N.A	N.A							
	Other activities												
OM200	Shoulder												No Edge Drop-Off Required
	Unsealed Shoulder	Lm	Nil	Nil	Nil	Nil							Not Required
OM201	(a) Edge Drop-off	Lm	Nil	Nil	Nil	Nil							No Holding Water Found
	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil	Nil	Nil							Not Required
	(c) Holding water	Lm	Nil	Nil	Nil	Nil							Not Required
OM202	Embankment Repair	M ³	Nil	Nil	Nil	Nil							Not Required
	Other activities (Rain Cuts)												Not Required
OM300	Drainage including culverts major												Not Required
OM301	Surface Drains & Verge	Lm	N.A	N.A	N.A	N.A							Not Required
OM302	Culvert Cleaning	No	Nil	Nil	Nil	Nil							Not Required
OM303	Culvert and pit Repair	M ³	Nil	Nil	Nil	Nil							Not Required
	Other activities(Whirl washing)	M ²	Nil	Nil	Nil	Nil							

No	standard Of Work Item	Work	Unit Of Required in each Kilometere										Comments
	Name	Unit	1	2	3	4	5	6	7	8	9	10	
OM400	Vegetation												
	Grass Control												
	(a) Roadside- General Tidy	Ha	Nil	Nil	Nil	Nil							Not Required
OM401	(b) Clear near Safety signs, kilometer posts and roadside furniture	Ha	Nil	Nil	Nil	Nil							Not Required
	Tree and Shrub Management	No	Nil	Nil	Nil	Nil							Not Required
OM402	Cutting Of Branches Of Trees	No	Nil	Nil	Nil	Nil							Not Required
	Cutting Of Shrubs From Road Way	No	Nil	Nil	Nil	Nil							Not Required
	Other activities (Trimming of Grass)	M ²	Nil	Nil	Nil	Nil							Not Required
OM500	Safety Signage and Road		Nil										Not Required
OM501	Signs Maintenance	No	Nil	Nil	Nil	Nil							Not Required
OM502	Guard Stones	Lm	N.A	N.A	N.A	N.A							Not Required
OM503	Distance Stones	No	N.A	N.A	N.A	N.A							Not Required
OM504	Road Marking	M ²	Nil	Nil	Nil	Nil							Not Required
	Other activities												

Bidder

Appendix

Executive Engineer, Works Division, **Hathua**

21/11/22

21/11/22

22/11/22
