

कार्यपालक अभियन्ता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमण्डल हथुआ।

पत्रांक:- 498 अनु० / हथुआ।

दिनांक:- 05/05/2022

प्रेषक,

कार्यपालक अभियन्ता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, हथुआ।

सेवा में,

सचिव,
बिहार ग्रामीण पथ विकास अभिकरण,
बिहार पटना।

विषय :- राशि उपलब्ध कराने के संबंध में।

महाशय,

उपरोक्त विषय के संबंध में कहना है कि बिहार ग्रामीण पथ नई अनुरक्षण नीति-2018 के तहत पंचवर्षीय अनुरक्षण अवधि के अधीन पथों में कराये गये त्रैमासिक अनुरक्षण कार्य हेतु राशि की अधियाचना उपलब्ध कराये गये प्रपत्र में सभी सूचनाओं के साथ अंकित कर समर्पित किया जाता है।

अनु०- यथोक्त।

विश्वासभाजन,



कार्यपालक अभियन्ता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, हथुआ।

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

PIU Name : E E RWD WORKS DIVISION - HATHUA

1st Quarter.

1	Name of the Road	SISAI TO BHOPATPUR		
2	Batch No.	AM / 60 / HAT / 19 / 0009		
3	Project ID	31407001011		
	Total Length of Road (in Km)	6.000		
5	Length of Road to Meet Required Service Level [Completed length] (in Km) [1]	6.000		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	52.55805		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	02.62790		
Compliance Criteria	Standard Job Description	Non- Compliance		Reduction Payments [6] = [3] / [1] * [2] * [4]
		Length Non-Compliant [3]	Weighted value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGEWAY)	0 0	60%	0 0
II	SHOULDERS AND EMBANMENTS	0 0	10%	0 0
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0 0	15%	0 0
IV	SIGNAGE AND ROAD SAFETY	0 0	10%	0 0
V	VEGATAION	0 0	5%	0 0
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				00
TO BE PAID FOR THE QUARTER / DEMAND (in Lakh) [6]				02.62790

Date of inspection by E/I or his agent

Prepared by Contractor's self Control unit

Name and Designation of person inspecting road

Rishi Ray (AE)
 11/03/22
 (Signature)

Date 11.03.2022.

Signature of person inspecting road

Certify by E/I [signature] Date: 11/03/22

Name of work		: Sisai to Bhopalpur													
Name of customer		: Awanish Construction													
(R)Rural Road															
Good		Average						Poor							
< 4000		4001 - 5000						> 5000							

Date	Time	Test No	Distance(m)	Total Distance(m)	BUM(cm)	Speed(Km/Hr)	Ultram(Km)	Corrected UI (mm/Km)	RI	Status	Latitude	Direction	Longitude	Direction1	Remarks
09/03/22	13:09:25	11	0	0	0.0 cm	17.1 Km/Hr	0.0 mm/Km	245	0.43	Good	26.4289160	N	84.0828104	E	Normal
09/03/22	13:09:39	11	100	100	23.0 cm	25.4 Km/Hr	2300.0 mm/Km	2398	3.3	Good	26.4289160	N	84.0828104	E	Normal
09/03/22	13:11:52	11	100	200	36.0 cm	13.7 Km/Hr	3600.0 mm/Km	3615	4.76	Good	26.4115438	N	84.1013193	E	Normal
09/03/22	13:12:05	11	100	300	35.0 cm	25.8 Km/Hr	3500.0 mm/Km	3521	4.65	Good	26.4115438	N	84.1013193	E	Normal
09/03/22	13:12:25	11	100	400	36.0 cm	20.3 Km/Hr	3600.0 mm/Km	3615	4.76	Good	26.4115438	N	84.1013193	E	Normal
09/03/22	13:12:42	11	100	500	34.0 cm	20.0 Km/Hr	3400.0 mm/Km	3428	4.54	Good	26.4115438	N	84.1013193	E	Normal
09/03/22	13:12:51	11	100	600	33.0 cm	38.7 Km/Hr	3300.0 mm/Km	3334	4.43	Good	26.4115438	N	84.1013193	E	Normal
09/03/22	13:13:00	11	100	700	18.0 cm	39.2 Km/Hr	1800.0 mm/Km	1930	2.72	Good	26.4115438	N	84.1013193	E	Normal
09/03/22	13:13:11	11	100	800	31.0 cm	34.2 Km/Hr	3100.0 mm/Km	3147	4.2	Good	26.4115438	N	84.1013193	E	Normal
09/03/22	13:13:20	11	100	900	28.0 cm	39.5 Km/Hr	2800.0 mm/Km	2866	3.87	Good	26.4115438	N	84.1013193	E	Normal
09/03/22	13:13:30	11	101	1001	26.0 cm	36.3 Km/Hr	2574.2 mm/Km	2655	3.61	Good	26.4115438	N	84.1013193	E	Normal
09/03/22	13:13:39	11	100	1101	29.0 cm	36.4 Km/Hr	2900.0 mm/Km	2960	3.98	Good	26.4115438	N	84.1013193	E	Normal
09/03/22	13:13:48	11	100	1201	24.0 cm	41.7 Km/Hr	2400.0 mm/Km	2492	3.41	Good	26.4115438	N	84.1013193	E	Normal
09/03/22	13:13:56	11	100	1301	29.0 cm	43.2 Km/Hr	2900.0 mm/Km	2960	3.98	Good	26.4115438	N	84.1013193	E	Normal
09/03/22	13:14:04	11	100	1401	33.0 cm	45.4 Km/Hr	3300.0 mm/Km	3334	4.43	Good	26.4115438	N	84.1013193	E	Normal
09/03/22	13:14:12	11	100	1501	38.0 cm	47.2 Km/Hr	3800.0 mm/Km	3802	4.98	Good	26.4115438	N	84.1013193	E	Normal
09/03/22	13:14:20	11	101	1602	32.0 cm	45.9 Km/Hr	3200.0 mm/Km	3241	4.32	Good	26.4115438	N	84.1013193	E	Normal
09/03/22	13:14:27	11	100	1702	31.0 cm	46.2 Km/Hr	3100.0 mm/Km	3147	4.2	Good	26.4115438	N	84.1013193	E	Normal
09/03/22	13:14:35	11	100	1802	37.0 cm	46.3 Km/Hr	3700.0 mm/Km	3709	4.87	Good	26.4115438	N	84.1013193	E	Normal
09/03/22	13:14:44	11	100	1902	25.0 cm	40.6 Km/Hr	2500.0 mm/Km	2585	3.53	Good	26.4115438	N	84.1013193	E	Normal
09/03/22	13:14:53	11	100	2002	34.0 cm	41.4 Km/Hr	3400.0 mm/Km	3428	4.54	Good	26.4115438	N	84.1013193	E	Normal

Name of work		: Sisal to Bhopalpur													
Name of customer		: Awanish Construction													
(R)Rural Road															
Good		Average		Poor											
< 4000		4001 - 5000		> 5000											
09/03/22	13:15:03	11	100	2102	26.0 cm	36.1 Km/Hr	2600.0 mm/Km	2679	3.64	Good	26.4115438	N	84.1013193	E	Normal
09/03/22	13:15:15	11	100	2202	25.0 cm	30.0 Km/Hr	2500.0 mm/Km	2585	3.53	Good	26.4115438	N	84.1013193	E	Normal
09/03/22	13:15:35	11	100	2302	23.0 cm	18.5 Km/Hr	2300.0 mm/Km	2398	3.3	Good	26.4115438	N	84.1013193	E	Normal
09/03/22	13:15:44	11	100	2402	27.0 cm	35.2 Km/Hr	2700.0 mm/Km	2773	3.75	Good	26.4115438	N	84.1013193	E	Normal
09/03/22	13:15:53	11	100	2502	38.0 cm	41.8 Km/Hr	3800.0 mm/Km	3802	4.98	Good	26.4115438	N	84.1013193	E	Normal
09/03/22	13:16:04	11	100	2602	23.0 cm	33.5 Km/Hr	2300.0 mm/Km	2398	3.3	Good	26.4115438	N	84.1013193	E	Normal
09/03/22	13:16:13	11	100	2702	25.0 cm	36.2 Km/Hr	2500.0 mm/Km	2585	3.53	Good	26.4115438	N	84.1013193	E	Normal
09/03/22	13:16:21	11	100	2802	16.0 cm	44.0 Km/Hr	1600.0 mm/Km	1743	2.48	Good	26.4115438	N	84.1013193	E	Normal
09/03/22	13:16:33	11	100	2902	36.0 cm	35.4 Km/Hr	3600.0 mm/Km	3615	4.76	Good	26.4115438	N	84.1013193	E	Normal
09/03/22	13:16:50	11	100	3002	26.0 cm	19.4 Km/Hr	2600.0 mm/Km	2679	3.64	Good	26.4115438	N	84.1013193	E	Normal
09/03/22	13:17:00	11	100	3102	18.0 cm	37.0 Km/Hr	1800.0 mm/Km	1930	2.72	Good	26.4115438	N	84.1013193	E	Normal
09/03/22	13:17:12	11	100	3202	36.0 cm	29.7 Km/Hr	3600.0 mm/Km	3615	4.76	Good	26.4115438	N	84.1013193	E	Normal
09/03/22	13:17:22	11	100	3302	33.0 cm	37.0 Km/Hr	3300.0 mm/Km	3334	4.43	Good	26.4115438	N	84.1013193	E	Normal
09/03/22	13:17:31	11	100	3402	29.0 cm	37.8 Km/Hr	2900.0 mm/Km	2960	3.98	Good	26.4115438	N	84.1013193	E	Normal
09/03/22	13:17:41	11	100	3502	37.0 cm	37.0 Km/Hr	3700.0 mm/Km	3709	4.87	Good	26.4115438	N	84.1013193	E	Normal
09/03/22	13:17:52	11	100	3602	22.0 cm	37.4 Km/Hr	2200.0 mm/Km	2305	3.18	Good	26.4115438	N	84.1013193	E	Normal
09/03/22	13:18:07	11	100	3702	15.0 cm	22.9 Km/Hr	1500.0 mm/Km	1649	2.36	Good	26.4115438	N	84.1013193	E	Normal
09/03/22	13:18:20	11	100	3802	37.0 cm	27.6 Km/Hr	3700.0 mm/Km	3709	4.87	Good	26.4115438	N	84.1013193	E	Normal
09/03/22	13:18:31	11	100	3902	28.0 cm	30.3 Km/Hr	2800.0 mm/Km	2866	3.87	Good	26.4115438	N	84.1013193	E	Normal
09/03/22	13:18:40	11	100	4002	30.0 cm	38.8 Km/Hr	3000.0 mm/Km	3053	4.09	Good	26.4115438	N	84.1013193	E	Normal
09/03/22	13:18:49	11	101	4103	35.0 cm	42.7 Km/Hr	3500.0 mm/Km	3521	4.65	Good	26.4115438	N	84.1013193	E	Normal
09/03/22	13:18:58	11	100	4203	27.0 cm	40.3 Km/Hr	2700.0 mm/Km	2773	3.75	Good	26.4115438	N	84.1013193	E	Normal


Name of work : Sisai to Bhopalpur															
Name of customer : Awanih Construction															
(R) Rural Road															
Good	Average	Poor													
< 4000	4001 - 5000	> 5000													
09/03/22	13.19.08	11	100	4303	36.0 cm	34.2 Km/Hr	3600.0 mm/Km	3615	4.76	Good	26.4115438	N	84.1013193	E	Normal
09/03/22	13.19.36	11	100	4403	37.0 cm	13.5 Km/Hr	3700.0 mm/Km	3709	4.87	Good	26.4115438	N	84.1013193	E	Normal
09/03/22	13.19.47	11	100	4503	37.0 cm	33.8 Km/Hr	3700.0 mm/Km	3709	4.87	Good	26.4115438	N	84.1013193	E	Normal
09/03/22	13.20.19	11	100	4603	31.0 cm	11.2 Km/Hr	3100.0 mm/Km	3147	4.2	Good	26.4115438	N	84.1013193	E	Normal
09/03/22	13.20.34	11	100	4703	26.0 cm	23.6 Km/Hr	2600.0 mm/Km	2679	3.64	Good	26.4115438	N	84.1013193	E	Normal
09/03/22	13.20.44	11	100	4803	31.0 cm	34.9 Km/Hr	3100.0 mm/Km	3147	4.2	Good	26.4115438	N	84.1013193	E	Normal
09/03/22	13.21.06	11	100	4903	30.0 cm	16.6 Km/Hr	3000.0 mm/Km	3053	4.09	Good	26.4115438	N	84.1013193	E	Normal
09/03/22	13.21.29	11	100	5003	32.0 cm	15.8 Km/Hr	3200.0 mm/Km	3241	4.32	Good	26.4115438	N	84.1013193	E	Normal
09/03/22	13.21.49	11	100	5103	34.0 cm	18.1 Km/Hr	3400.0 mm/Km	3428	4.54	Good	26.4115438	N	84.1013193	E	Normal
09/03/22	13.22.06	11	100	5203	39.0 cm	21.0 Km/Hr	3900.0 mm/Km	3896	5.09	Good	26.4115438	N	84.1013193	E	Normal
09/03/22	13.22.19	11	100	5303	38.0 cm	26.4 Km/Hr	3800.0 mm/Km	3802	4.96	Good	26.4115438	N	84.1013193	E	Normal
09/03/22	13.22.35	11	100	5403	35.0 cm	23.6 Km/Hr	3500.0 mm/Km	3521	4.65	Good	26.4115438	N	84.1013193	E	Normal
09/03/22	13.23.39	11	100	5503	35.0 cm	5.9 Km/Hr	3500.0 mm/Km	3521	4.65	Good	26.4115438	N	84.1013193	E	Normal
09/03/22	13.24.03	11	100	5603	37.0 cm	13.6 Km/Hr	3700.0 mm/Km	3709	4.87	Good	26.4115438	N	84.1013193	E	Normal
09/03/22	13.24.15	11	100	5703	37.0 cm	30.6 Km/Hr	3700.0 mm/Km	3709	4.87	Good	26.3794279	N	84.1253443	E	Normal
09/03/22	13.24.27	11	100	5803	33.0 cm	30.0 Km/Hr	3300.0 mm/Km	3334	4.43	Good	26.3794279	N	84.1253443	E	Normal
09/03/22	13.24.39	11	100	5903	39.0 cm	29.7 Km/Hr	3900.0 mm/Km	3896	5.09	Good	26.3794279	N	84.1253443	E	Normal
09/03/22	13.24.53	11	100	6003	38.0 cm	26.7 Km/Hr	3800.0 mm/Km	3802	4.98	Good	26.3819094	N	84.1264353	E	Normal
09/03/22	13.25.12	11	100	6103	39.0 cm	18.6 Km/Hr	3900.0 mm/Km	3896	5.09	Good	26.3827925	N	84.1264353	E	Normal

Sumit 9/13/22

Pratik 9/13/22 (PR)

Sumit 9/13/22 PR

Name of Customer: Awanish Construction . Machine no: 19193 . Road: Sisai to Bhopapur , Date: 09/03/22 , Section No: 11 , Equation: $Y=0.936X+245.3$

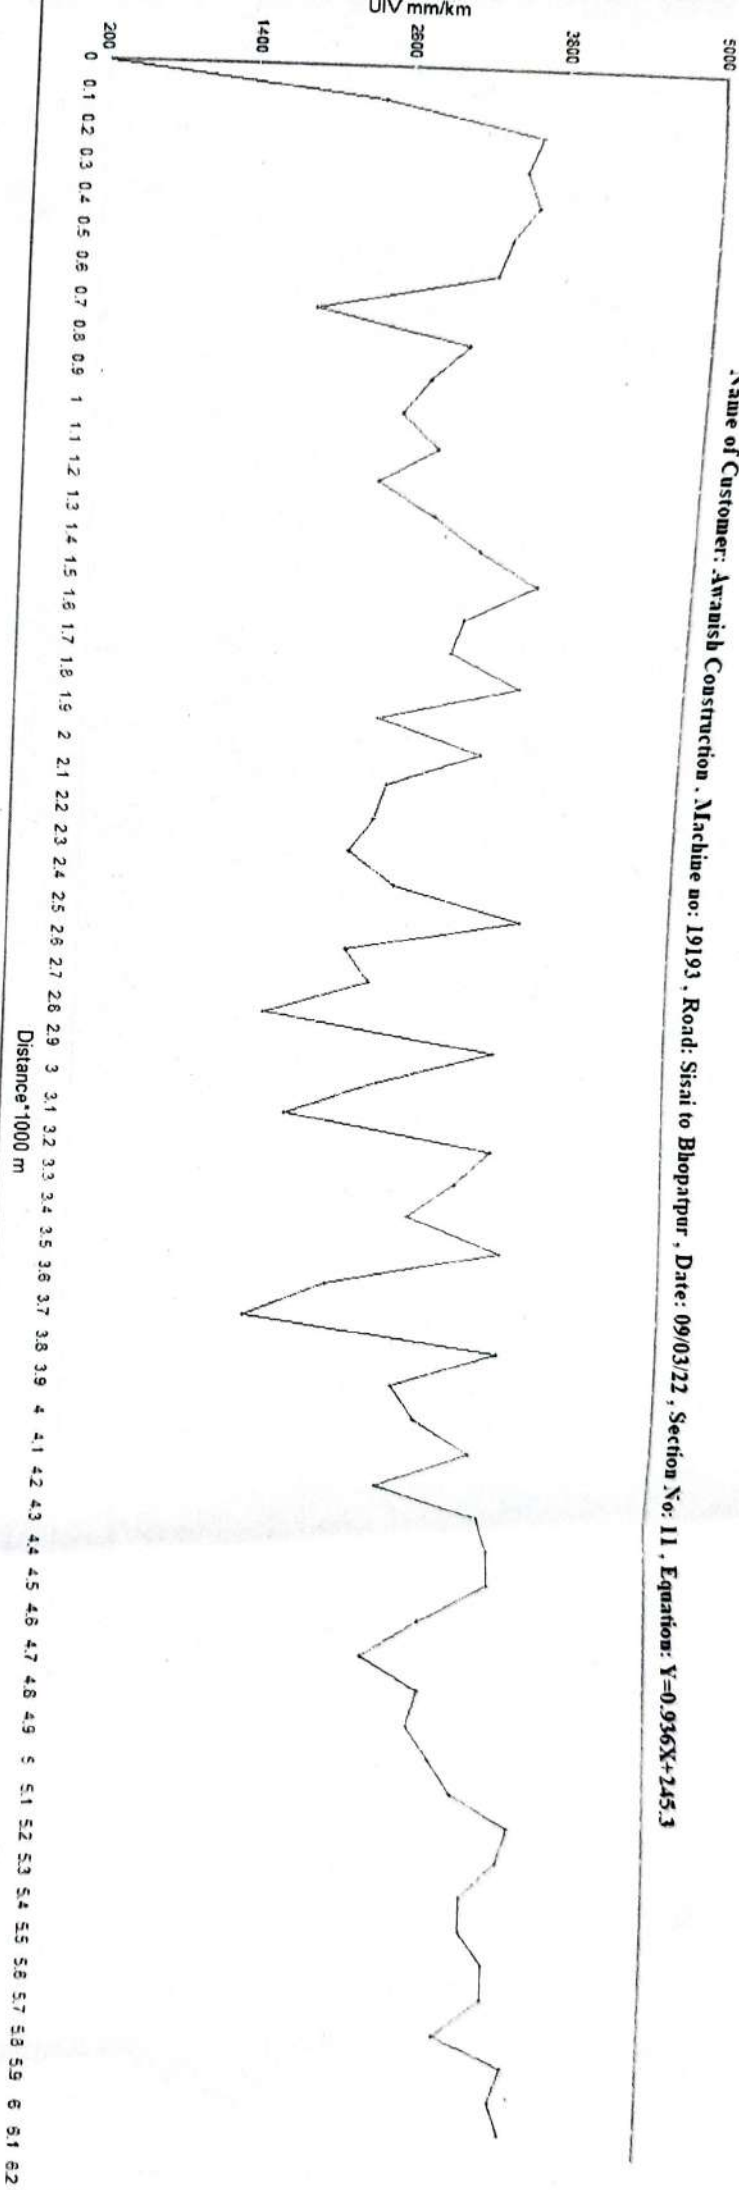

Sub/15/5

Sub/15/5

Sub/15/5

Requisition Formet for Scheme Head-MR-(3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

RWD, Works Division Hathua
Government Of Bihar

1 Year (1st Quarter)

OM01
Rural Works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From:- Sisai to Bhopatpur
(Package No.RM/GO/HAT/19/0009)
Length of Road :- 6.000 Km
Inspector :- J.E RWD Sub Division : Bhore

To:-

Executive Engineer
RWD, Works Division Hathua

Date:-

Position :- J.E

No	Standard Of Work Item Name	Work Unit	Unit Of Required in each Kilometer										Comments
OM100	Sealed payment		1	2	3	4	5	6	7	8	9	10	
OM101	Pothole Patching	m ²	Nil	Nil	Nil	Nil							No Pot Hole Found.
OM102	Surface Depression and Rut patching	m ³	Nil	Nil	Nil	Nil							Not Surface Depression & Rut Patching Found
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil							No Crack sealing Found
	Surface Treatment												
OM104	(a) Loss of Aggregate (Surface Raveling)	m ²	Nil	Nil	Nil	Nil							No Loss Of Aggregates (Surface Raveling) Found
	(b) Bleeding / Flushing	m ²	Nil	Nil	Nil	Nil							No Bleeding/ Flushing Required
	● Crocodile Cracking	m ²	Nil	Nil	Nil	Nil							No Crocodile Cracking Found
105	Edge Repair	m ²	Nil	Nil	Nil	Nil							No Edge Repair Required
106	Digouts	m ²	N.A	N.A	N.A	N.A							
107	Concrete pavement	m ³	N.A	N.A	N.A	N.A							
	Other activities												
OM200	Shoulder												
	Unsealed Shoulder	Lm	Nil	Nil	Nil	Nil							No Edge Drop-Off Required
OM201	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil	Nil	Nil							Not Required
	(c) Holding water	Lm	Nil	Nil	Nil	Nil							No Holding Water Found
OM202	Embankment Repair	M ³	Nil	Nil	Nil	Nil							Not Required
	Other activities (Rain Cuts)		Nil	Nil	Nil	Nil							Not Required
OM300	Drainage including culverts major	Lm	N.A	N.A	N.A	N.A							Not Required
OM301	Surface Drains & Verge	No	Nil	Nil	Nil	Nil							Not Required
OM302	Culvert Cleaning	M ³	Nil	Nil	Nil	Nil							Not Required
OM303	Culvert and pit Repair	M ³	Nil	Nil	Nil	Nil							Not Required
	Other activities(Whitewashing)	M ²	Nil	Nil	Nil	Nil							Not Required

No	Standard Of Work Item Name	Work Unit	Unit Of Required in each Kilometer										Comments
			1	2	3	4	5	6	7	8	9	10	
OM400	Vegetation												
	Grass Control												
	(a) Roadside- General Tidy	Ha	Nil	Nil	Nil	Nil							Not Required
OM401	(b) Clear near Safety signs, kilometer posts and roadside furniture	Ha	Nil	Nil	Nil	Nil							Not Required
	Tree and Shrub Management	No	Nil	Nil	Nil	Nil							Not Required
	Cutting Of Branches Of Trees	No	Nil	Nil	Nil	Nil							Not Required
OM402	Cutting Of Shrubs From Road Way	No	Nil	Nil	Nil	Nil							Not Required
	Other activities (Trimming of Grass)	M ²	Nil	Nil	Nil	Nil							Not Required
OM500	Safety Signage and Road		Nil										Not Required
OM501	Signs Maintenance	No	Nil	Nil	Nil	Nil							Not Required
OM502	Guard Stones	Lm	N.A	N.A	N.A	N.A							Not Required
OM503	Distance Stones	No	N.A	N.A	N.A	N.A							Not Required
OM504	Road Marking	M ²	Nil	Nil	Nil	Nil							Not Required
	Other activities												

26/11/22

26/11/22

26/11/22
