

कार्यपालक अभियन्ता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमण्डल हथुआ।

पत्रांक:- 498 अ० / हथुआ।

दिनांक:- 05/05/2022

प्रेषक,

कार्यपालक अभियन्ता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, हथुआ।

सेवा में,

सचिव,
बिहार ग्रामीण पथ विकास अभिकरण,
बिहार पटना।

विषय :- राशि उपलब्ध कराने के संबंध में।

महाशय,

उपरोक्त विषय के संबंध में कहना है कि बिहार ग्रामीण पथ नई अनुरक्षण नीति-2018 के तहत पंचवर्षीय अनुरक्षण अवधि के अधीन पथों में कराये गये त्रैमासिक अनुरक्षण कार्य हेतु राशि की अधियाचना उपलब्ध कराये गये प्रपत्र में सभी सूचनाओं के साथ अंकित कर समर्पित किया जाता है।

अनु०- यथोक्त।

विश्वासभाजन,



कार्यपालक अभियन्ता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, हथुआ।

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

PIU Name : E E RWD WORKS DIVISION - HATHUA

1st Quarter

1	Name of the Road	EMALIA - BAKHARIA		
2	Batch No.	RM/GD/HAT/19/0009		
3	Project ID	NEA22000607		
	Total Length of Road (in Km)	2.875		
5	Length of Road to Meet Required Service Level [Completed length] (in Km) [1]	2.875		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	27.4191		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	01.3710		
Compliance Criteria	Standard Job Description	Non- Compliance		Reduction Payments [6] = [3] / [1] * [2] * [4]
		Length Non-Compliant [3]	Weighted value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGEWAY)	00	60%	00
II	SHOULDERS AND EMBANMENTS	00	10%	00
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	00	15%	00
IV	SIGNAGE AND ROAD SAFETY	00	10%	00
V	VEGATAION	00	5%	00
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				00
TO HE PAID FOR THE QUARTER / DEMAND (in Lakh) [6]				01.3710

Date of inspection by E/I or his agent

Prepared by Contractor's self Control unit

Name and Designation of person inspecting road

Rishi Raj (AE)
13/03/22
(Signature)

Date 13.03.2022.

Signature of person inspecting road

Certify by E/I [signature] Date: 13/03/22

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From:- Emalla - Bakharra
(Package No.RM/SO/HAT/19/0009
Length of Road :- 2.88 Km
Inspector :- J.E RWD Sub Division : Bhore

To:-
Executive Engineer
RWD, Works Division Hathua
Date:-

Position :- J.E

No	Standard Of Work Item Name	Work Unit	Unit Of Required in each Kilometer										Comments
			1	2	3	4	5	6	7	8	9	10	
OM100	Sealed Payment												Comments
OM101	Pothole Patching	m ²	Nil	Nil	Nil	Nil							No Pot Hole Found.
OM102	Surface Depression and Rut patching	m ³	Nil	Nil	Nil	Nil							Not Surface Depression & Rut Patching Found
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil							No Crack sealing Found
	Surface Treatment												
OM104	(a) Loss of Aggregate (Surface Ravelling)	m ²	Nil	Nil	Nil	Nil							No Loss Of Aggregates (Surface Ravelling) Found
	(b) Bleeding / Flushing	m ²	Nil	Nil	Nil	Nil							No Bleeding/ Flushing Required
	● Crocodile Cracking	m ²	Nil	Nil	Nil	Nil							No Crocodile Cracking Found
105	Edge Repair	m ²	Nil	Nil	Nil	Nil							No Edge Repair Required
106	Digouts	m ²	Nil	Nil	Nil	Nil							
107	Concreate pavement	m ³	N.A	N.A	N.A	N.A							
	Other activities												
OM200	Shoulder												
	Unsealed Shoulder												
OM201	(a) Edge Drop-off	Lm	Nil	Nil	Nil	Nil							No Edge Drop-Off Required
	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil	Nil	Nil							Not Required
	(c) Holding water	Lm	Nil	Nil	Nil	Nil							No Holding Water Found
OM202	Embankment Repair	M ³	Nil	Nil	Nil	Nil							Not Required
	Other activities (Rain Cuts)												Not Required
OM300	Drainage Including culverts major												
OM301	Surface Drains & Verge	Lm	N.A	N.A	N.A	N.A							Not Required
OM302	Culvert Cleaning	No	Nil	Nil	Nil	Nil							Not Required
OM303	Culvert and pit Repair	M ³	Nil	Nil	Nil	Nil							Not Required
	Other activities(Whluw washing)	M ²	Nil	Nil	Nil	Nil							Not Required

No	Standard Of Work Item Name	Work Unit	Unit Of Required in each kilometere										Comments
			1	2	3	4	5	6	7	8	9	10	
OM400	Vegetation												Comments
	Grass Control												
	(a) Roadside- General Tidy	Ha	Nil	Nil	Nil	Nil							Not Required
OM401	(b) Clear near Safety signs, kilometer posts and roadside furniture	Ha	Nil	Nil	Nil	Nil							Not Required
	Tree and Shrub Management	No	Nil	Nil	Nil	Nil							Not Required
	Cutting Of Branches Of Trees	No	Nil	Nil	Nil	Nil							Not Required
OM402	Cutting Of Shrubs From Road Way	No	Nil	Nil	Nil	Nil							Not Required
	Other activities (Trimming of Grass)	M ²	Nil	Nil	Nil	Nil							Not Required
OM500	Safety Signage and Road												Not Required
OM501	Signs Maintenance	No	Nil	Nil	Nil	Nil							Not Required
OM502	Guard Stones	Lm	N.A	N.A	N.A	N.A							Not Required
OM503	Distance Stones	No	N.A	N.A	N.A	N.A							Not Required
OM504	Road Marking	M ²	Nil	Nil	Nil	Nil							Not Required
	Other activities												

Completed
16/11/22

Completed
16/11/22

Completed
16/11/22

Name of work : Emalia - Bakharia

Name of customer : Awanish Construction

(R)Rural Road		
Good	Average	Poor
< 4000	4001 - 5000	> 5000

Date	Time	Test No	Distance(m)	Total Distance(m)	BUMP(cm)	Speed(Km/Hr)	UT(m/Km)	Corrected UT (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks
09/03/22	17:31:31	19	0	0	0.0 cm	15.0 Km/Hr	0.0 mm/Km	245	0.43	Good	26.4066703	N	84.1027536	E	Normal
09/03/22	17:51:46	19	100	100	37.0 cm	9.6 Km/Hr	3700.0 mm/Km	3709	4.87	Good	26.4066079	N	84.1020623	E	Normal
09/03/22	17:52:01	19	100	200	34.0 cm	24.0 Km/Hr	3400.0 mm/Km	3428	4.54	Good	26.4066079	N	84.1020623	E	Normal
09/03/22	17:52:12	19	100	300	38.0 cm	30.9 Km/Hr	3800.0 mm/Km	3802	4.98	Good	26.4066079	N	84.1020623	E	Normal
09/03/22	17:52:22	19	100	400	36.0 cm	35.6 Km/Hr	3600.0 mm/Km	3615	4.76	Good	26.4066079	N	84.1020623	E	Normal
09/03/22	17:52:35	19	100	500	34.0 cm	29.3 Km/Hr	3400.0 mm/Km	3428	4.54	Good	26.4066079	N	84.1020623	E	Normal
09/03/22	17:52:47	19	100	600	36.0 cm	28.5 Km/Hr	3600.0 mm/Km	3615	4.76	Good	26.4066079	N	84.1020623	E	Normal
09/03/22	17:52:57	19	100	700	36.0 cm	36.3 Km/Hr	3600.0 mm/Km	3615	4.76	Good	26.4066079	N	84.1020623	E	Normal
09/03/22	17:53:07	19	100	800	37.0 cm	36.0 Km/Hr	3700.0 mm/Km	3709	4.87	Good	26.4066079	N	84.1020623	E	Normal
09/03/22	17:53:19	19	100	900	36.0 cm	31.2 Km/Hr	3600.0 mm/Km	3615	4.76	Good	26.4066079	N	84.1020623	E	Normal
09/03/22	17:53:29	19	100	1000	30.0 cm	36.7 Km/Hr	3000.0 mm/Km	3053	4.09	Good	26.4066079	N	84.1020623	E	Normal
09/03/22	17:53:37	19	100	1100	30.0 cm	41.8 Km/Hr	3000.0 mm/Km	3053	4.09	Good	26.4066079	N	84.1020623	E	Normal
09/03/22	17:53:46	19	100	1200	35.0 cm	43.2 Km/Hr	3500.0 mm/Km	3521	4.65	Good	26.4066079	N	84.1020623	E	Normal
09/03/22	17:54:06	19	100	1300	38.0 cm	18.3 Km/Hr	3800.0 mm/Km	3802	4.98	Good	26.4066079	N	84.1020623	E	Normal
09/03/22	17:54:19	19	100	1400	34.0 cm	26.7 Km/Hr	3400.0 mm/Km	3428	4.54	Good	26.4066079	N	84.1020623	E	Normal
09/03/22	17:54:32	19	100	1500	35.0 cm	29.4 Km/Hr	3500.0 mm/Km	3521	4.65	Good	26.4066079	N	84.1020623	E	Normal
09/03/22	17:54:46	19	100	1600	37.0 cm	22.7 Km/Hr	3700.0 mm/Km	3709	4.87	Good	26.4066079	N	84.1020623	E	Normal
09/03/22	17:55:07	19	100	1700	30.0 cm	18.1 Km/Hr	3000.0 mm/Km	3053	4.09	Good	26.4066079	N	84.1020623	E	Normal
09/03/22	17:55:34	19	100	1800	30.0 cm	13.7 Km/Hr	3000.0 mm/Km	3053	4.09	Good	26.4066079	N	84.1020623	E	Normal
09/03/22	17:55:53	19	100	1900	34.0 cm	18.3 Km/Hr	3400.0 mm/Km	3428	4.54	Good	26.4066079	N	84.1020623	E	Normal
09/03/22	17:56:09	19	100	2000	39.0 cm	23.4 Km/Hr	3900.0 mm/Km	3966	5.09	Good	26.4066079	N	84.1020623	E	Normal

Name of work : Emalia - Bakhtia

Name of customer : Awanish Construction

(R) Rural Road

Good

Average

Poor

< 4000

4001 - 5000

> 5000


09/03/22	17-56-28	19	100	2100	37.0 cm	17.8 Km/Hr	3700.0 mm/Km	3709	4.87	Good	26.4068079	N	84.1020823	E	Normal
09/03/22	17-56-43	19	100	2200	32.0 cm	24.7 Km/Hr	3200.0 mm/Km	3241	4.32	Good	26.4068079	N	84.1020823	E	Normal
09/03/22	17-56-59	19	100	2300	31.0 cm	22.7 Km/Hr	3100.0 mm/Km	3147	4.2	Good	26.4068079	N	84.1020823	E	Normal
09/03/22	17-57-14	19	100	2400	30.0 cm	23.1 Km/Hr	3000.0 mm/Km	3053	4.09	Good	26.4068079	N	84.1020823	E	Normal
09/03/22	17-57-27	19	100	2500	33.0 cm	27.5 Km/Hr	3300.0 mm/Km	3334	4.43	Good	26.4068079	N	84.1020823	E	Normal
09/03/22	17-57-42	19	100	2600	35.0 cm	24.9 Km/Hr	3500.0 mm/Km	3521	4.65	Good	26.4068079	N	84.1020823	E	Normal
09/03/22	17-58-00	19	100	2700	30.0 cm	18.6 Km/Hr	3000.0 mm/Km	3053	4.09	Good	26.4068079	N	84.1020823	E	Normal
09/03/22	17-58-12	19	100	2800	34.0 cm	29.1 Km/Hr	3400.0 mm/Km	3428	4.54	Good	26.4068079	N	84.1020823	E	Normal
09/03/22	17-58-21	19	100	2900	39.0 cm	39.5 Km/Hr	3900.0 mm/Km	3896	5.09	Good	26.4068079	N	84.1020823	E	Normal

17/5/22

16/5/22

13/5/22

Name of Customer: Awanish Construction, Machine no: 19193, Road: Emalia - Bahkaria, Date: 09/03/22, Section No: 19, Equation: $Y=0.936X+245.3$

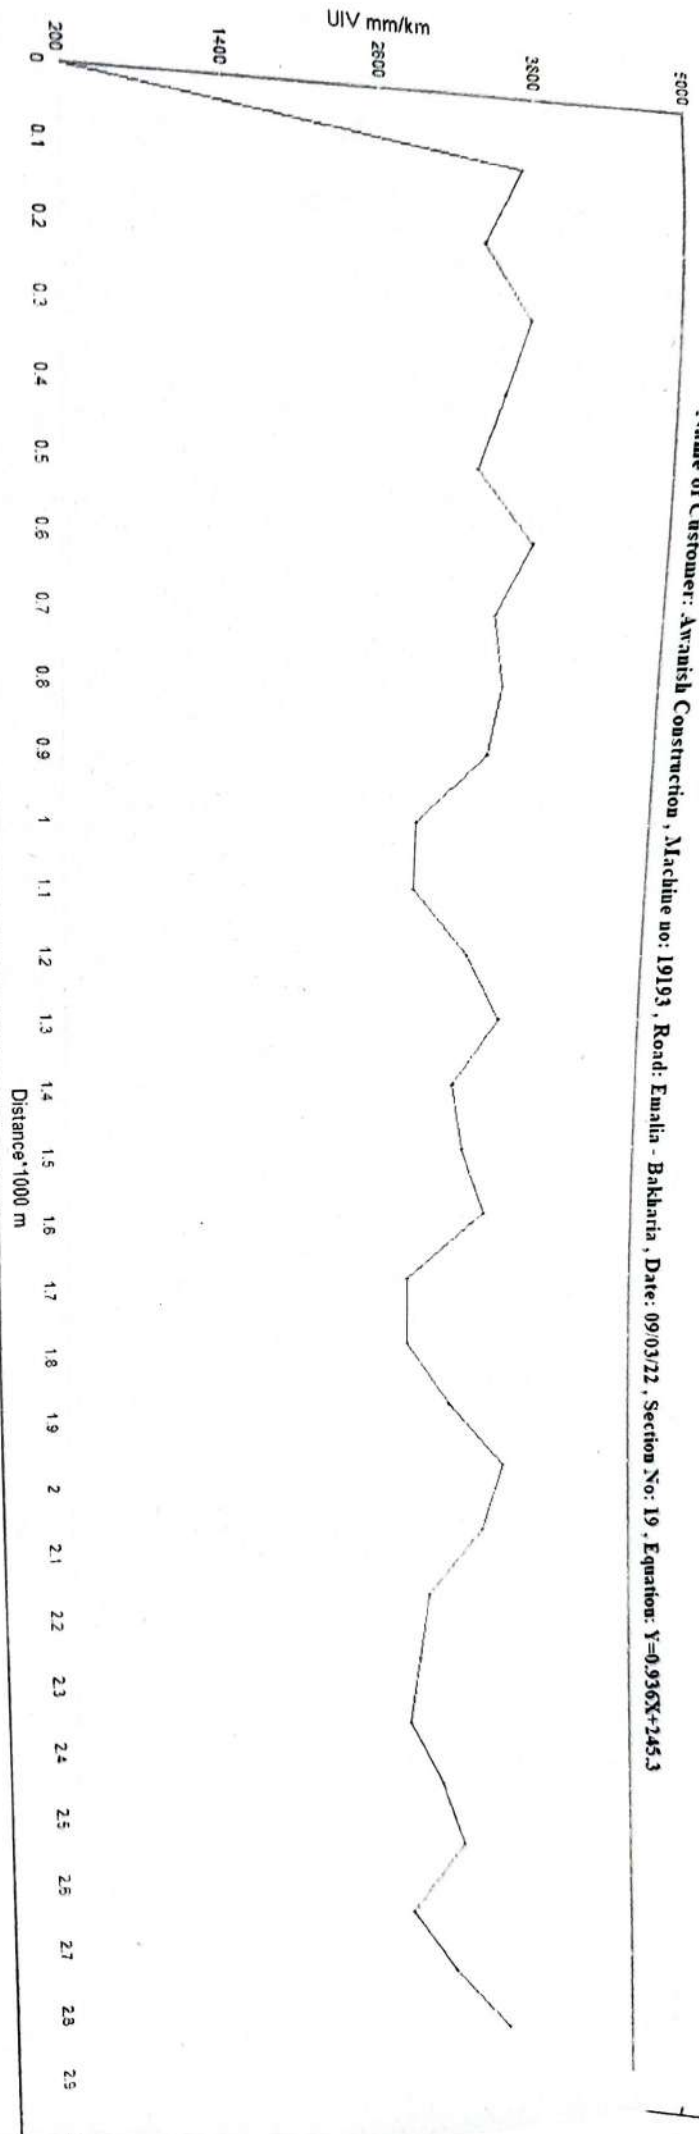

12/6/16

Rishi (K)

12/6/21
