

कार्यपालक अभियन्ता का कार्यालय,

ग्रामीण कार्य विभाग, कार्य प्रमण्डल हथुआ।

संख्या- 498 अह / हथुआ।

दिनांक- 05/05/2022

प्रति,

कार्यपालक अभियन्ता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, हथुआ।

सेवा में,

सचिव,
बिहार ग्रामीण पथ विकास अभिकरण,
बिहार पटना।

विषय - राशि उपलब्ध कराने के संबंध में।

संदर्भ -

उपरोक्त विषय के संबंध में कहना है कि बिहार ग्रामीण पथ नई अनुरक्षण नीति-2018 के तहत पंचवर्षीय अनुरक्षण अवधि के अधीन पथों में कराये गये त्रैमासिक अनुरक्षण कार्य हेतु राशि की अधिव्ययना उपलब्ध कराये गये प्रपत्र में सभी सूचनाओं के साथ अंकित कर समर्पित किया जाता है।

अनु- यथास्त।

विश्वासभाजन,



कार्यपालक अभियन्ता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, हथुआ।

STANDRAD FORMAT FOR ROADS QUARTERLY STATEMENT 1st Quarter
 PIU Name :- Er. Ashok Kumar, EE, RWD Works Division - Hathula

1	Name of the Road	XXX <u>Pieuli to Kailadava</u>		
2	Batch No.	XXX <u>RM/GOI/HAT/19/M12</u>		
3	Project ID	XXX <u>31406901009</u>		
4	Total Length of Road (in Km)	0.00 <u>3.95 KM</u>		
5	Length of Road to Meet Required Service Level [Completed length] (in Km) [1]	* <u>3.95 KM</u>		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	0 <u>34.054 lakh</u>		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	0 <u>1.702 lakh</u>		
Compliance Criteria	Standard Job Description	Non- Compliance		Reduction Payment [6] = [3] / [1] * [2] * [4]
		Length Non- Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGEWAY)	00	60%	0.00
II	SHOULDERS AND EMBANMENTS	00	10%	0.00
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	00	15%	0.00
IV	SIGNAGE AND ROAD SAFETY	00	10%	0.00
V	VEGATAION	00	5%	0.00
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0.00
TO BE PAID FOR THE QUARTER / DEMAND (in Lakh) [6]				0.00 <u>1.702 lakh</u>

Date of inspection by E/I or his agent
 Prepared by Contractor's self Control unit

20/03/2022
 Date

Signature of person inspecting road

20/3/22
 Name and Designation of person inspecting road

20/3/22
 (Signature)

Certify by E/I [signature] Date:-

Name of work		Preuli to Kolladava Road													
Name of customer		Shailcon Construction													
(R) Rural Road															
Good		Average				Poor									
< 4000		4001 - 5000				> 5000									

Date	Time	Test No	Distance(m)	Total Distance(m)	BUM(cm)	Speed(Km/Hr)	U(mm/Km)	Corrected UI (mm/Km)	RI	Status	Latitude	Direction	Longitude	Direction I	Remarks
15/03/22	11:17:49	33	0	0	0.0 cm	30.0 Km/Hr	0.0 mm/Km	245	0.43	Good	26.3635092	N	84.1973658	E	Normal
15/03/22	11:36:54	33	100	100	38.0 cm	11.4 Km/Hr	3800.0 mm/Km	3802	4.98	Good	26.3633556	N	84.1941767	E	Normal
15/03/22	11:37:06	33	100	200	34.0 cm	28.5 Km/Hr	3400.0 mm/Km	3428	4.54	Good	26.3630328	N	84.2153482	E	Normal
15/03/22	11:37:19	33	100	300	33.0 cm	29.0 Km/Hr	3300.0 mm/Km	3334	4.43	Good	26.3630328	N	84.2153482	E	Normal
15/03/22	11:37:32	33	100	400	39.0 cm	28.2 Km/Hr	3900.0 mm/Km	3896	5.09	Good	26.3630328	N	84.2153482	E	Normal
15/03/22	11:37:51	33	100	500	32.0 cm	18.5 Km/Hr	3200.0 mm/Km	3241	4.32	Good	26.3630328	N	84.2153482	E	Normal
15/03/22	11:38:03	33	100	600	36.0 cm	30.9 Km/Hr	3600.0 mm/Km	3615	4.76	Good	26.3630328	N	84.2153482	E	Normal
15/03/22	11:38:13	33	100	700	36.0 cm	36.0 Km/Hr	3600.0 mm/Km	3615	4.76	Good	26.3630328	N	84.2153482	E	Normal
15/03/22	11:38:21	33	100	800	32.0 cm	41.4 Km/Hr	3200.0 mm/Km	3241	4.32	Good	26.3630328	N	84.2153482	E	Normal
15/03/22	11:38:32	33	100	900	38.0 cm	34.9 Km/Hr	3800.0 mm/Km	3802	4.98	Good	26.3630328	N	84.2153482	E	Normal
15/03/22	11:38:42	33	100	1000	34.0 cm	36.0 Km/Hr	3400.0 mm/Km	3428	4.54	Good	26.3630328	N	84.2153482	E	Normal
15/03/22	11:39:26	33	100	1100	37.0 cm	8.6 Km/Hr	3700.0 mm/Km	3709	4.87	Good	26.3687129	N	84.2208338	E	Normal
15/03/22	11:39:47	33	100	1200	30.0 cm	17.0 Km/Hr	3000.0 mm/Km	3053	4.09	Good	26.3693652	N	84.2215052	E	Normal
15/03/22	11:40:03	33	100	1300	36.0 cm	22.7 Km/Hr	3600.0 mm/Km	3615	4.76	Good	26.3698439	N	84.2224283	E	Normal
15/03/22	11:40:21	33	100	1400	31.0 cm	20.0 Km/Hr	3100.0 mm/Km	3147	4.2	Good	26.3903093	N	84.2231455	E	Normal
15/03/22	11:40:37	33	100	1500	34.0 cm	22.0 Km/Hr	3400.0 mm/Km	3428	4.54	Good	26.3909235	N	84.2237787	E	Normal
15/03/22	11:40:50	33	100	1600	34.0 cm	26.4 Km/Hr	3400.0 mm/Km	3428	4.54	Good	26.3916674	N	84.2240915	E	Normal
15/03/22	11:41:02	33	100	1700	39.0 cm	31.2 Km/Hr	3900.0 mm/Km	3896	5.09	Good	26.3926477	N	84.2244120	E	Normal
15/03/22	11:41:12	33	100	1800	37.0 cm	35.6 Km/Hr	3700.0 mm/Km	3709	4.87	Good	26.3932104	N	84.2246103	E	Normal
15/03/22	11:41:22	33	100	1900	35.0 cm	34.5 Km/Hr	3500.0 mm/Km	3521	4.65	Good	26.3942270	N	84.2248850	E	Normal
15/03/22	11:41:43	33	100	2000	31.0 cm	18.8 Km/Hr	3100.0 mm/Km	3147	4.2	Good	26.3955202	N	84.2251673	E	Normal

15/3/22

15/3/22

15/3/22

Name of work : Pieult to Koliadeva Road
 Name of customer : Shailcon Construction


(R) Rural Road		
Good	Average	Poor
< 4000	4001 - 5000	> 5000

15/03/22	11:42:23	33	100	2100	31.0 cm	9.0 Km/Hr	3100.0 mm/Km	3147	4.2	Good	26.3955011	N	84.226158	E	Normal
15/03/22	11:42:44	33	100	2200	30.0 cm	17.2 Km/Hr	3000.0 mm/Km	3053	4.09	Good	26.3949423	N	84.2265635	E	Normal
15/03/22	11:43:17	33	100	2300	33.0 cm	11.1 Km/Hr	3300.0 mm/Km	3334	4.43	Good	26.3945694	N	84.2275995	E	Normal
15/03/22	11:43:28	33	100	2400	36.0 cm	31.6 Km/Hr	3500.0 mm/Km	3621	4.65	Good	26.3943453	N	84.2286158	E	Normal
15/03/22	11:43:38	33	100	2500	38.0 cm	34.2 Km/Hr	3800.0 mm/Km	3802	4.96	Good	26.3943815	N	84.2293634	E	Normal
15/03/22	11:43:56	33	100	2600	35.0 cm	21.8 Km/Hr	3500.0 mm/Km	3621	4.65	Good	26.3943815	N	84.2306689	E	Normal
15/03/22	11:44:06	33	100	2700	33.0 cm	34.2 Km/Hr	3300.0 mm/Km	3334	4.43	Good	26.3942804	N	84.2310877	E	Normal
15/03/22	11:44:15	33	100	2800	34.0 cm	39.9 Km/Hr	3400.0 mm/Km	3428	4.54	Good	26.3938608	N	84.2324381	E	Normal
15/03/22	11:44:24	33	100	2900	36.0 cm	40.0 Km/Hr	3600.0 mm/Km	3615	4.76	Good	26.3936987	N	84.2334452	E	Normal
15/03/22	11:44:33	33	101	3001	36.0 cm	40.6 Km/Hr	3564.3 mm/Km	3581	4.72	Good	26.3938815	N	84.2338037	E	Normal
15/03/22	11:44:43	33	100	3101	34.0 cm	36.3 Km/Hr	3400.0 mm/Km	3428	4.54	Good	26.3931570	N	84.2353830	E	Normal
15/03/22	11:45:01	33	100	3201	30.0 cm	19.8 Km/Hr	3000.0 mm/Km	3053	4.09	Good	26.3928633	N	84.2362299	E	Normal
15/03/22	11:45:10	33	100	3301	34.0 cm	40.5 Km/Hr	3400.0 mm/Km	3428	4.54	Good	26.3928363	N	84.2371454	E	Normal
15/03/22	11:45:19	33	100	3401	32.0 cm	39.5 Km/Hr	3200.0 mm/Km	3241	4.32	Good	26.3924494	N	84.2383127	E	Normal
15/03/22	11:45:41	33	100	3501	39.0 cm	16.0 Km/Hr	3900.0 mm/Km	3896	5.09	Good	26.3921690	N	84.2392893	E	Normal
15/03/22	11:45:51	33	100	3601	37.0 cm	32.0 Km/Hr	3700.0 mm/Km	3709	4.87	Good	26.3919887	N	84.2402811	E	Normal
15/03/22	11:45:59	33	100	3701	30.0 cm	43.2 Km/Hr	3000.0 mm/Km	3053	4.09	Good	26.3919649	N	84.2406397	E	Normal
15/03/22	11:46:09	33	100	3801	33.0 cm	37.4 Km/Hr	3300.0 mm/Km	3334	4.43	Good	26.3919649	N	84.2433634	E	Normal
15/03/22	11:46:40	33	100	3901	25.0 cm	12.4 Km/Hr	2500.0 mm/Km	2585	3.53	Good	26.3913145	N	84.2433634	E	Normal
15/03/22	11:46:50	33	100	4001	25.0 cm	12.6 Km/Hr	2500.0 mm/Km	2585	3.53	Good	26.3913145	N	84.2433634	E	Normal

15/03/22
 15/03/22
 15/03/22

15/03/22
 15/03/22
 15/03/22

Name of Customer: Shankon Construction, Machine no: 19193, Road: Pienh to Kolladeva Road, Date: 15/03/22, Section No: 33, Equation: $Y=0.936X+245.3$

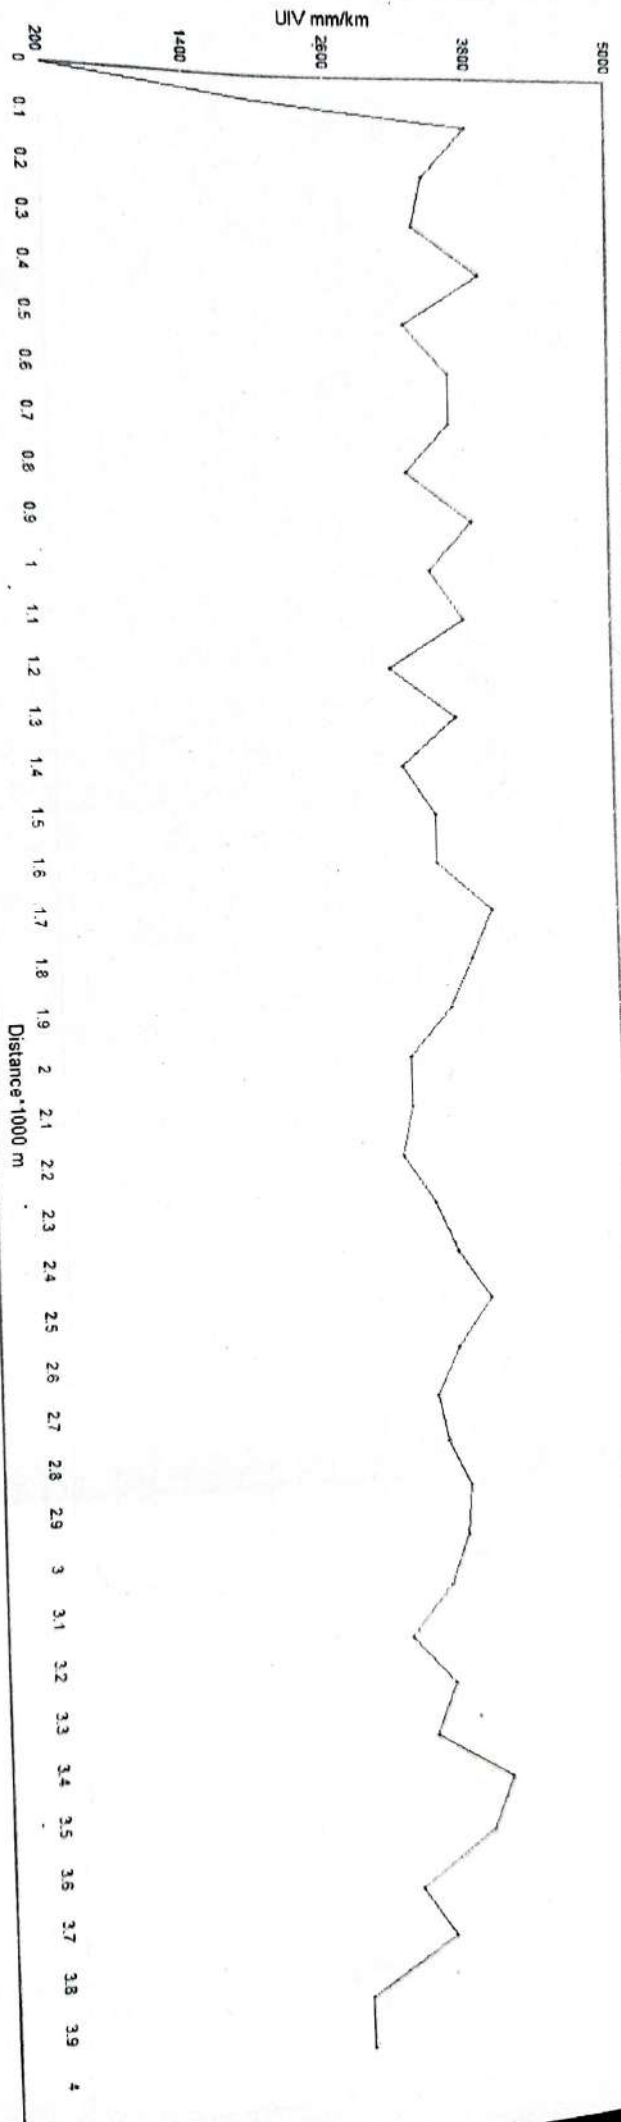

[Signature]
15/3/22
[Signature]

[Signature]
15/3/22
[Signature]

[Signature]
15/3/22
[Signature]

1 Year (1st Quarter)

RWDD, Works Division Hathua

Government Of Bihar

Rural Works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

To:-

Executive Engineer
RWD, Works Division Hathua

Date:

Position :- J.E

Road From:- Pileuli to Koliadeva Road
(Package No.RM/GO/HAT/19/0012)
Length of Road :- 3.95 Km
Inspector :- J.E RWD Sub Division : Hathua

[illegible]

No	standard Of Work Item Name	Work Unit	Unit Of Required in each Kilometere										Comments
OM400	Vegetation	Unit	1	2	3	4	5	6	7	8	9	10	
	Grass Control												
	(a) Roadside- General Tidy	Ha	Nil	Nil	Nil	Nil							Not Required
OM401	(b) Clear near Safety signs, kilometer posts and roadside furniture	Ha	Nil	Nil	Nil	Nil							Not Required
	Tree and Shrub Management	No	Nil	Nil	Nil	Nil							Not Required
	Cutting Of Branches Of Trees	No	Nil	Nil	Nil	Nil							Not Required
OM402	Cutting Of Shrubs From Road Way	No	Nil	Nil	Nil	Nil							Not Required
	Other activities (Trimming of Grass)	M ²	Nil	Nil	Nil	Nil							Not Required
OM500	Safety Signage and Road		Nil										Not Required
OM501	Signs Maintenance	No	Nil	Nil	Nil	Nil							Not Required
OM502	Guard Stones	Lm	N.A	N.A	N.A	N.A							Not Required
OM503	Distance Stones	No	N.A	N.A	N.A	N.A							Not Required
OM504	Road Marking	M ²	Nil	Nil	Nil	Nil							Not Required
	Other activities												


 20/3/22

 20/3/22
 AC


 20/03/22
