

कार्यपालक अभियन्ता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमण्डल हथुआ।

पत्रांक:- 498 अनु० / हथुआ।

दिनांक:- 05/05/2022

प्रेषक,

कार्यपालक अभियन्ता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, हथुआ।

सेवा में,

सचिव,
बिहार ग्रामीण पथ विकास अभिकरण,
बिहार पटना।

विषय :- राशि उपलब्ध कराने के संबंध में।

महाशय,

उपरोक्त विषय के संबंध में कहना है कि बिहार ग्रामीण पथ नई अनुरक्षण नीति-2018 के तहत पंचवर्षीय अनुरक्षण अवधि के अधीन पथों में कराये गये त्रैमासिक अनुरक्षण कार्य हेतु राशि की अधियाचना उपलब्ध कराये गये प्रपत्र में सभी सूचनाओं के साथ अंकित कर समर्पित किया जाता है।

अनु०- यथोक्त।

विश्वासभाजन,



कार्यपालक अभियन्ता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, हथुआ।

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

PIU Name : **EE RND WORKS DIVISION - HATHVA**

1st Quarter

1	Name of the Road	RAMPUR - KARMASI		
2	Batch No.	RM/40/HAT/19/00/1		
3	Project ID	31406902093		
	Total Length of Road (in Km)	3.458		
5	Length of Road to Meet Required Service Level [Completed length] (in Km) [1]	3.458		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	25.55009		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	01.27750		
Compliance Criteria	Standard Job Description	Non- Compliance		Reduction Payments [6] = [3] / [1] * [2] * [4]
		Length Non-Compliant [3]	Weighted value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGEWAY)	00	60%	00
II	SHOULDERS AND EMBANMENTS	00	10%	00
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	00	15%	00
IV	SIGNAGE AND ROAD SAFETY	00	10%	00
V	VEGATAION	00	5%	00
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				00
TO BE PAID FOR THE QUARTER / DEMAND (in Lakh) [6]				01.27750

Date of inspection by E/I or his agent

Prepared by Contractor's self Control unit

Rishi Raj
11/3/22 (AE)

Name and Designation of person inspecting road

11/3/22

Date

(Signature)

Signature of person inspecting road

Certify by E/I [signature] Date: 11/3/22

Name of work : RAMPUR - KARMASI

Name of customer : Gopalganj Construction Private Limited

(R)Rural Road

Good	Average	Poor
< 4000	4001 - 5000	> 5000

Date	Time	Test No	Distance(m)	Total Distance(m)	BUMI(cm)	Speed(Km/Hr)	Ultrasonic(mm/Km)	Corrected UI (mm/Km)	RI	Status	Latitude	Direction	Longitude	Direction1	Remarks
09/03/22	13:25:15	12	0	0	0.0 cm	18.6 Km/Hr	0.0 mm/Km	245	0.43	Good	26.3829794	N	84.1284811	E	Normal
09/03/22	13:46:45	12	100	100	37.0 cm	12.3 Km/Hr	3700.0 mm/Km	3709	4.87	Good	26.4021692	N	84.1188288	E	Normal
09/03/22	13:47:02	12	100	200	22.0 cm	21.2 Km/Hr	2200.0 mm/Km	2305	3.18	Good	26.4027605	N	84.1195002	E	Normal
09/03/22	13:47:15	12	100	300	28.0 cm	26.7 Km/Hr	2800.0 mm/Km	2866	3.87	Good	26.4031591	N	84.1203470	E	Normal
09/03/22	13:47:27	12	100	400	34.0 cm	31.5 Km/Hr	3400.0 mm/Km	3428	4.54	Good	26.4031591	N	84.1203470	E	Normal
09/03/22	13:47:37	12	100	500	38.0 cm	32.7 Km/Hr	3900.0 mm/Km	3896	5.09	Good	26.4044733	N	84.1219688	E	Normal
09/03/22	13:47:47	12	100	600	37.0 cm	37.8 Km/Hr	3700.0 mm/Km	3709	4.87	Good	26.4051161	N	84.1223307	E	Normal
09/03/22	13:47:59	12	100	700	31.0 cm	30.9 Km/Hr	3100.0 mm/Km	3147	4.2	Good	26.4061613	N	84.1230478	E	Normal
09/03/22	13:48:15	12	100	800	23.0 cm	23.8 Km/Hr	2300.0 mm/Km	2388	3.3	Good	26.4064131	N	84.1237802	E	Normal
09/03/22	13:48:32	12	100	900	21.0 cm	20.2 Km/Hr	2100.0 mm/Km	2211	3.07	Good	26.4065733	N	84.1243372	E	Normal
09/03/22	13:48:46	12	100	1000	33.0 cm	26.4 Km/Hr	3300.0 mm/Km	3334	4.43	Good	26.4072065	N	84.1250696	E	Normal
09/03/22	13:48:59	12	100	1100	27.0 cm	28.8 Km/Hr	2700.0 mm/Km	2773	3.75	Good	26.4076376	N	84.1261377	E	Normal
09/03/22	13:49:18	12	100	1200	34.0 cm	18.3 Km/Hr	3400.0 mm/Km	3428	4.54	Good	26.4081354	N	84.1269083	E	Normal
09/03/22	13:49:29	12	100	1300	36.0 cm	32.0 Km/Hr	3600.0 mm/Km	3615	4.76	Good	26.4090548	N	84.1270380	E	Normal
09/03/22	13:49:41	12	100	1400	36.0 cm	30.6 Km/Hr	3600.0 mm/Km	3615	4.76	Good	26.4095793	N	84.1271443	E	Normal
09/03/22	13:49:52	12	100	1500	32.0 cm	33.4 Km/Hr	3200.0 mm/Km	3241	4.32	Good	26.4105310	N	84.1276865	E	Normal
09/03/22	13:50:03	12	100	1600	37.0 cm	32.0 Km/Hr	3700.0 mm/Km	3709	4.87	Good	26.4116507	N	84.1283503	E	Normal
09/03/22	13:50:13	12	100	1700	37.0 cm	33.4 Km/Hr	3700.0 mm/Km	3709	4.87	Good	26.4123011	N	84.1289759	E	Normal
09/03/22	13:50:23	12	100	1800	31.0 cm	39.2 Km/Hr	3100.0 mm/Km	3147	4.2	Good	26.4126768	N	84.1293268	E	Normal
09/03/22	13:50:32	12	100	1900	37.0 cm	36.7 Km/Hr	3700.0 mm/Km	3709	4.87	Good	26.4135962	N	84.1300287	E	Normal
09/03/22	13:50:40	12	100	2000	30.0 cm	44.5 Km/Hr	3000.0 mm/Km	3053	4.09	Good	26.4145479	N	84.1306467	E	Normal

Name of work : RAMPUR - KARMASI

Name of customer : Gopalganj Construction Private Limited

(R)Rural Road

Good	Average	Poor
< 4000	4001 - 5000	> 5000


09/03/22	13:50:48	12	100	2100	30.0 cm	48.5 Km/Hr	3000.0 mm/Km	3053	4.09	Good	26.4150724	N	84.1309595	E	Normal
09/03/22	13:50:56	12	100	2200	29.0 cm	42.3 Km/Hr	2900.0 mm/Km	2960	3.98	Good	26.4161556	N	84.1315470	E	Normal
09/03/22	13:51:05	12	100	2300	38.0 cm	41.4 Km/Hr	3800.0 mm/Km	3802	4.98	Good	26.4170904	N	84.1320810	E	Normal
09/03/22	13:51:15	12	100	2400	37.0 cm	37.8 Km/Hr	3700.0 mm/Km	3709	4.87	Good	26.4179621	N	84.1325541	E	Normal
09/03/22	13:51:43	12	100	2500	30.0 cm	13.3 Km/Hr	3000.0 mm/Km	3053	4.09	Good	26.4186907	N	84.1325235	E	Normal
09/03/22	13:51:59	12	100	2600	32.0 cm	22.0 Km/Hr	3200.0 mm/Km	3241	4.32	Good	26.4192476	N	84.1331568	E	Normal
09/03/22	13:52:19	12	100	2700	31.0 cm	17.1 Km/Hr	3100.0 mm/Km	3147	4.2	Good	26.4199305	N	84.1337748	E	Normal
09/03/22	13:52:33	12	100	2800	33.0 cm	27.0 Km/Hr	3300.0 mm/Km	3334	4.43	Good	26.4203215	N	84.1340189	E	Normal
09/03/22	13:52:47	12	100	2900	31.0 cm	24.4 Km/Hr	3100.0 mm/Km	3147	4.2	Good	26.4203215	N	84.1340189	E	Normal
09/03/22	13:52:58	12	100	3000	37.0 cm	31.2 Km/Hr	3700.0 mm/Km	3709	4.87	Good	26.4203215	N	84.1340189	E	Normal
09/03/22	13:53:11	12	100	3100	33.0 cm	28.5 Km/Hr	3300.0 mm/Km	3334	4.43	Good	26.4203215	N	84.1340189	E	Normal
09/03/22	13:53:26	12	100	3200	37.0 cm	25.4 Km/Hr	3700.0 mm/Km	3709	4.87	Good	26.4203215	N	84.1340189	E	Normal
09/03/22	13:53:55	12	100	3300	34.0 cm	12.6 Km/Hr	3400.0 mm/Km	3428	4.54	Good	26.4203215	N	84.1340189	E	Normal
09/03/22	13:56:42	12	100	3400	31.0 cm	2.1 Km/Hr	3100.0 mm/Km	3147	4.2	Good	26.4203215	N	84.1340189	E	Normal
09/03/22	13:56:59	12	100	3500	31.0 cm	3.1 Km/Hr	3100.0 mm/Km	3147	4.2	Good	26.4203215	N	84.1340189	E	Normal

6/3/22

Pratik

4/3/22

Name of Customer: Gopalraj Construction Private Limited, Machine no: 19193, Road: RAMPUR - KARVASI, Date: 09/03/22, Section No: 12, Equation: $Y=0.936X+245.3$

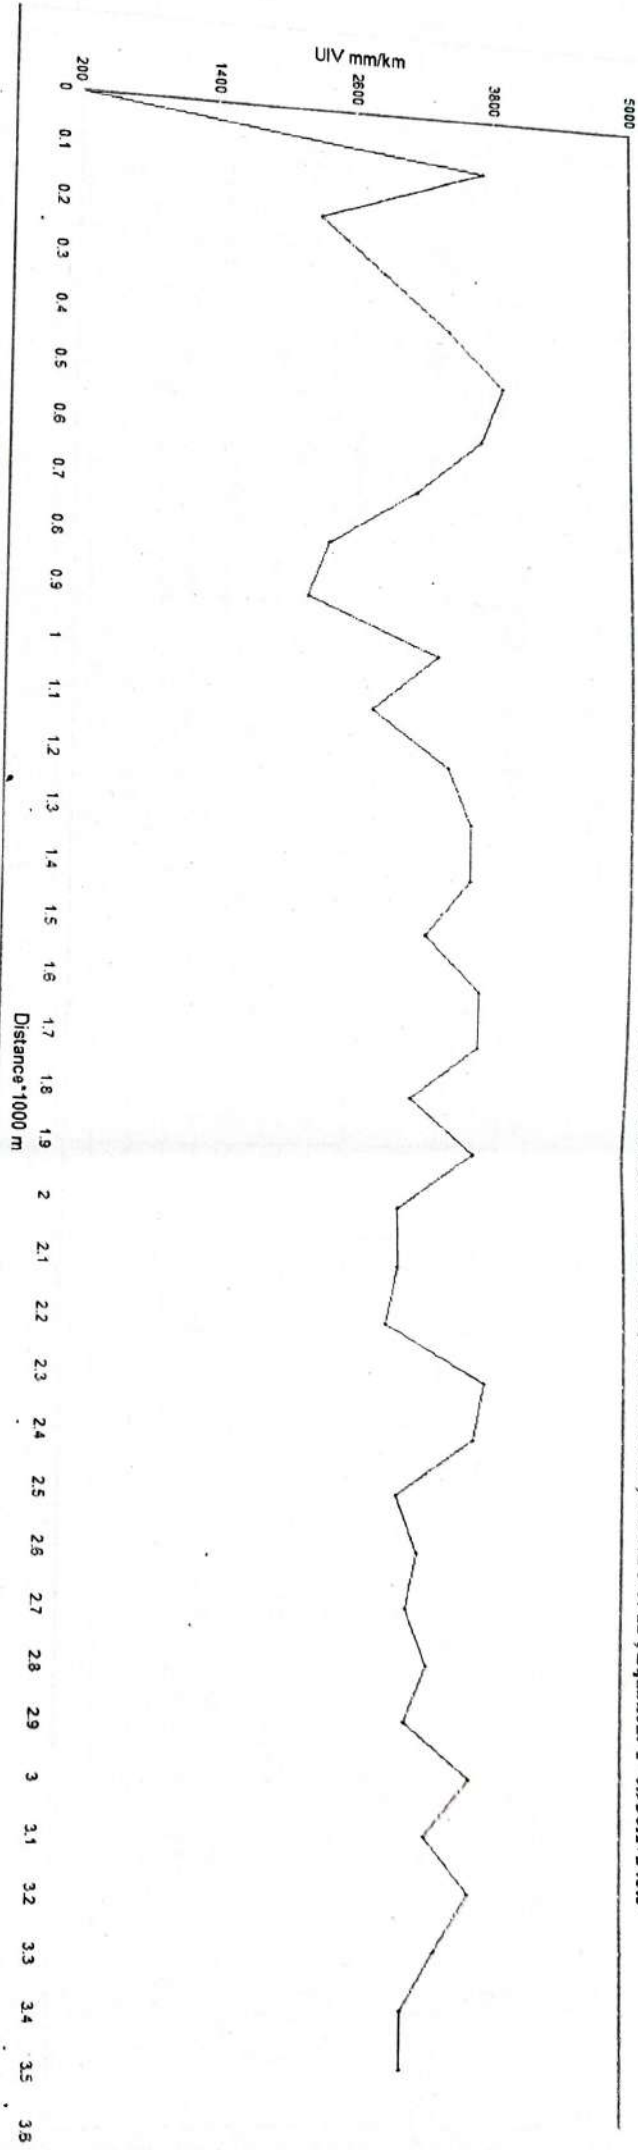

Handwritten signature
09/03/22

Handwritten signature
09/03/22

Handwritten signature
09/03/22

1 Year (1st Quarter)

RWD, Works Division Hathua

Government Of Bihar

Rural Works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

To:-

Executive Engineer
RWD, Works Division Hathua

Date:

Road From:- RAMPUR - KARMAJI
(Package No.RM/GO/HAT/19/0011)

Length of Road :- 3.46 Km

Inspector :- J.E RWD Sub Division : Bhore

Position :- J.E

No	Standard Of Work Item Name	Work Unit	Unit Of Required in each kilometre										Comments
			1	2	3	4	5	6	7	8	9	10	
OM100	Sealed payment	m ²	Nil	Nil	Nil	Nil							No Pot Hole Found.
OM101	Pothole Patching	m ³	Nil	Nil	Nil	Nil							Not Surface Depression & Rut Patching Found
OM102	Surface Depression and Rut patching	Lm	Nil	Nil	Nil	Nil							No Crack sealing Found
OM103	Crack Sealing												
	Surface Treatment	m ²	Nil	Nil	Nil	Nil							No Loss Of Aggregates (Surface Ravelling) Found
OM104	(a) Loss of Aggregate (Surface Ravelling)	m ²	Nil	Nil	Nil	Nil							No Bleeding/ Flushing Required
	(b) Bleeding / Flushing	m ²	Nil	Nil	Nil	Nil							No Crocodile Cracking Found
	© Crocodile Cracking	m ²	Nil	Nil	Nil	Nil							No Edge Repair Required
105	Edge Repair	m ²	Nil	Nil	Nil	Nil							
106	Digouts	m ²	N.A	N.A	N.A	N.A							
107	Concrete pavement	m ³	N.A	N.A	N.A	N.A							
	Other activities												
OM200	Shoulder												No Edge Drop-Off Required
	Unsealed Shoulder												Not Required
OM201	(a) Edge Drop-off	Lm	Nil	Nil	Nil	Nil							No Holding Water Found
	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil	Nil	Nil							Not Required
	(c) Holding water	M ³	Nil	Nil	Nil	Nil							Not Required
OM202	Embankment Repair		Nil	Nil	Nil	Nil							
	Other activities (Rain Cuts)												
OM300	Drainage including culverts major												Not Required
OM301	Surface Drains & Verge	Lm	N.A	N.A	N.A	N.A							Not Required
OM302	Culvert Cleaning	No	Nil	Nil	Nil	Nil							Not Required
OM303	Culvert and pit Repair	M ³	Nil	Nil	Nil	Nil							Not Required
	Other activities(Whilw washing)	M ²	Nil	Nil	Nil	Nil							

No	Standard Of Work Item Name	Work Unit	Unit Of Required in each Kilometer										Comments
			1	2	3	4	5	6	7	8	9	10	
OMA00	Vegetation												Not Required
	Grass Control												Not Required
	(a) Roadside- General Tidy	Ha	Nil	Nil	Nil	Nil	Nil						Not Required
OMA01	(b) Clear near Safety signs, kilometer posts and roadside furniture	Ha	Nil	Nil	Nil	Nil	Nil						Not Required
	Tree and Shrub Management	No	Nil	Nil	Nil	Nil	Nil						Not Required
	Cutting Of Branches Of Trees	No	Nil	Nil	Nil	Nil	Nil						Not Required
	Cutting Of Shrubs From Road Way	No	Nil	Nil	Nil	Nil	Nil						Not Required
OMA02	Other activities (Trimming of Grass)	M ²	Nil	Nil	Nil	Nil	Nil						Not Required
OMA500	Safety Signage and Road												Not Required
OMA501	Signs Maintenance	No	Nil	Nil	Nil	Nil	Nil						Not Required
OMA502	Guard Stones	Lm	N.A	N.A	N.A	N.A	N.A						Not Required
OMA503	Distance Stones	No	N.A	N.A	N.A	N.A	N.A						Not Required
OMA504	Road Marking	M ²	Nil	Nil	Nil	Nil	Nil						Not Required
	Other activities												

28/11/12
B.B.

28/11/12
B.B.

28/11/12
B.B.
