

कार्यपालक अभियन्ता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमण्डल हथुआ।

पत्रांक:- 498 3190 / हथुआ।

दिनांक:- 05/05/2022

प्रेषक,

कार्यपालक अभियन्ता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, हथुआ।

सेवा में,

सचिव,
बिहार ग्रामीण पथ विकास अभिकरण,
बिहार पटना।

विषय :- राशि उपलब्ध कराने के संबंध में।

महाशय,

उपरोक्त विषय के संबंध में कहना है कि बिहार ग्रामीण पथ नई अनुरक्षण नीति-2018 के तहत पंचवर्षीय अनुरक्षण अवधि के अधीन पथों में कराये गये त्रैमासिक अनुरक्षण कार्य हेतु राशि की अधियाचना उपलब्ध कराये गये प्रपत्र में सभी सूचनाओं के साथ अंकित कर समर्पित किया जाता है।

अनु0- यथोक्त।

विश्वासभाजन,



कार्यपालक अभियन्ता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, हथुआ।

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

1st Quarter

PIU Name : E E RWD WORKS DIVISION - HATHUA

1	Name of the Road	Mazirwa khura lo Beragi tala.		
2	Batch No.	RM/CHDHAT/19/0015		
3	Project ID	NEA22000735		
	Total Length of Road (in Km)	5.15 KM		
5	Length of Road to Meet Required Service Level [Completed length] (in Km) [1]	5.15 KM		
6	No. of Total Quarter (ic 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	50.195 lakh		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	2.509 lakh		
Compliance Criteria	Standard Job Description	Non- Compliance		Reduction Payments [6] = [3] / [1] * [2] * [4]
		Length Non-Compliant [3]	Weighted value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGEWAY)	00	60%	
II	SHOULDERS AND EMBANMENTS	00	10%	
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	00	15%	
IV	SIGNAGE AND ROAD SAFETY	00	10%	
V	VEGATAION	00	5%	
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				
TO HE PAID FOR THE QUARTER / DEMAND (in Lakh) [6]				2.509 lakh

Date of inspection by E/I or his agent

Prepared by Contractor's self Control unit

Name and Designation of person inspecting road

Date

Signature of person inspecting road

Certify by E/I [signature] Date:-

Name of work : Majiwakhuud - Baragola

Name of customer : M/S Pawan Construction

(R) Rural Road		
Good	Average	Poor
< 4000	4001 - 5000	> 5000

Date	Time	Test No	Distance(m)	Total Distance(m)	BUMP/cm	Speed(Km/Hr)	Ultimate(Km)	Corrected UI (mm/Km)	RI	Status	Latitude	Direction	Longitude	Direction	Remarks
27/03/22	19:23:45	4	0	0	0.0 cm	17.4 Km/Hr	0.0 mm/Km	245	0.43	Good	26.4096613	N	84.1939072	E	Normal
27/03/22	19:42:18	4	100	100	32.0 cm	7.2 Km/Hr	3200.0 mm/Km	3241	4.32	Good	26.4411802	N	84.1933908	E	Normal
27/03/22	19:42:31	4	100	200	30.0 cm	27.5 Km/Hr	3000.0 mm/Km	3053	4.09	Good	26.4411802	N	84.1933908	E	Normal
27/03/22	19:42:43	4	100	300	36.0 cm	30.6 Km/Hr	3600.0 mm/Km	3615	4.76	Good	26.4411802	N	84.1933908	E	Normal
27/03/22	19:42:56	4	100	400	35.0 cm	27.6 Km/Hr	3500.0 mm/Km	3521	4.65	Good	26.4411802	N	84.1933908	E	Normal
27/03/22	19:43:13	4	100	500	38.0 cm	21.8 Km/Hr	3800.0 mm/Km	3802	4.98	Good	26.4411802	N	84.1933908	E	Normal
27/03/22	19:43:35	4	100	600	36.0 cm	16.3 Km/Hr	3600.0 mm/Km	3615	4.76	Good	26.4411802	N	84.1933908	E	Normal
27/03/22	19:44:05	4	100	700	30.0 cm	11.6 Km/Hr	3000.0 mm/Km	3053	4.09	Good	26.4411802	N	84.1933908	E	Normal
27/03/22	19:44:17	4	100	800	37.0 cm	29.7 Km/Hr	3700.0 mm/Km	3709	4.87	Good	26.4411802	N	84.1933908	E	Normal
27/03/22	19:44:30	4	100	900	35.0 cm	29.1 Km/Hr	3500.0 mm/Km	3521	4.65	Good	26.4411802	N	84.1933908	E	Normal
27/03/22	19:44:43	4	100	1000	32.0 cm	27.7 Km/Hr	3200.0 mm/Km	3241	4.32	Good	26.4411802	N	84.1933908	E	Normal
27/03/22	19:45:25	4	100	1100	36.0 cm	8.2 Km/Hr	3600.0 mm/Km	3615	4.76	Good	26.4411802	N	84.1933908	E	Normal
27/03/22	19:45:40	4	100	1200	37.0 cm	23.4 Km/Hr	3700.0 mm/Km	3709	4.87	Good	26.4411802	N	84.1933908	E	Normal
27/03/22	19:45:56	4	100	1300	30.0 cm	22.9 Km/Hr	3000.0 mm/Km	3053	4.09	Good	26.4411802	N	84.1933908	E	Normal
27/03/22	19:46:23	4	100	1400	32.0 cm	14.1 Km/Hr	3200.0 mm/Km	3241	4.32	Good	26.4411802	N	84.1933908	E	Normal
27/03/22	19:46:42	4	100	1500	38.0 cm	18.4 Km/Hr	3800.0 mm/Km	3802	4.98	Good	26.4411802	N	84.1933908	E	Normal
27/03/22	19:47:00	4	100	1600	31.0 cm	20.8 Km/Hr	3100.0 mm/Km	3147	4.2	Good	26.4411802	N	84.1933908	E	Normal
27/03/22	19:47:23	4	100	1700	37.0 cm	15.7 Km/Hr	3700.0 mm/Km	3709	4.87	Good	26.4411802	N	84.1933908	E	Normal
27/03/22	19:47:48	4	100	1800	31.0 cm	13.8 Km/Hr	3100.0 mm/Km	3147	4.2	Good	26.4411802	N	84.1933908	E	Normal
27/03/22	19:48:07	4	100	1900	30.0 cm	20.0 Km/Hr	3000.0 mm/Km	3053	4.09	Good	26.4411802	N	84.1933908	E	Normal
27/03/22	19:48:26	4	100	2000	32.0 cm	19.4 Km/Hr	3200.0 mm/Km	3241	4.32	Good	26.4411802	N	84.1933908	E	Normal

27/3/22

27/3/22

27/3/22

Name of work : Maljhakhurd - Baragiola

Name of customer : M/S Pawan Construction

(R/Rural Road

Good	Average	Poor
< 4000	4001 - 5000	> 5000

27/03/22	19-48-44	4	100	2100	30.0 cm	19.6 Km/Hr	3000.0 mm/Km	3053	4.09	Good	26.4411802	N	84.1933908	E	Normal
27/03/22	19-49-00	4	100	2200	34.0 cm	21.8 Km/Hr	3400.0 mm/Km	3428	4.54	Good	26.4411802	N	84.1933908	E	Normal
27/03/22	19-49-36	4	100	2300	36.0 cm	10.2 Km/Hr	3600.0 mm/Km	3615	4.76	Good	26.4411802	N	84.1933908	E	Normal
27/03/22	19-49-55	4	100	2400	37.0 cm	18.9 Km/Hr	3700.0 mm/Km	3708	4.87	Good	26.4411802	N	84.1933908	E	Normal
27/03/22	19-50-09	4	100	2500	32.0 cm	24.9 Km/Hr	3200.0 mm/Km	3241	4.32	Good	26.4411802	N	84.1933908	E	Normal
27/03/22	19-50-28	4	100	2600	35.0 cm	19.8 Km/Hr	3500.0 mm/Km	3521	4.65	Good	26.4411802	N	84.1933908	E	Normal
27/03/22	19-50-45	4	100	2700	33.0 cm	20.6 Km/Hr	3300.0 mm/Km	3334	4.43	Good	26.4411802	N	84.1933908	E	Normal
27/03/22	19-51-02	4	100	2800	34.0 cm	20.7 Km/Hr	3400.0 mm/Km	3428	4.54	Good	26.4411802	N	84.1933908	E	Normal
27/03/22	19-51-36	4	100	2900	33.0 cm	11.0 Km/Hr	3300.0 mm/Km	3334	4.43	Good	26.4411802	N	84.1933908	E	Normal
27/03/22	19-51-52	4	100	3000	36.0 cm	22.2 Km/Hr	3600.0 mm/Km	3615	4.76	Good	26.4411802	N	84.1933908	E	Normal
27/03/22	19-52-15	4	100	3100	32.0 cm	15.9 Km/Hr	3200.0 mm/Km	3241	4.32	Good	26.4411802	N	84.1933908	E	Normal
27/03/22	19-52-32	4	100	3200	32.0 cm	20.2 Km/Hr	3200.0 mm/Km	3241	4.32	Good	26.4411802	N	84.1933908	E	Normal
27/03/22	19-52-47	4	100	3300	38.0 cm	24.0 Km/Hr	3600.0 mm/Km	3802	4.98	Good	26.4411802	N	84.1933908	E	Normal
27/03/22	19-52-59	4	100	3400	38.0 cm	30.6 Km/Hr	3800.0 mm/Km	3802	4.98	Good	26.4411802	N	84.1933908	E	Normal
27/03/22	19-53-11	4	100	3500	32.0 cm	30.3 Km/Hr	3200.0 mm/Km	3241	4.32	Good	26.4411802	N	84.1933908	E	Normal
27/03/22	19-53-23	4	100	3600	37.0 cm	29.4 Km/Hr	3700.0 mm/Km	3709	4.87	Good	26.4411802	N	84.1933908	E	Normal
27/03/22	19-53-36	4	100	3700	39.0 cm	25.4 Km/Hr	3900.0 mm/Km	3896	5.09	Good	26.4411802	N	84.1933908	E	Normal
27/03/22	19-54-00	4	100	3800	37.0 cm	16.5 Km/Hr	3700.0 mm/Km	3709	4.87	Good	26.4411802	N	84.1933908	E	Normal
27/03/22	20-01-07	4	100	3900	31.0 cm	0.8 Km/Hr	3100.0 mm/Km	3147	4.2	Good	26.4411802	N	84.1933908	E	Normal
27/03/22	20-01-22	4	100	4000	23.0 cm	23.9 Km/Hr	2300.0 mm/Km	2388	3.3	Good	26.4411802	N	84.1933908	E	Normal
27/03/22	20-01-38	4	100	4100	30.0 cm	22.5 Km/Hr	3000.0 mm/Km	3053	4.09	Good	26.4411802	N	84.1933908	E	Normal
27/03/22	20-02-22	4	100	4200	32.0 cm	8.1 Km/Hr	3200.0 mm/Km	3241	4.32	Good	26.4411802	N	84.1933908	E	Normal

27/3/22
27/3
18

27/3/22
27/3
18


Name of work		: Majhiwathurd - Baragitola													
Name of customer		: M/S Pawan Construction													
(R)Rural Road															
Good		Average				Poor									
< 4000		4001 - 5000				> 5000									
27/03/22	20-02-41	4	100	4300	30.0 cm	19.8 Km/Hr	3000.0 mm/Km	3053	4.09	Good	28.4411802	N	84.1933908	E	Normal
27/03/22	20-03-07	4	100	4400	31.0 cm	13.7 Km/Hr	3100.0 mm/Km	3147	4.2	Good	28.4411802	N	84.1933908	E	Normal
27/03/22	20-03-18	4	100	4500	39.0 cm	31.3 Km/Hr	3900.0 mm/Km	3896	5.09	Good	28.4411802	N	84.1933908	E	Normal
27/03/22	20-03-28	4	100	4600	38.0 cm	37.0 Km/Hr	3800.0 mm/Km	3802	4.98	Good	28.4411802	N	84.1933908	E	Normal
27/03/22	20-03-39	4	100	4700	36.0 cm	33.0 Km/Hr	3600.0 mm/Km	3615	4.76	Good	28.4411802	N	84.1933908	E	Normal
27/03/22	20-03-52	4	100	4800	35.0 cm	27.8 Km/Hr	3500.0 mm/Km	3521	4.65	Good	28.4411802	N	84.1933908	E	Normal
27/03/22	20-04-02	4	100	4900	31.0 cm	34.2 Km/Hr	3100.0 mm/Km	3147	4.2	Good	28.4411802	N	84.1933908	E	Normal
27/03/22	20-04-14	4	100	5000	34.0 cm	31.8 Km/Hr	3400.0 mm/Km	3428	4.54	Good	28.4411802	N	84.1933908	E	Normal
27/03/22	20-04-28	4	100	5100	35.0 cm	26.4 Km/Hr	3500.0 mm/Km	3521	4.65	Good	28.4411802	N	84.1933908	E	Normal
27/03/22	20-04-43	4	100	5200	37.0 cm	24.1 Km/Hr	3700.0 mm/Km	3709	4.87	Good	28.4411802	N	84.1933908	E	Normal

MAJ
27/3/22
6

MAJ
27/3/22
AS

MAJ
27/3/22
AS

Name of Customer: M/S Pawan Construction, Machine no: 19193, Road: Majhrakhard - Baragola, Date: 27/03/22, Section No: 04, Equation: $Y=0.936X+245.3$

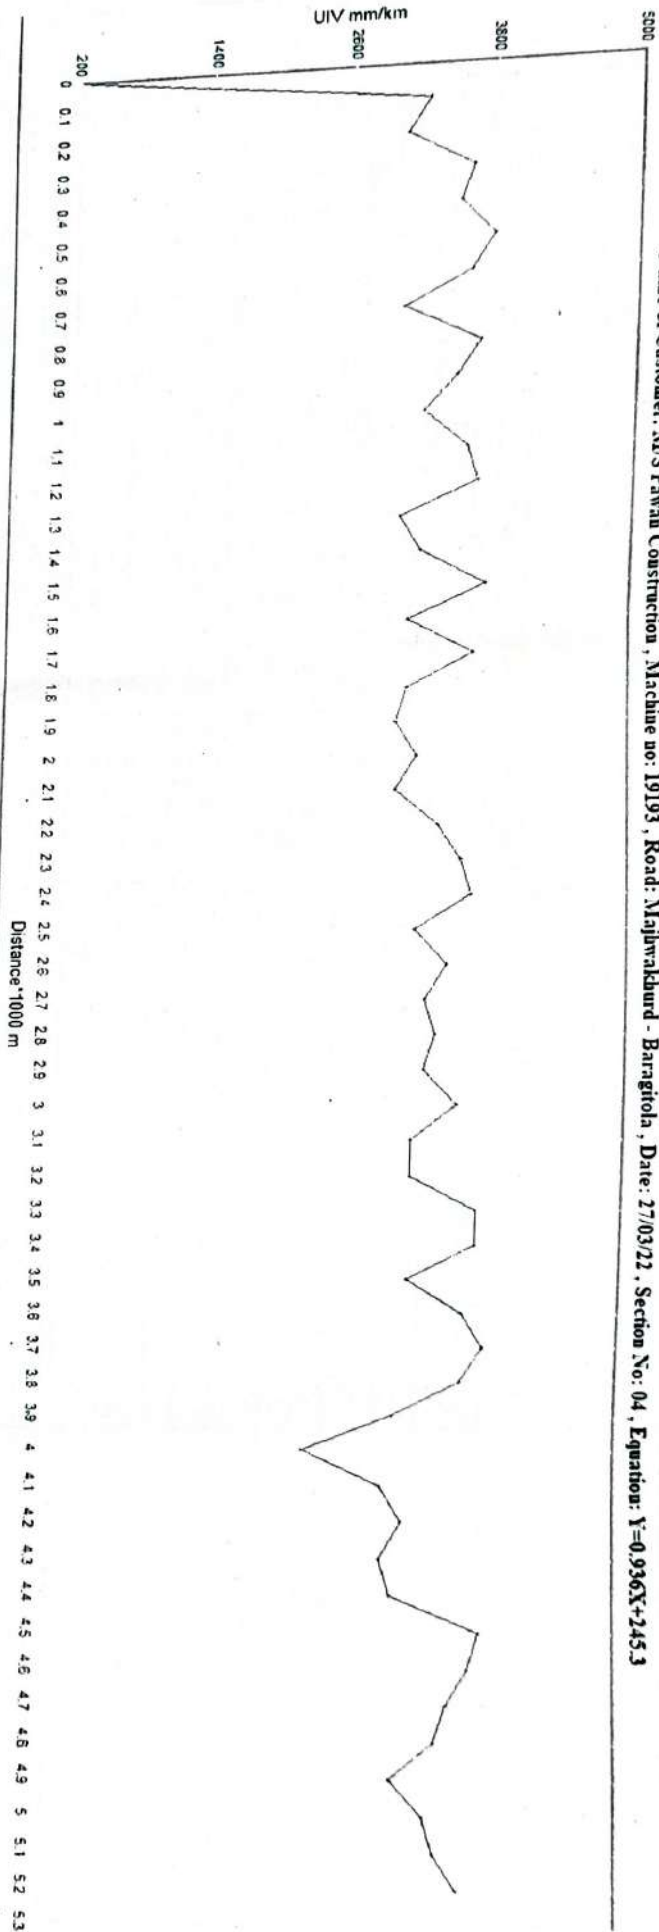

M/S
27/3/22
AB

M/S
27/3/22
AB

26
27/3/22

No	Standard Of Work Item Name	Work Unit	Unit Of Required in each Kilometer										Comments
			1	2	3	4	5	6	7	8	9	10	
OM400	Vegetation												Not Required
	Grass Control												Not Required
OM401	(a) Roadside- General Tidy	Ha	Nil	Nil	Nil	Nil							Not Required
	(b) Clear near Safety signs, kilometer posts and roadside furniture	Ha	Nil	Nil	Nil	Nil							Not Required
OM402	Tree and Shrub Management	No	Nil	Nil	Nil	Nil							Not Required
	Cutting Of Branches Of Trees	No	Nil	Nil	Nil	Nil							Not Required
	Cutting Of Shrubs From Road Way	No	Nil	Nil	Nil	Nil							Not Required
	Other activities (Trimming of Grass)	M ²	Nil	Nil	Nil	Nil							Not Required
OM500	Safety Signage and Road		Nil										Not Required
OM501	Signs Maintenance	No	Nil	Nil	Nil	Nil							Not Required
OM502	Guard Stones	Lm	N/A	N/A	N/A	N/A							Not Required
OM503	Distance Stones	No	N/A	N/A	N/A	N/A							Not Required
OM504	Road Marking	M ²	Nil	Nil	Nil	Nil							Not Required
	Other activities												

Bidder

Appendix

Executive Engineer, Works Division, Mochhari

[Signature]
24/3/22

[Signature]
27/3/22

[Signature]
28/3/22
