

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, सहरसा।

दिनांक- 15/11/2022

पत्रांक- 1614323/सहरसा

प्रेषक:-

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल सहरसा।

सेवा में,

नोडल पदाधिकारी,
MR 3054,
ग्रामीण कार्य विभाग, विहार, पटना।

विषय:-

नई अनुरक्षण नीति 2018 शीर्ष अंतर्गत वित्तीय वर्ष 2020-21 एवं 2021-22 में व्यय हेतु
अनुरक्षण मद में आवंटन की मांग।

महाशय,

उपर्युक्त विषयक नई अनुरक्षण नीति 2018 शीर्ष अंतर्गत वित्तीय वर्ष 2020-21 एवं
2021-22 में व्यय हेतु अनुरक्षण मद में संलग्न विवरणी के अनुसार रुपये 10,04,556.00 (दस लाख चार
हजार पाँच सौ छप्पन रुपये) मात्र का आवंटन उपलब्ध कराने की कृपा की जाय, ताकि किये गये कार्यों
का भुगतान किया जा सके।

अनुलग्नक:- यथोक्त।

विश्वासभाजन

15-11-2022

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमण्डल, सहरसा।

14/11/22

Maintenance Requisition for Scheme Road (NRJCE4) Under Bihar Rural Road Maintenance Policy- 2018

Name of Work Division - Saharsa																																
Road Details				A. A. Details				Agreement Details						Actual Maintenance Expenditure										Current Demand for Maintenance Amount (in Lacs)								
Sl No	Road Name	Batch No	Project ID	Actual Date of Completion	Main work Amount	Maintenance Amount	Main Work Amount	Maintenance of Agreement Amount 1st Year	Agreement 2	Agreement 3	Agreement 4	Agreement 5	Total Maint. Amount	Length	1st Year Maint Exp	2nd Year Maint Exp	3rd Year Maint Exp	4th Year Maint Exp	5th Year Maint Exp	Total Maint Exp	Length as per Bump Report 1st Year	IRI As per Bump Report	1st Quarter	2nd Quarter	3rd Quarter	4th Quarter	5th Quarter	6th Quarter	Total	Remarks		
1	706- Chahla Tola	RM.SA.SA H19/0006	20964302112	28/09/2020	24.18300	16.14300	33.39600	1.54632	2.00826	4.82282	2.46664	5.13528	13.97382	1.470	0	0	0	0	0	0	1.473		0.79669	0.79669	0.79669	0.79669			3.19476			
2	143km - Bhangar	RM.SA.SA H19/0006	20964302119	17/11/2020	27.99400	13.63100	37.18200	1.39353	1.58761	4.12608	2.19548	4.43645	13.74047	1.300	0	0	0	0	0	0	1.300		0.68702	0.68702	0.68702	0.68702			2.71408			
3	X Road L/34 Bhangar Vard	RM.SA.SA H19/0006	20964302137	17/11/2020	54.76000	25.74000	54.52700	2.33620	3.09285	7.84428	3.84091	3.31834	20.51358	2.500	0	0	0	0	0	0	2.500		1.02568	1.02568	1.02568	1.02568			4.10272			
																											10.04256					

Executive Engineer
RWD, Saharsa
15/11/2022

15-11-2022

STANDARD FORMAT FOR QUARTERLY STATEMENT

PIU NAME- RWD, Saharsa 4th Quarter (18-8-21 to 17-11-21)

1	Name of the Road	X Road L034 - Ramnagar Verna		
2	Batch No / Package no	MR-N/19-20 Saharsa/06		
3	Project ID	20904302137		
4	Total Length of Road (in Km)	2.50 Km		
5	Length of Road to Meet Required Service Level [Completed Length] (in KM) [1]	2.50 Km		
6	No of Total Quarter (ie 3 Months as a unit) in 5 years.	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	20.51358 Lakh		
8	Quarterly Payment :1/20 of Ordinary Maintenance Cost as par Schedule (in Lakh) [2]	1.02568 Lakh		
Compliance ceriterla	Standard job Description	Non- Compliance		Reduction Payment [6] = [3] / [1] * [2] * [4]
		Length Non - Compliance [3]	Weighted Value for Payment Reduction (%) [4]	
1	PAVED ROADS (CARRIAGEWAY)	0.00	60%	0.00
2	SHOULDERS AND EMBANMENTS	0.00	10%	0.00
3	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0.00	15%	0.00
4	SIGNAGE AND ROAD SAFETY	0.00	10%	0.00
5	VEGATATION	0.00	5%	0.00
TOTAL PAYMENT REDUCATION FOR THE QUARTER (in Lakh) [5]				0.00
TOTAL PAID FOR THE QUARTER / DEMAND (in Lakh) [6]				1.02568

BUDDHA CONSTRUCTION

[Signature]
PROPRIETOR

Date of inpection by E / I his agent prepared by Contractor's self Control unit

MANOJ SAH
Name and Designation of person inspecting road

[Signature]
Signature of person innspecting road

[Signature]
15-11-2022

Certify by E / I [singnature] Date:-



Government of Bihar
OM01

ORDINARY MAINTENANCE INSPECTION REPORT
Form OM01

Form

Rural Works Department

Road From: X Road to 34 Ramnagar via

Length of Road : 2.50 Km

Period: 4th Quarter (18-08-21 to 17-11-21)

Inspector : J.E., RWD, Sub Division, Nalhabatta

To :

EXECUTIVE ENGINEER,

RWD, Works Division, Saharsa

Position : J.E.

Date:

No.	Name	Work Units	Unit of work required in each kilometre										Comments
			1	2	3	4	5	6	7	8	9	10	
OM100	Sealed Pavement												
OM101	Pothole Patching	m ²	Nil	Nil	Nil								
OM102	Surface Depression and Rut Patching	m ²	Nil	Nil	Nil								
OM103	Crack Sealing	Lm	Nil	Nil	Nil								
OM104	Surface Treatment												
	(a) Loss of Aggregate (Surface Ravelling)	m ²	Nil	Nil	Nil								
	(b) Bleeding/ Flushing	m ²	Nil	Nil	Nil								
	(c) Crocodile Cracking	m ²	Nil	Nil	Nil								
OM105	Edge Repair	m ²	Nil	Nil	Nil								
OM106	Digouts	m ²	N.A.	N.A.	N.A.								
OM107	Concrete Pavement	m ³	N.A.	N.A.	N.A.								
	Other activities												
OM200	Shoulder												
OM201	Unsealed Shoulder												
	(a) Edge Drop-Off	Lm	Nil	Nil	Nil								
	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil	Nil								
	(c) Holding water	Lm	Nil	Nil	Nil								
OM202	Embankment Repair	m ³	Nil	Nil	Nil								
	Other activities												
OM300	Drainage including culverts major and minor bridges												
OM301	Surface Drains & Verges	Lm	N.A.	N.A.	N.A.								
OM302	Culvert Cleaning	No	Nil	Nil	Nil								
OM303	Culvert and Pit Repair	m ³	Nil	Nil	Nil								
	Other activities	m ³	Nil	Nil	Nil								

BUDDHA CONSTRUCTION

Bidder

21/11/21 (16)
PRIETOR

14/11/21
SE

14/11/21
SE

15/11/2022

Executive Engineer, Work Division

Standard work item		Work	Unit of work required in each kilometre										Comments
No.	Name	Units	1	2	3	4	5	6	7	8	9	10	
OM400 Vegetation													
OM401	Grass Control												
	(a) Road side - General Tidy	Ha	Nil	Nil	Nil								Not required.
	(b) Clean near safety signs, kilometre posts and roadside furniture	Ha	Nil	Nil	Nil								Not required.
OM402	Tree and Shrub Management												
	Cutting tree	No.	Nil	Nil	Nil								Not required.
	Cutting Shrubs	No.	Nil	Nil	Nil								Not required.
	Other activities												
OM500 Safety Signage and Road													
OM501	Signs Maintenance	No.	Nil	Nil	Nil								Not required.
OM502	Guard Stones	Lm	N.A	N.A	N.A								Not required.
OM503	Distance Stance	No.	N.A	N.A	N.A								Not required.
OM504	Road Marking	m2	Nil	Nil	Nil								Not required.
	Other activities												

BUDDHA CONSTRUCTION

Signature of Contractor/ Authorized representative
PRIYOTOP

Date

Time

Place **Executive Engineer**

Rural Work Department
Works Division, Saharsa

Signature
14/11/22

Signature
14/11/22

Signature
15-11-2022



Name of work : L034 to Ramnagar Bhama
 Name of customer : Budha Construction

(R) Rural Road		
Good	Average	Poor
< 4000	4001 - 8000	> 8000

Date	Time	Test No	Distance(m)	Total Distance(m)	Bluff(m)	Speed(Km/Hr)	Lat(mm/Km)	Corrected Lat (mm/Km)	RII	Relise	Latitude	Direction	Longitude	Direction1	Remarks
10/11/22	18:58:00	81	100	100	38.0 cm	30.8 Km/Hr	3800.0 mm/Km	3451	4.57	Good	25.9519778	N	86.4983806	E	Drabar
10/11/22	18:58:16	81	100	200	11.0 cm	23.1 Km/Hr	1100.0 mm/Km	1116	1.87	Good	25.9530402	N	86.4981023	E	Normal
10/11/22	18:58:35	81	100	300	12.0 cm	18.2 Km/Hr	1200.0 mm/Km	1200	1.78	Good	25.9531077	N	86.4985361	E	Normal
10/11/22	18:58:57	81	100	400	12.0 cm	17.0 Km/Hr	1200.0 mm/Km	1200	1.78	Good	25.9542246	N	86.4981846	E	Normal
10/11/22	18:59:17	81	100	500	20.0 cm	17.2 Km/Hr	2000.0 mm/Km	1996	2.79	Good	25.9545086	N	86.4989016	E	Normal
10/11/22	18:59:33	81	100	600	14.0 cm	22.0 Km/Hr	1400.0 mm/Km	1396	2.03	Good	25.9547854	N	86.5008036	E	Normal
10/11/22	18:59:54	81	100	700	25.0 cm	17.8 Km/Hr	2500.0 mm/Km	2337	4.45	Good	25.9544491	N	86.5018442	E	Normal
10/11/22	19:00:09	81	100	800	18.0 cm	30.8 Km/Hr	1800.0 mm/Km	1843	2.28	Good	25.9544491	N	86.5015413	E	Drabar
10/11/22	19:00:08	81	100	900	18.0 cm	30.8 Km/Hr	1800.0 mm/Km	1843	2.28	Good	25.9544491	N	86.5015413	E	Normal
10/11/22	19:00:15	81	100	1000	17.0 cm	37.0 Km/Hr	1700.0 mm/Km	1676	2.4	Good	25.9549864	N	86.5015447	E	Normal
10/11/22	19:00:25	81	100	1100	15.0 cm	37.4 Km/Hr	1500.0 mm/Km	1448	2.16	Good	25.9581480	N	86.5014658	E	Normal
10/11/22	19:00:34	81	100	1200	13.0 cm	36.7 Km/Hr	1300.0 mm/Km	1303	1.91	Good	25.9597088	N	86.5014200	E	Normal
10/11/22	19:00:47	81	100	1300	13.0 cm	30.3 Km/Hr	1300.0 mm/Km	1303	1.91	Good	25.9597750	N	86.5013814	E	Normal
10/11/22	19:01:01	81	100	1400	10.0 cm	26.7 Km/Hr	1000.0 mm/Km	1022	1.54	Good	25.9603281	N	86.5017405	E	Normal
10/11/22	19:01:12	81	100	1500	16.0 cm	31.5 Km/Hr	1600.0 mm/Km	1543	2.28	Good	25.9603281	N	86.5017405	E	Normal
10/11/22	19:01:28	81	100	1600	12.0 cm	22.5 Km/Hr	1200.0 mm/Km	1209	1.78	Good	25.9613754	N	86.5034647	E	Normal
10/11/22	19:01:50	81	100	1700	21.0 cm	18.2 Km/Hr	2100.0 mm/Km	2050	2.87	Good	25.9622374	N	86.5034342	E	Normal
10/11/22	19:02:07	81	100	1800	19.0 cm	21.0 Km/Hr	1900.0 mm/Km	1843	2.43	Good	25.9628112	N	86.5028001	E	Normal
10/11/22	19:02:20	81	100	1900	17.0 cm	27.7 Km/Hr	1700.0 mm/Km	1678	2.4	Good	25.9631110	N	86.5020380	E	Drabar
10/11/22	19:02:37	81	100	2000	19.0 cm	22.0 Km/Hr	1900.0 mm/Km	1863	2.03	Good	25.9632750	N	86.5007029	E	Normal

14/11/22


14/11/22 A.E.

15/11/2022

Executive Engineer
 Survey Work Department
 Roads Division, Saharsa

ActiveX Control

Instruction , Machine no: 19215 , Road: L034 to Ramnagar Bhama , Date: 12/11/22 , Section No: 61 , Equation: Y=

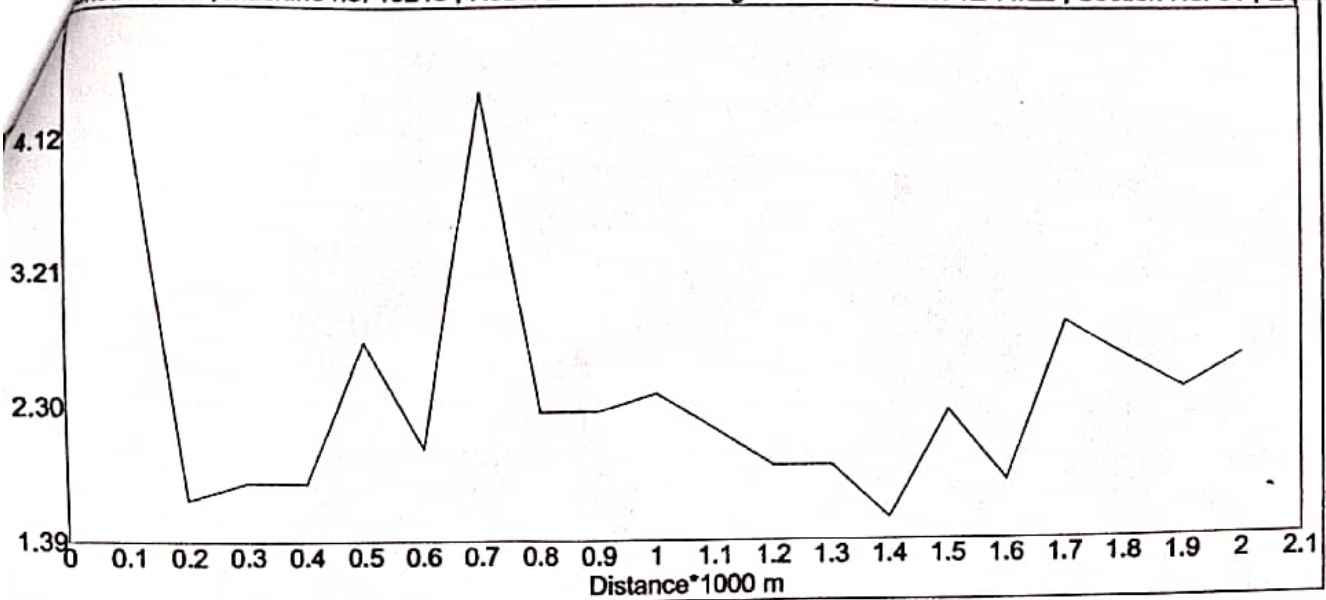

14/11/22

14/11/22
A.E.

15-11-2022

Executive Engineer,
Rural Work Department
Works Division, Saharsa
