

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल, रक्सौल।

पत्रांक :- 1377

रक्सौल, / दिनांक :- 10/11/2022

प्रेषक :-

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, रक्सौल।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव,
बिहार ग्रामीण पथ विकास अभिकरण,
ग्रामीण कार्य विभाग, बिहार, पटना।

विषय :- बिहार ग्रामीण पथ अनुरक्षण नीति-2018 अन्तर्गत पॉच वर्षीय रूटीन अनुरक्षण कार्य मद
योजना अन्तर्गत आवंटन निर्गत करने हेतु अधियाचना के संबंध में।


महाशय,

उपर्युक्त विषयक बिहार ग्रामीण पथ अनुरक्षण नीति-2018 अन्तर्गत पॉच वर्षीय रूटीन अनुरक्षण
कार्य मद में संलग्न सूची के अनुसार आवंटन अधियाचना संबंधित प्रपत्र में भरकर आवश्यक कार्रवाई हेतु
समर्पित किया जाता है।

अनुलग्नक :- संलग्न सूची

1. पथों का आवंटन अधियाचना प्रपत्र।
2. Bump Integrator Report

विश्वासभाजन,



कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, रक्सौल।

Standard Format For Roads Quarterly Statement (1st Quarter)

PIU Name:- Rural Works Department, (Works) Division, Raxaul

1	Name of the Road	PWD Road at Matter chowk to Ekdari		
2	Batch No.	RM/EA/RAX/20/0003		
3	Project ID	317851032016		
4	Total Length of Road (In Km)	2.460		
5	Length of Road to Meet Required Service Level [Completed Length] (In Km) [1]	2.460		
6	No. of Total Quarter (i.e. 3 Months as a unit) in 5 Years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	25.37684		
8	Quarterly Payment: 1/20 of ordinary Maintenance Cost as per Schedule (in Lakh) [2]	1.26884		
Compliance Criteria	Standard Job Description	Non Compliance		
		Length Non Compliant [3]	Weighted Value for Payment Reduction (%) [4]	Reduction Payment [6] = [3]/[1]*[2]*[4]
I	Paved Roads (Carriageway)	0	60%	0.00000
II	Shoulders and Embanments	0	10%	0.00000
III	Cross Drainage Including Culverts and Bridge	0	15%	0.00000
IV	Signage and Road Safety	0	10%	0.00000
V	Vegataion	1	5%	0.02579
Total Payment Reduction For the Quarterly (In Lakh) [5]				0.02579
To be Paid for the Quarter / Demand (In Lakh) [6]				1.24305

Date of Inspection by E/I or his agent 05/11/22

Prepared by Contractor's self Control Unit

Shyam Sundar Rai
Name and Designation of person inspecting road

Date: 05-11-2022
Signature of person inspecting road

05/11/22
(Signature)
Certified by E/I [Signature] Date

Rural Works Department, Works Division, Raxaul
Government of Bihar
OM01Q

1st Quarter
Summary of Ordinary Maintenance Inspection Report

Rural Works Department
Road From: PWD Road at Matter Chowk To: Ekdari
(Package No. RM/EA/RAX/20/0003)
Length of Road: 2.46 Km

Period: From 17.06.2021 to 16.09.2021

Inspector: A.E., RWD, Works Sub Division, Chhauradano

Position: Good


Date: 05/11/22

Standard Work Item		Work	Unit of work required in each Kilometre										Comments
No	Name	Units	1	2	3	4	5	6	7	8	9	10	
OM100 Sealed Pavement													
OM101	Pothole Patching	m ²	Nil	Nil	Nil								No Pot Hole Found
OM102	Surface Depression and Rut Patching	m ²	Nil	Nil	Nil								No Surface Depression and Rut Patching Found
OM103	Crack Sealing	Lm	Nil	Nil	Nil								No Crack Sealing Found
OM104	Surface Treatment												
	(a) Loss of Aggregate (Surface Ravelling)	m ²	Nil	Nil	Nil								No Loss of Aggregate (Surface Ravelling) Found
	(b) Bleeding / Flushing	m ²	Nil	Nil	Nil								No Bleeding / Flushing Required
	(c) Crocodile Cracking	m ²	Nil	Nil	Nil								No Crocodile Cracking Found
OM105	Edge Repair	m ²	Nil	Nil	Nil								No Edge Repair Required
OM106	Digouts	m ²	NA	NA	NA								
OM107	Concrete Pavement	m ³	NA	NA	NA								
	Other activities												
OM200 Shoulder													
	Unsealed Shoulder												
	(a) Edge Drop-off	Lm	Nil	Nil	Nil								No Edge Drop-off Required
OM201	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil	Nil								Not Required
	(c) Holding Water	Lm	Nil	Nil	Nil								No Holding Water Found
OM202	Embankment Repair	m ³	Nil	Nil	Nil								Not Required
	Other activities												

Standard Work Item		Work	Unit of work required in each Kilometre										Comments
No	Name	Units	1	2	3	4	5	6	7	8	9	10	
OM300 Drainage including culverts major and minor bridges													
OM301	Surface Drains & Verge	Lm	NA	NA	NA								Not Required
OM302	Culvert Cleaning	Lm	Nil	Nil	Nil								Not Required
OM303	Culvert and Pit Repair	m ³	Nil	Nil	Nil								Not Required
	Other activities												Not Required
OM400 Vegetation													
Grass Control													Not Required
OM401	(a) Roadside General Tidy	Ha	Nil	Nil	Nil								Not Required
	(b) Clear near safety signs, kilometer posts and roadside furniture	Ha	Nil	Nil	Nil								Not Required
OM402	Tree and Shrub Management	Ha	Nil	Nil	Nil								Not Required
	Other activities												
OM500 Signage and Road Safety													
OM501	Signs Maintenance	No	Nil	Nil	Nil								Not Required
OM502	Guard stones	Lm	NA	NA	NA								Not Required
OM503	Distance Stones	No	NA	NA	NA								Not Required
OM504	Road Markings	No	Nil	Nil	Nil								Not Required
	Other activities												


Bidder


Appendix


Executive Engineer,
RWD, Works Division, Raxaul

Name of Customer : Barhonia Engicon pvt. Ltd.
 Name of Work/Road : PWD Madar Chauk To Ekdhan
 Lab Job number :
 Date : 27-08-2022
 Section No. : 4


Test Date : 27-08-2022 Road Name : PWD Madar Chauk To Ekdhan
 Machine No : 378 Road Type : (R) RURAL ROAD
 Start S No : Side :
 Start E No : Interval
 Weather : N UV Range : 706 To 5000 mm/km
 Start Location : PWD Madar C Dist Range : 0 To 2.6 0.1 1000 m
 End Location : Ekdhan Equation : $Y=0 \cdot X^2 + 0.998 \cdot X + 109.5$

Print Generate Report and Graph

Redraw Graph

Map View

File C:\Users\RWD-ATM\Desktop\Bump Mothani\Barauniya Engicon\PWD Madar Chauk To
 Name of Customer : Barhonia Engicon pvt. Ltd. Name of Work/Road : PWD Madar Chauk To Ekdhan, Lab Job

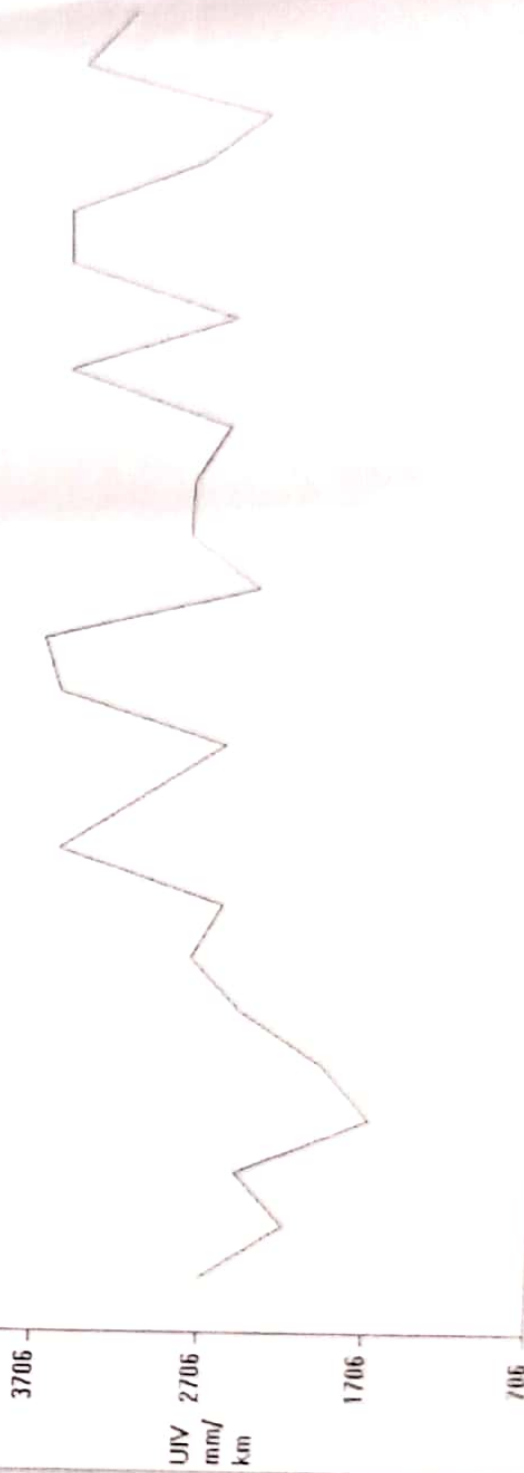

0 01 02 03 04 05 06 07 08 09 1 11 12 13 14 15 16 17 18 19 20 21 22 23 24 25

Distance : 1000 m

27-08-2022
 05-11-2022
 J.F.

DEEPA
 05/11/22

Road Name:-PWD Madar Chauk To Ekdhari
Contractor Name:-Barhonia Engicon pvt. Ltd


Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI,TEGORY mm/km	Latitude ongitude	Event
27/8/22	12:2:0	4	0.1	260	0	2600	2704 G	26.8402	84.99938 Normal
27/8/22	12:2:0	4	0.1	210	30.3	2100	2205 G	26.84001	85.353 Normal
27/8/22	12:2:30	4	0.1	240	30.3	2400	2504 G	26.83991	85.138 Normal
27/8/22	12:2:30	4	0.1	160	30.3	1600	1706 G	26.83978	85.234 Normal
27/8/22	12:2:30	4	0.1	190	40.4	1900	2005 G	26.83961	85.322 Normal
27/8/22	12:3:5	4	0.1	240	30.3	2400	2504 G	26.83941	85.428 Normal
27/8/22	12:3:5	4	0.1	270	20.2	2700	2804 G	26.83919	85.531.8 Curve
27/8/22	12:3:5	4	0.1	250	20.2	2500	2604 G	26.83994	85.552.2 Normal
27/8/22	12:3:40	4	0.1	350	10.1	3500	3602 G	26.84082	85.5605 Normal
27/8/22	12:4:0	4	0.1	300	20.2	3000	3103 G	26.84178	85.569 Normal
27/8/22	12:4:14	4	0.1	250	20.2	2500	2604 G	26.84262	85.574 Normal
27/8/22	12:4:14	4	0.1	350	10.1	3500	3602 G	26.84354	85.5638 Normal
27/8/22	12:5:0	4	0.1	360	10.1	3600	3702 G	26.84441	85.5437 Normal
27/8/22	12:5:0	4	0.1	230	20.2	2300	2404 G	26.84527	85.5403 Normal
27/8/22	12:5:25	4	0.1	270	10.1	2700	2804 G	26.84565	85.5958 Normal
27/8/22	12:6:0	4	0.1	270	20.2	2700	2804 G	26.84564	85.6902 Normal
27/8/22	12:6:36	4	0.1	250	20.2	2500	2604 G	26.84556	85.7928 Normal
27/8/22	12:7:11	4	0.1	350	10.1	3500	3602 G	26.84544	85.8888 Normal
27/8/22	12:7:11	4	0.1	250	20.2	2500	2604 G	26.84551	85.9865 Normal
27/8/22	12:8:21	4	0.1	350	10.1	3500	3602 G	26.84579	85.10655 Normal
27/8/22	12:8:21	4	0.1	350	20.2	3500	3602 G	26.84579	85.11648 Normal
27/8/22	12:9:0	4	0.1	270	20.2	2700	2804 G	26.8461	85.12525 Normal
27/8/22	12:9:0	4	0.1	230	20.2	2300	2404 G	26.84664	85.13182 Normal
27/8/22	12:9:32	4	0.1	340	10.1	3400	3502 G	26.84687	85.13972 Normal
27/8/22	12:10:7	4	0.087	270	10.1	3103	3206 G	26.84769	85.14175 Normal

Total IRI	71591
Average IRI	2863.64

27/8/22
65-11-2022
7.5

27/8/22



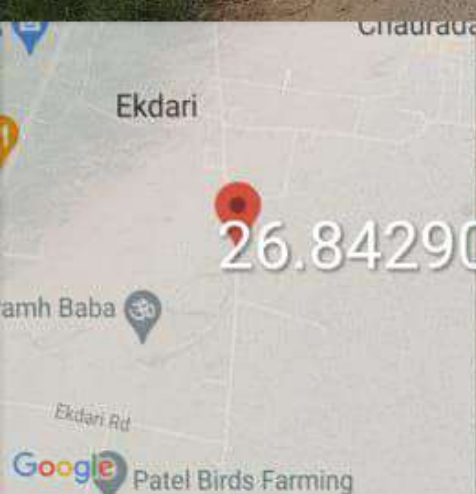

26.842908491380513N 85.00572899356484E

16 Oct 2022 11:49:36


Altitude:2.0m

Speed:0.0km/h

PWD Matter Chowk to Eakdari



16 Oct 2022 11:56:16
26.845895256847143N 85.01207132823765E
Altitude: 12.0m
Speed: 0.0km/h
PWD Matter Chowk to Eakdari

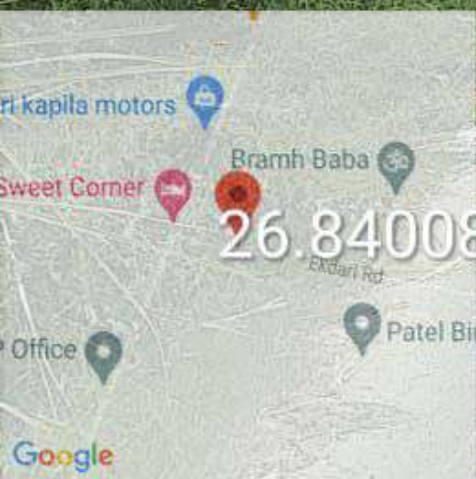


26.840084460563958N 84.99987691640854E

16 Oct 2022 11:42:28

Altitude:2.0m

Speed:0.0km/h

PWD Matter Chowk to Eakdari

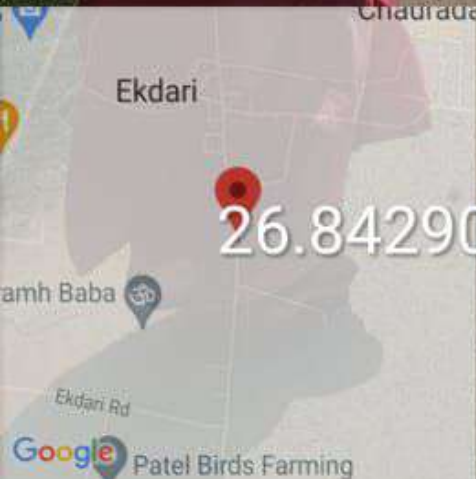

16 Oct 2022 11:49:34
26.842908449470997N 85.00572958029807E

Altitude:2.0m

Speed:0.0km/h

PWD Matter Chowk to Eakdari



मुख्यमंत्री ग्रामीण पथअनुरक्षण कार्यक्रम

योजना का नाम पी. डण्डु से एक्दारी तक की
 पथ की लम्बाई 2.416 कि.मी. विद्युत्तित पथाना पी.सी.सी. पथाना
 मानकनित राशि 56.13831 / 48 लाख रुपया
 पथ स्थान तक रस्ते रस्ते राशि 25.42882 लाख रुपया
 पुर्तिया काज पूरा
 आरम्भ की तिथि-15-08-2020 योजना पूर्ण की तिथि-12-05-2021
 संवत् 2078 वर्तमाना डिजिटल प्रालि राजीव नगर पालिका
 कार्यकारी अधिकारी: कार्यकारी प्रभियंता ग्रामीण कार्य विभाग कार्यप्रकार समिति

विभाग: जनरल	
पथ का नाम	पी. डण्डु से एक्दारी तक की
पथ की लम्बाई	2.416 कि.मी.
पथ का प्रकार	पी.सी.सी. पथ
पथ का स्थान	पी. डण्डु से एक्दारी तक
पथ का रस्ते	रस्ते राशि 25.42882 लाख रुपया
पथ का पूरा	पूरा
पथ का तिथि	12-05-2021
पथ का प्रालि	राजीव नगर पालिका
पथ का कार्यकारी	कार्यकारी प्रभियंता
पथ का कार्यप्रकार	कार्यप्रकार समिति

श्री नीलेश कुमार
 श्री नीलेश कुमार
 श्री नीलेश कुमार
