

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल, रक्सौल।

पत्रांक :- 1377

रक्सौल, / दिनांक :- 10/11/2022

प्रेषक :-

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, रक्सौल।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव,
बिहार ग्रामीण पथ विकास अभिकरण,
ग्रामीण कार्य विभाग, बिहार, पटना।

विषय :- बिहार ग्रामीण पथ अनुरक्षण नीति-2018 अन्तर्गत पाँच वर्षीय रूटीन अनुरक्षण कार्य मद
योजना अन्तर्गत आवंटन निर्गत करने हेतु अधियाचना के संबंध में।

महाशय,

उपर्युक्त विषयक बिहार ग्रामीण पथ अनुरक्षण नीति-2018 अन्तर्गत पाँच वर्षीय रूटीन अनुरक्षण
कार्य मद में संलग्न सूची के अनुसार आवंटन अधियाचना संबंधित प्रपत्र में भरकर आवश्यक कार्रवाई हेतु
समर्पित किया जाता है।

अनुलग्नक :- संलग्न सूची

1. पथों का आवंटन अधियाचना प्रपत्र।
2. Bump Integrator Report

विश्वासभाजन,



कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, रक्सौल।

Standard Format For Roads Quarterly Statement (2nd Quarter)

PIU Name:- Rural Works Department, (Works) Division, Raxaul

1	Name of the Road	Sripur to Kudarkat		
2	Batch No.	RM/EA/RAX/20/0004		
3	Project ID	317851032017		
4	Total Length of Road (In Km)	3.560		
5	Length of Road to Meet Required Service Level [Completed Length] (In Km) [1]	3.560		
6	No. of Total Quarter (i.e. 3 Months as a unit) in 5 Years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	35.85983		
8	Quarterly Payment: 1/20 of ordinary Maintenance Cost as per Schedule (in Lakh) [2]	1.79299		
Compliance Criteria	Standard Job Description	Non Compliance		Reduction Payment [6] = [3]/[1]*[2]*[4]
		Length Non Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	Paved Roads (Carriageway)	0	60%	0.00000
II	Shoulders and Embanments	0	10%	0.00000
III	Cross Drainage Including Culverts and Bridge	0	15%	0.00000
IV	Signage and Road Safety	0	10%	0.00000
V	Vegataion	1	5%	0.02518
Total Payment Reduction For the Quarterly (In Lakh) [5]				0.02518
To be Paid for the Quarter / Demand (In Lakh) [6]				1.76781

Date of Inspection by E/I or his agent

05/11/22

Prepared by Contractor's self Control Unit

Syam Sundar Rai

Name and Designation of person inspecting road

Date:

05-11-2022

N Kumar
05-11-2022
J.E

Signature of person inspecting road

(Signature)

Certified by E/I [Signature] Date

Rural Works Department, Works Division, Raxaul
Government of Bihar
OM01Q
Rural Works Department
Road From: Stripur
(Package No. RM/E/A/RAX/20/0004)
Length of Road. 3.56 Km
Period: From 14.08.2021 to 13.11.2021
Inspector: A.E., RWD, Works Sub Division, Chhauradano

2nd Quarter

Summary of Ordinary Maintenance Inspection Report

To: Kudarkant

Date 05/11/22


Position: Good

Standard Work Item			Work	Unit of work required in each Kilometre										Comments
No	Name	Units	1	2	3	4	5	6	7	8	9	10		
OM100 Sealed Pavement														
OM101	Pothole Patching	m ²	Nil	Nil	Nil	Nil							No Pot Hole Found	
OM102	Surface Depression and Rut Patching	m ²	Nil	Nil	Nil	Nil							No Surface Depression and Rut Patching Found	
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil							No Crack Sealing Found	
OM104	Surface Treatment													
	(a) Loss of Aggregate (Surface Ravelling)	m ²	Nil	Nil	Nil	Nil							No Loss of Aggregate (Surface Ravelling) Found	
	(b) Bleeding / Flushing	m ²	Nil	Nil	Nil	Nil							No Bleeding / Flushing Required	
	(c) Crocodile Cracking	m ²	Nil	Nil	Nil	Nil							No Crocodile Cracking Found	
OM105	Edge Repair	m ²	Nil	Nil	Nil	Nil							No Edge Repair Required	
OM106	Digouts	m ²	NA	NA	NA	NA								
OM107	Concrete Pavement	m ³	NA	NA	NA	NA								
	Other activities													
OM200 Shoulder														
	Unsealed Shoulder													
OM201	(a) Edge Drop-off	Lm	Nil	Nil	Nil	Nil							No Edge Drop-off Required	
	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil	Nil	Nil							Not Required	
	(c) Holding Water	Lm	Nil	Nil	Nil	Nil							No Holding Water Found	
OM202	Embankment Repair	m ³	Nil	Nil	Nil	Nil							Not Required	
	Other activities													

Standard Work Item		Work	Unit of work required in each Kilometre										Comments
No	Name	Units	1	2	3	4	5	6	7	8	9	10	
OM300 Drainage including culverts major and minor bridges													
OM301	Surface Drains & Verge	Lm	NA	NA	NA	NA							Not Required
OM302	Culvert Cleaning	Lm	Nil	Nil	Nil	Nil							Not Required
OM303	Culvert and Pit Repair	m ³	Nil	Nil	Nil	Nil							Not Required
	Other activities												Not Required
OM400 Vegetation													
OM401	Grass Control												Not Required
	(a) Roadside General Tidy	Ha	Nil	Nil	Nil	Nil							Not Required
	(b) Clear near safety signs, kilometer posts and roadside furniture	Ha	Nil	Nil	Nil	Nil							Not Required
OM402	Tree and Shrub Management	Ha	Nil	Nil	Nil	Nil							Not Required
	Other activities												
OM500 Signage and Road Safety													
OM501	Signs Maintenance	No	Nil	Nil	Nil	Nil							Not Required
OM502	Guard stones	Lm	NA	NA	NA	NA							Not Required
OM503	Distance Stones	No	NA	NA	NA	NA							Not Required
OM504	Road Markings	No	Nil	Nil	Nil	Nil							Not Required
	Other activities												


Bidder


29/11/22
Appendix


Executive Engineer,
RWD, Works Division, Raxaul

Name of Customer : Barahonia Engicon Pvt. Ltd
 Name of Work/ Road : Shreepur To Kudarkat
 Lab Job number :
 Date : 27-08-2022
 Section No. : 2


Test Date : 27-08-2022
 Machine No : 378
 Start S No :
 Start E No :
 Weather :
 Start Location : Shreepur
 End Location : Kudarkat
 Road Name : Shreepur To Kudarkat
 Road Type : (R) RURAL ROAD
 Side :
 Interval :
 IIV Range : 1005 To 5000
 Dist Range : 0 To 37
 Equation : $Y = 0.0002 \cdot X^2 + 0.398 \cdot X + 109.5$

Print Generate Report and Graph

Redraw Graph

Map View

File : C:\Users\RWD-AITM\Desktop\Bump Motihari\Barahonia Engicon\Shreepur To Kudarkat\27081706.Xls.
 Name of Customer : Barahonia Engicon Pvt. Ltd, Name of Work/ Road : Shreepur To Kudarkat, Lab Job number :

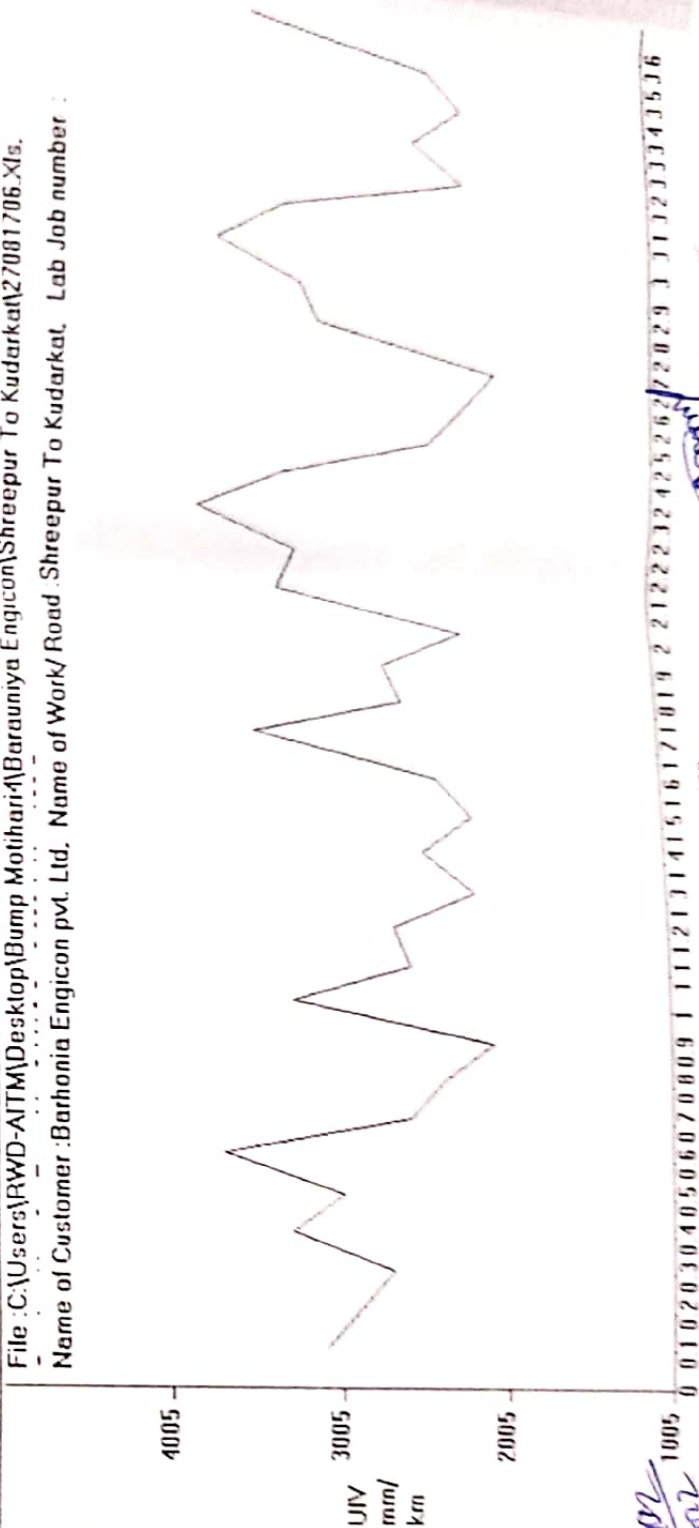

05-11-2022
 5-E
 27/11/22
 0 010203040506070009 1 111213141516171819 2 212223242526272829 3 313233343536

Road Name:-Shreepur To Kudarkat
Contractor Name:-Barhonia Engicon pvt. Ltd

Date	Time	Section No.	Length in km	Bumps in mm	Rate	Speed mm/km	OR mm/km	IRI,TEGORY ROAD	Latitude	ongitude	Event
27/8/22	11:31:38	2	0.1	300	0	3000	3103 G		26.81941	84.9896	Normal
27/8/22	11:32:0	2	0.1	280	20.2	2800	2903 G		26.81934	84.99056	Normal
27/8/22	11:32:14	2	0.1	260	10.1	2600	2704 G		26.81973	84.99148	Speed Breaker
27/8/22	11:32:50	2	0.1	320	10.1	3200	3303 G		26.81985	84.99237	Normal
27/8/22	11:33:0	2	0.1	290	20.2	2900	3003 G		26.82002	84.99333	Normal
27/8/22	11:33:25	2	0.1	360	10.1	3600	3702 G		26.8201	84.99428	Normal
27/8/22	11:33:25	2	0.1	250	30.3	2500	2604 G		26.81997	84.99519	Normal
27/8/22	11:33:25	2	0.1	230	40.4	2300	2404 G		26.8199	84.99621	Normal
27/8/22	11:34:0	2	0.1	200	30.3	2000	2105 G		26.81978	84.99727	Normal
27/8/22	11:34:0	2	0.1	320	10.1	3200	3303 G		26.81974	84.99823	Normal
27/8/22	11:34:0	2	0.1	250	40.4	2500	2604 G		26.81969	84.99919	Normal
27/8/22	11:34:0	2	0.1	260	40.4	2600	2704 G		26.81962	85.12	Normal
27/8/22	11:34:0	2	0.1	210	40.4	2100	2205 G		26.81951	85.1178	Normal
27/8/22	11:34:36	2	0.1	240	40.4	2400	2504 G		26.81938	85.2137	Normal
27/8/22	11:34:36	2	0.1	210	40.4	2100	2205 G		26.81915	85.3113	Normal
27/8/22	11:35:0	2	0.1	230	40.4	2300	2404 G		26.8189	85.4073	Normal
27/8/22	11:35:0	2	0.1	340	20.2	3400	3502 G		26.81861	85.507	Normal
27/8/22	11:35:11	2	0.1	250	30.3	2500	2604 G		26.81831	85.5992	Normal
27/8/22	11:35:11	2	0.1	260	40.4	2600	2704 G		26.81824	85.6952	Normal
27/8/22	11:35:11	2	0.1	210	30.3	2100	2205 G		26.81822	85.8013	Normal
27/8/22	11:35:46	2	0.1	320	10.1	3200	3303 G		26.81789	85.8922	Normal
27/8/22	11:36:0	2	0.1	310	10.1	3100	3203 G		26.81714	85.9242	Normal
27/8/22	11:37:0	2	0.1	370	10.1	3700	3802 G		26.81622	85.9377	Normal
27/8/22	11:37:32	2	0.1	320	10.1	3200	3303 G		26.81541	85.909	Normal
27/8/22	11:38:0	2	0.1	230	20.2	2300	2404 G		26.81459	85.8803	Normal
27/8/22	11:38:7	2	0.1	210	20.2	2100	2205 G		26.81373	85.8513	Normal
27/8/22	11:38:7	2	0.1	190	20.2	1900	2005 G		26.81292	85.8265	Normal
27/8/22	11:38:42	2	0.1	300	20.2	3000	3103 G		26.81202	85.7978	Normal
27/8/22	11:39:0	2	0.1	310	20.2	3100	3203 G		26.81117	85.7677	Normal
27/8/22	11:39:17	2	0.1	360	20.2	3600	3702 G		26.81033	85.7390	Normal
27/8/22	11:39:17	2	0.1	320	10.1	3200	3303 G		26.80951	85.7120	Normal
27/8/22	11:39:17	2	0.1	210	40.4	2100	2205 G		26.81292	85.8265	Normal
27/8/22	11:40:0	2	0.1	240	40.4	2400	2504 G		26.81202	85.7988	Normal
27/8/22	11:40:0	2	0.1	210	40.4	2100	2205 G		26.81117	85.7677	Normal
27/8/22	11:40:0	2	0.1	230	40.4	2300	2404 G		26.81033	85.739	Normal
27/8/22	11:40:0	2	0.1	340	20.2	3400	3502 G		26.8095	85.712	Normal
27/8/22	11:40:55	2	0.1	340	20.2	3400	3502 G		26.8095	85.712	Normal
							Total IRI	101131			
							Average IRI	2809.194			





Latitude: 26.82494
Longitude: 84.991667
Altitude: 12.56±48 m
Accuracy: 2500.0 m
Time: 11-08-2022 12:42
Note: sripur to kudarkat

Powered by NoteCam



Latitude: 26.82494
Longitude: 84.991667
Elevation: 79.17±48 m
Accuracy: 2500.0 m
Time: 11-08-2022 12:43
Note: sripur to kudarkat

Powered by NoteCam



Latitude: 26.821129
Longitude: 84.977366
Elevation: 79.22±48 m
Accuracy: 2800.0 m
Time: 11-08-2022 12:40
Note: sripur to kudarkat

Powered by NoteCam



Latitude: 26.821129
Longitude: 84.977366
Elevation: 79.22±48 m
Accuracy: 2800.0 m
Time: 11-08-2022 12:39
Note: sripur to kudarkat

Powered by NoteCam

