

कार्यपालक अभियंता, का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, बिहारशरीफ

पत्रांक 1770(315) बिहारशरीफ, दिनांक 17-11-22

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बिहारशरीफ।

सेवा में,

नोडल पदाधिकारी (MR-3054)
ग्रामीण कार्य विभाग,
बिहार, पटना।

विषय :- नई अनुरक्षण नीति-2018 (MR-3054) योजनान्तर्गत पथ में कराये गये
अनुरक्षण कार्य के विरुद्ध आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपर्युक्त विषयक के संबंध में कहना है कि नई अनुरक्षण नीति-2018 (MR-3054) योजनान्तर्गत पथ में कराये गये अनुरक्षण कार्य के लिए संवेदक को भुगतान करने हेतु अध्याचना विहित प्रपत्र में भरकर आवश्यक कार्रवाई हेतु समर्पित की जा रही है।

अनु०-यथोक्त।

विश्वासभाजन

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बिहारशरीफ

16/11/22

Requisition Format for Scheme Head-MR-(3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

RWD, Works Division Bihar Sharif

1 Year (1st Quarter)

Government Of Bihar
OM01
Rural Works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From:- T03 - DHANAWA
(Package No.RM/NA/BIH/20/0003)
Length of Road :- 0.96 Km
Inspector :- J.E RWD Sub Division : Samera

To:-

Executive Engineer
RWD, Works Division ~~Samera~~ *Bihar Sharif*

Date:-

Position :- j.e

No	standard Of Work Item Name	Work Unit	Unit Of Required in each Kilometer										Comments
			1	2	3	4	5	6	7	8	9	10	
OM100	Sealed payment												
OM101	Pothole Patching	m ²	Nil	Nil	Nil	Nil							No Pot Hole Found.
OM102	Surface Depression and Rut patching	m ³	Nil	Nil	Nil	Nil							Not Surface Depression & Rut Patching Found
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil							No Crack sealing Found
OM104	Surface Treatment												
	(a) Loss of Aggregate (Surface Raveling)	m ²	Nil	Nil	Nil	Nil							No Loss Of Aggregates (Surface Raveling) Found
	(b) Bleeding / Flushing	m ²	Nil	Nil	Nil	Nil							No Bleeding/ Flushing Required
	@ Crocodile Cracking	m ²	Nil	Nil	Nil	Nil							No Crocodile Cracking Found
105	Edge Repair	m ²	Nil	Nil	Nil	Nil							No Edge Repair Required
106	Digouts	m ²	N.A	N.A	N.A	N.A							
107	Concrete pavement	m ³	N.A	N.A	N.A	N.A							
OM200	Other activities												
	Shoulder												
	Unsealed Shoulder												
	(a) Edge Drop-off	Lm	Nil	Nil	Nil	Nil							No Edge Drop-Off Required
OM201	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil	Nil	Nil							Not Required
	(c) Holding water	Lm	Nil	Nil	Nil	Nil							No Holding Water Found
	Embankment Repair	M ³	Nil	Nil	Nil	Nil							Not Required
OM202	Other activities (Rain Cuts)		Nil	Nil	Nil	Nil							Not Required
OM300	Drainage including culverts major												
OM301	Surface Drains & Verge	Lm	N.A	N.A	N.A	N.A							Not Required
OM302	Culvert Cleaning	No	Nil	Nil	Nil	Nil							Not Required
OM303	Culvert and pit Repair	M ³	Nil	Nil	Nil	Nil							Not Required
	Other activities(Whilw washing)	M ²	Nil	Nil	Nil	Nil							Not Required

Standard Of Work Item		Work	Unit Of Required in each Kilometer										Comments
No	Name	Unit	1	2	3	4	5	6	7	8	9	10	
OM400	Vegetation												
	Grass Control												
OM401	(a) Roadside- General Tidy	Ha	Nil	Nil	Nil	Nil							Not Required
	(b) Clear near Safety signs, kilometer posts and roadside furniture	Ha	Nil	Nil	Nil	Nil							Not Required
OM402	Tree and Shrub Management	No	Nil	Nil	Nil	Nil							Not Required
	Cutting Of Branches Of Trees	No	Nil	Nil	Nil	Nil							Not Required
	Cutting Of Shrubs From Road Way	No	Nil	Nil	Nil	Nil							Not Required
	Other activities (Trimming of Grass)	M ²	Nil	Nil	Nil	Nil							Not Required
OM500	Safety Signage and Road		Nil										Not Required
OM501	Signs Maintenance	No	Nil	Nil	Nil	Nil							Not Required
OM502	Guard Stones	Lm	N.A	N.A	N.A	N.A							Not Required
OM503	Distance Stones	No	N.A	N.A	N.A	N.A							Not Required
OM504	Road Marking	M ²	Nil	Nil	Nil	Nil							Not Required
	Other activities												

10/11/22
S.E.

10/11/22
A.E.

Executive Engineer
Rural Work Department
Work Division Bihar Sharif

15/11/22

STANDRAD FORMAT FOR ROADS QUARTERLY STATEMENT

1	Name of the Road-			
2	Batch No.-			
3	Project ID -			T03 - DHANAWA
4	Total Length of Road (in Km)			RM/NA/BIH/20/0003
5	Length of Road to Meet Required Service Level [Completed length] (in Km)			10200602033
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years			0.96
7	Ordinary Maintenance Cost as per Schedule (Agreement Amount for Maintenance) (in Lakh)			0.96
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh)			20
				13.75435
				0.68772
Compliance Criteria	Standard Job Description	Non-Compliant		Reduction Payment (6) = (3) / (1) * (2) * (4)
		Length Non Compliant (3)	Weighted Value for Payment Reduction (%) (4)	
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0.00000
II	SHOULDER AND EMBANMENTS	0	10%	0.00000
III	CROSS DRAINAGE INCLUDING CULVERTS AND	0	15%	0.00000
IV	SIGNAGE AND ROAD SAFETY	0	10%	0.00000
V	VEGATAION		5%	0.00000
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0.00000
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh) [6]				0.00000
				0.68772

Signature of person inspecting road

Date

Signature of person inspecting road

Signature of person inspecting road

Name and Designation of person inspecting road

Certify by E/I (signature) Date

Scheme-NEW MR
Road Name-T03 se Dhanawa Road
Contractor-Maa Tara Construction


Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event	$Y = 0 \cdot X^2 + 0.816 \cdot X + 249$	$X = 3100$	$Y = 2778$	(R) RURAL ROAD	Good <4000	Average 4001-5000	Poor >5001
1/5/22	8:35:8	77	0.1	250	0	2500	2288	G	25.298805	85.76168	Normal							
1/5/22	8:35:8	77	0.1	280	10.1	2800	2533	G	25.298503	85.762777	Normal							
1/5/22	8:36:18	77	0.1	340	10.1	3400	3023	G	25.298235	85.76367	Normal							
1/5/22	8:36:18	77	0.1	240	10.1	2400	2207	G	25.297968	85.764628	Normal							
1/5/22	8:36:53	77	0.1	270	10.1	2700	2452	G	25.297422	85.765555	Normal							
1/5/22	8:37:0	77	0.1	280	10.1	2800	2533	G	25.297093	85.76648	Normal							
1/5/22	8:37:0	77	0.1	350	10.1	3500	3104	G	25.296777	85.767473	Normal							
1/5/22	8:37:0	77	0.1	260	10.1	2600	2370	G	25.296507	85.76842	Normal							
1/5/22	8:39:0	77	0.1	320	10.1	3200	2860	G	25.296507	85.769192	Normal							
1/5/22	8:39:15	77	0.1	290	20.2	2900	2615	G	25.296808	85.768332	Normal							
Total							25985											
IRI Value							2598											

Signature
 10/11/22
 J.E

Signature
 10/11/22
 J.E

Signature
 10/11/22
 A.E
 15/11/22

File : E:\Bump Machine\Bump Reading\Maa Tara Construction\01051720.Xls. Section No. : 77. Eqn : $Y = 0 \cdot X^2 +$
 Name of Customer : Maa Tara Construction. Name of Work/ Road : T03 - DHANAWA. Lab Job number :

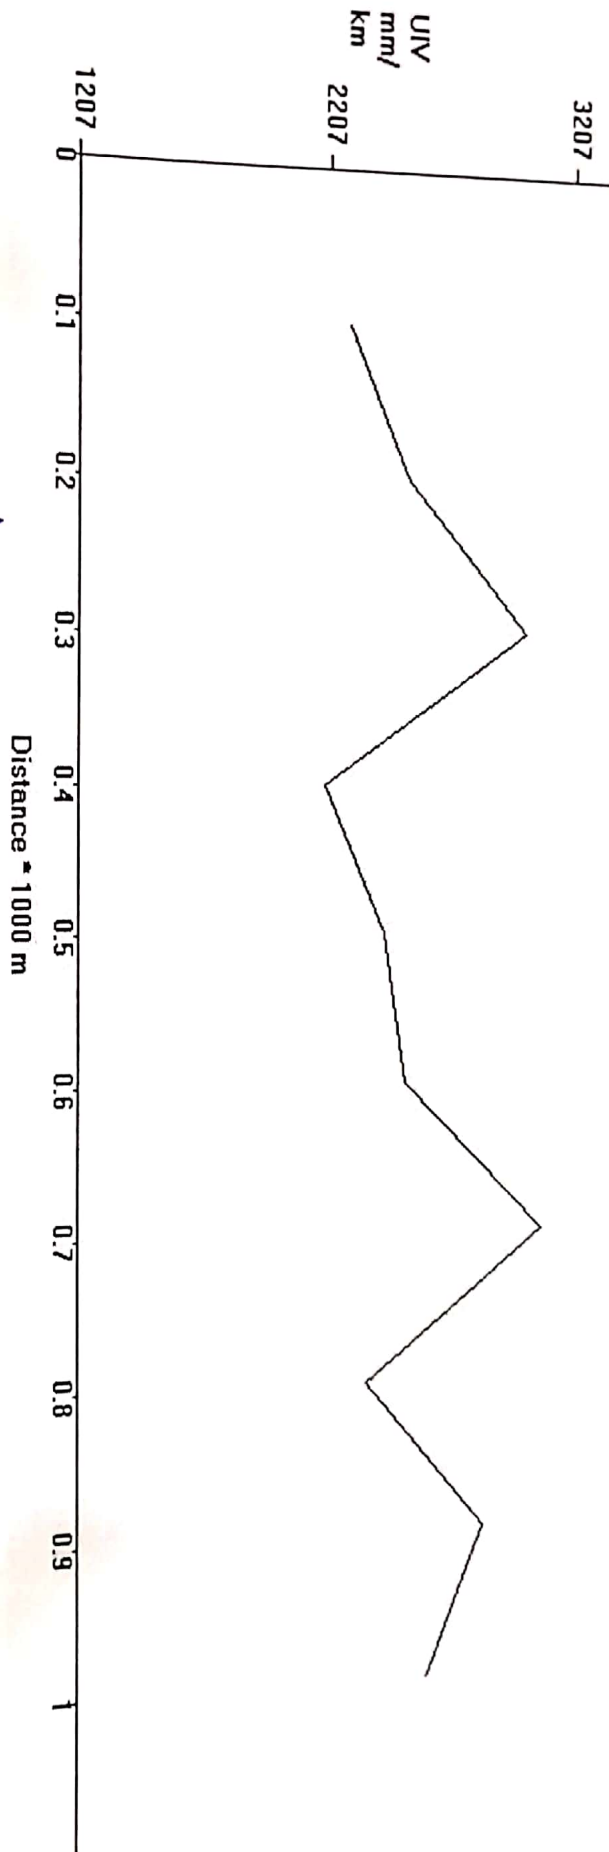

Signature
 10/11/22
 mm

Signature
 10/11/22

Signature
 10/11/22
 AE
