

कार्यपालक अभियन्ता का कार्यालय

ग्रामीण कार्य विभाग, कार्य प्रमंडल, नरकटियागंज

Mobile No- 8986915814

Email ID- eerwdwd2bettiah@gmail.com

पत्रांक- 19/4-866/ नरकटियागंज, दिनांक- 29/9/2022

प्रेषक,

कार्यपालक अभियन्ता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, नरकटियागंज।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी,
—सह— सचिव नोडल पदाधिकारी,
ग्रामीण कार्य विभाग,
बिहार पटना।

विषय:- **MR-3054 (New Maint. Policy-2018) योजना अन्तर्गत 5 (पाँच) वर्षीय अनुरक्षण का आवंटन उपलब्ध कराने के संबंध में।**

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि **MR-3054 (New Maint. Policy-2018) योजना अन्तर्गत 5 (पाँच) वर्षीय अनुरक्षण का आवंटन उपलब्ध कराने के लिए सूची बनाकर इस पत्र में संलग्न कर अवलोकनार्थ एवं आवश्यक कार्रवाई हेतु समर्पित की जाती है।**

अनु०:- 1. उपयोगिता प्रमाण-पत्र From GFR 19A

2. अधियाचना पत्र।

विश्वासभाजन,

कार्यपालक अभियन्ता,

ग्रा०का०वि०, का०प्र०, नरकटियागंज।

28/09/2022

FORM GFR 19-A

(See Government of India's decision (I) below rule- 150)
Form of Utilization certificate up to the month of SEP.-2022
PIU:- E.E RWD(W)DIV-NARKATIAGANJ

SL.NO.	Name of Schemes	Sanction No.& Date with Amount (In Lacs)	Amount received (In Lacs)	Particulars
1	2	3	4	5
1	Maintenance Fund of MR(3054) New Maintenance Policy- 2018	Letter No:-27 Date:-26.08.2022	23.79597	Certified that out of Rs. 23.79597 Lacs of grants-in-aid sanctioned during the years 2022-23 in favour of Executive Engineer R. W. D. Works Division, Narkatiaganj a sum of Rs. 23.79597 Lacs has been utilized for the purpose of Maintenance Fund of MR(3054) New Maintenance Policy-2018 Schemes as given in the margin for which it was sanctioned and that the balance of Rs. NIL Lac remaining unutilized at the end of the period under report.
		TOTAL	23.79597	

2. Certified that I have satisfied myself that the conditions on which the grant-in-aid was sanctioned have been duly fulfilled, are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.

Kinds of checks exercised:-

- Works has been supervised by Executive Engineer / Superintending Engineer.
- Periodic as inspection has been conducted by Executive Engineer / Superintending Engineer.
- Construction materials have been tested.
- Measurements have been recorded in the MBs and test check conducted by the Assistant Engineer / Executive Engineer.
- All other codal formalities have been observed.

3. Physical Progress achieved:-

- Construction of Road Works.
- Construction of CD Works.


Executive Engineer
R.W.D. Works Division, Narkatiaganj

Requisition Format for Scheme Head - 5 Year Maintenance of MR(3054) under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and surface Renewal)

Name of Division :- Narkataganj

Name of Circle :- Bettiah

Sl. No.	Package No.	Name of Road	Project ID as per MIS	Administrative Sanction Letter No & Date	Administrative Approval (AA)		Agreement Amount (in Lac)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Current Maintenance Demand (in Lac)				Remarks
					Length (in km)	Amount of (in Lakh)	Initial Rectification with surface Renewal (in Lakh)	5 Years Routine Maintenance (in Lakh)				1st Qtr Maint Demand	2nd Qtr Maint Demand	3rd Qtr Maint Demand	4th Qtr Maint Demand	
1	RM/WE/NAR/1/9/0004	Domath - Ratani	31808802074	1876 24.06.2019	1.293	59.5038	42.56	12.2202	65/2019-20 21.07.2020	04.02.2021	21.02.2021	0.61101	0.61101	0.61101	0.00000	
2	RM/WE/NAR/1/9/0004	Done Canal - Bajara	31808802075	1876 24.06.2019	0.6	24.4996	16.707	5.5723	65/2019-20 21.07.2020	04.02.2021	10.02.2021	0.27862	0.27862	0.27862	0.00000	
3	RM/WE/NAR/1/9/0004	Done Canal - Baria	31808802076	1876 24.06.2019	0.9	35.7738	24.841	8.5052	65/2019-20 21.07.2020	04.02.2021	13.02.2021	0.42526	0.42526	0.42526	0.00000	
4	RM/WE/NAR/1/9/0004	Kanawa - Dhanajice	31808802084	1876 24.06.2019	1.78	73.8333	51.603	16.6346	65/2019-20 21.07.2020	04.02.2021	24.10.2020	0.83173	0.83173	0.83173	0.83173	
5	RM/WE/NAR/1/9/0004	Kanaw PWD - Pakkani	31808802091	1876 24.06.2019	1.424	55.3634	37.804	13.3059	65/2019-20 21.07.2020	04.02.2021	09.01.2021	0.66530	0.66530	0.66530	0.00000	
6	RM/WE/NAR/1/9/0004	PWD Road - Matajogin	31808802112	1876 24.06.2019	0.9	39.5843	27.818	8.45905	65/2019-20 21.07.2020	04.02.2021	04.02.2021	0.42295	0.42295	0.42295	0.00000	
7	RM/WE/NAR/1/9/0004	Gonaha RLY Station to Sidi Village	31808802237	1876 24.06.2019	0.9	35.3504	23.941	8.4946	65/2019-20 21.07.2020	04.02.2021	21.02.2021	0.42473	0.42473	0.42473	0.00000	
8	RM/WE/NAR/1/9/0004	Biswalya middle school se Changama	10109121	3350 01-08-2019	1.4	70.302	51.468	13.21285	65/2019-20 21.07.2020	04.02.2021	28.10.2020	0.66064	0.66064	0.66064	0.66064	

Executive Engineer
Rural Works Department
Works Division Narkataganj

28/09/2022

RWD, Works Division, Narkatiaganj

3rd Quarter

Government Of Bihar

OM01

Rural Works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From:- Done Canal - Bajara

Length of Road : 0.6 KM

Inspector :- A.E. RWD WORKS SUB DIVISION, GAUNAHA

To:-

Executive Engineer
RWD, Works Division Narkatiaganj

Date:-

Position :- A.E.

No	standard Of Work Item Name	Work Unit	Unit Of Required in each Kilometer										Comments
			1	2	3	4	5	6	7	8	9	10	
OM100	Scaled payment												
OM101	Pothole Patching	m ²	NIL	NIL	NIL								No pothole found
OM102	Surface Depression and Rut patching	m ³	NIL	NIL	NIL								No Surface Depression and Rut patching found
OM103	Crack Sealing	Lm	NIL	NIL	NIL								No crack Not required
	Surface Treatment		NIL	NIL	NIL								No Loss of Aggregate (Surface ravelling) found
OM104	(a) Loss of Aggregate (Surface Ravelling)	m ²	NIL	NIL	NIL								No bleeding / furnishing found
	(b) Bleeding / Flushing	m ²	NIL	NIL	NIL								No Crocodile cracking found
	(c) Crocodile Cracking	m ²	NIL	NIL	NIL								Notified & repaired
OM105	Edge Repair	m ²	NIL	NIL	NIL								
OM106	Digouts	m ²	N.A.	N.A.	N.A.								
OM107	Concrete pavement	m ³	N.A.	N.A.	N.A.								
	Other activities												
OM200	Shoulder												
	Unsealed Shoulder												
OM201	(a) Edge Drop-off	Lm	NIL	NIL	NIL								No Edge Drop off found
	(b) Roughness, Scouring or Potholes	Lm	NIL	NIL	NIL								No Roughness, Scouring or Potholes found
	(c) Holding water	Lm	NIL	NIL	NIL								No Holding Water found
OM202	Embankment Repair	M ³	NIL	NIL	NIL								Notified & repaired
	Other activities (Rain Cuts)		N.A.	N.A.	N.A.								
OM300	Drainage including culverts major												NA
OM301	Surface Drains & Verge	Lm	N.A.	N.A.	N.A.								DONE
OM302	Culvert Cleaning	No	NIL	NIL	NIL								DONE
OM303	Culvert and pit Repair	M ³	NIL	NIL	NIL								Not required
	Other activities (Whitewashing)	M ²	NIL	NIL	NIL								

Contractor

J.E

A.E

E.E

No	Standard Of Work Item Name	Work Unit	Unit Of Required in each Kilometer										Comments
			1	2	3	4	5	6	7	8	9	10	
OM400	Vegetation												Done
	Grass Control												Done
	(a) Roadside- General Tidy	Ha	NIL	NIL	NIL								Done
OM401	(b) Clear near Safety signs, kilometer posts and roadside furniture	Ha	NIL	NIL	NIL								Done
	Tree and Shrub Management	No	NIL	NIL	NIL								Done
	Cutting Of Branches Of Trees	No	NIL	NIL	NIL								Done
	Cutting Of Shrubs From Road Way	No	NIL	NIL	NIL								Done
OM402	Other activities (Trimming of Grass)	M ²	NIL	NIL	NIL								Not Required
OM500	Safety Signage and Road												Not Required
OM501	Signs Maintenance	No	NIL	NIL	NIL								N.A.
OM502	Guard Stones	Lm	NA	NA	NA								N.A.
OM503	Distance Stones	No	NA	NA	NA								Not Required
OM504	Road Marking	M ²	NIL	NIL	NIL								Not Required
	Other activities												

Contractor

J.E

A.E

Executive Engineer
Rural works Department
Works Division, Narkatiaganj

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

PIU Name :- RWD, Works Division, Narkatiaganj

3rd Quarter

1	Name of the Road	Done Canal - Bajara		
2	Batch No.	RM/WE/NAR/19/0004		
3	Project ID	31808802075		
4	Total Lenth of Road (in KM)	0.600		
5	Length of Road to Meet Required Service Level [Completed length](in Km) [1]	0.600		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	5.5723		
8	Quarterly Payment : 4/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	0.2786150		
Compliance Criteria	Standard Job Description.	Non-Compliance		Reduction Payment [6]=[3]/[1]*[2]*[4]
		Length Non-Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0.00
II	SHOULDERS AND EMBANMENTS	0	10%	0.00
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0	15%	0.00
IV	SIGNAGE AND ROAD SAFETY	0	10%	0.00
V	VEGATION	0	5%	0.00
TOTAL PAYMENT REDUCTION FOR THE QUARTER (IN Lakh) [5]				0.00000
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh) [6]				0.2786150

Date of inspection by E/I or his agent

Prepare by Contractor's self Control unit


Name and Designation of person inspecting road

Date


Signature of person inspecting road


12/09/2022
AE

(Signature)


Certify by E/I [Signature] Date:-
Executive Engineer
Rural Works Department
Works Division, Narkatiaganj



Name of Road - Done Canal - Bajara (Sec-52)

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD			
3/9/22	12:36:0	52	0.1	220	20.2	2200	2235	G	27.19793	84.55505	Normal
3/9/22	12:36:4	52	0.1	270	20.2	2700	2716	G	27.19881	84.555168	Normal
3/9/22	12:36:5	52	0.1	250	20.2	2500	2516	G	27.19966	84.555555	Normal
3/9/22	12:37:0	52	0.1	260	20.2	2600	2655	G	27.20051	84.555958	Normal
3/9/22	12:37:4	52	0.1	250	20.1	2500	2525	G	27.20135	84.556295	Normal
3/9/22	12:37:5	52	0.1	230	20.2	2300	2341	G	27.20226	84.556515	Normal
Average IRI Value=							2498				

[Signature]

WSD 7-9-22
GRE

Rece
12/09/22
AC

Name of Customer: M/S Nav Bharat Construction C
 Name of Work: Done Canal - Bajera
 Road:
 Lab Job number:
 Date: 03-Sep-22
 Section No. 52


Test Date: 03-Sep-22 Road Name: Done Canal - Bajera
 Machine No: 402 Road Type: (R) RURAL ROAD
 Start S No: Side: Interval:
 Start E No:
 Weather:
 UV Range: 1235 To 4000 1000 mm/km
 Start Location: Dist Range: 0 To 0.7 0.1 * 1000 m
 End Location: Equation: $Y = 0 * X^2 + 1.136 * X + 1325$

Print Generate Report and Graph

Redraw Graph

Map View

File F:\02091504.xlsx Section No. 52. Egn: $Y = 0 * X^2 + 1.136 * X + 1325$
 Name of Customer: M/S Nav Bharat Construction Company, Name of Work/ Road: Done Canal - Bajera, Lab Job

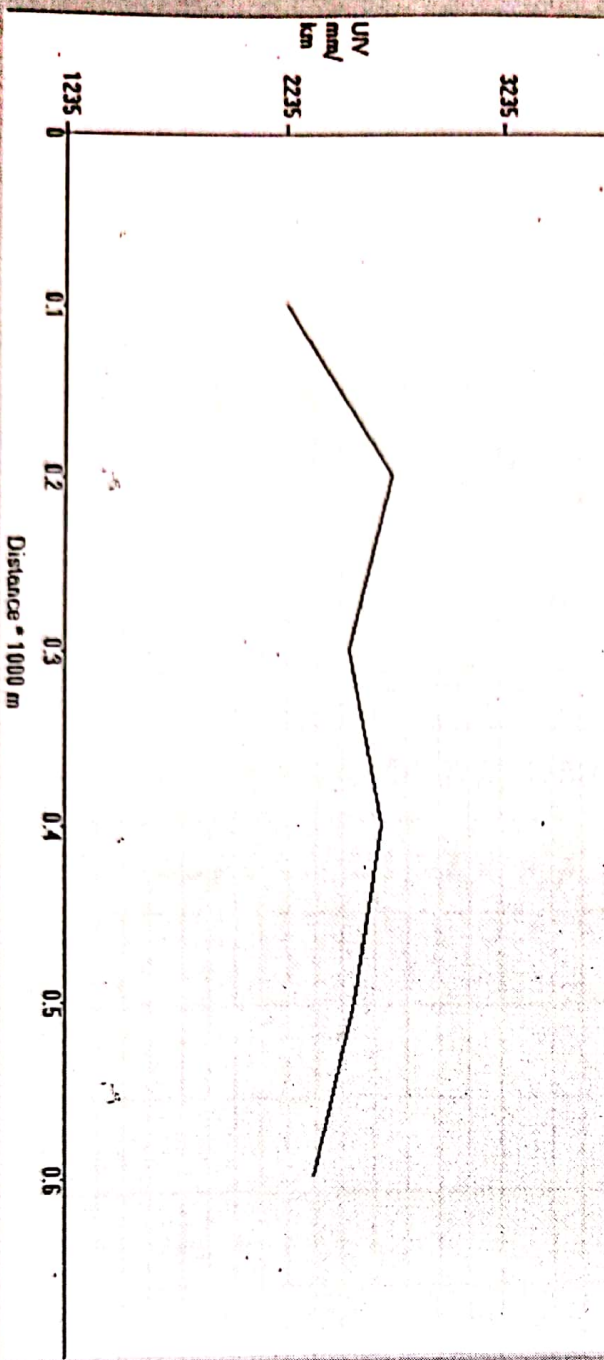

M/S Nav Bharat Construction C
Done Canal - Bajera
03-Sep-22
52
03-Sep-22
402
(R) RURAL ROAD
0 To 0.7 0.1 * 1000 m
 $Y = 0 * X^2 + 1.136 * X + 1325$
03-Sep-22
1235 To 4000 1000 mm/km
0 To 0.7 0.1 * 1000 m
03-Sep-22
