

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग
कार्य प्रमंडल सोनपुर

पत्रांक.....1681.....सोनपुर, दिनांक.....07/10/22.....

प्रेषक,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल सोनपुर

सेवा में,

अपर मुख्य कार्यपालक
पदाधिकारी-सह-सचिव,
बिहार ग्रामीण पथ विकास अभिकरण
(BRRDA)
बिहार, पटना।

विषय:- बिहार ग्रामीण पथ अनुरक्षण निति-2018 योजनान्तर्गत अनुरक्षण हेतु
राशि की अधियाचना के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि बिहार ग्रामीण पथ अनुरक्षण निति-2018 के अंतर्गत पथों का अनुरक्षण की राशि की मांग रुपये 18,54,011.00 (अठारह लाख चौवन हजार ग्यारह) मात्र विहित प्रपत्र में अंकित कर आवश्यक कार्रवाई हेतु समर्पित किया जा रहा है।

अनुरोध है कि उपर्युक्त योजना में आवंटन उपलब्ध कराने की कृपा की जाये। कार्य का निरीक्षण किया गया कार्य संतोषप्रद है। उक्त पथ में ए0टी0आर0 लंबित नहीं है।

अनु0:-Standard Formate for Roads
Quarterly Statement

विश्वासभाजन



कार्यपालक अभियंता
ग्रामीण कार्य विभाग

कार्य प्रमंडल सोनपुर
27/10/22

FORM GER 19-A

(See Government of India's Decision (I) below Rule-150
Form of Utilization Certificate up to the month of **October-2022**

PIU:- E.E.,R.W.D. Works Division Sonapur.



Sl. No.	Name of Scheme	Sanction No. & Date with Amount (in lacs Rs.)	Amount Received (in lac Rs.)	Particulars
1	2	3	4	5
1	Construction of Rural Roads under New Maintenance Policy-18 (Maintenance)		66.42492	Certified that out of Rs 66.42492 lakh received during the years 2020-21 to 2022-23 in favour of E.E.R.W.D. works division Sonapur a sum of Rs 5.93449 Lakh has been utilized for the purpose of New Maintenance Policy-18 (Maintenance) Scheme as given in the margin for which it was sanctioned and that the balance of Rs 60.49043 Lakh remaining unutilized at the end of the period under report.

Certified that I have satisfied that the condition of which the grants-in-aid was sanctioned have been duly fulfilled/ are being fulfilled and that I have exercised the following checks to see that the money was actually for the purpose for which it was sanctioned.

Kind of Checks:-

- Words have been supervised by Executive/superintending Engineer.
 - Periodical inspection has been conducted by Executive Engineer/ superintending Engineer.
 - Construction material has been tested.
 - Measurements have been recorded in the MBS and test conducted by the Assistant Engineer/ Executive Engineer.
 - All other nodal formalities have been observed.
- 3 physical Progress achieved-
- Construction of Road Works.
 - Construction of CD works

D.A.O
R.W.D. Works Division Sonpur.


EXECUTIVE ENGINEER
R.W.D. Works Division Sonpur.


Maintenance Requisition Formate for Scheme Head- MR (3054) Under Bihar Rural Road Maintenance Policy-2018

Name of Works Division:- SONPUR

Name of Works Division:- SONPUR										Road Details		AA Details		Agreement								Actual Maintenance Expenditure						Current Maintenance Demand					Remarks
Sl. No.	Name of Raods	Batch No.	Project ID	Actual Date of Completion	Main Work Amount (in Lakh	Maintenan ce Amount (in lakh)	Main Work Amount (in Lakh)	Agre ement-1	Agree ment-2	Agree ment-3	Agreem ent-4	Agree ment-5	Total Maintenance	Length h (in KM)	1st. Year Maintenance	2nd. Year Maintenance	3rd. Year Maintenance	4th Year Maintenance	5th Year Maintenance	Total Maintenance Expenditure	Length as per Bump Report	IRI As per bump Report	1st QTR Maintenance	2nd QTR Maintenance	3rd QTR Maintenance	4 th QTR Maintenance	Total						
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	30	31						
1	Anjani se kapsar tak path nirman	RM/SA/SON/19/0004	31306301002	16.06.20	42.97700	19.94500	37.78100	3.58868	3.58868	3.58868	3.58868	3.58868	17.94340	1.600	0.000	0.000	0.000	0.000	0.000	0.000	1.600	2460.00	0.89717	0.89717	0.89717	0.89717	3.58868						
2	BASAUTI - BHIMABANDH	RM/SA/SON/19/0004	31306402009	16.06.20	93.57400	45.44000	94.63100	8.02617	8.02617	8.02617	8.02617	8.02617	40.13085	4.100	0.000	0.000	0.000	0.000	0.000	0.000	4.100	2700.00	2.00654	2.00654	2.00654	2.00654	8.02617						
3	DIGHRA - BHIKHARI CHAPRA	RM/SA/SON/19/0004	31306402024	08.01.21	82.19500	39.22100	82.99400	6.92526	6.92526	6.92526	6.92526	6.92526	34.62630	3.580	0.000	0.000	0.000	0.000	0.000	0.000	3.580	2390.00	1.73132	1.73132	1.73132	1.73132	6.92526						
Total				-----																					18.54011								


 Executive Engineer
 R.W.D. Works Division
 SONPUR
 7/10/22

STANDRAD FORMAT FOR ROADS QUARTERLY STATEMENT

1	Name of the Road	Basauti To Bhima Bandh		
2	Batch No.	RM/SA/SON/20/0004		
3	Project ID	31306402009		
4	Total Length of Road (in Km)	4.100		
5	Length of Road to Meet Required Service Level [Completed length] (in Km) (1)	4.100		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule (Agreement Amount for Maintenance) (in Lakh)	35.54279		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) (2)	1.77714		
Compliance Criteria	Standard Job Description	Non-Compliant		Reduction Payment (6) = (3) / (1) * (2) * (4)
		Length Non Compliant (3)	Weighted Value for Payment Reduction (%) (4)	
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0.00000
II	SHOULDERS AND EMBANMENTS	0	10%	0.00000
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0	15%	0.00000
IV	SIGNAGE AND ROAD SAFETY	0	10%	0.00000
V	VEGATAION		5%	0.00000
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0.00000
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh) [6]				1.77714

Date of inspection by E/1 or his agent Prepared by
Contractor's self Control unit

Date




Signature of person inspecting road

Name and Designation of person inspecting road
(Signature)

Certify by E/1 (signature) Date

Name of work : BASAUTI - BHIMABANDH	
Name of customer : Er Ap Construction Private Limited	
(R) Rural Road	
Good	Average
< 4000	4001 - 5000
Poor	> 5000

Date	Time	Test No	Distance(m)	Total Distance(m)	BUMP(cm)	Speed(Km/Hr)	UI(mm/Km)	Corrected UI (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks
13/04/22	12:54:41	24	100	100	20.0 cm	19.4 Km/Hr	2000.0 mm/Km	1983	2.78	Good	25.8159762	N	85.0575190	E	Normal
13/04/22	13:15:55	24	100	200	18.0 cm	4.0 Km/Hr	1800.0 mm/Km	1798	2.55	Good	25.8147021	N	85.0693369	E	Normal
13/04/22	13:16:44	24	100	300	20.0 cm	7.1 Km/Hr	2000.0 mm/Km	1983	2.78	Good	25.8153582	N	85.0698252	E	Normal
13/04/22	13:17:04	24	100	400	18.0 cm	18.0 Km/Hr	1600.0 mm/Km	1612	2.31	Good	25.8161459	N	85.0700235	E	Normal
13/04/22	13:17:33	24	100	500	17.0 cm	12.4 Km/Hr	1700.0 mm/Km	1705	2.43	Good	25.8171607	N	85.0702829	E	Normal
13/04/22	13:18:09	24	100	600	19.0 cm	9.9 Km/Hr	1900.0 mm/Km	1890	2.67	Good	25.8181239	N	85.0704889	E	Normal
13/04/22	13:19:06	24	100	700	26.0 cm	16.4 Km/Hr	2600.0 mm/Km	2540	3.47	Good	25.8190146	N	85.0705576	E	Normal
13/04/22	13:20:20	24	100	800	25.0 cm	5.0 Km/Hr	2500.0 mm/Km	2447	3.36	Good	25.8198424	N	85.0710764	E	Normal
13/04/22	13:20:51	24	100	900	23.0 cm	11.6 Km/Hr	2300.0 mm/Km	2262	3.13	Good	25.8200980	N	85.0715799	E	Normal
13/04/22	13:21:21	24	100	1000	25.0 cm	11.8 Km/Hr	2500.0 mm/Km	2447	3.36	Good	25.8196955	N	85.0729532	E	Normal
13/04/22	13:22:02	24	100	1100	20.0 cm	18.8 Km/Hr	2000.0 mm/Km	1983	2.78	Good	25.8191939	N	85.0727396	E	Normal
13/04/22	13:23:22	24	100	1200	19.0 cm	14.5 Km/Hr	1900.0 mm/Km	1890	2.67	Good	25.8182917	N	85.0727549	E	Normal
13/04/22	13:24:00	24	100	1300	27.0 cm	19.5 Km/Hr	2700.0 mm/Km	2633	3.59	Good	25.8179732	N	85.0738764	E	Normal
13/04/22	13:27:57	24	100	1400	22.0 cm	11.4 Km/Hr	2200.0 mm/Km	2169	3.02	Good	25.8179656	N	85.0739298	E	Normal
13/04/22	13:28:35	24	100	1500	32.0 cm	19.4 Km/Hr	3200.0 mm/Km	3097	4.14	Good	25.8180476	N	85.0735712	E	Normal
13/04/22	13:29:24	24	100	1600	28.0 cm	17.3 Km/Hr	2800.0 mm/Km	2726	3.7	Good	25.8180476	N	85.0735712	E	Normal
13/04/22	13:30:04	24	100	1700	34.0 cm	29.0 Km/Hr	3400.0 mm/Km	3283	4.37	Good	25.8180476	N	85.0735712	E	Normal
13/04/22	13:30:48	24	100	1800	21.0 cm	18.1 Km/Hr	2100.0 mm/Km	2076	2.9	Good	25.8180476	N	85.0735712	E	Normal
13/04/22	13:31:21	24	100	1900	17.0 cm	10.6 Km/Hr	1700.0 mm/Km	1705	2.43	Good	25.8180476	N	85.0735712	E	Normal
13/04/22	13:31:49	24	100	2000	23.0 cm	12.9 Km/Hr	2300.0 mm/Km	2262	3.13	Good	25.8180476	N	85.0735712	E	Normal
13/04/22	13:32:10	24	100	2100	25.0 cm	17.2 Km/Hr	2500.0 mm/Km	2447	3.36	Good	25.8180476	N	85.0735712	E	Normal

Name of work : BASAUTI - BHIMABANDH


Name of customer : Er Ap Construction Private Limited

(R)Rural Road

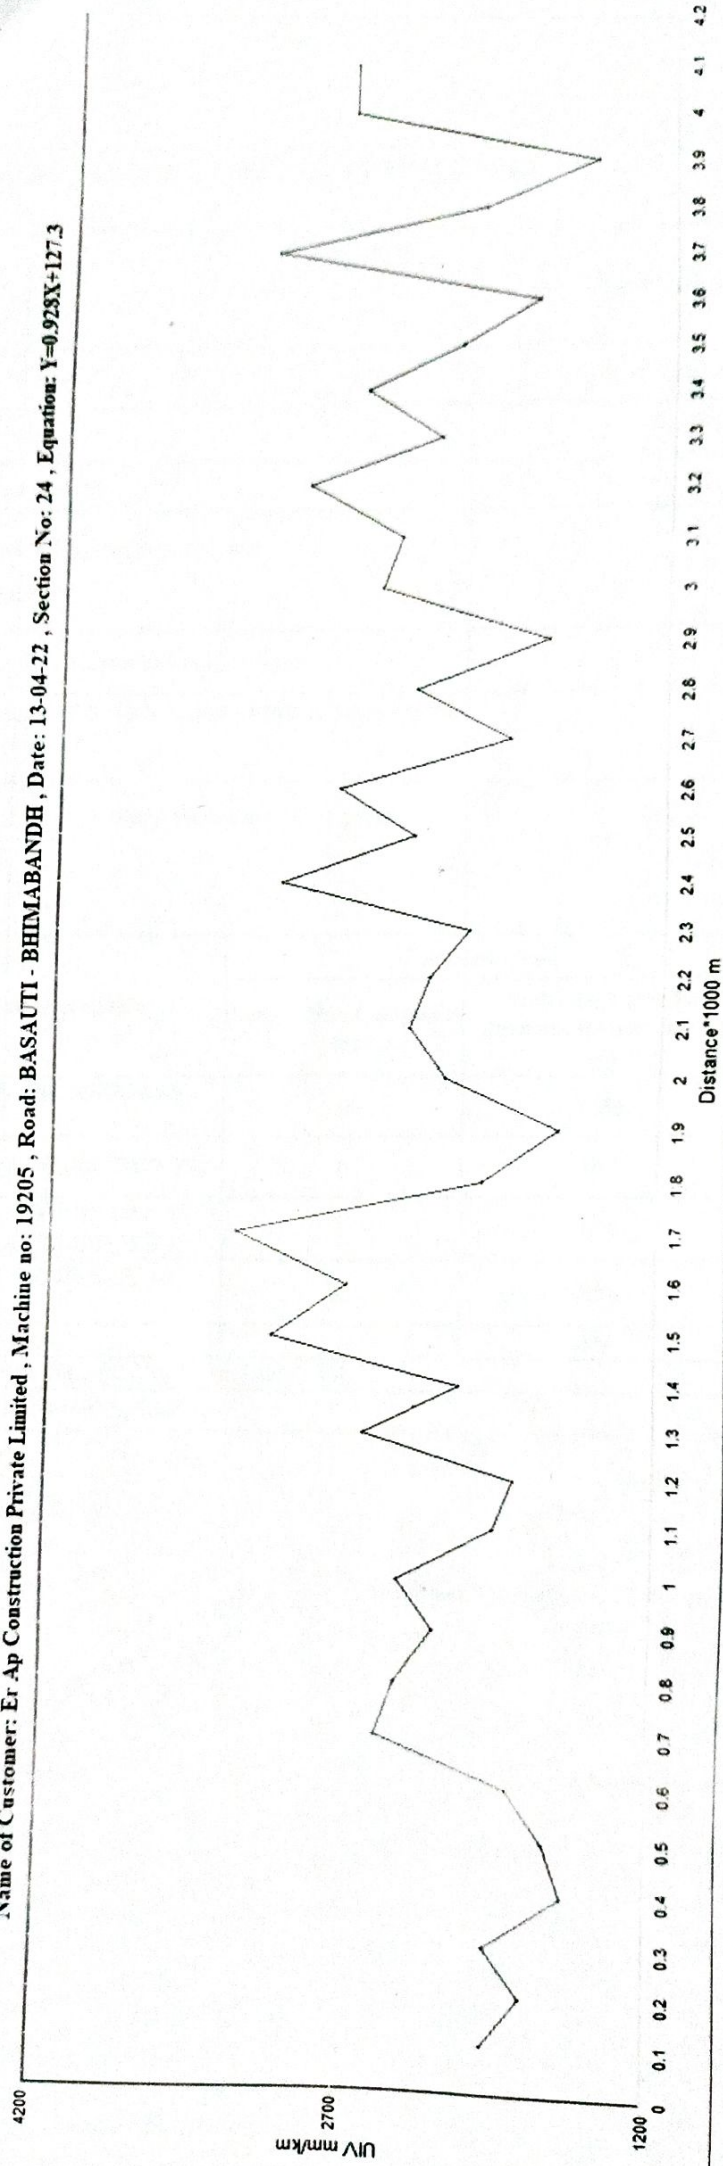
Good		Average				Poor									
< 4000		4001 - 5000				> 5000									
13/04/22	13.32.53	24	100	2200	24.0 cm	18.7 Km/Hr	2400.0 mm/Km	2355	3.24	Good	25.8180476	N	85.0735712	E	Normal
13/04/22	13.33.31	24	100	2300	22.0 cm	19.4 Km/Hr	2200.0 mm/Km	2169	3.02	Good	25.8180476	N	85.0735712	E	Normal
13/04/22	13.34.18	24	100	2400	32.0 cm	17.6 Km/Hr	3200.0 mm/Km	3097	4.14	Good	25.8180476	N	85.0735712	E	Normal
13/04/22	13.34.57	24	100	2500	25.0 cm	19.1 Km/Hr	2500.0 mm/Km	2447	3.36	Good	25.8180476	N	85.0735712	E	Normal
13/04/22	13.35.18	24	100	2600	28.0 cm	16.5 Km/Hr	2900.0 mm/Km	2819	3.81	Good	25.8180476	N	85.0735712	E	Normal
13/04/22	13.35.39	24	100	2700	20.0 cm	16.6 Km/Hr	2000.0 mm/Km	1983	2.78	Good	25.8180476	N	85.0735712	E	Normal
13/04/22	13.36.05	24	100	2800	25.0 cm	14.1 Km/Hr	2500.0 mm/Km	2447	3.36	Good	25.8180476	N	85.0735712	E	Normal
13/04/22	13.36.30	24	100	2900	18.0 cm	14.6 Km/Hr	1800.0 mm/Km	1798	2.55	Good	25.8180476	N	85.0735712	E	Normal
13/04/22	13.36.53	24	100	3000	27.0 cm	15.7 Km/Hr	2700.0 mm/Km	2633	3.59	Good	25.8180476	N	85.0735712	E	Normal
13/04/22	13.37.20	24	100	3100	26.0 cm	13.1 Km/Hr	2600.0 mm/Km	2540	3.47	Good	25.8180476	N	85.0735712	E	Normal
13/04/22	13.37.48	24	100	3200	31.0 cm	13.2 Km/Hr	3100.0 mm/Km	3004	4.03	Good	25.8180476	N	85.0735712	E	Normal
13/04/22	13.38.19	24	100	3300	24.0 cm	11.7 Km/Hr	2400.0 mm/Km	2355	3.24	Good	25.8180476	N	85.0735712	E	Normal
13/04/22	13.38.46	24	100	3400	28.0 cm	12.9 Km/Hr	2800.0 mm/Km	2726	3.7	Good	25.8180476	N	85.0735712	E	Normal
13/04/22	13.39.14	24	100	3500	23.0 cm	12.7 Km/Hr	2300.0 mm/Km	2262	3.13	Good	25.8180476	N	85.0735712	E	Normal
13/04/22	13.39.39	24	100	3600	19.0 cm	14.4 Km/Hr	1900.0 mm/Km	1890	2.67	Good	25.8180476	N	85.0735712	E	Normal
13/04/22	13.40.19	24	100	3700	33.0 cm	9.3 Km/Hr	3300.0 mm/Km	3190	4.26	Good	25.8180476	N	85.0735712	E	Normal
13/04/22	13.40.49	24	100	3800	22.0 cm	12.1 Km/Hr	2200.0 mm/Km	2169	3.02	Good	25.8180476	N	85.0735712	E	Normal
13/04/22	13.41.22	24	100	3900	16.0 cm	10.8 Km/Hr	1600.0 mm/Km	1612	2.31	Good	25.8180476	N	85.0735712	E	Normal
13/04/22	13.41.53	24	100	4000	29.0 cm	11.7 Km/Hr	2900.0 mm/Km	2819	3.81	Good	25.8180476	N	85.0735712	E	Normal
13/04/22	13.42.17	24	100	4100	29.0 cm	14.7 Km/Hr	2900.0 mm/Km	2819	3.81	Good	25.8180476	N	85.0735712	E	Normal








Name of Customer: Er Ap Construction Private Limited, Machine no: 19205, Road: BASAUTI - BHIMABANDH, Date: 13-04-22, Section No: 24, Equation: $Y=0.928X+127.3$





 Basant Kumar

 23/06/22

 Ar 2.
