

STANDRAD FORMAT FOR ROADS QUARTERLY STATEMENT

1	Name of the Road	Mehandia Usari Road - Abgila		
2	Batch No.	RM/AR/ARW/19/0007		
3	Project ID	10603102013		
4	Total Length of Road (in Km)	2.54		
5	Length of Road to Meet Required Service Level [Completed length] (in Km) (1)	2.5		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule (Agreement Amount for Maintenance) (in Lakh)	21.56998		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) (2)	1.07850		
Compliance Criteria	Standard Job Description	Non-Compliant		Reduction Payment (6) = (3) / (1) * (2) * (4)
		Length Non Compliant (3)	Weighted Value for Payment Reduction (%) (4)	
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0.00000
II	SHOULDERS AND EMBANMENTS	0	10%	0.00000
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0	15%	0.00000
IV	SIGNAGE AND ROAD SAFETY	0	10%	0.00000
V	VEGATAION		5%	0.00000
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0.00000
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh) [6]				1.07850

Date of inpection by E/I or his agent Prepared by
Contractor's self Control unit

Date

Signature of person inspecting road

Name and Designation of person inspecting road
(Signature)

Certify by E/I (signature) Date

Requisition Format for Scheme Head - MR (3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)													
Name of Works Division :- Arwal			SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT										
Government of Bihar OM01 Rural works Department			To: Executive Engineer RWD Works Division Arwal Date: _____ Position: A.E										
Road From- Mehandia Usari Road - Abgila Length of Road: 2.54 KM Period : From..... Inspector: A.E RWD Sub Division, Karpi													
Standard Work item		Work	Units of work required in each kilometre										Comments
S No	Name	Units	1	2	3	4	5	6	7	8	9	10	
OM100 Sealed Pavement													
OM101	Pothole Patching	m2	Nil	Nil	Nil	Nil	Nil						No. Pothole found
OM102	Surface Depression and Rut Patching	m2	Nil	Nil	Nil	Nil	Nil						No Surface Depression and Rut Patching found
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil	Nil						No Crack Sealing found
Surface Treatment													
OM104	(a) Loss of Aggregate (Surface Ravelling)	m2	Nil	Nil	Nil	Nil	Nil						No Loss of Aggregate (Surface Ravelling) found
	(b) Bleeding/Flushing	m2	Nil	Nil	Nil	Nil	Nil						No Bleeding/Flushing Required
	(c) Crocodile Cracking	m2	Nil	Nil	Nil	Nil	Nil						No Crocodile Cracking found
OM105	Edge Repair	m2	Nil	Nil	Nil	Nil	Nil						No Edge Repair Required
OM106	Digouts	m2	N/A	N/A	N/A	N/A	N/A						
OM107	Concrete Pavement	m3	N/A	N/A	N/A	N/A	N/A						
Other activities													
OM200 Shoulder													
Unsealed Shoulder			No										
OM201	(a) Edge Drop off	Lm	Nil	Nil	Nil	Nil	Nil						No Edge Drop off Required
	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil	Nil	Nil	Nil						Defects rectified within stipulated time
	(c) Holding Water	Lm	Nil	Nil	Nil	Nil	Nil						No Holding water found
OM202	Embankment Repair	No	Nil	Nil	Nil	Nil	Nil						No Embankment Repair Required
	Other Activities (Raincut)		3%	1%	2%	Nil	Nil						Defects rectified within stipulated time

ROAD NAME: Mehandia Usari Road - Abgila

CONT.NAME:-R K Construction & Co

$$Y = 0 * X^2 + 1.136 * X + 132.5$$

$$X = 8500$$

$$Y = 9788$$

(R) RURAL ROAD
Good Average Poor
<4000 4001-5000 >5001

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	UJIV	CATEGORY ROAD	IRI	Latitude	Longitude	Event
10/7/22	10:23:31	58	0.1	220	30.3	2200	2631 G		3.58	25.131923	84.59838	Normal
10/7/22	10:24:0	58	0.1	260	30.3	2600	3086 G		4.13	25.131278	84.59776	Normal
10/7/22	10:24:8	58	0.1	250	30.3	2500	2972 G		3.99	25.130572	84.597053	Normal
10/7/22	10:24:8	58	0.1	320	30.3	3200	3767 G		4.93	25.129903	84.59643	Normal
10/7/22	10:24:8	58	0.1	220	30.3	2200	2631 G		3.58	25.129212	84.596295	Normal
10/7/22	10:24:8	58	0.1	260	30.3	2600	3086 G		4.13	25.128768	84.597087	Normal
10/7/22	10:24:43	58	0.1	260	30.3	2600	3086 G		4.13	25.12815	84.597928	Normal
10/7/22	10:25:0	58	0.1	250	30.3	2500	2972 G		3.99	25.127538	84.598	Normal
10/7/22	10:25:19	58	0.1	220	30.3	2200	2631 G		3.58	25.12707	84.599225	Normal
10/7/22	10:25:19	58	0.1	260	30.3	2600	3086 G		4.13	25.126348	84.599612	Normal
10/7/22	10:26:0	58	0.1	210	10.1	2100	2518 G		3.44	25.12583	84.60015	Normal
10/7/22	10:26:0	58	0.1	250	10.1	2500	2972 G		3.99	25.125495	84.601077	Normal
10/7/22	10:26:29	58	0.1	240	10.1	2400	2858 G		3.85	25.125252	84.602103	Normal
10/7/22	10:26:29	58	0.1	310	10.1	3100	3654 G		4.8	25.125023	84.602995	Normal
10/7/22	10:26:29	58	0.1	300	10.1	3000	3540 G		4.66	25.124112	84.60271	Normal
10/7/22	10:27:4	58	0.1	310	10.1	3100	3654 G		4.8	25.123477	84.603198	Normal
10/7/22	10:27:4	58	0.1	210	10.1	2100	2518 G		3.44	25.12267	84.602912	Normal
10/7/22	10:27:4	58	0.1	250	10.1	2500	2972 G		3.99	25.122057	84.602288	Normal
10/7/22	10:27:39	58	0.1	240	10.1	2400	2858 G		3.85	25.121162	84.602205	Normal
10/7/22	10:28:0	58	0.1	210	10.1	2100	2518 G		3.44	25.120288	84.60177	Normal
10/7/22	10:28:14	58	0.1	250	10.1	2500	2972 G		3.99	25.119425	84.601447	Normal
10/7/22	10:28:14	58	0.1	320	20.2	3200	3767 G		4.93	25.119335	84.600487	Normal
10/7/22	10:28:14	58	0.1	210	10.1	2100	2518 G		3.44	25.11856	84.600235	Normal
10/7/22	10:29:0	58	0.1	250	10.1	2500	2972 G		3.99	25.1177	84.600505	Normal
10/7/22	10:29:25	58	0.1	270	10.1	2700	3199 G		4.26	25.116915	84.599982	Normal
10/7/22	10:29:25	58	0.1									
AVERAGE							3017					

10/7/22


J.E.

10/7/22
A.E.

11/10/22

FILE NO. : 1153 - Copy X1s, SECTION NO. : 38, Egn : $\gamma = \psi - \chi$ Z *

Name of Customer : R K Construction Co, Name of Work/ Road : Mehandia Usari Road - Abgila Lab Job number :

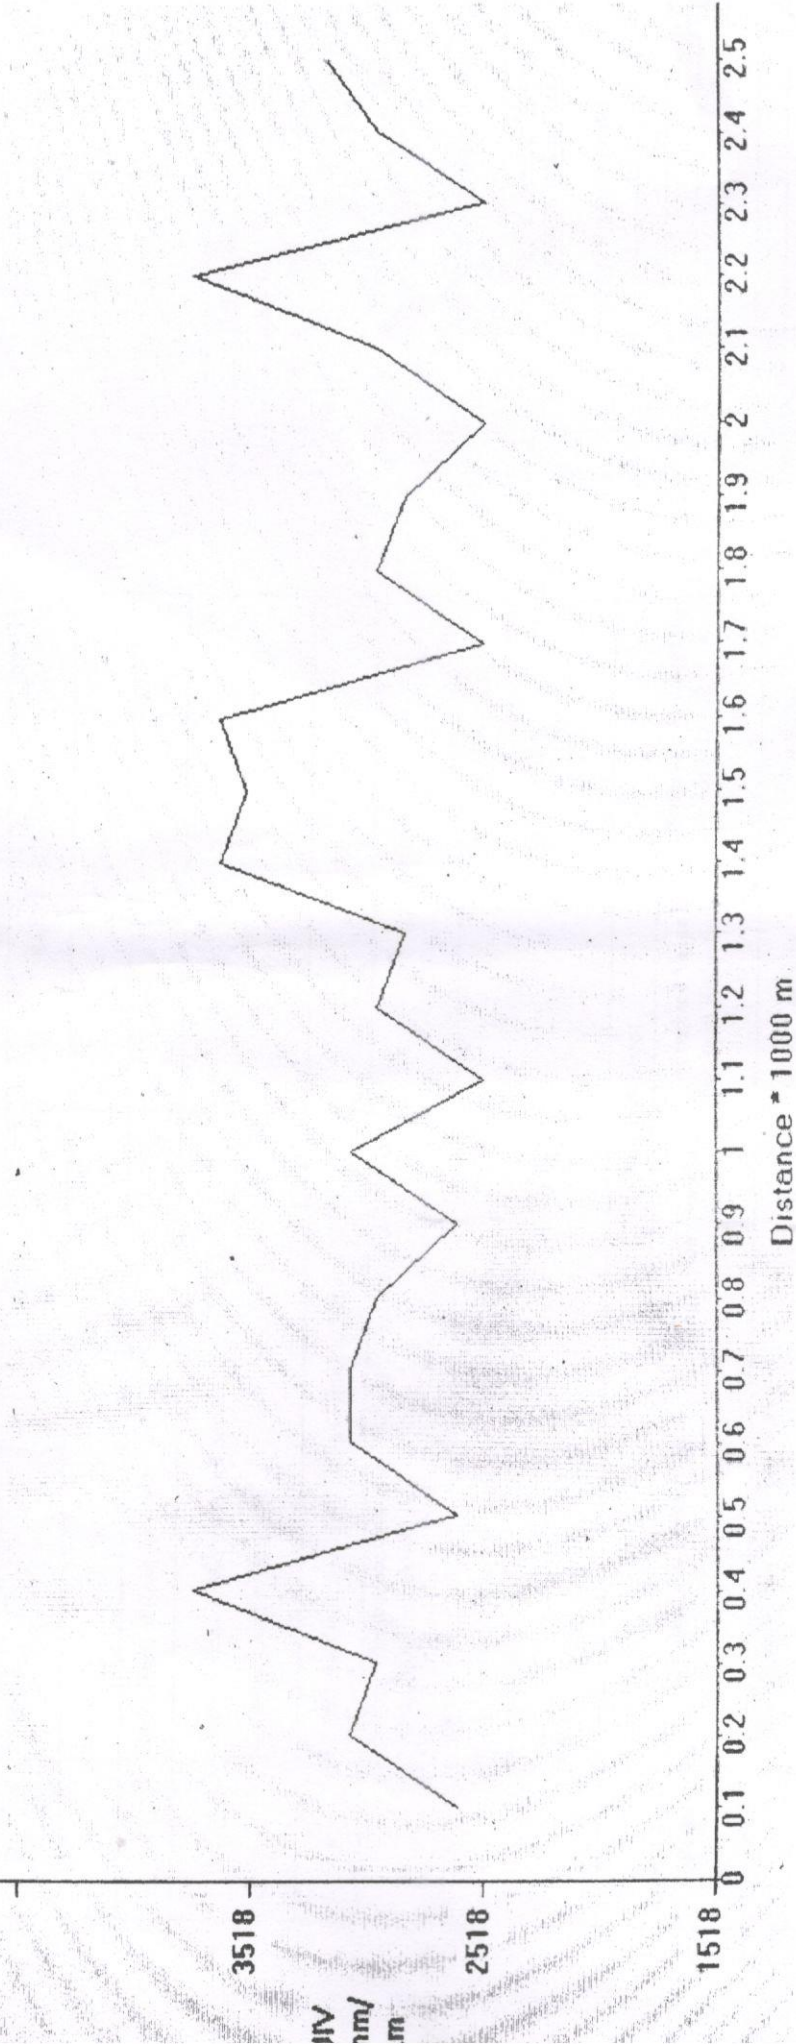

Handwritten signature
10/11/2011

Handwritten signature
10/11/2011

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, अरवल।

पत्रांक 944

अरवल / दिनांक 11/10/22

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, अरवल

सेवा में,

नोडल पदाधिकारी (MR 3054)
ग्रामीण कार्य विभाग
पटना, बिहार

विषय :- नई अनुरक्षण नीति-2018MR (3054) योजना के अंतर्गत पथ में कराये गये कार्य के विरुद्ध आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपरोक्त विषय के संबंध में सूचित करना है कि नई अनुरक्षण नीति-2018 MR (3054) योजना के अंतर्गत पथ में कराये गये कार्य के लिए संवेदक को भुगतान करने हेतु अधियाचना विहित प्रपत्र में भरकर आवश्यक कार्यवाही हेतु समर्पित की जाती है।

अनु :- यथोक्त।

विश्वासभाजन




कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, अरवल।

11/10/22

Name of Works Division:- Atwal

Maintenance Requisition Formate for Scheme Head- MR (3054) Under

Road Details					Agreement									
Sl No	Name of Roads	Batch No.	Project ID	Actual Date of Completion	AA Details			Agreement						
					Main Work Amount (in Lakh)	Maintenance Amount (in lakh)	Main Work Amount (in Lakh)	Agreement-1	Agreement-2	Agreement-3	Agreement-4	Agreement-5	Total Maintenance	Length (in km)
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15
1	Bhadasi Pakharpur Rd. - Daryapur	RM/AR/A RW/19/0 002	10603102006	5/11/2020	17.623	9.203	17.33	0.61336	1.12456	2.84462	1.45907	3.0679	9.10951	0.93
2	Kardi - Karthua via Dhamai	RM/AR/A RW/19/0 002	10603102008	5/11/2020	29.797	15.959	29.289	1.07451	1.99173	4.91815	2.5373	5.28791	15.8096	1.59
3	Mehandia Usari Road - Abgila	RM/AR/A RW/19/0 007	10603102013	12/2/2021	48.713	25.564	50.7454	1.56672	2.48148	6.69468	3.54514	7.28196	21.57	2.54
4	Rasulpur Parvari - Salempur	RM/AR/A RW/19/0 002	10603102016	5/11/2020	18.318	9.277	18.005	0.62707	1.14852	2.85161	1.48493	3.07647	9.1886	0.92
5	Bhadasi Pali Road Patnak Bigha	RM/AR/A RW/19/0 002	10603102030	5/11/2020	24.286	12.654	23.866	0.85877	1.57176	3.89238	2.01981	4.19762	12.5403	1.26
6	Samar Telpa - Kharasin	RM/AR/A RW/19/0 007	10603102065	12/2/2021	61.14	33.648	63.6137	2.06755	3.28502	8.93848	4.37913	9.60528	28.2755	3.37
Total					199.87700	106.30500	202.84912	6.80798	11.60307	30.13992	15.42538	32.51714	96.49349	10.61


Executive Engineer
 R.W.D (M) Division
 11/10/22

Bihar Rural Road Maintenance Policy-2018

Actual Maintenance Expenditure						Current Maintenance Demand										Remarks
1st Year Maintenance	2nd Year Maintenance	3rd Year Maintenance	4th Year Maintenance	5th Year Maintenance	Total Maintenance Expenditure	Length as per Bump Report	IRI As per bump Report	1st QTR Maintenance	2nd QTR Maintenance	3rd QTR Maintenance	4th QTR Maintenance	5th QTR Maintenance	6th QTR Maintenance	7th QTR Maintenance	Total	
16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	32
0.000	0.000	0.000	0.000	0.000	0.000	0.9	3325	0.45548	0.45548	0.45548	0.45548	0.000	0.000	0.000	1.82192	
0.000	0.000	0.000	0.000	0.000	0.000	1.5	3214	0.79048	0.79048	0.79048	0.79048	0.000	0.000	0.000	3.16192	
0.000	0.000	0.000	0.000	0.000	0.000	2.5	3017	1.07850	1.07850	1.07850	0.000	0.000	0.000	0.000	3.23550	
0.000	0.000	0.000	0.000	0.000	0.000	0.9	3060	0.45943	0.45943	0.45943	0.45943	0.000	0.000	0.000	1.83772	
0.000	0.000	0.000	0.000	0.000	0.000	1.2	3028	0.62702	0.62702	0.62702	0.62702	0.000	0.000	0.000	2.50808	
0.000	0.000	0.000	0.000	0.000	0.000	3.3	3116	1.41377	1.41377	1.41377	0.000	0.000	0.000	0.000	4.24131	
								4.82468	4.82468	4.82468	2.33241	0.000000	0.000000	0.000000	16.80645	

Executive Engineer
R.W.D. Works Division

Amul

11/10/22

11/10/22

11/10/22

11/10/22

11/10/22

11/10/22
