

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, पालीगंज।

पत्रांक : 1406 (अनु०)

पालीगंज/दिनांक : 19/10/22

प्रेषक :

कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, पालीगंज।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी,
—सह—सचिव,
बिहार ग्रामीण पथ विकास, अभिकरण
ग्रामीण कार्य विभाग, पटना।

विषय:—शीर्ष—MR, 3054 Under-Bihar Rural Road Maintenance Policy-2018 योजना अन्तर्गत आवंटन का
अधियाचना के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि शीर्ष—MR, 3054 Under-Bihar Rural Road Maintenance Policy-2018 योजना अन्तर्गत पथों का अधियाचना का भौग विहित प्रपत्र में तैयार कर Signed Hard Copy of Recorded IRI के साथ अधियाचना हेतु भेजी जा रही है।

अतः अनुरोध है कि उक्त योजना का आवंटन उपलब्ध करने की कृपा की जाय, ताकि संबंधित का भुगतान हो सके।


अनु०:—यथोक्त।


13/10/22

विश्वनाथराज


13/10/22

कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, पालीगंज।


13/10/22

Requisition Format for Scheme Head -MR (3054) Under Bihar Rural Road Maintenance Policy 2018(Initial Rectification and surface Renewal)

Name Of Work division- Paliganj																		
Sl No	Package	Name Of Road	Project ID as per MIS	Administrative Approval Letter No & Date	Administrative		Agreement Amount		Agreement Date	Date of completion as per Agreement	Actual Date of completion	Value of mrrl(in mrrl/m)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allocated Amount (in Lakh)	Up-to - date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (in KM)	Amount of (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Year Routine Maintenance (in Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	20/0001	Maner Road Canal Naphar Tola East Zone	NEA22000907	LT No 6459 dt. 13.12.2019	1.2	49.74400	29.64800	12.47456	05/MRD/2020-21 & 18.06.202	17.03.2021	24.06.2022	2.60857	25 mm (SDBC)	5.01%	0.00000	0.00000	17.22430	Work done as per specification & verification by a Bump indicator machine 100% Measurement checked by AE & SPM by TE

(Signature)
13/10/22
Sr. Divisional Accounts Officer
Rural Work Department
Works Division Paliganj

(Signature)
13/10/22
Executive Engineer
Rural Works Deptt.
Work Division Paliganj

(Signature)
13/10/22


FORM GFR 19-A

(See Government of India's Decision (1) below Rule-150)
Form of utilisation Certificate up to the end of September 2022



PIU: RWD Works Division , Paliganj

Sl No.	Name of Scheme	Sanction No. & Date with Amount	Amount Received (In Rs.)	Particulars
1	Construction of Rural roads under Rural Road Maintenance Policy 2018		216554097.00	Certified that out of Rs 216554097.00 received during the year 2022-23 in favour of Ex. Engineer, RWD, Works Div. Paliganj Bihar a sum of Rs 215318468.00 has been utilized for the purpose of const of road under Schemes as given in the margin for which it was sanctioned and that the balance of Rs. 1235629.00 remaining unutilized at the end to the period under
Total			216554097.00	

2. Certified that I have satisfied myself that the conditions of which the grants sanction Sanctioned have been duly fulfilled/are being fulfilled and I have exercised the checks to see the money was actually utilised for the purpose for which it was sanctioned.


13/10/22

Sr. Divisional Accounts Officer
Rural Work Department
Works Division Paliganj


13/10/22
Executive Engineer
Rural works Deptt.
Works Division, Paliganj


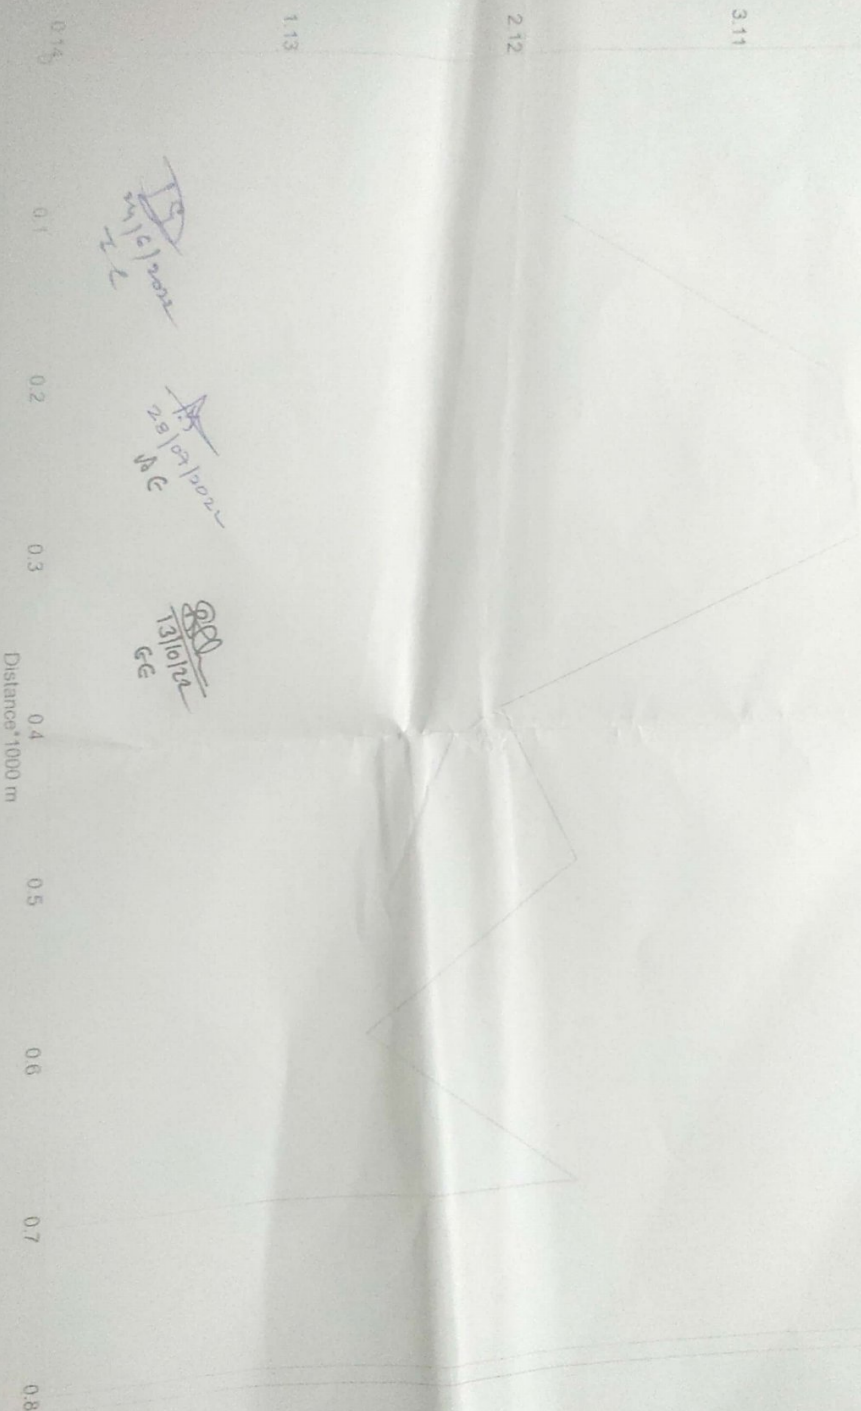
Name of work		Maine Road Canal- Nujhar Tola East Zone													
Name of customer		SANTOSH KUMAR													
(R)Rural Road															
		Good		Average		Poor									
		< 4000		4001 - 5000		> 5000									
Date	Time	Test No	Distancem (m)	Total Distancem (m)	BLM/Fcm	Speed(Km/Hr)	Ultram (m)	Corrected U (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction ¹	Remarks
29/01/22	18:19:21	10	100	100	17.0 cm	12.8 Km/Hr	1700.0 mm/Km	1643	2.35	Good	25.411713	N	84.837229	E	Normal
29/01/22	18:19:51	10	100	200	28.0 cm	17.8 Km/Hr	2800.0 mm/Km	2657	3.01	Good	25.446232	N	84.838179	E	Normal
29/01/22	18:20:10	10	100	300	29.0 cm	18.7 Km/Hr	2900.0 mm/Km	2749	3.73	Good	25.467322	N	84.838179	E	Normal
29/01/22	18:20:30	10	100	400	15.0 cm	16.5 Km/Hr	1500.0 mm/Km	1458	2.12	Good	25.487322	N	84.838179	E	Normal
29/01/22	18:20:49	10	100	500	18.0 cm	19.0 Km/Hr	1800.0 mm/Km	1735	2.47	Good	25.492322	N	84.838179	E	Normal
29/01/22	18:21:07	10	100	600	10.0 cm	21.0 Km/Hr	1000.0 mm/Km	997	1.51	Good	25.492322	N	84.838179	E	Normal
29/01/22	18:26:04	10	100	700	18.0 cm	1.2 Km/Hr	1800.0 mm/Km	1735	2.47	Good	25.450166	N	84.840077	E	Breaker
			0	700				75	0.15	Good					

29/1/22
S.C

29/01/22
A.E

29/01/22
E

Customer: SANTOSH KUMAR, Machine no. 19206, Road: Mahner Road Cannel- Naghar Tola East Zone, Date: 04-02-22, Section No: 10, Equation: $y=0.922x+75.3$



कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, क्षेत्रीय प्रयोगशाला, गुलजारबाग
पटना - 800007

पत्रांक :- 35/MB

पटना/दिनांक : 21-01-2022

प्रेषक,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
क्षेत्रीय प्रयोगशाला, गुलजारबाग पटना-7

सेवा में,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमण्डल पालीगंज

विषय :- योजना / गैर योजना शीर्ष MR-357 अंतर्गत निर्माणाधीन पथ/पुल/पुलिया कार्यों में प्रयुक्त निर्माण सामग्रियों की गुणवत्ता के जाँचफल प्रतिवेदन के संबंध में।

प्रसंग :- कार्यपालक अभियंता / सहायक अभियंता कार्य प्रमण्डल/कार्य अवर प्रमण्डल पालीगंज
का पत्रांक 47 दिनांक 27.12.2021 एवं 49 दिनांक 30.12.2021

महाशय,

उपर्युक्त बिषयक प्रासंगिक पत्र के संदर्भ में योजना / गैर योजना शीर्ष MR-357 अंतर्गत निर्माणाधीन पथ/पुल/पुलिया कार्यों में प्रयुक्त निर्माण सामग्रियों के गुणवत्ता जाँचफल प्रतिवेदन आवश्यक कारवाई हेतु भेजी जाती है जो निम्नवत है:-

क्रम संख्या	पथ/पुल/पुलिया का नाम	जाँच का प्रकार
1.	Naghar main Canal to Naghar Tola East zone	Stone chips (13.2mm to 0.9mm) (i) 50% chips (ii) Bitumen Content for 50%
2.		

अनु० :- यथोक्त

विश्वासभाजन

Y. Khatun
21/01/22

कार्यपालक अभियंता
ग्रामीण कार्य विभाग

क्षेत्रीय प्रयोगशाला, गुलजारबाग पटना - 7

OFFICE OF THE EXECUTIVE ENGINEER

REGIONAL LABORATORY, R. W. D., GULZARBAGH, PATNA - 7

PHYSICAL AND GRADATION TEST OF COARSE AGGREGATE

Name of Project/Road :- Naghar main Canal to Naghar Tola East
 Name of Scheme :- MR 3054
 Name of Agency :- Santosh Kumar
 Nature of sample :- Mix seal (12.5mm to 75mm) Date of Collection/Received :- 12/11/2022
 Location :- 190M Date of Test :- 21/11/2022
 Ref :- Material sent by E.E./A.E./W.D. WORKS Division/Sub Division - Paligani
 vide letter No. 42(3054) dt. 27/12/2021
 Agreement No / Package No. :- 05/MBO/2020-21

Sl. No.	A.I.V.	
	Average Test Value	Required Value(Max)
1.	30%	

Sl. No.	Sieve Size in (mm)	Weight of Sample Taken Kgs 19.480				Required Value		Remarks
		Weight Retd.	% of Wt. Retained	% of Cumm. Retained	% of Passing	Type A	Type B	
1	2.0	0.00	0.00	0.00	100	—	100	
2	4.75	0.347	1.78	1.78	98.22	100	88-100	
3	7.5	0.347	1.78	3.56	96.44	52-88	33-52	
4	15	0.347	1.78	5.34	94.66	14-38	5-25	
5	30	0.347	1.78	7.12	92.88	0-5	0-5	

Regional Laboratory
 R. W. D. Gulzarbagh
 Patna - 7

Regional Laboratory
 R. W. D. Gulzarbagh
 Patna - 7

Regional Laboratory
 R. W. D. Gulzarbagh
 Patna - 7

OFFICE OF THE EXECUTIVE ENGINEER

REGIONAL LABORATORY, R. W. D., GULZARBAGH, PATNA - 7

PHYSICAL AND GRADATION TEST OF COARSE AGGREGATE

Name of Project/Road :- Naghar main canal to Naghar Pola East zone.

Name of Scheme:- MR-3554

Name of Agency :- Santosh Kumar

Nature of sample : Semi Dense Bituminous Concrete Date of Collection/Received :- 12/11/2022

Location :- 260m/rf Date of Test :- 21/11/2022

Ref :- Material sent by E.E./A.E. R.W.D. WORKS Division/Sub Division - Paligani

vide letter No. 47(43) Dt. 27/12/2021

Agreement No / Package No. : 05/M30/2020-21

Sl.No	A.I.V.	
	Average Test Value	Required Value(Max)
1.		30%

Sl. No	Sieve Size in (mm)	Weight of Sample Taken Kgs 19.460					Remarks
		Weight Retd.	% of Wt. Retained	% of Cumm. Retained	% of Passing	Required Value	
1	13.2	0.000	0.00	0.00	100	100	
2	9.5	1.041	5.35	5.35	94.65	90-100	
3	4.75	8.932	45.90	51.25	48.75	35-51	
4	2.36	2.578	13.25	64.50	35.50	24-39	
5	1.18	1.703	8.75	73.25	26.75	15-30	
6	0.300	2.170	11.15	84.40	15.60	9-19	
7	0.075	1.917	9.85	94.25	5.75	3-8	

R.A. 21/11/2022

Regional Laboratory
R.W.D. Guljarbagh
patna - 7

21/11/2022

A.E.
Regional Laboratory
R.W.D. Guljarbagh
patna - 7

21/11/22

E. E.
Regional Laboratory
R.W.D. Guljarbagh
patna - 7

OFFICE OF THE EXECUTIVE ENGINEER

REGIONAL LABORATORY, R. W. D., GULJARBAGH, PATNA - 7

Name of Project/Road :- Naghar Main Canal to Naghar Tola End zone
Name of Scheme:- NR-3554
Name of Agency :- Sanjesh Kumar
Nature of sample :- Bitumen content for - SORC
Location :- 820 m

Ref :- Material sent by E.E./A.E.R.W.D. WORKS Division/Sub Division

Agreement No / Package No. : 05/1120/2020-21

Date of Collection/Received :- 12/11/2022
Date of Test :- 21/11/2022
vide letter No. 49 Dt. 30.12.2021

SL. NO.	SAMPLE NO.	1	2	3	REMARKS
1	Wt. of mix taken before extraction (a)	507.00	500.00	502.00	
2	Wt. of Dry chips after extraction (b)	481.55	475.00	476.90	
3	Percentage of bitumen (in the mix) $[(a-b)*100/a]$	5.02	5.00	5.00	
4	Average % bitumen	5.01			

Sanjesh Kumar
21/11/2022

Regional Laboratory
R. W. D. Guljarbagh patna - 7

Sanjesh Kumar
21/11/2022

Regional Laboratory
R. W. D. Guljarbagh patna - 7

Sanjesh Kumar
21/11/2022

Regional Laboratory
R. W. D. Guljarbagh patna - 7
