

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, डुमराँव ।

पत्रांक 1001/अनु

डुमराँव, दिनांक 29-09-2022

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, डुमराँव ।

सेवा में,

नोडल पदाधिकारी,
3054(MR)
ग्रामीण कार्य विभाग,
बिहार, पटना ।

विषय:— शीर्ष MR New Maintenance Policy 2018 योजना अन्तर्गत 5(पाँच) वर्षीय अनुरक्षण का
आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपर्युक्त विषयक के संबंध में कहना है कि शीर्ष MR New Maintenance Policy 2018
योजना अन्तर्गत 5(पाँच) वर्षीय अनुरक्षण के पथों का पथवार मांगी जाने वाली आवंटन की सूची पत्र के
साथ भवदीय के अवलोकनार्थ एवं आवश्यक कार्रवाई हेतु समर्पित की जा रही है।

सूचनार्थ सादर समर्पित।

अनु०— यथोक्त

विश्वासभाजन

[Signature]
29/09/2022

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमण्डल, डुमराँव।

[Signature]
29/09/2022

FORM GFR 19-A

(See Government of India's Decision (I) below Rule-150)

Form of Utilization Certificate up to the Date 31 Mar 2021

RWD, Works Division, Dumraon

Sl. No	Name of Scheme	Sanction No. & Date with Amount (in lacs Rs.)	Amount Received (in lacs Rs.)	Particulars
1	Maintenance of Rural roads Maintenance Policy-2018 under MR-3054	Allotment Received Through CFMS vide Letter - Date-	0.000 Lakh	Certified that out of Rs. 0.0 lacs of grants-in-aid sanctioned during the years 2022-23 in favors of E-in-C, RWD Bihar, Patna a sum of Rs. 0.0 lacs has been utilized for the purpose of MR (3054) Schemes as given in the margin for which it was sanctioned and that the balance of Rs. 0.000 Lacs remaining unutilized at the end of the period under report.
Total :-			Rs.- 0.0 Lakh	

1. Certified that I have satisfied myself that the conditions on which the grants-in-aid was sanctioned have been duly fulfilled/ are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.


Kind of Checks exercised: -

- Works have been supervised by Executive Engineer/ Superintending Engineer.
- Periodical inspection has been conducted by Executive Engineer/ Superintending Engineer.
- Construction materials have been tested.
- Measurements have been recorded in the MBs and test check conducted by the Assistant Engineer/ Executive Engineer.
- All other codal formalities have been observed.

2. Physical Progress achieved :-

- Maintenance of Road Works.
- Maintenance of CD works


D. A. O.
RWD Works, Division, Dumraon


Executive Engineer
RWD Works, Division, Dumraon

12/09/2022

Acquisition Format for Scheme Head - 5 Year Maintenance of MR(3054) under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and surface Renewal)

Name of Division :- Dumraon

Name of Circle :- Ara

Sl. No.	Name of Road	Name of Agency	Batch No	Project ID as per MIS	Administrative Letter No & Date.	Administrative Approval (AA)		Agreement Amount (in Lac)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Current Maintenance Demand (In Lacs)					Remarks.
						Length (in km)	Amount of (in Lakh)	Initial Rectification with surface Renewal	5 Years Routine Maintenance (in Lakh)				1st Qtr Maint Demand	2nd Qtr Maint Demand	3rd Qtr Maint Demand	4th Qtr Maint Demand	Total Demand	
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	Baghathpur Railway Gunt to Dhothampurva	JAWAHAR LAL YADAV	RM/BU/DUM/19/0003	10402001011	It. No 2014 dt. 02-July-2019	0.700	21.646	12.706	5.26133	13MBD/2019-20 & 10.12.2019	9-Sep-20	1/10/2020	0.26307	0.26307	0.26307	0.26307	1.05228	
2	BRAHMPUR BAGEN ROAD - KHIOCHERIA	JAWAHAR LAL YADAV	RM/BU/DUM/19/0003	10401902027	It. No 2014 dt. 02-July-2019	3.16	104.432	60.231	26.72399	13MBD/2019-20 & 10.12.2019	9-Sep-20	10/9/2020	1.3362	1.3362	1.3362	1.3362	5.3448	
3	BRAHMPUR BAGEN ROAD - RAHATHUA	JAWAHAR LAL YADAV	RM/BU/DUM/19/0003	10401902028	It. No 2014 dt. 02-July-2019	3.631	121.842	70.285	31.13961	13MBD/2019-20 & 10.12.2019	9-Sep-20	1/10/2020	1.55698	1.55698	1.55698	1.55698	6.22792	
4	BRAHMPUR PETROL PUMP - PARASIA	JAWAHAR LAL YADAV	RM/BU/DUM/19/0003	10401902029	It. No 2014 dt. 02-July-2019	1.750	51.571	30.009	12.77193	13MBD/2019-20 & 10.12.2019	9-Sep-20	3/1/2021	0.63860	0.63860	0.63860	-	1.9158	
5	CHANDANPURA BAZAR - CHANDRAPURA	JAWAHAR LAL YADAV	RM/BU/DUM/19/0003	10401902034	It. No 2014 dt. 02-July-2019	0.500	15.246	9.124	3.47517	13MBD/2019-20 & 10.12.2019	9-Sep-20	1/10/2020	0.17376	0.17376	0.17376	0.17376	0.69504	
6	NH 84 DEOKULI SCHOOL - KOTHA	JAWAHAR LAL YADAV	RM/BU/DUM/19/0003	10401902052	It. No 2014 dt. 02-July-2019	1.600	50.893	29.595	12.69504	13MBD/2019-20 & 10.12.2019	9-Sep-20	1/10/2020	0.63475	0.63475	0.63475	0.63475	2.539	
7	SUKARAIL LOCK - NABAHAMDIH	JAWAHAR LAL YADAV	RM/BU/DUM/19/0008	10402002054	It. No 2014 dt. 02-July-2019	2.960	97.961	55.284	26.29856	18MBD/2019-20 & 7.01.2020	6-Oct-20	9/10/2020	1.31493	1.31493	1.31493	1.31493	5.25972	
8	Salsala Natar Pool - Mahadev Ganj via Salsala, Ramnagar	JAWAHAR LAL YADAV	RM/BU/DUM/19/0008	NEA220001776	It. No 2014 dt. 02-July-2019	3.225	104.059	59.136	27.08233	18MBD/2019-20 & 7.01.2020	6-Oct-20	9/10/2020	1.35412	1.35412	1.35412	1.35412	5.41648	
9	NH-30 - Samosar natar Pool Path	JAWAHAR LAL YADAV	RM/BU/DUM/19/0008	NEA220001791	It. No 2014 dt. 02-July-2019	2.300	76.747	43.353	20.52623	18MBD/2019-20 & 7.01.2020	6-Oct-20	9/10/2020	1.02631	1.02631	1.02631	1.02631	4.10524	
10	NH-30 - Teerthia Via Padniya	JAWAHAR LAL YADAV	RM/BU/DUM/19/0008	NEA220001920	It. No 2014 dt. 02-July-2019	1.650	54.809	31.701	14.04099	18MBD/2019-20 & 7.01.2020	6-Oct-20	9/10/2020	0.70205	0.70205	0.70205	0.70205	2.8082	
11	Purniya - B.C. Pool Path Via Babaganj English, Koriyadh	JAWAHAR LAL YADAV	RM/BU/DUM/19/0008	NEA220001921	It. No 2014 dt. 02-July-2019	2.300	80.638	46.619	20.52623	18MBD/2019-20 & 7.01.2020	6-Oct-20	9/10/2020	1.02631	1.02631	1.02631	1.02631	4.10524	

DIVISIONAL ACCOUNTS OFFICER
R.W.D. Works Division,
Dumraon

Date: 26/09/2022

Executive Engineer
Rural Works Department
Works Division Dumraon

Date: 26/09/2022

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

PIU Name :- RWD, Works Division, Dumraon

1	Name of the Road	BRAHMPUR BAGEN ROAD - KHHOCHERIA		
2	Batch No.	RM/BU/DUM/19/0003		
3	Project ID	10401902027		
4	Total Lenth of Road (in KM)	3.160		
5	Length of Road to Meet Required Service Level [Completed length](in Km) [1]	3.160		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	26.72399		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	1.33620		
Compliance Criteria	Standard Job Description	Non-Compliance		Reduction Payment [6]=[3]/[1]*[2]*[4]
		Length Non-Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0.00
II	SHOULDERS AND EMBANMENTS	0	10%	0.00
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0	15%	0.00
IV	SIGNAGE AND ROAD SAFETY	0	10%	0.00
V	VEGATION	0	5%	0.00
TOTAL PAYMENT REDUCTION FOR THE QUARTER (IN Lakh) [5]				0.00000
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh) [6]				1.33620

Date of inspection by E/I or his agent
Prepare by Contractor's self Control unit

Name and Designation of person inspecting road

Date

AKW
22/09/21
JE

AE
24.08.2023
AE

(Signature)

Gopal
19/09/2021

Signature of person inspecting road

Certify by E/I [signature] Date:-
Executive Engineer
Rural Works Department
Works Division, Dumraon

Requisition Formlet for Scheme Head-MR-(3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

RWD, Works Division, Dumraon

Government Of Bihar

OM01

Rural Works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From: BRAHMPUR BAGEN ROAD - KHHOCHERLA
Length of Road : 3.16 KM
Inspector :-

To:-

Executive Engineer
RWD, Works Division Dumraon

Date:-

Position :-

No	Standard Of Work Item Name	Work Unit	Unit Of Required in each Kilometer																	Comments
			1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	
OM100	Sealed pavement																			
OM101	Pothole Patching	m ²	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	No pothole found
OM102	Surface Depression and Rut patching	m ³	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	No Surface Depression and Rut patching found
OM103	Crack Sealing	Lm	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	No crack found
	Surface Treatment		NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	Not required
OM104	(a) Loss of Aggregate (Surface/Ravelling)	m ²	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	No Loss of Aggregate (Surface ravelling) found
	(b) Bleeding / Flushing	m ²	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	No bleeding / flushing found
	Crocodile Cracking	m ²	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	No Crocodile cracking found
OM105	Edge Repair	m ²	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	Notified & repaired
OM106	Digouts	m ²	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	
OM107	Concrete pavement	m ³	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	
	Other activities																			
OM200	Shoulder																			
	Unsealed Shoulder																			
	(a) Edge Drop-off	Lm	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	No Edge Drop off found
OM201	(b) Roughness, Scouring or Potholes	Lm	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	No Roughness, Scouring or Potholes found
	(c) Holding water	Lm	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	No Holding Water Found
OM202	Embankment Repair	M ³	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	Notified & repaired
	Other activities (Rain Cuts)		N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	
OM300	Drainage including culverts major																			
OM301	Surface Drains & Verge	Lm	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	NA
OM302	Culvert Cleaning	No	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	DONE
OM303	Culvert and pit Repair	M ³	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	DONE
	Other activities (Whitewashing)	M ²	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	Not required

APW
22/09/21
SE

WV
24.08.2020
AE

No	standard Of Work Item Name	Work Unit	Unit Of Required in each Kilometer										Comments
			1	2	3	4	5	6	7	8	9	10	
OM400	Vegetation												
	Grass Control												
OM401	(a) Roadside- General Tidy	Ha	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	Done
	(b) Clear near Safety signs, kilometer posts and roadside	Ha	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	Done
	Tree and Shrub Management	No	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	Done
OM402	Cutting Of Branches Of Trees	No	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	Done
	Cutting Of Shrubs From Road Way	No	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	Done
	Other activities (Trimming of Grass)	M ²	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	Done
OM500	Safety Signage and Road												Not Required
OM501	Signs Maintenance	No	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	Not Required
OM502	Guard Stones	Lm	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	N.A.
OM503	Distance Stones	No	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	N.A.
OM504	Road Marking	M ²	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	Not Required
	Other activities												

Alfon
22/09/21
JE

W/L
24/08.2022
AE

Executive Engineer
Rural Works Department
Works Division, Dumraon
22/09/2022

Name of Customer : JAWAHAR LAL YADAV
 Name of Work/ Road : Brahmpur began road to Khochena
 Lab Job number :
 Date : 9/21/2021
 Section No. : 39


Test Date : 9/21/2021 Road Name : npur began road to Khochena
 Machine No : 312 Road Type : (R) RURAL ROAD
 Start S No : Side :
 Start E No : Interval
 Weather : UV Range : 1675 To 4000 1000 mm/km
 Start Location : n began road Dist Range : 0 To 33 01 * 1000 m
 End Location : Khochena Equation : $Y = 0 * X^2 + 1.047 * X - 63.36$

Print

Generate Report and Graph

Redraw Graph

Map View

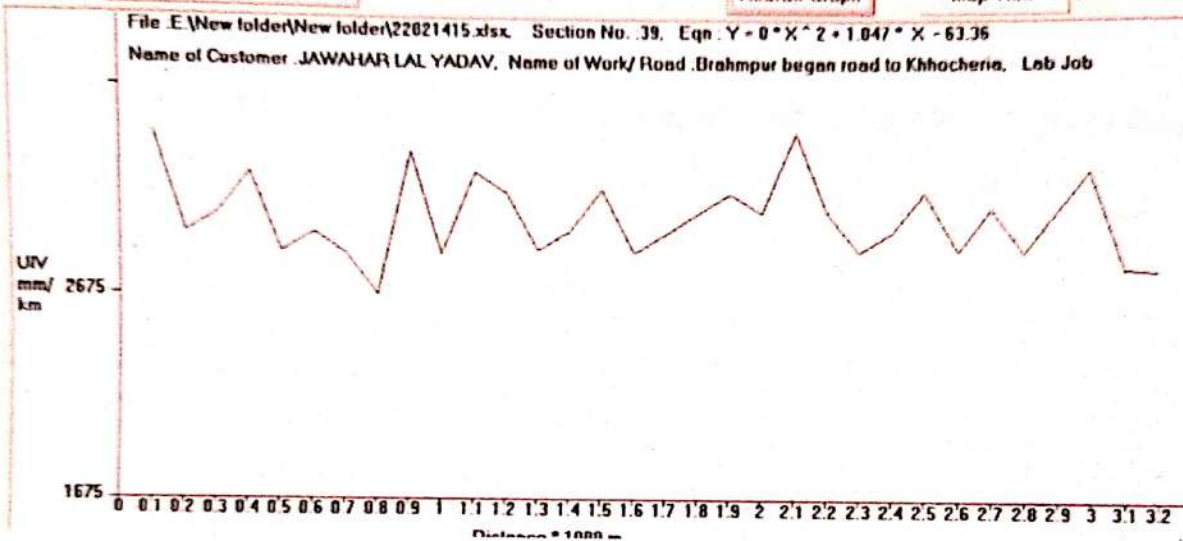

Aksh
 22/09/21
 JE

ht
 24.08.2020
 AE

Gopal
 19/09/2021
 AE

Name of Road :-KHOCHERIYA TO BRAHMPUTRA BAGEN PATH . (MACHINE - BUXAR)

Date	Time	Section	Length	Bumps	Speed	OR	IRI	GATEGORY	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	mm/km	Road			
21/9/21	14:17:45	39	0.1	340	0	3400	3462	G	25.523332	84.270572	Normal
21/9/21	14:18:0	39	0.1	290	30.2	2900	2973	G	25.523345	84.271532	Normal
21/9/21	14:18:33	39	0.1	300	31.5	3000	3069	G	25.523348	84.272525	Normal
21/9/21	14:19:0	39	0.1	320	32.5	3200	3265	G	25.523227	84.27348	Normal
21/9/21	14:20:0	39	0.1	280	30.2	2800	2881	G	25.5232	84.27446	Normal
21/9/21	14:20:43	39	0.1	290	31.5	2900	2973	G	25.52349	84.275185	Curve
21/9/21	14:21:0	39	0.1	280	32.5	2800	2872	G	25.523343	84.27616	Normal
21/9/21	14:21:18	39	0.1	260	30.2	2600	2675	G	25.523402	84.277103	Normal
21/9/21	14:21:53	39	0.1	330	31.5	3300	3364	G	25.523357	84.278113	Culvert
21/9/21	14:22:0	39	0.1	280	30.2	2800	2872	G	25.523352	84.279073	Normal
21/9/21	14:22:28	39	0.1	320	31.5	3200	3265	G	25.523425	84.28003	Normal
21/9/21	14:23:4	39	0.1	310	32.5	3100	3167	G	25.523887	84.280707	Normal
21/9/21	14:23:44	39	0.1	280	30.2	1600	2885	G	25.52364	84.28168	Normal
21/9/21	14:24:0	39	0.1	290	31.5	2900	2981	G	25.523762	84.282677	Normal
21/9/21	14:24:14	39	0.1	310	30.2	3100	3180	G	25.523735	84.283635	Normal
21/9/21	14:25:0	39	0.1	280	32.5	2800	2878	G	25.523922	84.284578	Normal
21/9/21	14:25:25	39	0.1	290	31.2	2900	2970	G	25.52387	84.285572	Normal
21/9/21	14:26:0	39	0.1	300	30.2	3000	3069	G	25.523518	84.286463	Normal
21/9/21	14:26:35	39	0.1	310	31.5	3100	3167	G	25.5234	84.28739	Normal
21/9/21	14:27:11	39	0.1	300	32.5	3000	3069	G	25.523437	84.28838	Normal

Akew
22/09/21
JE

HT
24.08.2022
AE

Gopal
19/09/2022
GE

Date	Time	Section	Length	Bumps	Speed	OR	IRI	GATEGORY	Latitude	Longitude	Event
		No.	In km	In mm	Rate	mm/km	mm/km	Road			
21/9/21	14:27:41	39	0.1	340	30.2	3400	3462	G	25.523438	84.289343	Normal
21/9/21	14:28:0	39	0.1	300	31.5	3000	3069	G	25.523407	84.290302	Normal
21/9/21	14:28:21	39	0.1	280	32.5	2800	2873	G	25.523418	84.291363	Normal
21/9/21	14:28:41	39	0.1	290	30.2	2900	2970	G	25.523337	84.29234	Normal
21/9/21	14:29:0	39	0.1	310	31.5	3100	3167	G	25.523405	84.293332	Normal
21/9/21	14:29:32	39	0.1	280	32.5	2800	2877	G	25.523328	84.294325	Normal
21/9/21	14:30:0	39	0.1	300	30.2	3000	3081	G	25.52345	84.295268	Normal
21/9/21	14:30:42	39	0.1	280	31.5	2800	2872	G	25.523502	84.296195	Normal
21/9/21	14:31:18	39	0.1	300	32.5	3000	3069	G	25.52362	84.297153	Normal
21/9/21	14:31:48	39	0.1	320	30.2	3200	3265	G	25.522837	84.297137	Normal
21/9/21	14:32:0	39	0.1	270	31.2	2700	2786	G	25.521937	84.296952	Normal
21/9/21	14:32:28	39	0.06	270	30.5	2700	2777	G	25.521015	84.29677	Normal
							CUMULATIVE	97305			
							AVERAGE IRI	3041			

Akshar
22/09/21
JE

BL
24.08.2022
AE

gopal
19/09/2022
CE
