

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, डुमराँव ।

पत्रांक 1001/अनु

डुमराँव, दिनांक 29-09-2022

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, डुमराँव ।

सेवा में,

नोडल पदाधिकारी,
3054(MR)
ग्रामीण कार्य विभाग,
बिहार, पटना ।

विषय:— शीर्ष MR New Maintenance Policy 2018 योजना अन्तर्गत 5(पाँच) वर्षीय अनुरक्षण का
आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपर्युक्त विषयक के संबंध में कहना है कि शीर्ष MR New Maintenance Policy 2018
योजना अन्तर्गत 5(पाँच) वर्षीय अनुरक्षण के पथों का पथवार मांगी जाने वाली आवंटन की सूची पत्र के
साथ भवदीय के अवलोकनार्थ एवं आवश्यक कार्रवाई हेतु समर्पित की जा रही है।

सूचनार्थ सादर समर्पित।

अनु०— यथोक्त

विश्वासभाजन

[Signature]
29/09/2022

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमण्डल, डुमराँव।

[Signature]
29/09/2022

FORM GFR 19-A

(See Government of India's Decision (I) below Rule-150)

Form of Utilization Certificate up to the Date 31 Mar 2021

RWD, Works Division, Dumraon

Sl. No	Name of Scheme	Sanction No. & Date with Amount (in lacs Rs.)	Amount Received (in lacs Rs.)	Particulars
1	Maintenance of Rural roads Maintenance Policy-2018 under MR-3054	Allotment Received Through CFMS vide Letter - Date-	0.000 Lakh	Certified that out of Rs. 0.0 lacs of grants-in-aid sanctioned during the years 2022-23 in favors of E-in-C, RWD Bihar, Patna a sum of Rs. 0.0 lacs has been utilized for the purpose of MR (3054) Schemes as given in the margin for which it was sanctioned and that the balance of Rs. 0.000 Lacs remaining unutilized at the end of the period under report.
Total :-			Rs.- 0.0 Lakh	

1. Certified that I have satisfied myself that the conditions on which the grants-in-aid was sanctioned have been duly fulfilled/ are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.

Kind of Checks exercised: -

- Works have been supervised by Executive Engineer/ Superintending Engineer.
- Periodical inspection has been conducted by Executive Engineer/ Superintending Engineer.
- Construction materials have been tested.
- Measurements have been recorded in the MBs and test check conducted by the Assistant Engineer/ Executive Engineer.
- All other codal formalities have been observed.

2. Physical Progress achieved :-

- Maintenance of Road Works.
- Maintenance of CD works

[Signature]
D. A. O.
RWD Works, Division, Dumraon

[Signature]
Executive Engineer
RWD Works, Division, Dumraon
12/09/2022

Acquisition Format for Scheme Head - 5 Year Maintenance of MR(3054) under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and surface Renewal)

Name of Division :- Dumraon

Name of Circle :- Ara

Sl. No.	Name of Road	Name of Agency	Batch No	Project ID as per MIS	Administrative Letter No & Date.	Administrative Approval (AA)		Agreement Amount (in Lac)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Current Maintenance Demand (In Lacs)					Remarks.
						Length (in km)	Amount of (in Lakh)	Initial Rectification surface (in Lakh)	5 Years Routine Maintenance (in Lakh)				1st Qtr Maint Demand	2nd Qtr Maint Demand	3rd Qtr Maint Demand	4th Qtr Maint Demand	Total Demand	
1	Reginathpur Railway Gunt to Dhodanpurva	JAWAHAR LAL YADAV	RM/BU/DUM/19/0003	10402001011	It. No 2014 dt. 02-July-2019	0.700	21.646	12.706	5.26133	13MBD/2019-20 & 10.12.2019	9-Sep-20	1/10/2020	0.26307	0.26307	0.26307	0.26307	1.05228	
2	BRAHMPUR BAGEN ROAD - KIHOCHEIRA	JAWAHAR LAL YADAV	RM/BU/DUM/19/0003	10401902027	It. No 2014 dt. 02-July-2019	3.16	104.432	60.231	26.72399	13MBD/2019-20 & 10.12.2019	9-Sep-20	10/9/2020	1.3362	1.3362	1.3362	1.3362	5.3448	
3	BRAHMPUR BAGEN ROAD - RAHAITHUA	JAWAHAR LAL YADAV	RM/BU/DUM/19/0003	10401902028	It. No 2014 dt. 02-July-2019	3.631	121.842	70.285	31.13961	13MBD/2019-20 & 10.12.2019	9-Sep-20	1/10/2020	1.55698	1.55698	1.55698	1.55698	6.22792	
4	BRAHMPUR PETROL PUMP - PARASIA	JAWAHAR LAL YADAV	RM/BU/DUM/19/0003	10401902029	It. No 2014 dt. 02-July-2019	1.750	51.571	30.009	12.77193	13MBD/2019-20 & 10.12.2019	9-Sep-20	3/1/2021	0.63860	0.63860	0.63860	-	1.9158	
5	CHANDANPURA BAZAR - CHANDRAPURA	JAWAHAR LAL YADAV	RM/BU/DUM/19/0003	10401902034	It. No 2014 dt. 02-July-2019	0.500	15.246	9.124	3.47517	13MBD/2019-20 & 10.12.2019	9-Sep-20	1/10/2020	0.17376	0.17376	0.17376	0.17376	0.69504	
6	NH 84 DEOKULI SCHOOL - KOTHA	JAWAHAR LAL YADAV	RM/BU/DUM/19/0003	10401902052	It. No 2014 dt. 02-July-2019	1.600	50.893	29.595	12.69504	13MBD/2019-20 & 10.12.2019	9-Sep-20	1/10/2020	0.63475	0.63475	0.63475	0.63475	2.539	
7	SIKARAU LOCK - NABAHAMDIH	JAWAHAR LAL YADAV	RM/BU/DUM/19/0008	10402000354	It. No 2014 dt. 02-July-2019	2.960	97.961	55.284	26.29856	18MBD/2019-20 & 7.01.2020	6-Oct-20	9/10/2020	1.31493	1.31493	1.31493	1.31493	5.25972	
8	Salsala Natar Pool - Mahadev Ganj via Salsala, Ramnagar	JAWAHAR LAL YADAV	RM/BU/DUM/19/0008	NEA220001776	It. No 2014 dt. 02-July-2019	3.225	104.059	59.136	27.08233	18MBD/2019-20 & 7.01.2020	6-Oct-20	9/10/2020	1.35412	1.35412	1.35412	1.35412	5.41648	
9	NH-30 - Samosar natar Pool Path	JAWAHAR LAL YADAV	RM/BU/DUM/19/0008	NEA220001791	It. No 2014 dt. 02-July-2019	2.300	76.747	43.353	20.52623	18MBD/2019-20 & 7.01.2020	6-Oct-20	9/10/2020	1.02631	1.02631	1.02631	1.02631	4.10524	
10	NH-30 - Teerthal Via Padniya	JAWAHAR LAL YADAV	RM/BU/DUM/19/0008	NEA220001920	It. No 2014 dt. 02-July-2019	1.650	54.809	31.701	14.04099	18MBD/2019-20 & 7.01.2020	6-Oct-20	9/10/2020	0.70205	0.70205	0.70205	0.70205	2.8082	
11	Purniya - B.C. Pool Path Via Babganj English, Koriyadh	JAWAHAR LAL YADAV	RM/BU/DUM/19/0008	NEA220001921	It. No 2014 dt. 02-July-2019	2.300	80.638	46.619	20.52623	18MBD/2019-20 & 7.01.2020	6-Oct-20	9/10/2020	1.02631	1.02631	1.02631	1.02631	4.10524	

DIVISIONAL ACCOUNTS OFFICER
R.W.D. Works Division,
Dumraon

Executive Engineer
Rural Works Department
Works Division Dumraon

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

PIU Name :- RWD, Works Division, Dumraon

1	Name of the Road	Puraniya - B.C. Pool Path Via Babuganj English, Korrayadih		
2	Batch No.	RM/BU/DUM/19/0008		
3	Project ID	NEA220001921		
4	Total Lenth of Road (in KM)	2.300		
5	Length of Road to Meet Required Service Level [Completed length](in Km) [1]	2.300		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	20.52623		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	1.02631		
Compliance Criteria	Standard Job Description	Non-Compliance		Reduction Payment [6]=[3]/[1]*[2]*[4]
		Length Non-Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0.00
II	SHOULDERS AND EMBANMENTS	0	10%	0.00
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0	15%	0.00
IV	SIGNAGE AND ROAD SAFETY	0	10%	0.00
V	VEGATION	0	5%	0.00
TOTAL PAYMENT REDUCTION FOR THE QUARTER (IN Lakh) [5]				0.00000
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh) [6]				1.02631

Date of inspection by E/I or his agent
Prepare by Contractor's self Control unit

M. Mondal
22/09/2021
Name and Designation of person inspecting road

Date

M. Mondal
22/09/2021
Signature of person inspecting road

(Signature)

Gopal
19/09/2022
Certify by E/I [signature] Date:-
Executive Engineer
Rural Works Department
Works Division, Dumraon

Government Of Bihar

10301

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

To:-

Executive Engineer
RWD, Works Division Dumraon

Date:-

Road From: Purniya - B.C. Pool Path Via Babuganj English, Karmayada
Length of Road ~2-300 KM
Inspector :-

Position :-

No	Standard Of Work Item	Unit	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	Comments
OM1/00	Scaled pavement	m ²	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	No pothole found
OM1/01	Pothole Patching	m ³	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	No Surface Depression and Rut patching found
OM1/02	Surface Depression and Rut patching	m ³	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	No crack found
OM1/03	Crack Sealing	Lm	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	No required
	Surface Treatment	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	No Loss of Aggregate (Surface raveling) found
OM1/04	(a) Loss of Aggregate (Surface raveling)	m ³	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	No bleeding / furnishing found
	(b) Bleeding / Flushing	m ²	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	No Crocodile cracking found
OM1/05	c Crocodile Cracking	m ²	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	Notified & repaired
OM1/06	Edge Repair	m ²	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	
OM1/07	Digouts	m ²	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	
	Concrete pavement	m ³	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	
	Other activities																			
OM2/00	Shoulder																			
	Unsealed Shoulder																			
	(a) Edge Drop-off	Lm	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	No Edge Drop off found
OM2/01	(b) Roughness, Scouring or Potholes	Lm	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	No Roughness, Scouring or Potholes found
	(c) Holding water	Lm	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	No Holding Water Found
OM2/02	Embankment Repair	M ³	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	Notified & repaired
	Order activities (Rain Cuts)	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	
OM3/00	Drainage including culverts and/or																			
OM3/01	Surface Drains & Verge	Lm	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	NA
OM3/02	Curbcut Cheeking	No	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	DONE
OM3/03	Curbcut and pit Repair	M ³	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	DONE
	Order activities (Mallow washing)	M ²	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	NIL	Not required

Unit Of Required in each Kilometer														Comments
standard Of Work Item	Work Unit	1	2	3	4	5	6	7	8	9				
No	Name													
OM400	Vegetation													
	Grass Control													
OM401	Ha	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	Done
	(a) Roadside- General Tidy	Ha	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	Done
	(b) Clear near Safety signs, kilometer posts and roadside	Ha	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	Done
OM402	Tree and Shrub Management	No	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	Done
	Cutting Of Branches Of Trees	No	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	Done
	Cutting Of Shrubs From Road Way	No	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	Done
OM500	Other activities (Trimming of Grass)	M ²	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	Done
	Safety Signage and Road													Not Required
OM501	Signs Maintenance	No	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	Not Required
OM502	Guard Stones	Lm	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	N.A.
OM503	Distance Stones	No	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	N.A.
OM504	Road Marking	M ²	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	NIL	Not Required
	Other activities													

2022/09/16/2022

Executive Engineer
Rural works Department
Works Division, Durnraon
2022/09/16/2022

Name of Customer : JAWAHAR LAL YADAV
 Name of Work/ Road : Purniya to BC nahar pool via ba
 Lab Job number :
 Date : 9/23/2021
 Section No. : 44


Test Date : 9/23/2021 Road Name : Purniya to BC nahar pool via bc
 Machine No : 312 Road Type : (R) RURAL ROAD
 Start S No : Side : Interval
 Start E No :
 Weather : UV Range : 1530 To 5000 1000 mm/km
 Start Location : Purniya Dist Range : 0 To 24 01 * 1000 m
 End Location : babuganj eng Equation : $Y = 0 * X^2 + 1.047 * X - 63.36$

Print

Generate Report and Graph

Redraw Graph

Map View

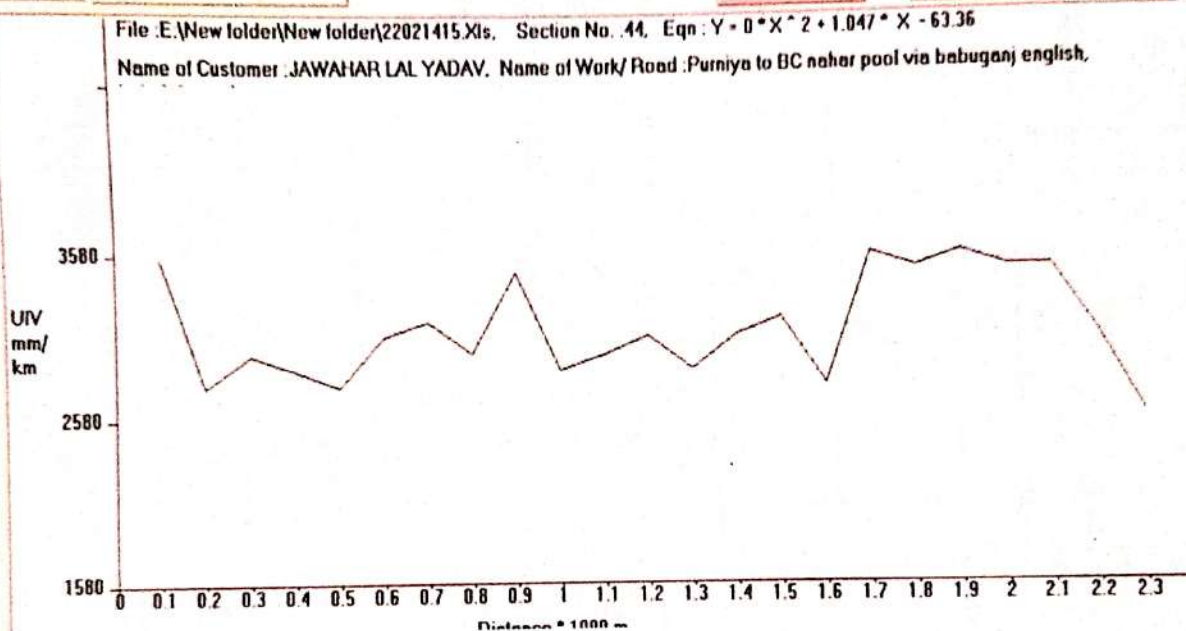

Handwritten signature
 23/9/2021

Handwritten signature
 19/09/2021

Name of Road :-PURANIVA TO BC POOL PATH VIA BABUGANJ ENGLISH KORRAYADIH . (MACHINE - BUXAR)

Date	Time	Section	Length	Bumps	Speed	OR	IRI	GATEWAY	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	mm/km	Road			
23/9/21	13:15:0	44	0.1	350	0	3500	3561	G	25.378637	84.2718	Normal
23/9/21	13:15:16	44	0.1	270	30.3	2700	2773	G	25.377803	84.271885	Normal
23/9/21	13:15:16	44	0.1	290	31.5	2900	2970	G	25.37693	84.271935	Normal
23/9/21	13:15:16	44	0.1	280	32.5	2800	2872	G	25.375955	84.272003	Normal
23/9/21	13:15:16	44	0.1	270	31.2	2700	2775	G	25.375097	84.272087	Normal
23/9/21	13:15:16	44	0.1	300	32.5	3000	3075	G	25.374092	84.272153	Normal
23/9/21	13:15:51	44	0.1	310	31.5	3100	3167	G	25.373172	84.272238	Normal
23/9/21	13:16:0	44	0.1	290	30.3	2900	2975	G	25.372202	84.272305	Speed Breaker
23/9/21	13:16:26	44	0.1	340	32.5	3400	3462	G	25.3713	84.27239	Normal
23/9/21	13:16:26	44	0.1	280	30.3	2800	2875	G	25.370392	84.272457	Normal
23/9/21	13:16:26	44	0.1	290	30.3	2900	2970	G	25.369552	84.272542	Normal
23/9/21	13:16:26	44	0.1	300	30.3	3000	3078	G	25.368628	84.272575	Normal
23/9/21	13:17:1	44	0.1	280	30.3	2800	2877	G	25.367708	84.272658	Normal
23/9/21	13:17:1	44	0.1	300	31.2	3000	3080	G	25.366788	84.272727	Normal
23/9/21	13:17:1	44	0.1	310	30.3	3100	3175	G	25.365868	84.27281	Normal
23/9/21	13:17:1	44	0.1	270	30.3	2700	2773	G	25.364937	84.272878	Normal
23/9/21	13:17:37	44	0.1	350	30.3	3500	3561	G	25.36402	84.272962	Normal
23/9/21	13:17:37	44	0.1	340	30.3	3400	3462	G	25.363113	84.273013	Normal
23/9/21	13:18:0	44	0.1	350	30.3	3500	3561	G	25.362218	84.272793	Normal
23/9/21	13:18:11	44	0.1	340	30.3	3400	3462	G	25.36147	84.272103	Normal
23/9/21	13:18:11	44	0.1	340	30.3	3400	3462	G	25.360848	84.271413	Normal

Date	Time	Section	Length	Bumps	Speed	OR	IRI	GATEGORY	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	mm/km	Road			
23/9/21	13:18:11	44	0.1	300	30.3	3000	3069	G	25.360172	84.270622	Normal
23/9/21	13:18:46	44	0.1	250	32.5	2500	2580	G	25.360002	84.270403	Normal
CUMULATIVE											
AVERAGE IRI											
								71615			
								3114			

Recd.
25/9/2023

Robert
12/19/09/2002
DE
