

कार्यपालक अभियंता का कार्यालय

ग्रामीण कार्य विभाग

कार्य प्रमंडल सोनपुर

पत्रांक.....1774.....सोनपुर, दिनांक.....21/10/22.....
प्रेषक,

कार्यपालक अभियंता

ग्रामीण कार्य विभाग

कार्य प्रमंडल सोनपुर

सेवा में,

अपर मुख्य कार्यपालक

पदाधिकारी—सह—सचिव,

बिहार ग्रामीण पथ विकास अभिकरण

(BRRDA)

बिहार, पटना।

विषय:— बिहार ग्रामीण पथ अनुरक्षण निति—2018 योजनान्तर्गत अनुरक्षण हेतु राशि की अधियाचना के संबंध में।


महाशय,

उपर्युक्त विषय के संबंध में कहना है कि बिहार ग्रामीण पथ अनुरक्षण निति—2018 के अंतर्गत पथों का अनुरक्षण की राशि की मांग रुपये 7,29,138.00 (सात लाख उनतीस हजार एक सौ अड़तीस) मात्र विहित प्रपत्र में अंकित कर आवश्यक कार्रवाई हेतु समर्पित किया जा रहा है।

अनुरोध है कि उपर्युक्त योजना में आवंटन उपलब्ध कराने की कृपा की जाये। कार्य का निरीक्षण किया गया कार्य संतोषप्रद है। उक्त पथ में ए0टी0आर0 लंबित नहीं है।

अनु0:—Standard Formate for Roads
Quarterly Statement

विश्वासभाजन



कार्यपालक अभियंता

ग्रामीण कार्य विभाग

कार्य प्रमंडल सोनपुर

21/10/22

FORM GER 19-A

(See Government of India's Decision (I) below Rule-150
Form of Utilization Certificate up to the month of **October-2022**

PIU:- E.E.,R.W.D. Works Division Sonapur.

Sl. No.	Name of Scheme	Sanction No. & Date with Amount (in lacs Rs.)	Amount Received (in lac Rs.)	Particulars
1	2	3	4	5
1	Construction of Rural Roads under New Maintenance Policy-18 (Maintenance)		175.42789	Certified that out of Rs 175.42789 lakh received during the years 2020-21 to 2022-23 in favour of E.E.R.W.D. works division Sonapur a sum of Rs 66.35226 Lakh has been utilized for the purpose of New Maintenance Policy-18 (Maintenance) Scheme as given in the margin for which it was sanctioned and that the balance of Rs 109.07563 Lakh remaining unutilized at the end of the period under report.

Certified that I have satisfied that the condition of which the grants-in-aid was sanctioned have been duly fulfilled/ are being fulfilled and that I have exercised the following checks to see that the money was actually for the purpose for which it was sanctioned.

Kind of Checks:-

- Words have been supervised be Executive/superintending Engineer.
 - Periodical inspection has been conducted by Executive Engineer/ superintending Engineer.
 - Construction material has been tested.
 - Measurements have been recorded in the MBS and test conducted by the Assistant Engineer/ Executive Engineer.
 - All other nodal formalities have been observed.
- 3 physical Progress achieved-
- Construction of Road Works.
 - Construction of CD works

D.A.O

R.W.D. Works Division Sonpur.

EXECUTIVE ENGINEER

R.W.D. Works Division Sonpur.

Maintenance Requisition Formate for Scheme Head- MR (3054) Under Bihar Rural Road Maintenance Policy-2018

Name of Works Division:- SONPUR

Name of Works Division:- SONIPUR																												
Road Details				AA Details		Agreement								Actual Maintenance Expenditure					Current Maintenance Demand			Remarks						
Sl. No.	Name of Raods	Batch No.	Project ID	Actual Date of Completion	Main Work Amount (in Lakh	Maintenace Amount (in lakh)	Main Work Amount (in Lakh)	Agreement-1-1	Agreement-2	Agreement-3	Agreement-4	Agreement-5	Total Maintenance	Length h (in KM)	1st. Year Maintenance	2nd. Year Maintenance	3rd. Year Maintenance	4th Year Maintenance	5th Year Maintenance	Total Maintenance Expenditure	Length as per Bump Report		IRI As per bump Report	1st OTR Maintenance	2nd OTR Maintenance	3rd OTR Maintenance	4th OTR Maintenance	Total
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	30	31	
1	Brahampur to Visunpur tak path nirman	RM/SA/SON /20/0016	31306202086	15-01-2021	36.82600	16.57700	36.95400	3.24118	3.24118	3.24118	3.24118	3.24118	16.20590	1.500	0.000	0.000	0.000	0.000	0.000	0.000	1.500	3074	0.81030	0.81030	0.00000	0.00000	1.62059	
2	Gram panchayat raj anyay antargat marand R E O sadak se patel chowk se Baligaon tak sadak nirman	RM/SA/SON /20/0016	31306202090	24-12-2020	52.77700	24.20500	52.76700	4.74976	4.74976	4.74976	4.74976	4.74976	23.74880	2.200	0.000	0.000	0.000	0.000	0.000	0.000	2.200	2875	1.18744	1.18744	0.00000	0.00000	2.37488	
3	Anjani to banaura via futami chowk	RM/SA/SON /20/0016	31306202171	01-12-2020	97.79900	32.94000	97.83400	6.59181	6.59181	6.59181	6.59181	6.59181	32.95905	3.000	0.000	0.000	0.000	0.000	0.000	0.000	3.000	2813	1.64795	1.64795	0.00000	0.00000	3.29591	
Total																											7.29138	

(Signature)
D.A.O.-
RWD WORKS DIVISION
Sonapur

(Signature)
Executive Engineer
R.W.D. Works Division
SONPUR
11/10/22

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT				
1	Name of the Road	Anjani to banauta via futani chowk		
2	Batch No.	RM/SA/SON/20/0016		
3	Project ID	31306202171		
4	Total Length of Road (in Km)	3.000		
5	Length of Road to Meet Required Service Level [Completed length] (in Km) (1)	3.000		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule (Agreement Amount for Maintenance) (in Lakh)	32.95905		
8	Quarterly Payment :1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) (2)	1.64795		
Compliance Criteria	Standard Job Description	Non-Compliant		Reduction Payment (6) = (3) / (1) * (2) * (4)
		Length Non Compliant (3)	Weighted Value for Payment Reduction (%) (4)	
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0.00000
II	SHOULDERS AND EMBANMENTS	0	10%	0.00000
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0	15%	0.00000
IV	SIGNAGE AND ROAD SAFETY	0	10%	0.00000
V	VEGATAION		5%	0.00000
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0.00000
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh) [6]				1.64795

Date of inspection by E/I or his agent Prepared by
Contractor's self Control unit

Date

Signature of person inspecting road

Name and Designation of person inspecting road
(Signature)

Certify by E/I (Signature) Date
Rural Works Department
Work Division, Sonam

Requisition Format for Scheme Head - MR (3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division :- Sonpur

Government of Bihar
OM01

Rural works Department

Road From- Anjani to banauta via futani chowk

Length of Road: 3.000 KM

Period : From.....

Inspector: A.E RWD Sub Division, Parsa

To: Executive Engineer

RWD Works Division Sonpur

Date:

Position: A.E

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Standard Work item			Work Units	Units of work required in each kilometre										Comments
S No	Name			1	2	3	4	5	6	7	8	9	10	
OM100 Sealed Pavement														
OM101	Pothole Patching	m2												No Pothole found
OM102	Surface Depression and Rut Patching	m2												No Surface Depression and Rut Patching found
OM103	Crack Sealing	Lm												No Crack Sealing found
Surface Treatment														
OM104	(a) Loss of Aggregate (Surface Ravelling)	m2												No Loss of Agreegate (Surface Ravelling) found
	(b) Bleeding/Flushing	m2												No Bleeding/Flushing Required
	(c) Crocodile Cracking	m2												No Crocodile Cracking found
OM105	Edge Repair	m2												No Edge Repair Required
OM106	Digouts	m2												
OM107	Concrete Pavement	m3												
Other activities		Lm												
OM200 Shoulder														
OM201	Unsealed Shoulder	No												No Edge Drop off Required
	(a) Edge Drop off	Lm												Not required
	(b) Roughness, Scouring or Potholes	Lm												No Holding water found
	(c) Holding Water	Lm												No Embankment Repair Required
OM202	Embankment Repair	No												Defects rectified within stipulated time.
	Other Activite (Raincut)													
OM 300 Drainage including culverts major														
OM301	Surface Drains & Verge	Lm												Not Required
OM302	Culvert Cleaning	Lm												Culvert maintain within stipulated time
OM303	Culvert and Pit repair	m2												Not Required

By: 15/10/2018
Signature
Date: 15/10/2018

Am 21/10/18

Name of work : Anjani to banauta via futani chowk
Name of customer : Kbs Construction Prop- Kamlesh Kumar Ray

(R)Rural Road		
Good	Average	Poor
< 4000	4001 - 5000	> 5000

IRI VALUE= 2813

Date	Time	Test No	Distance (m)	Total Distance (m)	BUMP (cm)	Speed (Km/Hr)	UI (mm/Km)	Corrected UI (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction 1	Remarks
11-09-22	13:40:52	94	0	0	29.0 cm	23.6 Km/Hr	2900.0 mm/Km	2819	3.81	Good	25.9152556	N	85.0615549	E	Normal
11-09-22	13:50:56	94	100	100	30.0 cm	7.6 Km/Hr	3000.0 mm/Km	2911	3.92	Good	25.9273406	N	85.0469751	E	Normal
11-09-22	13:51:26	94	100	200	35.0 cm	11.7 Km/Hr	3500.0 mm/Km	3375	4.48	Good	25.9278212	N	85.0468454	E	Normal
11-09-22	13:52:04	94	100	300	22.0 cm	9.4 Km/Hr	2200.0 mm/Km	2169	3.02	Good	25.9286261	N	85.0467768	E	Normal
11-09-22	13:52:23	94	100	400	18.0 cm	18.4 Km/Hr	1800.0 mm/Km	1798	2.55	Good	25.9292784	N	85.0460749	E	Normal
11-09-22	13:52:45	94	100	500	15.0 cm	16.6 Km/Hr	1500.0 mm/Km	1519	2.19	Good	25.9292784	N	85.0460749	E	Normal
11-09-22	13:53:02	94	100	600	21.0 cm	21.0 Km/Hr	2100.0 mm/Km	2076	2.9	Good	25.9292784	N	85.0460749	E	Normal
11-09-22	13:53:36	94	100	700	30.0 cm	11.0 Km/Hr	3000.0 mm/Km	2911	3.92	Good	25.9292784	N	85.0460749	E	Normal
11-09-22	13:54:28	94	100	800	27.0 cm	6.8 Km/Hr	2700.0 mm/Km	2633	3.59	Good	25.9292784	N	85.0460749	E	Normal
11-09-22	13:54:56	94	100	900	33.0 cm	12.8 Km/Hr	3300.0 mm/Km	3190	4.26	Good	25.9292784	N	85.0460749	E	Normal
11-09-22	13:55:20	94	100	1000	30.0 cm	15.0 Km/Hr	3000.0 mm/Km	2911	3.92	Good	25.9292784	N	85.0460749	E	Normal
11-09-22	13:55:41	94	100	1100	28.0 cm	16.9 Km/Hr	2800.0 mm/Km	2726	3.7	Good	25.9292784	N	85.0460749	E	Normal
11-09-22	13:56:04	94	100	1200	23.0 cm	15.4 Km/Hr	2300.0 mm/Km	2262	3.13	Good	25.9292784	N	85.0460749	E	Normal
11-09-22	13:56:25	94	100	1300	33.0 cm	18.1 Km/Hr	3300.0 mm/Km	3190	4.26	Good	25.9292784	N	85.0460749	E	Normal
11-09-22	13:57:07	94	100	1400	24.0 cm	8.5 Km/Hr	2400.0 mm/Km	2355	3.24	Good	25.9292784	N	85.0460749	E	Normal
11-09-22	13:57:31	94	100	1500	29.0 cm	14.8 Km/Hr	2900.0 mm/Km	2819	3.81	Good	25.9292784	N	85.0460749	E	Normal
11-09-22	13:57:57	94	100	1600	33.0 cm	13.9 Km/Hr	3300.0 mm/Km	3190	4.26	Good	25.9292784	N	85.0460749	E	Normal
11-09-22	13:58:16	94	100	1700	30.0 cm	17.8 Km/Hr	3000.0 mm/Km	2911	3.92	Good	25.9292784	N	85.0460749	E	Normal
11-09-22	13:58:33	94	100	1800	27.0 cm	20.9 Km/Hr	2700.0 mm/Km	2633	3.59	Good	25.9292784	N	85.0460749	E	Normal
11-09-22	13:58:48	94	100	1900	21.0 cm	23.8 Km/Hr	2100.0 mm/Km	2076	2.9	Good	25.9292784	N	85.0460749	E	Normal
11-09-22	13:59:03	94	100	2000	32.0 cm	25.4 Km/Hr	3200.0 mm/Km	3097	4.14	Good	25.9292784	N	85.0460749	E	Normal
11-09-22	13:59:15	94	100	2100	31.0 cm	29.1 Km/Hr	3100.0 mm/Km	3004	4.03	Good	25.9292784	N	85.0460749	E	Normal
11-09-22	13:59:28	94	100	2200	29.0 cm	28.5 Km/Hr	2900.0 mm/Km	2819	3.81	Good	25.9292784	N	85.0460749	E	Normal
11-09-22	13:59:44	94	100	2300	32.0 cm	22.6 Km/Hr	3200.0 mm/Km	3097	4.14	Good	25.9292784	N	85.0460749	E	Normal
11-09-22	14:00:03	94	100	2400	28.0 cm	18.6 Km/Hr	2800.0 mm/Km	2726	3.7	Good	25.9292784	N	85.0460749	E	Normal
11-09-22	14:00:21	94	100	2500	36.0 cm	20.6 Km/Hr	3600.0 mm/Km	3468	4.59	Good	25.9292784	N	85.0460749	E	Normal
11-09-22	14:00:39	94	100	2600	33.0 cm	20.2 Km/Hr	3300.0 mm/Km	3190	4.26	Good	25.9292784	N	85.0460749	E	Normal

Signature

Signature

15/10/22


11-09-22	14.09.33	94	100	2700	28.0 cm	0.6 Km/Hr	2800.0 mm/Km	2726	3.7	Good	25.9318572	N	85.0235071	E	Normal
11-09-22	14.09.49	94	100	2800	34.0 cm	21.8 Km/Hr	3400.0 mm/Km	3283	4.37	Good	25.9309702	N	85.0234690	E	Normal
11-09-22	14.10.01	94	100	2900	26.0 cm	28.5 Km/Hr	2600.0 mm/Km	2540	3.47	Good	25.9302550	N	85.0234537	E	Normal
11-09-22	14.10.14	94	100	3000	20.0 cm	28.8 Km/Hr	2000.0 mm/Km	1983	2.78	Good	25.9302550	N	85.0234537	E	Normal

RB
15/10/24

Light
15/10/24

Km
21/10/24
Executive Engineer
Rural Works Department
Work Division, Sonapat

Name of Customer: Kbs Construction Prop- Kamlesh Kumar Ray , Machine no: 19205 , Road: Anjani to banauta via futani chowk , Date: 11-09-22 , Section No: 94 , Equation: $Y=0.928X+127.3$

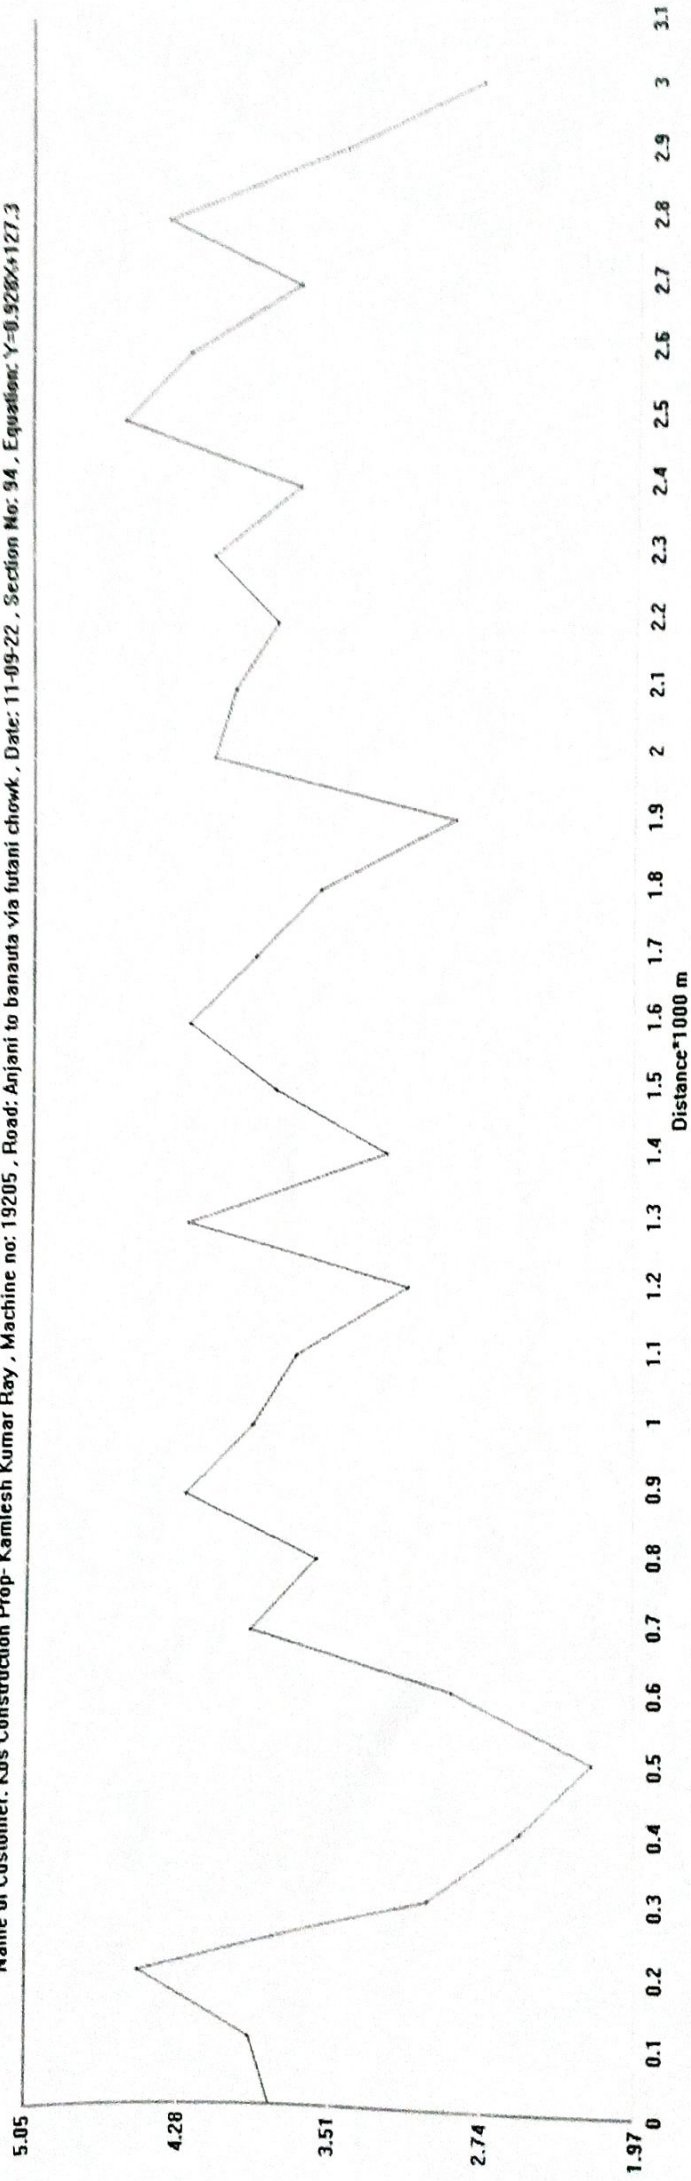

[Handwritten signatures and dates]
15/10/22
15/10/22
15/10/22
