

**कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल, रक्सौल।**

पत्रांक :- 973 अमु०

रक्सौल, / दिनांक :- 02/09/22

प्रेषक :-

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, रक्सौल।
सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-साह-राधिव,
बिहार ग्रामीण पथ विकास अभिकरण,
ग्रामीण कार्य विभाग, बिहार, पटना।



विषय :- बिहार ग्रामीण पथ अनुरक्षण नीति-2018 अन्तर्गत पॉच वर्षीय रूटीन अनुरक्षण कार्य मद
योजना अन्तर्गत आवंटन निर्गत करने हेतु अधियाचना के संबंध में।
महाशय,

उपर्युक्त विषयक बिहार ग्रामीण पथ अनुरक्षण नीति-2018 अन्तर्गत पॉच वर्षीय रूटीन अनुरक्षण
कार्य मद में संलग्न सूची के अनुसार आवंटन अधियाचना संबंधित प्रपत्र में भरकर आवश्यक कार्रवाई हेतु
समर्पित किया जाता है।

अनुलग्नक :- संलग्न सूची

1. पथों का आवंटन अधियाचना प्रपत्र।
2. Bump Integrator Report

विश्वासभाजन,


कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, रक्सौल।

01-09-22

Standard Format For Roads Quarterly Statement (2nd Quarter)

PIU Name:- Rural Works Department, (Works) Division, Raxaul

1	Name of the Road	Harnahi - Pantoka Path Rest Part 2.000 K.M	
2	Batch No.	RM/EA/RAX/20/0014	
3	Project ID	317851031889	
4	Total Length of Road (In Km)	1.100	
5	Length of Road to Meet Required Service Level [Completed Length] (In Km) [1]	1.100	
6	No. of Total Quarter (i.e. 3 Months as a unit) in 5 Years	20	
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	9.99290	
8	Quarterly Payment 1/20 of ordinary Maintenance Cost as per Schedule (in Lakh) [2]	0.49965	
Compliance Criteria	Standard Job Description	Non Compliance	
		Length Non Compliant [3]	Weighted Value for Payment Reduction (%) [4]
I	Paved Roads (Carriageway)	1	60%
II	Shoulders and Embanments	0	10%
III	Cross Drainage Including Culverts and Bridge	0	15%
IV	Signage and Road Safety	0	10%
V	Vegataion	1	5%
Total Payment Reduction For the Quarterly (In Lakh) [5]			0.27253
To be Paid for the Quarter / Demand (In Lakh) [6]			0.20440

Date of Inspection by E/I or his agent 15/06/22

Prepared by Contractor's self Control Unit

Sanjay Kumar (A.E.)
Name and Designation of person inspecting road

Date: 15/6/22

(Signature)

Signature of person inspecting road

Certify by E/I [Signature] Date 15/6/22

Standard Work Item		Work	Unit of work required in each Kilometre										Comments
No	Name	Units	1	2	3	4	5	6	7	8	9	10	
OM300 Drainage including culverts major and minor bridges													
OM301	Surface Drains & Verge	Lm	NA	NA									Not Required
OM302	Culvert Cleaning	Lm	Nil	Nil									Not Required
OM303	Culvert and Pit Repair	m ³	Nil	Nil									Not Required
	Other activities												Not Required
OM400 Vegetation													
OM401	Grass Control												Not Required
	(a) Roadside General Tidy	Ha	Nil	Nil									Not Required
	(b) Clear near safety signs, kilometer posts and roadside furniture	Ha	Nil	Nil									Not Required
OM402	Tree and Shrub Management	Ha	Nil	Nil									Not Required
	Other activities												
OM500 Signage and Road Safety													
OM501	Signs Maintenance	No	Nil	Nil									Not Required
OM502	Guard stones	Lm	NA	NA									Not Required
OM503	Distance Stones	No	NA	NA									Not Required
OM504	Road Markings	No	Nil	Nil									Not Required
	Other activities												

Asim G. M. He
Bidder

15/6/22
Appendix

15/6/22
Executive Engineer,
RWD, Works Division, Raxaul

Time Section No. Length in km Bumps in mm Speed Rate mm/km OR mm/km IRI, CATEGORY ROAD

23/4/22	17:31:38	14	0.1	250	10.1	2500	2405 G	ROAD NAME - HARNNAH - PANTOKA PATH
23/4/22	17:32:0	14	0.1	280	20.2	2800	2666 G	
23/4/22	17:32:14	14	0.1	300	10.1	3000	2839 G	
23/4/22	17:36:21	14	0.1	250	10.1	2500	2405 G	
23/4/22	17:36:21	14	0.1	300	10.1	3000	2839 G	
23/4/22	17:37:0	14	0.1	250	10.1	2500	2405 G	
23/4/22	17:37:0	14	0.1	230	10.1	2300	2231 G	
23/4/22	17:38:0	14	0.1	250	10.1	2500	2405 G	
23/4/22	17:38:42	14	0.1	300	10.1	3000	2839 G	
23/4/22	17:39:17	14	0.1	250	10.1	2500	2405 G	
23/4/22	17:39:52	14	0.1	210	10.1	2100	2057 G	
				TOTAL		27496		

AVERAGE 2499.63

Latitude ongitude Event

$$Y = 0 \cdot X \wedge 2 + 0.869 \cdot X + 232.9$$

26.96939	84.82345	Normal	X = 2111
26.97024	84.82384	Normal	Y = 2067
26.97113	84.82411	Normal	
26.97193	84.82446	Normal	(R) RURAL ROAD
26.97275	84.82483	Normal	Good Average Poor
26.97359	84.82517	Normal	<4000 4001-5000 >5001
26.97446	84.82549	Normal	
26.97533	84.82562	Normal	
26.97621	84.82584	Normal	
26.97709	84.82601	Normal	
26.97786	84.82648	Normal	

23/4/22
23/4/22

23/4/22
23/4/22

23/4/22

Steco Analyser

Name of Customer: VIJAY KUMAR SINGH
 Name of Work/Road: HARNNAHI - PANTOKA PATH
 Lab Job number:
 Date: 23-04-2022
 Section No: 14

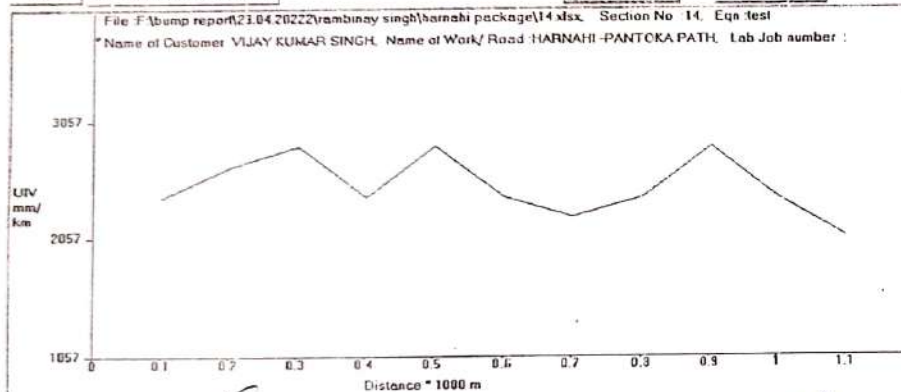
Test Date: 23-04-2022	Road Name: HARNNAHI - PANTOKA PATH
Machine No: 406	Road Type: (A) ASPHALTIC
Start S No:	Side:
Start E No:	Interval
Weather:	UV Range: 105.7 To 4000 1000 mm/km
Start Location: HARNNAHI	Dist Range: 0 To 1.2 0.1 * 1000 m
End Location: PANTOKA PATH	Equation: test

Print

Generate Report and Graph

Redraw Graph

Map View



Handwritten signature
 23/4/22

Handwritten signature
 15/6/22

Handwritten signature



Latitude: 26.977789
Longitude: 84.826387
Elevation: 71.69±24 m
Accuracy: 53.4 m
Time: 08-16-2022 16:31
Note: Harnahi Pantoka path

Powered by NoteCam



Latitude: 26.973827
Longitude: 84.825391
Elevation: 67.36±48 m
Accuracy: 64.9 m
Time: 08-16-2022 16:28
Note: Harnahi Pantoka path

Powered by NoteCam



Latitude: 26.977316
Longitude: 84.826278
Elevation: 71.07±48 m
Accuracy: 72.2 m
Time: 08-16-2022 16:30
Note: Harnahi Pantoka path

Powered by NoteCam



Latitude: 26.977676
Longitude: 84.82628
Elevation: 66.88±64 m
Accuracy: 86.3 m
Time: 08-16-2022 16:31
Note: Harnahi Pantoka path

Powered by NoteCam



Latitude: 26.968971
Longitude: 84.82324
Elevation: 71.14±48 m
Accuracy: 49.7 m
Time: 08-16-2022 16:21
Note: Harnahi Pantoka path

Powered by NoteCam
