

कार्यपालक अभियंता का कार्यालय, ग्रामीण कार्य विभाग, कार्य प्रमंडल, टिकारी।

पत्रांक: 18403नु०

टिकारी, दिनांक: 3.9.22

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, टिकारी।

सेवा में,

नोडल पदाधिकारी, MR 3054
ग्रामीण कार्य विभाग,
बिहार, पटना।


विषय :- शीर्ष Bihar Rural Road Maintenance Policy - 2018 अन्तर्गत कराये जा रहे अनुरक्षण कार्य के भुगतान हेतु राशि अधियाचना के संबंध में।

महाशय,

उपर्युक्त विषयक संबंध में कहना है कि शीर्ष Bihar Rural Road Maintenance Policy - 2018 अन्तर्गत पथ में कराये जा रहे अनुरक्षण कार्य के भुगतान हेतु राशि की अधियाचना विहित प्रपत्र में संलग्न कर समर्पित किया जाता है।

अनु० - यथोक्त।

विश्वासभाजन,



कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, टिकारी।

Maintenance Requisition Formate for Scheme Head-MR (3054) under Bihar Rural Road Maintenance Policy - 2018 (Initial Rectification and Surface Renewal)

Division:- Tekari

Road Details				Actual Date of Completion	AA Details			Agreement (in lakh)						Actual Maintenance Expenditure (in Lakh)								Length (in KM)	IRI As per bump Report	Current Maintenance Demand					Remarks
Sl. No.	Name of Raods	Batch No.	Project ID		Main Work Amount (in Lakh)	Maintenace Amount (in lakh)	Main Work Amount (in Lakh)	Agreement-1	Agreement-2	Agreement-3	Agreement-4	Agreement-5	Total Maintenance	1st. Year Maintenance	2nd. Year Maintenance	3rd. Year Maintenance	4th. Year Maintenance	5th. Year Maintenance	Total Maintenance Expenditure	1st QTR Maintenance (in Lakh)	2nd QTR Maintenance (in lakh)			3rd QTR Maintenance (in lakh)	4th QTR Maintenance (in lakh)	Total			
1	Bela Barabar road to Kaj Fatehpur (Daultpur) Road	RM/GA /TIK/1 9/0002	10502101004	26-12-2020	38.828	16.44	38.67200	1.202	1.844	4.535	2.209	4.671	14.46100	1.70	0.00	0.00	0.00	0.00	0.00	1.700	3641	0.72305	0.72305	0.72305	0.00000	2.16915	1st qtr,2nd qtr & 3rd qtr		
2	Chandauli to Fatehpur road (Old)	RM/GA /TIK/1 9/0002	10502101013	26-12-2020	30.846	15.38	30.45400	1.195	1.758	4.165	2.138	4.216	13.47200	1.50	0.00	0.00	0.00	0.00	0.00	1.500	3452	0.67360	0.67360	0.67360	0.00000	2.02080	1st qtr,2nd qtr & 3rd qtr		
3	Nimchak to Shahpur road	RM/GA /TIK/1 9/0002	10502101051	26-12-2020	47.298	20.44	21.66100	1.516	2.313	5.621	2.736	5.77	17.95600	2.10	0.00	0.00	0.00	0.00	0.00	2.100	3509	0.89780	0.89780	0.89780	0.00000	2.69340	1st qtr,2nd qtr & 3rd qtr		
4	Construction of Road from Bela Panchanpur road Bhuintoli to Singhaul.	RM/GA /TIK/1 9/0002	10502201020	29-01-2021	27.939	14.21	27.08800	0.784	1.537	4.348	4.598	4.254	15.52100	1.90	0.00	0.00	0.00	0.00	0.00	1.900	3421	0.77605	0.77605	0.77605	0.00000	2.32815	1st qtr,2nd qtr & 3rd qtr		
5	Construction of Road from Gaya Patna main road to village Harigaon.	RM/GA /TIK/1 9/0002	10502201031	29-01-2021	22.125	9.591	46.61400	0.736	1.101	2.605	1.305	2.612	8.35900	0.95	0.00	0.00	0.00	0.00	0.00	0.950	3489	0.41795	0.41795	0.41795	0.00000	1.25385	1st qtr,2nd qtr & 3rd qtr		
6	Road from Bela-Barabar Road to Daryapur.	RM/GA /TIK/1 9/0002	10502501023	26-12-2020	20.282	8.409	20.05500	0.623	0.936	2.29	1.149	2.442	7.44000	0.84	0.00	0.00	0.00	0.00	0.00	0.844	3443	0.37200	0.37200	0.37200	0.00000	1.11600	1st qtr,2nd qtr & 3rd qtr		
Total -----							184.54400	6.05600	9.48900	23.56400	14.13500	23.96500	77.20900	8.99400	0.00000	0.00000	0.00000	0.00000	0.00000			3.86045	3.86045	3.86045	0.00000	11.58135			

Amount in Word :- Eleven Lacs Fifty Eight Thousand One Hundred Thirty Five Only.

8/3/22
Executive Engineer
RWD, Works Division, Tekari

Name of work : Chandauti to Fatehpur road (Old)
Name of customer : M G Construction And CO


(R)Rural Road		
Good	Average	Poor
< 4000	4001 - 5000	> 5000

Date	Time	Test No	Distance(m)	Total Distance(m)	BUMP(cm)	Speed(Km/Hr)	UI(mm/Km)	Corrected UI (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks
16-08-22	19:45:27	70	100	100	30.0 cm	10.0 Km/Hr	3000.0	3127	4.18	Good	24.9691344	N	85.0368509	E	Normal
16-08-22	19:46:18	70	100	200	38.0 cm	15.8 Km/Hr	3800.0	3871	5.06	Good	24.9582777	N	85.0359049	E	Normal
16-08-22	19:46:39	70	100	300	34.0 cm	16.8 Km/Hr	3400.0	3499	4.62	Good	24.9582777	N	85.0359049	E	Normal
16-08-22	19:46:59	70	100	400	24.0 cm	17.6 Km/Hr	2400.0	2568	3.51	Good	24.9582777	N	85.0359049	E	Normal
16-08-22	19:47:20	70	100	500	29.0 cm	17.8 Km/Hr	2900.0	3034	4.07	Good	24.9582777	N	85.0359049	E	Normal
16-08-22	19:47:39	70	100	600	36.0 cm	18.1 Km/Hr	3600.0	3685	4.84	Good	24.9582777	N	85.0359049	E	Normal
16-08-22	19:48:01	70	100	700	36.0 cm	16.6 Km/Hr	3600.0	3685	4.84	Good	24.9582777	N	85.0359049	E	Normal
16-08-22	19:48:20	70	100	800	34.0 cm	18.8 Km/Hr	3400.0	3499	4.62	Good	24.9582777	N	85.0359049	E	Normal
16-08-22	19:48:41	70	100	900	38.0 cm	17.6 Km/Hr	3800.0	3871	5.06	Good	24.9582777	N	85.0359049	E	Normal
16-08-22	19:49:00	70	100	1000	30.0 cm	18.4 Km/Hr	3000.0	3127	4.18	Good	24.9582777	N	85.0359049	E	Normal
16-08-22	19:49:20	70	100	1100	34.0 cm	18.8 Km/Hr	3400.0	3499	4.62	Good	24.9582777	N	85.0359049	E	Normal
16-08-22	19:49:41	70	100	1200	37.0 cm	17.8 Km/Hr	3700.0	3778	4.95	Good	24.9557906	N	85.0430384	E	Normal
16-08-22	19:49:54	70	100	1300	31.0 cm	15.9 Km/Hr	3100.0	3220	4.29	Good	24.9557219	N	85.0441904	E	Normal
16-08-22	19:50:11	70	100	1400	38.0 cm	12.9 Km/Hr	3800.0	3871	5.06	Good	24.9557219	N	85.0451975	E	Normal
Total Length			1400				Average	3452							

MG
2/9/22
JE

8/9/22

Name of Customer: M G Construction And CO , Machine no: 19211 . Road: Road from Bela Barabar Road to Dariyapur . , Date: 27-09-22 , Section No: 70 , Equation: $Y=0.931X+333.6$

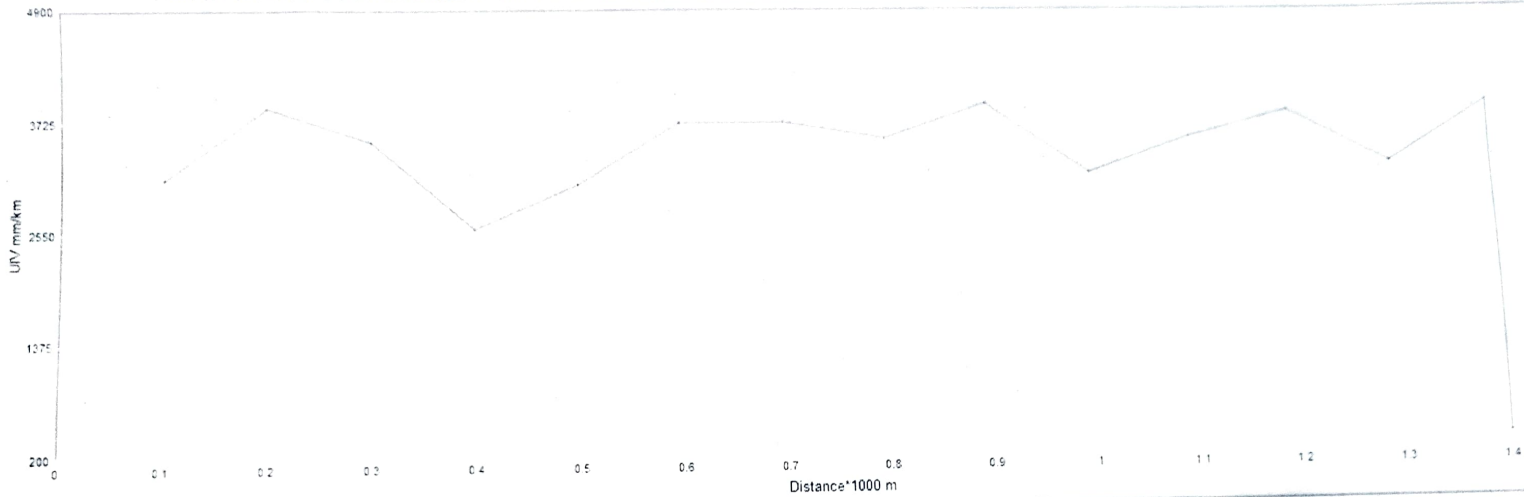

~~19~~
21/9/22
JE

83/9/22

STANDRAD FORMAT FOR ROADS QUARTERLY STATEMENT

1	Name of Road	Chandauti to Fatehpur road (Old)		
2	Batch No.	RM/GA/TIK/19/0002		
3	Project ID	10502101013		
4	Total Length of Road (in km.)	1.500		
5	Length of Road to Meet Required Service Level {Completed Length} (in km) [1]	1.350		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 Years	3rd		
7	Ordinary Maintenance Cost as per Shedule [Agreement Amount for Maintenance) in lakh	13.47200		
8	Quarterly Payment:1/20 of Ordinary Mainten ance Cost as per shedule (in Lakh) [2]	0.67360		
Compliance Criteria	Standard job Decription	Non Compliance		Reduction Payment [6]=[3]/[1]*[2]*[4]
		Length Non Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	Paved Roads (CARRIAGEWAY)	0%	60%	0.00
II	SHOULDERS AND EMANMENTS	0%	10%	0.00
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0%	15%	0.00
IV	SIGNAGE AND ROAD SAFETY	0%	10%	0.00
V	VEGATAION	0%	5%	0.00
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0.00
TO BE PAIF FOR THE QUARTER / DEMAND (in Lakh) [6]				0.67360

Date of inspection by E/I or his agent
Prepared by contractor's self control unit


Name and Designation of person inspecting road
Signature

Date
Signature of person inspecting road

3rd Quarter

Government of Bihar
OM01
Rural Work Department

ORDINARY MAINTENANCE INSPECTION REPORT
Form OM01

Form

Road

From : Chandauti to Fatehpur road (Old)

Length of Road : 1.500 Km.

Period:- from 29.06.21 to 29.09.21

Inspector :J.E., RWD Sub Division Belanganj

To : ... Executive Engineer

RWD, Works Division Tekari

Date : ...

Position : ...J.E


Standard work Item		Work	Unit of work required in each kilometre										Comments
No.	Name	Units	1	2	3	4	5	6	7	8	9	10	
OM100 Sealed Pavement													
OM101	Pothole Patching	m ²	Nil	Nil									No. Pothole found
OM102	Surface Depression and Rut patching	m ²	Nil	Nil									No Surface Depression and Rut patching found.
OM103	Crack Sealing	Lm	Nil	Nil									No Crack Sealing found
OM104	Surface Treatment												
	(a) Loss of Aggreagate (Surface Ravelling)	m ²	Nil	Nil									No Loss of Aggreagate (Surface Ravelling) found
	(b) Bleeding / Flushing	m ²	Nil	Nil									No Bleeding / Flushing Required
	(c) Crocodile Cracking	m ²	Nil	Nil									No Crocodile Cracking found
OM105	Edge Repair	m ²	Nil	Nil									No Edge Repair Required
OM106	Digouts	m ²	N.A.	N.A.									
OM107	Concrete Pavement	m ³	N.A.	N.A.									
	Other activities												
OM200 Shoulder													
OM201	Unsealed Shoulder												
	(a) Edge Drop-off	Lm	Nil	Nil									No Edge Drop-off Required
	(b) Roughness, Scouring or Potholes /	Lm / m2	2%	Nil									Defects rectified within stipulated time.
	(c) Holding water	Lm	Nil	Nil									No Holding water Found
OM202	Embankment Repair	M ³	Nil	Nil									No Embankment Repair Required
	Other activities (Raincut)		Nil	Nil									Not Required
OM300 Drainage including culverts major													
OM301	Surface Drains & Verge	Lm	N.A.	N.A.									Not Required
OM302	Culvert Cleaning	No.	Nil	Nil									Not Required
OM303	Culvrt and pit Repair	M ³	Nil	Nil									Not Required
	Other activities (White Washing)	M ²	100%	100%									white washing within stipulated time.

Bidder

Appendix

Executive Engineer, Works Division Tekari

Standard work Item		Work Units	Unit of work required in each kilometre										Comments
No.	Name		1	2	3	4	5	6	7	8	9	10	
OM400 Vegetation													
OM401	Grass Control												
	a) Roadside- General Tidy	Ha	Nil	Nil									Not Required
	b) Clear near Safety signs, kilometre posts and roadside furniture	Ha	Nil	Nil									Not Required
OM402	Tree and Shrub Management	No.	Nil	Nil									Not Required
	(Cutting Trees)	No.	100%	100%									Cutting of Trees & shrub within time period
	(Cutting shrubs)	No.											
	Other activities (Trimming of Grass)	M ²	100%	100%									Trimming of Grass within time period
OM500 Safety Signage and Road													
OM501	Signs Maintenance	No.	Nil	Nil									Not Required
OM502	Guard Stones	Lm	N.A.	N.A.									Not Applicable
OM503	Distance Stones	No.	N.A.	N.A.									Not Applicable
OM504	Road marking	M ²	Nil	Nil									Not Required
Other activities													


(Signature of Contractor/Authorized representative)

Date

Time

Place

Note:- Enclose photographs with this report.
