

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल, रक्सौल।

पत्रांक :- 995 उसु०

रक्सौल, / दिनांक :- 08/09/22

प्रेषक :-

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, रक्सौल।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव,
बिहार ग्रामीण पथ विकास अभिकरण,
ग्रामीण कार्य विभाग, बिहार, पटना।

विषय :- बिहार ग्रामीण पथ अनुरक्षण नीति-2018 अन्तर्गत पॉच वर्षीय रूटीन अनुरक्षण कार्य मद
योजना अन्तर्गत आवंटन निर्गत करने हेतु अधियाचना के संबंध में।


महाशय,

उपर्युक्त विषयक बिहार ग्रामीण पथ अनुरक्षण नीति-2018 अन्तर्गत पॉच वर्षीय रूटीन अनुरक्षण
कार्य मद में संलग्न सूची के अनुसार आवंटन अधियाचना संबंधित प्रपत्र में भरकर आवश्यक कार्रवाई हेतु
समर्पित किया जाता है।


अनुलग्नक :- संलग्न सूची

1. पथों का आवंटन अधियाचना प्रपत्र।
2. Bump Integrator Report

विश्वासभाजन,



कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, रक्सौल।


08.09.22

Standard Format For Roads Quarterly Statement (3rd Quarter)

PIU Name:- Rural Works Department, (Works) Division, Raxaul

1	Name of the Road	Koriya BOP to GBC		
2	Batch No.	RM/EA/RAX/20/0008		
3	Project ID	317851033022		
4	Total Length of Road (In Km)	3.820		
5	Length of Road to Meet Required Service Level [Completed Length] (In Km) [1]	3.820		
6	No. of Total Quarter (i.e. 3 Months as a unit) in 5 Years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	39.82195		
8	Quarterly Payment: 1/20 of ordinary Maintenance Cost as per Schedule (in Lakh) [2]	1.99110		
Compliance Criteria	Standard Job Description	Non Compliance		Reduction Payment [6] = [3]/[1]*[2]*[4]
		Length Non Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	Paved Roads (Carriageway)	0	60%	0.00000
II	Shoulders and Embanments	0	10%	0.00000
III	Cross Drainage Including Culverts and Bridge	0	15%	0.00000
IV	Signage and Road Safety	0	10%	0.00000
V	Vegataion	1	5%	0.02606
Total Payment Reduction For the Quarterly (In Lakh) [5]				0.02606
To be Paid for the Quarter / Demand (In Lakh) [6]				1.96504

Date of Inspection by E/I or his agent

Prepared by Contractor's self Control Unit

Date: 14/9/22

Signature of person inspecting road

ABHISHEK KUMAR (AE)
Name and Designation of person inspecting road

Abhishek
14/09/22
(Signature)

Certify by [Signature] Date 14/9/22

[illegible]

Standard Work Item		Work	Unit of work required in each Kilometre										Comments
No	Name	Units	1	2	3	4	5	6	7	8	9	10	
OM300 Drainage including culverts major and minor bridges													
OM301	Surface Drains & Verge	Lm	NA	NA	NA	NA							Not Required
OM302	Culvert Cleaning	Lm	Nil	Nil	Nil	Nil							Not Required
OM303	Culvert and Pit Repair	m ³	Nil	Nil	Nil	Nil							Not Required
	Other activities												Not Required
OM400 Vegetation													
	Grass Control												Not Required
OM401	(a) Roadside General Tidy	Ha	Nil	Nil	Nil	Nil							Not Required
	(b) Clear near safety signs, kilometer posts and roadside furniture	Ha	Nil	Nil	Nil	Nil							Not Required
OM402	Tree and Shrub Management	Ha	Nil	Nil	Nil	Nil							Not Required
	Other activities												
OM500 Signage and Road Safety													
OM501	Signs Maintenance	No	Nil	Nil	Nil	Nil							Not Required
OM502	Guard stones	Lm	NA	NA	NA	NA							Not Required
OM503	Distance Stones	No	NA	NA	NA	NA							Not Required
OM504	Road Markings	No	Nil	Nil	Nil	Nil							Not Required
	Other activities												

Uttar Bihar Construction Co
Bidder

Phishu
14/8/22
Appendix

09/09/22
Executive Engineer,
RWD, Works Division, Raxaul

Name of Customer : M/S Uttar Bihar Construction Co.
 Name of Work/ Road : Koriya BPO to G.B.C.
 Lab Job number :
 Date : 30-07-2022
 Section No. : 25


Test Date : 30-07-2022
 Machine No : 437
 Start S No :
 Start E No :
 Weather : Normal
 Start Location :
 End Location :
 Road Name : Koriya BPO to G.B.C.
 Road Type : (R) RURAL ROAD
 Side :
 UV Range : 1936 To 5000 mm/km
 Dist Range : 0 To 3.9 Interval 0.1
 Equation : $Y = 0 \cdot X^2 + 0.954 \cdot X + 134.5$

Print Generate Report and Graph

Redraw Graph

Map View

File : D:\2022\Bump Integrator 2022\Raxaul Div Bump\Raxaul Bump e 30.7.22\Raxaul Bmp e 30.7.22\30071640.Xls.
 Name of Customer : M/S Uttar Bihar Construction Com., Name of Work/ Road : Koriya BPO to G.B.C. Lab Job number



1936 0 0.1 0.2 0.3 0.4 0.5 0.6 0.7 0.8 0.9 1 1.1 1.2 1.3 1.4 1.5 1.6 1.7 1.8 1.9 2 2.1 2.2 2.3 2.4 2.5 2.6 2.7 2.8 2.9 3 3.1 3.2 3.3 3.4 3.5 3.6 3.7 3.8

Distance * 1000 m

30/7/22

30/7/22

8/19/22

Name of Road :- Koriya BPO to G.B.C
Contractor Name:- M/S Uttar Bihar Construction Com.

Scheme:- MR New Maintenance Policy
Division:- Raxaul

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km ROAD	CATEGORY	Latitude	Longitude	Event
30/7/22	10:1:7	25	0.1	360	0	3600	3568 G		26.89603	84.97781	Normal
30/7/22	10:1:7	25	0.1	360	20.2	3600	3568 G		26.89603	84.97885	Normal
30/7/22	10:2:0	25	0.1	380	20.2	3800	3759 G		26.89655	84.97974	Normal
30/7/22	10:2:17	25	0.1	380	20.2	3800	3759 G		26.89737	84.97959	Normal
30/7/22	10:2:17	25	0.1	400	30.3	4000	3950 G		26.89819	84.97932	Normal
30/7/22	10:2:17	25	0.1	310	30.3	3100	3091 G		26.89903	84.98035	Normal
30/7/22	10:2:17	25	0.1	320	40.4	3200	3187 G		26.89974	84.98075	Normal
30/7/22	10:2:52	25	0.1	340	40.4	3400	3378 G		26.89997	84.98190	Normal
30/7/22	10:3:0	25	0.1	380	20.2	3800	3759 G		26.89995	84.98304	Normal
30/7/22	10:3:0	25	0.1	340	20.2	3400	3378 G		26.89964	84.98402	Normal
30/7/22	10:3:28	25	0.1	390	10.1	3900	3855 G		26.90048	84.98420	Normal
30/7/22	10:4:0	25	0.1	350	30.3	3500	3473 G		26.90132	84.98425	Normal
30/7/22	10:4:3	25	0.1	400	40.4	4000	3950 G		26.90227	84.98430	Normal
30/7/22	10:4:3	25	0.1	320	30.3	3200	3187 G		26.90323	84.98443	Normal
30/7/22	10:4:3	25	0.1	400	30.3	4000	3950 G		26.90405	84.98488	Normal
30/7/22	10:4:3	25	0.1	370	20.2	3700	3664 G		26.90485	84.98523	Normal
30/7/22	10:4:38	25	0.1	360	20.2	3600	3568 G		26.90492	84.98626	Normal
30/7/22	10:5:0	25	0.1	350	30.3	3500	3473 G		26.90514	84.98718	Normal
30/7/22	10:5:14	25	0.1	390	20.2	3900	3855 G		26.90525	84.98814	Normal
30/7/22	10:5:14	25	0.1	380	20.2	3800	3759 G		26.90627	84.98867	Normal
30/7/22	10:6:0	25	0.1	370	20.2	3700	3664 G		26.90714	84.98900	Normal
30/7/22	10:6:24	25	0.1	360	20.2	3600	3568 G		26.90800	84.98919	Normal
30/7/22	10:6:59	25	0.1	340	20.2	3400	3378 G		26.90848	84.98932	Normal
30/7/22	10:7:0	25	0.1	390	20.2	3900	3855 G		26.90907	84.99062	Normal
30/7/22	10:7:35	25	0.1	300	20.2	3000	2996 G		26.90942	84.99151	Normal
30/7/22	10:8:10	25	0.1	380	20.2	3800	3759 G		26.90954	84.99217	Normal
30/7/22	10:20:0	25	0.1	370	20.2	3700	3664 G		26.89889	84.98456	Normal
30/7/22	10:20:18	25	0.1	400	20.2	4000	3950 G		26.89820	84.98525	Normal
30/7/22	10:20:18	25	0.1	300	30.3	3000	2996 G		26.89763	84.98601	Normal
30/7/22	10:20:18	25	0.1	310	40.4	3100	3091 G		26.89706	84.98673	Normal
30/7/22	10:20:18	25	0.1	310	30.3	3100	3091 G		26.89644	84.98752	Normal
30/7/22	10:21:0	25	0.1	370	10.1	3700	3664 G		26.89588	84.98831	Normal
30/7/22	10:21:28	25	0.1	390	20.2	3900	3855 G		26.89529	84.98909	Normal
30/7/22	10:22:02	25	0.1	400	20.2	4000	3950 G		26.89460	84.98986	Normal
30/7/22	10:22:13	25	0.1	400	20.2	4000	3950 G		26.89460	84.98986	Normal
30/7/22	10:22:18	25	0.1	400	20.2	4000	3950 G		26.89461	84.98986	Normal
30/7/22	10:22:19	25	0.1	400	20.2	4000	3950 G		26.89461	84.98986	Normal
30/7/22	10:22:36	25	0.1	400	20.2	4000	3950 G		26.89461	84.98986	Normal
Total:-							137412				
Avg IRI :-							3616				

$$Y = 0 * X^2 + 0.954 * X + 134.5$$

$$X = 11695$$

$$Y = 11291$$

(R) RURAL ROAD


Good Average Poor

<4000 4001-5000 >5001

Handwritten signature and date 30/9/22


Handwritten signature and date 30/9/22

Handwritten signature and date 30/9/22

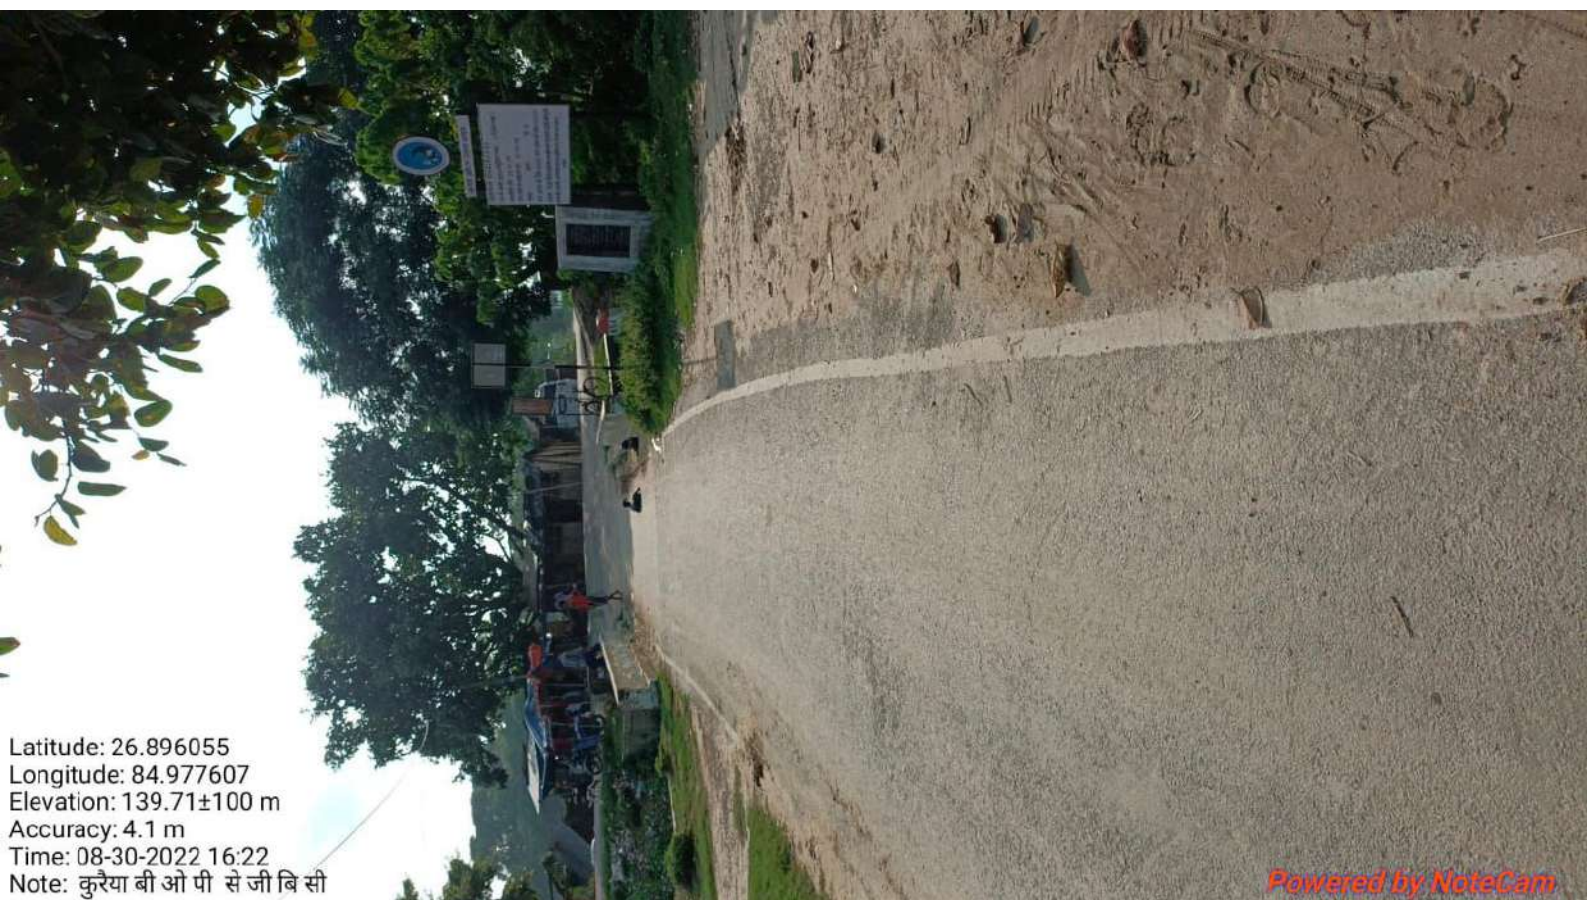


Latitude: 26.896055
Longitude: 84.977607
Elevation: 139.71±100 m
Accuracy: 4.1 m
Time: 08-30-2022 16:22
Note: कुरैया बी ओ पी से जी बि सी

Powered by NoteCam

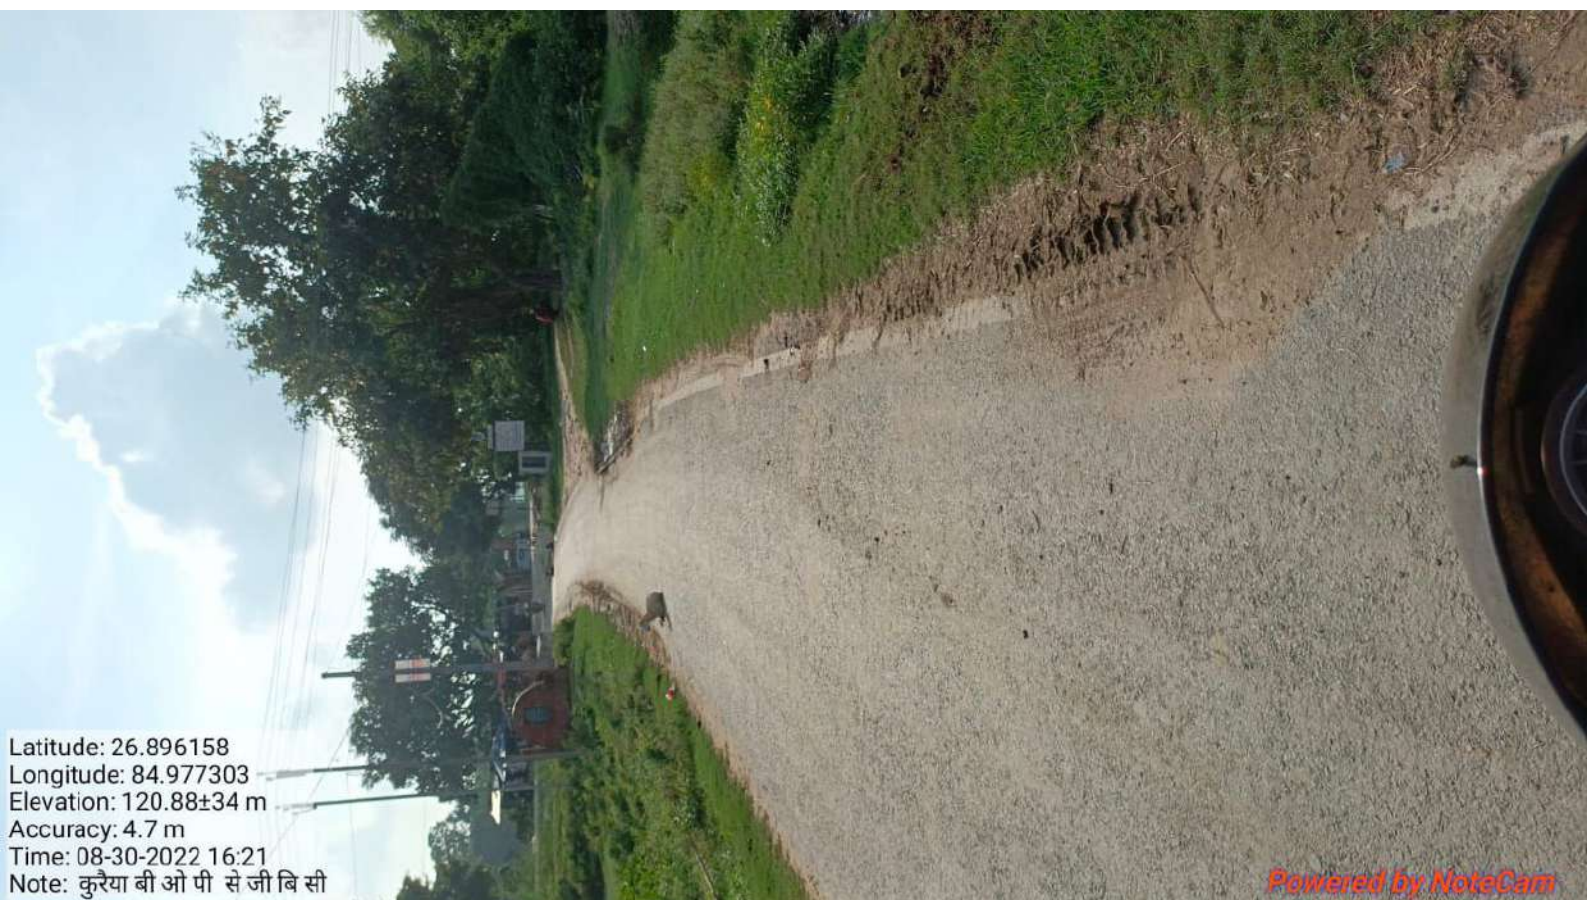


Latitude: 26.896158
Longitude: 84.977303
Elevation: 120.88±34 m
Accuracy: 4.7 m
Time: 08-30-2022 16:21
Note: कुरेया बी ओ पी से जी बि सी

Powered by NoteCam

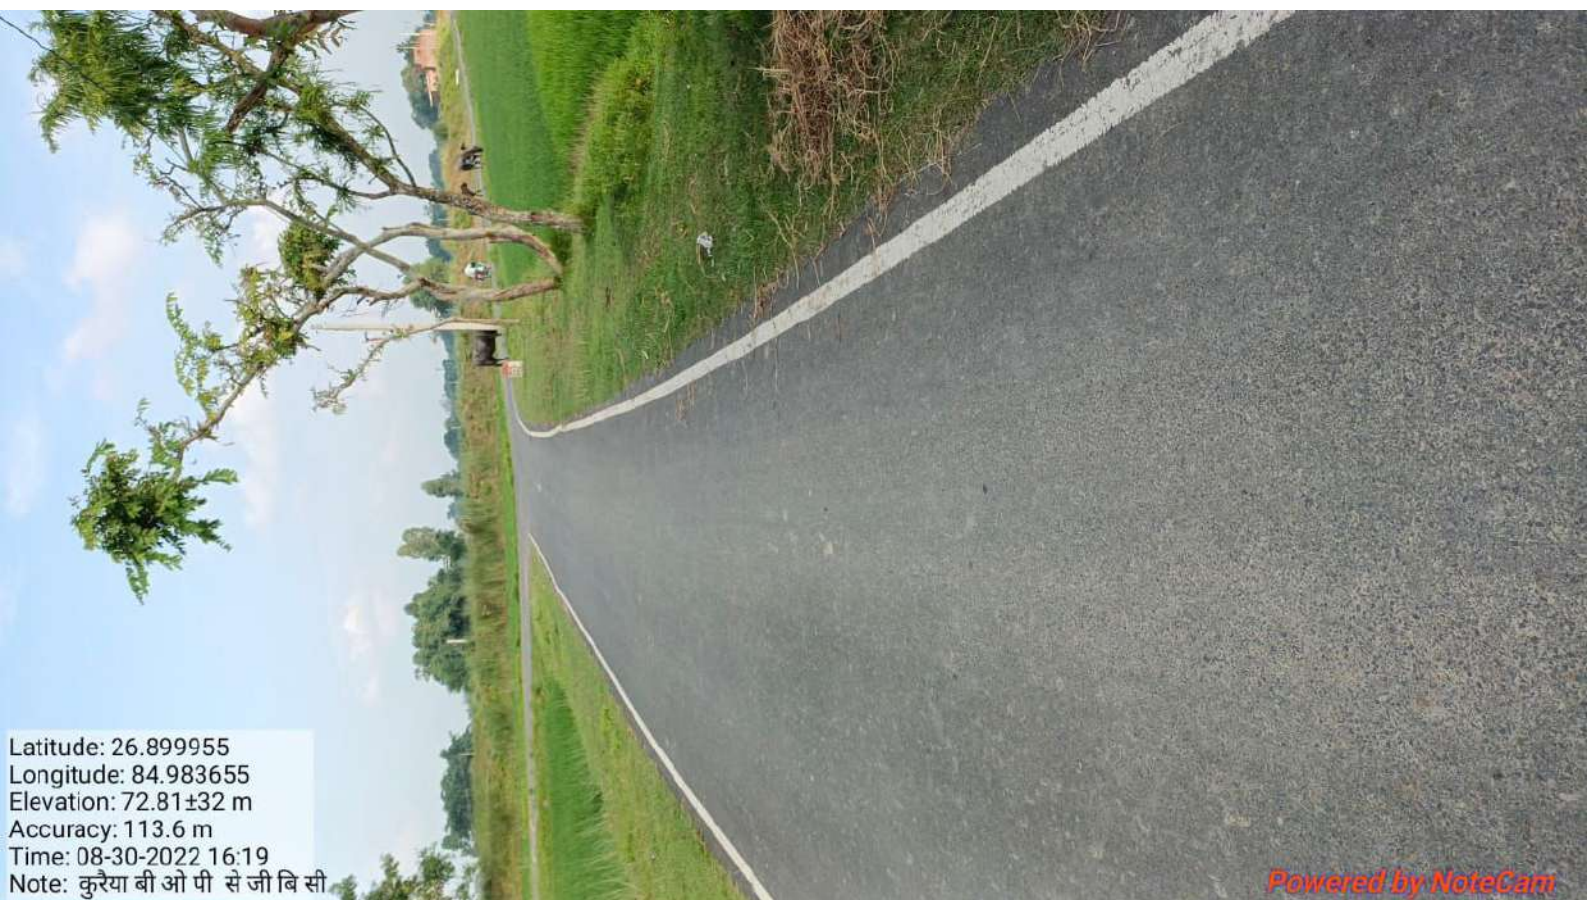


Latitude: 26.899955
Longitude: 84.983655
Elevation: 72.81±32 m
Accuracy: 113.6 m
Time: 08-30-2022 16:19
Note: कुरैया बी ओ पी से जी बि सी

Powered by NoteCam

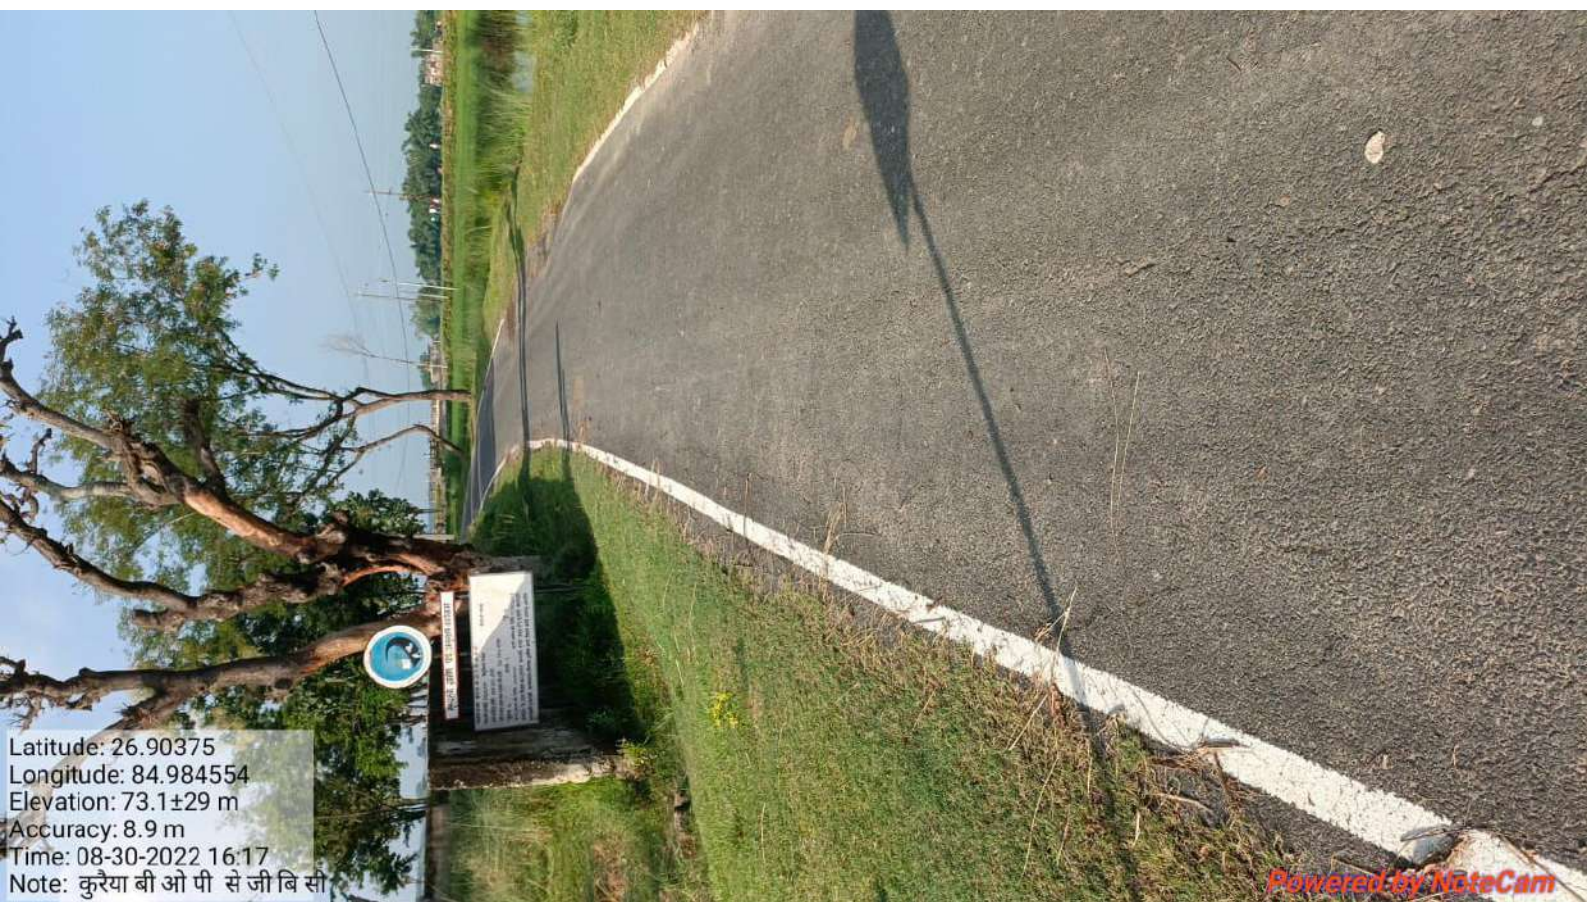

Latitude: 26.90375
Longitude: 84.984554
Elevation: 73.1±29 m
Accuracy: 8.9 m
Time: 08-30-2022 16:17
Note: कुरेया बी ओ पी से जी बि सी

Powered by NoteCam

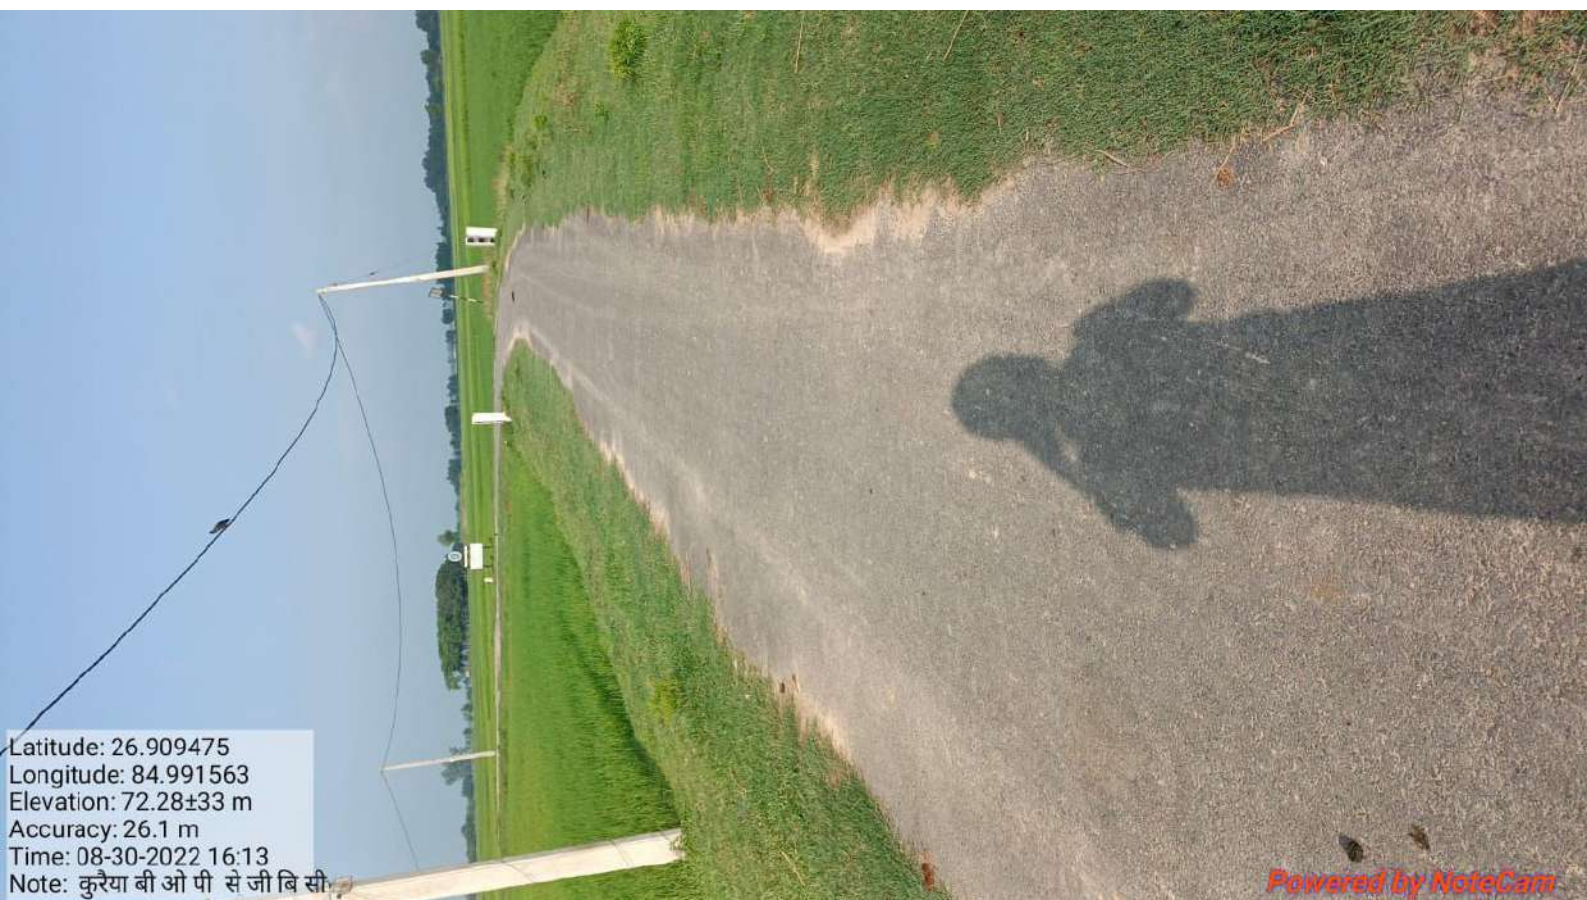

Latitude: 26.909475
Longitude: 84.991563
Elevation: 72.28±33 m
Accuracy: 26.1 m
Time: 08-30-2022 16:13
Note: कुरेया बी ओ पी से जी बि सी

Powered by NoteCam
