

कार्यपालक अभियंता का कार्यालय ग्रामीण कार्य विभाग, कार्य प्रमण्डल, औरंगाबाद

पत्रांक 1938 अनु0

प्रेषक,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमण्डल, औरंगाबाद।

सेवा में,

नोडल पदाधिकारी, (MR304

ग्रामीण कार्य विभाग, पटना, बिहार।

औरंगाबाद, दिनांक 09-09-2022

विषय:-


नई अनुरक्षण नीति-2018 MR(3054) योजना के अन्तर्गत पाँच वर्षीय रख-रखाव पथ में कराये गये कार्य के विरुद्ध आवंटन उपलब्ध कराने के संबंध में।


महाशय,

उपरोक्त विषय के संबंध में सूचित करना है कि नई अनुरक्षण नीति-2018 MR(3054) योजना के अन्तर्गत पाँच वर्षीय रख-रखाव पथ में कराये गये कार्य के लिए सम्वेदक को भुगतान करने हेतु अधिचाचना विहित प्रपत्र में भरकर आवश्यक कार्रवाई हेतु समर्पित की जाती है।

अनु0:-आवंटन माँग पत्र की प्रति संलग्न।

विश्वासभाजन


कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमण्डल, औरंगाबाद।


21/9/22

Name of Works Division:- Aurangabad

Aurangabad (Bihar)

Executive Engineer
RWD, Works Division
Aurangabad (Bihar)

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

Pr. Name **3rd A. Aurangabad**

1	Name of the Road	XXX	Amba Nabinagar to Suh	
2	Batch No	XXX	RM/AU/AUR/19/0026	
3	Project ID	XXX	NEA22000/78	
4	Total Length of Road (in Km)	0.00	2.4 km	
5	Length of Road to Meet Required Service Level [Completed length] (in Km) [1]	0	2.4 km	
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20	—	
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	0	23.020 lac	
8	Quarterly Payment 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	0	1.15100 lac	
Compliance Criteria	Standard Job Description	Non- Compliance		Reduction Payment [6] - [3] / [1] * [2] * [4]
		Length Non- Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGEWAY)		60%	0.00 0.00
II	SHOULDERS AND EMBANKMENTS		10%	0.00 0.00
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES		15%	0.00 0.00
IV	SIGNAGE AND ROAD SAFETY		10%	0.00 0.00
V	VEGETATION		5%	0.00 0.00
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]			0.00	0.00
TO BE PAID FOR THE QUARTER / DEMAND (in Lakh) [6]			0.00	1.15100 lac

Inspected by E/I or his agent

Controlled by Contractor's self Control unit

Sah
06/09/2022
AE

Name and designation of person inspecting road

(Signature)

Date

Pranav
6/9/2022

Signature of person inspecting road

Certify by E/I [signature] Date:-

Pranav
06/9/22
EE

Name of Contractor: Chandan kr singh

Name of road : Amba nabinagar road to Suhri

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR	IRI, CATEGORY	Latitude	ongitude	Event	Y * 0 * X ^ 2 + 0.816 * X + 249
11/8/22	10:48:32	45	0.1	280	0	2800	2533 G	24.61542	84.21099	Normal	X = 3400
11/8/22	10:49:9	45	0.1	280	20.2	2800	2533 G	24.61636	84.21106	Normal	Y = 2815
11/8/22	10:49:9	45	0.1	340	20.2	3400	3023 G	24.61726	84.21114	Normal	
11/8/22	10:49:45	45	0.1	290	20.2	2900	2615 G	24.61815	84.2112	Normal	
11/8/22	10:50:0	45	0.1	290	20.2	2900	2615 G	24.61904	84.21123	Normal	(R) RURAL ROAD
11/8/22	10:50:0	45	0.1	380	20.2	3800	3349 G	24.61996	84.2113	Normal	Good
11/8/22	10:50:20	45	0.1	250	20.2	2500	2288 G	24.6209	84.21136	Normal	<4000
11/8/22	10:51:0	45	0.1	360	10.1	3600	3186 G	24.62183	84.21143	Normal	
11/8/22	10:51:31	45	0.1	360	10.1	3600	3186 G	24.62272	84.2115	Normal	
11/8/22	10:51:31	45	0.1	250	20.2	2500	2288 G	24.62359	84.21162	Normal	
11/8/22	10:52:6	45	0.1	260	20.2	2600	2370 G	24.62449	84.21175	Curve	
11/8/22	10:52:6	45	0.1	250	20.2	2500	2288 G	24.6247	84.21091	Normal	
11/8/22	10:52:41	45	0.1	320	20.2	3200	2860 G	24.62519	84.2104	Normal	
11/8/22	10:53:0	45	0.1	300	20.2	3000	2696 G	24.6261	84.21069	Normal	
11/8/22	10:53:16	45	0.1	350	10.1	3500	3104 G	24.62702	84.21082	Speed Breaker	
11/8/22	10:53:16	45	0.1	290	10.1	2900	2615 G	24.62792	84.21099	Normal	
11/8/22	10:54:0	45	0.1	380	10.1	3800	3349 G	24.62851	84.21064	Normal	
11/8/22	10:54:26	45	0.1	260	10.1	2600	2370 G	24.62894	84.20988	Normal	
11/8/22	10:54:26	45	0.1	380	10.1	3800	3349 G	24.62986	84.21005	Normal	
11/8/22	10:55:1	45	0.1	310	10.1	3100	2778 G	24.63062	84.21047	Normal	
11/8/22	10:55:16	45	0.1	310	10.1	3100	2778 G	24.63062	84.21047	Normal	
11/8/22	10:55:37	45	0.1	380	10.1	3800	3349 G	24.63141	84.21086	Speed Breaker	
11/8/22	10:56:12	45	0.1	340	10.1	3400	3023 G	24.63232	84.21071	Normal	
11/8/22	10:56:12	45	0.1	340	10.1	3400	3023 G	24.63322	84.21045	Normal	

JE
11/8/22

AE
11/8/22

EE
11/8/22

Steco Anal/zer

Name of Customer : Chondan kumar Singh
Name of Work/ Road : Amba Nabunagar road to Suhli
Lab Job number :
Date : 11-08-2022
Section No. : 45

Print

Generate Report and Graph

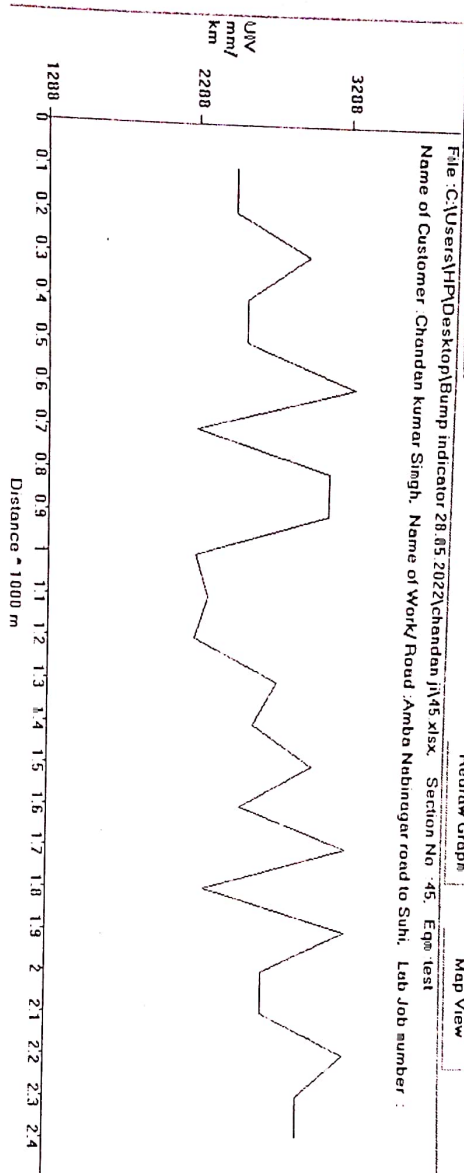
File : C:\Users\HP\Desktop\Bump Indicator 28.05.2022\chondan jk45.xlsx Section No : 45, Ego : test

Name of Customer : Chondan kumar Singh, Name of Work/ Road : Amba Nabunagar road to Suhli, Lab Job number :

Test Date :	11-08-2022	Road Name :	
Machine No :		Road Type :	(R) RURAL ROAD
Start S No :		Side :	
Start E No :		U/V Range :	1288 To 4000 Interval 1000
Weather :		Dist Range :	0 To 5 0.1 = 1000 m
Start Location :		Equation :	test
End Location :			

Redraw Graph

Map View



Chondan kumar Singh
JE

AE
18/08/22

AE
18/08/22
