

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, सिवान-2

पत्रांक.....1784 अनु०..... सिवान, दिनांक 15/09/2022

प्रेषक,
कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, सिवान-2

सेवा में,
नोडल पदाधिकारी
बिहार ग्रामीण पथ नई अनुरक्षण नीति-2018
ग्रामीण कार्य विभाग, बिहार, पटना।

विषय:- योजना शीर्ष बिहार ग्रामीण पथ नई अनुरक्षण नीति-2018 के तहत पूर्ण कराये गये पथों के अनुरक्षण कार्य का आवंटन उपलब्ध कराने के संबंध में।

महाशय,


उपर्युक्त विषय के संबंध में कहना है कि योजना शीर्ष बिहार ग्रामीण पथ नई अनुरक्षण नीति-2018 के अन्तर्गत पूर्ण कराये गये पथों का अनुरक्षण कार्य के भुगतान हेतु विवरणी विहित प्रपत्र में तैयार कर इस पत्र के साथ संलग्न किया जा रहा है।

अतः अनुरोध है कि प्रपत्र के अनुसार आवंटन उपलब्ध कराने की कृपा की जाए। ताकि संवेदक के अनुरक्षण की राशि ससमय भुगतान किया जा सके।

अनु०-यथोक्त।

विश्वासभाजन


कार्यपालक अभियंता
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
सिवान-2


15/9/22

Bihar Rural Road Maintenance Policy-2018

Sl.No.	Actual Maintenance Expenditure						Length as per Bump Report	IRI As per bump Report	Current Maintenance Demand (in Lakhs)							Remarks	
	1st. Year Maintenance	2nd. Year Maintenance	3rd. Year Maintenance	4th Year Maintenance	5th Year Maintenance	Total Maintenance Expenditure			1st QTR Maintenance	2nd QTR Maintenance	3rd QTR Maintenance	4th QTR Maintenance	5th QTR Maintenance	6th QTR Maintenance	7th QTR Maintenance		Total
1	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	32
1	-	-	-	-	-	-	2.5	3623	1.29979	-	-	-	-	-	-	1.29979	
2	-	-	-	-	-	-	5.8	3729	3.13645	-	-	-	-	-	-	3.13645	
3	-	-	-	-	-	-	2.8	3730	0.7505	0.7505	0.7505	0.7505	-	-	-	3.0020	
4	-	-	-	-	-	-	1.7	3149	0.76902	0.76902	0.76902	0.76902	-	-	-	3.07068	
5	-	-	-	-	-	-	10.4	3590	4.98023	4.98023	4.98023	4.98023	-	-	-	19.92092	
																30.42984	

Divisional Accounts Officer
RWD, Works Div. Siwan-2

T.P. Saha
15/09/22
A.E.

Executive Engineer
R.W.D. Works Division
Siwan-2
15-9-22

Requisition Format for Scheme Head - MRR (3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division :- Siwan-2

Government of Bihar

OM01

Rural works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From- Repair of Road from Guthani to Solhagara

Length of Road: 10.4 KM

Period : From.....

Inspector: A.E RWD Sub Division, Guthani

To: Executive Engineer
RWD Works Division Siwan-2

Date:

Position: A.E

Inspector: A.E.RWD Sub Division, Guttamati			Units of work required in each kilometre										Comments
Standard Work item		Work	1	2	3	4	5	6	7	8	9	10	
S No	Name	Units											
OM100 Sealed Pavement													
OM101	Pothole Patching	m2	Nil	Nil	Nil	Nil							No. Pothole found.
OM102	Surface Depression and Rut Patching	m2	Nil	Nil	Nil	Nil							No Surface Depression and Rut Patching found
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil							No Crack Sealing found
Surface Treatment													
OM104	(a) Loss of Aggregate (Surface Ravelling)	m2	Nil	Nil	Nil	Nil							No Loss of Aggregate (Surface Ravelling) found
	(b) Bleeding/Flushing	m2	Nil	Nil	Nil	Nil							No Bleeding/Flushing Required
	(c) Crocodile Cracking	m2	Nil	Nil	Nil	Nil							No Crocodile Cracking found
OM105	Edge Repair	m2	Nil	Nil	Nil	Nil							No Edge Repair Required
OM106	Digouts	m2	N/A	N/A	N/A	N/A							
OM107	Concrete Pavement	m3	N/A	N/A	N/A	N/A							
Other activities		Lm											
OM200 Shoulder													
Unsealed Shoulder		No											No Edge Drop off Required
OM201	(a) Edge Drop off	Lm	Nil	Nil	Nil	Nil							Defects rectified within stipulated time.
	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil	Nil	Nil							No Holding water found
	(c) Holding Water	Lm	Nil	Nil	Nil	Nil							No Embankment Repair Required
	Embankment Repair	No	Nil	Nil	Nil	Nil							Defects rectified within stipulated time.
OM202	Other Activitie (Raincut)		3%	1%	2%	Nil							
OM 300 Drainage including culverts major													
OM301	Surface Drains & Verge	Lm	N/A	N/A	N/A	N/A							Not Required
OM302	Culvert Cleaning	Lm											Culvert maintain within stipulated time
OM303	Culvert and Pit repair	m2	Nil	Nil	Nil	Nil							Not Required

	Other activities (White washing)	m ²	Nil	Nil	Nil	Nil												Not Required
	OM 400 Vegetation																	Not Required
	Grass Control																	Not Required
	a) Roadside-General Tidy	Ha	Nil	Nil	Nil	Nil												Not Required
OM401	b) Clear near Safety signs, kilometre posts and roadside furniture	Ha	Nil	Nil	Nil	Nil												Not Required
	Tree and shrub management	No	Nil	Nil	Nil	Nil												Not Required
	Cutting trees	No	Nil	Nil	Nil	Nil												Not Required
OM402	Cutting Shrubs	No	Nil	Nil	Nil	Nil												Not Required
	Other activities (Trimming of Grass)	M2	Nil	Nil	Nil	Nil												Not Required
OM500	Safety Signage and Road																	Not Required
OM501	Signs Maintenance	No	Nil	Nil	Nil	Nil												Not Applicable
OM502	Guard Stones	Lm	N/A	N/A	N/A	N/A												Not Applicable
OM503	Distance Stones	No	N/A	N/A	N/A	N/A												Not Required
OM504	Road Marking	m ²	Nil	Nil	Nil	Nil												Not Required
	Other activities																	

Bidder

Appendix

Executive Engineer, Rural Work Department, Work
Division, Siwan-2

15/6/22

7.1.12
13/09/22
A-2

13-06-22

Name of work : Repair of Road from Gulthani to Sohagara

Name of customer : M/S KUNAL CONSTRUCTION

(R)Rural Road

Good	Average	Poor
< 4000	4001 - 5000	> 5000

Date	Time	Test No	Distance(m)	Total Distance(m)	BUM(cm)	Speed(Km/Hr)	Ulmv/Km	Corrected Ul (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction	Remarks
20/05/22	10:21:59	37	100	100	13.0 cm	13.9 Km/Hr	1300.0 mm/Km	1428	2.08	Good	26.1681566	N	84.0400248	E	Breaker
20/05/22	10:22:58	37	100	200	21.0 cm	16.0 Km/Hr	2100.0 mm/Km	2151	2.99	Good	26.1678438	N	84.0401392	E	Normal
20/05/22	10:23:37	37	100	300	32.0 cm	19.0 Km/Hr	3200.0 mm/Km	3145	4.2	Good	26.1681566	N	84.0401697	E	Normal
20/05/22	10:24:06	37	100	400	25.0 cm	22.3 Km/Hr	2500.0 mm/Km	2512	3.44	Good	26.1681566	N	84.0401697	E	Normal
20/05/22	10:24:42	37	100	500	30.0 cm	20.1 Km/Hr	3000.0 mm/Km	2964	3.99	Good	26.1681566	N	84.0401697	E	Normal
20/05/22	10:25:10	37	100	600	34.0 cm	23.1 Km/Hr	3400.0 mm/Km	3328	4.42	Good	26.1681566	N	84.0401697	E	Normal
20/05/22	10:25:39	37	100	700	30.0 cm	22.2 Km/Hr	3000.0 mm/Km	2964	3.99	Good	26.1681566	N	84.0401697	E	Normal
20/05/22	10:26:15	37	100	800	31.0 cm	20.1 Km/Hr	3100.0 mm/Km	3055	4.09	Good	26.1681566	N	84.0401697	E	Normal
20/05/22	10:27:02	37	100	900	27.0 cm	17.7 Km/Hr	2700.0 mm/Km	2693	3.66	Good	26.1681566	N	84.0401697	E	Normal
20/05/22	10:27:51	37	100	1000	23.0 cm	17.2 Km/Hr	2300.0 mm/Km	2332	3.22	Good	26.1681566	N	84.0401697	E	Breaker
20/05/22	10:28:33	37	100	1100	32.0 cm	18.4 Km/Hr	3200.0 mm/Km	3145	4.2	Good	26.1681566	N	84.0401697	E	Normal
20/05/22	10:28:59	37	100	1200	26.0 cm	13.9 Km/Hr	2600.0 mm/Km	2603	3.55	Good	26.1681566	N	84.0401697	E	Normal
20/05/22	10:29:23	37	100	1300	29.0 cm	14.8 Km/Hr	2900.0 mm/Km	2874	3.88	Good	26.1681566	N	84.0401697	E	Normal
20/05/22	10:29:49	37	100	1400	29.0 cm	13.9 Km/Hr	2900.0 mm/Km	2874	3.88	Good	26.1681566	N	84.0401697	E	Breaker
20/05/22	10:30:14	37	100	1500	28.0 cm	14.1 Km/Hr	2800.0 mm/Km	2784	3.77	Good	26.1681566	N	84.0401697	E	Normal
20/05/22	10:30:38	37	100	1600	27.0 cm	15.0 Km/Hr	2700.0 mm/Km	2693	3.66	Good	26.1681566	N	84.0401697	E	Normal
20/05/22	10:31:01	37	100	1700	24.0 cm	15.7 Km/Hr	2400.0 mm/Km	2422	3.33	Good	26.1681566	N	84.0401697	E	Normal
20/05/22	10:31:24	37	100	1800	26.0 cm	15.7 Km/Hr	2600.0 mm/Km	2803	3.55	Good	26.1681566	N	84.0401697	E	Normal
20/05/22	10:31:46	37	100	1900	27.0 cm	16.2 Km/Hr	2700.0 mm/Km	2693	3.66	Good	26.1819154	N	84.0468912	E	Normal
20/05/22	10:32:08	37	100	2000	29.0 cm	16.5 Km/Hr	2900.0 mm/Km	2874	3.88	Good	26.1829958	N	84.0471353	E	Normal
20/05/22	10:32:32	37	100	2100	28.0 cm	15.3 Km/Hr	2800.0 mm/Km	2784	3.77	Good	26.1837339	N	84.0473337	E	CD

Name of work : Repair of Road from Gultani to Sohagara															
Name of customer : MIS KUNAL CONSTRUCTION															
(R)Rural Road															
Good		Average				Poor									
< 4000		4001 - 6000				> 6000									
20/05/22	10.32.53	37	100	2200	26.0 cm	16.6 Km/Hr	2600.0 mm/Km	2603	3.55	Good	26.1845713	N	84.0475244	E	Normal
20/05/22	10.33.16	37	100	2300	26.0 cm	15.4 Km/Hr	2600.0 mm/Km	2784	3.77	Good	26.1855603	N	84.0476923	E	Normal
20/05/22	10.33.38	37	100	2400	26.0 cm	15.5 Km/Hr	2600.0 mm/Km	2784	3.77	Good	26.1864519	N	84.0481653	E	Normal
20/05/22	10.34.02	37	100	2500	29.0 cm	16.2 Km/Hr	2900.0 mm/Km	2874	3.88	Good	26.1872358	N	84.0484705	E	Normal
20/05/22	10.34.36	37	100	2600	31.0 cm	10.5 Km/Hr	3100.0 mm/Km	3055	4.09	Good	26.1877050	N	84.0486002	E	Normal
20/05/22	10.34.59	37	100	2700	33.0 cm	16.3 Km/Hr	3300.0 mm/Km	3236	4.31	Good	26.1877050	N	84.0486002	E	CD
20/05/22	10.35.30	37	100	2800	26.0 cm	11.5 Km/Hr	2600.0 mm/Km	2803	3.55	Good	26.1877050	N	84.0486002	E	Normal
20/05/22	10.36.06	37	100	2900	20.0 cm	19.3 Km/Hr	2000.0 mm/Km	2060	2.88	Good	26.1877050	N	84.0486002	E	Normal
20/05/22	10.36.32	37	100	3000	26.0 cm	15.3 Km/Hr	2600.0 mm/Km	2803	3.55	Good	26.1877050	N	84.0486002	E	Normal
20/05/22	10.36.57	37	100	3100	21.0 cm	14.2 Km/Hr	2100.0 mm/Km	2151	2.99	Good	26.1877050	N	84.0486002	E	Normal
20/05/22	10.37.21	37	100	3200	25.0 cm	15.0 Km/Hr	2500.0 mm/Km	2512	3.44	Good	26.1877050	N	84.0486002	E	Normal
20/05/22	10.37.45	37	100	3300	29.0 cm	14.8 Km/Hr	2900.0 mm/Km	2874	3.88	Good	26.1877050	N	84.0486002	E	Normal
20/05/22	10.38.09	37	100	3400	27.0 cm	15.3 Km/Hr	2700.0 mm/Km	2893	3.66	Good	26.1877050	N	84.0486002	E	Breaker
20/05/22	10.38.40	37	100	3500	25.0 cm	11.3 Km/Hr	2500.0 mm/Km	2512	3.44	Good	26.1877050	N	84.0486002	E	Normal
20/05/22	10.39.04	37	100	3600	21.0 cm	15.1 Km/Hr	2100.0 mm/Km	2151	2.99	Good	26.1877050	N	84.0486002	E	Normal
20/05/22	10.39.31	37	100	3700	26.0 cm	13.2 Km/Hr	2600.0 mm/Km	2603	3.55	Good	26.1877050	N	84.0486002	E	Normal
20/05/22	10.40.39	37	100	3800	26.0 cm	15.4 Km/Hr	2600.0 mm/Km	2803	3.55	Good	26.1877050	N	84.0486002	E	Normal
20/05/22	10.41.19	37	100	3900	25.0 cm	19.0 Km/Hr	2500.2 mm/Km	2512	3.44	Good	26.1877050	N	84.0486002	E	Curve
20/05/22	10.41.52	37	100	4000	28.0 cm	20.8 Km/Hr	2800.0 mm/Km	2784	3.77	Good	26.1877050	N	84.0486002	E	Normal
20/05/22	10.42.14	37	100	4100	30.0 cm	16.5 Km/Hr	3000.0 mm/Km	2964	3.99	Good	26.1877050	N	84.0486002	E	Normal
20/05/22	10.42.37	37	100	4200	24.0 cm	16.0 Km/Hr	2400.0 mm/Km	2422	3.33	Good	26.1877050	N	84.0486002	E	Normal
20/05/22	10.43.04	37	100	4300	24.0 cm	17.8 Km/Hr	2400.0 mm/Km	2422	3.33	Good	26.1877050	N	84.0486002	E	Normal

Name of work		Repair of Road from Gulhani to Sohagara													
Name of customer		M/S KUNAL CONSTRUCTION													
(R)Rural Road															
Good		Average						Poor							
< 4000		4001 - 5000						> 5000							
20/05/22	10.43.31	37	100	4400	24.0 cm	15.5 Km/Hr	2400.0 mm/Km	2422	3.33	Good	26.1877050	N	84.0486002	E	Normal
20/05/22	10.43.52	37	100	4500	26.0 cm	16.5 Km/Hr	2600.0 mm/Km	2603	3.55	Good	26.1877050	N	84.0486002	E	Normal
20/05/22	10.44.14	37	100	4600	28.0 cm	16.9 Km/Hr	2600.0 mm/Km	2603	3.55	Good	26.1877050	N	84.0486002	E	Normal
20/05/22	10.44.34	37	100	4700	23.0 cm	17.5 Km/Hr	2300.0 mm/Km	2332	3.22	Good	26.2058153	N	84.0469751	E	Normal
20/05/22	10.44.56	37	100	4800	31.0 cm	16.7 Km/Hr	3100.0 mm/Km	3055	4.09	Good	26.2066336	N	84.0467005	E	Curve
20/05/22	10.45.16	37	100	4900	33.0 cm	17.5 Km/Hr	3300.0 mm/Km	3236	4.31	Good	26.2073088	N	84.0459452	E	Normal
20/05/22	10.45.36	37	100	5000	30.0 cm	16.5 Km/Hr	3000.0 mm/Km	2964	3.99	Good	26.2079229	N	84.0452667	E	Normal
20/05/22	10.46.00	37	100	5100	28.0 cm	16.6 Km/Hr	2800.0 mm/Km	2784	3.77	Good	26.2085752	N	84.0446939	E	Normal
20/05/22	10.46.22	37	100	5200	33.0 cm	16.0 Km/Hr	3300.0 mm/Km	3236	4.31	Good	26.2094736	N	84.0446100	E	Curve
20/05/22	10.46.48	37	100	5300	32.0 cm	14.1 Km/Hr	3200.0 mm/Km	3145	4.2	Good	26.2101488	N	84.0441904	E	Breaker
20/05/22	10.47.24	37	100	5400	27.0 cm	19.9 Km/Hr	2700.0 mm/Km	2693	3.66	Good	26.2103815	N	84.0431986	E	Normal
20/05/22	10.47.57	37	100	5500	25.0 cm	17.1 Km/Hr	2500.0 mm/Km	2512	3.44	Good	26.2104578	N	84.0429392	E	Normal
20/05/22	10.48.20	37	100	5600	25.0 cm	15.7 Km/Hr	2500.0 mm/Km	2512	3.44	Good	26.2104578	N	84.0429392	E	Curve
20/05/22	10.48.56	37	100	5700	23.0 cm	19.5 Km/Hr	2300.0 mm/Km	2332	3.22	Good	26.2104578	N	84.0429392	E	Normal
20/05/22	10.49.26	37	100	5800	25.0 cm	18.8 Km/Hr	2500.0 mm/Km	2512	3.44	Good	26.2104578	N	84.0429392	E	Normal
20/05/22	10.50.01	37	100	5900	28.0 cm	19.2 Km/Hr	2800.0 mm/Km	2784	3.77	Good	26.2104578	N	84.0429392	E	Normal
20/05/22	10.50.26	37	100	6000	31.0 cm	14.5 Km/Hr	3100.0 mm/Km	3055	4.09	Good	26.2104578	N	84.0429392	E	Normal
20/05/22	10.50.51	37	100	6100	29.0 cm	14.1 Km/Hr	2900.0 mm/Km	2874	3.88	Good	26.2104578	N	84.0429392	E	Normal
20/05/22	10.51.19	37	100	6200	34.0 cm	12.8 Km/Hr	3400.0 mm/Km	3326	4.42	Good	26.2104578	N	84.0429392	E	Normal
20/05/22	10.51.47	37	100	6300	23.0 cm	12.9 Km/Hr	2300.0 mm/Km	2332	3.22	Good	26.2104578	N	84.0429392	E	Normal
20/05/22	10.52.15	37	100	6400	26.0 cm	12.8 Km/Hr	2600.0 mm/Km	2603	3.55	Good	26.2104578	N	84.0429392	E	Normal
20/05/22	10.52.41	37	100	6500	26.0 cm	16.5 Km/Hr	2600.0 mm/Km	2603	3.55	Good	26.2104578	N	84.0429392	E	Curve

Name of work : Repair of Road from Guhani to Sohagara

Name of customer : M/S KUNAL CONSTRUCTION

(R)Rural Road

Good	Average	Poor
< 4000	4001 - 5000	> 5000

20/05/22	10.53.06	37	100	6600	23.0 cm	14.7 Km/Hr	2300.0 mm/Km	2332	3.22	Good	26.2104578	N	84.0429392	E	Normal
20/05/22	10.53.30	37	100	6700	25.0 cm	14.8 Km/Hr	2500.0 mm/Km	2512	3.44	Good	26.2104578	N	84.0429392	E	Normal
20/05/22	10.53.52	37	100	6800	21.0 cm	16.5 Km/Hr	2100.0 mm/Km	2151	2.99	Good	26.2104578	N	84.0429392	E	Normal
20/05/22	10.54.16	37	100	6900	20.0 cm	14.9 Km/Hr	2000.0 mm/Km	2060	2.88	Good	26.2104578	N	84.0429392	E	Normal
20/05/22	10.54.39	37	100	7000	28.0 cm	15.8 Km/Hr	2800.0 mm/Km	2784	3.77	Good	26.2104578	N	84.0429392	E	Normal
20/05/22	10.55.01	37	100	7100	30.0 cm	16.3 Km/Hr	3000.0 mm/Km	2964	3.99	Good	26.2104578	N	84.0429392	E	Normal
20/05/22	10.55.22	37	100	7200	30.0 cm	16.8 Km/Hr	3000.0 mm/Km	2964	3.99	Good	26.2104578	N	84.0429392	E	Normal
20/05/22	10.55.44	37	100	7300	22.0 cm	16.5 Km/Hr	2200.0 mm/Km	2241	3.11	Good	26.2104578	N	84.0429392	E	Normal
20/05/22	10.56.05	37	100	7400	26.0 cm	16.6 Km/Hr	2600.0 mm/Km	2603	3.55	Good	26.2104578	N	84.0429392	E	Normal
20/05/22	10.56.27	37	100	7500	26.0 cm	16.5 Km/Hr	2600.0 mm/Km	2603	3.55	Good	26.2104578	N	84.0429392	E	Normal
20/05/22	10.56.50	37	100	7600	25.0 cm	16.0 Km/Hr	2500.0 mm/Km	2512	3.44	Good	26.2104578	N	84.0429392	E	Normal
20/05/22	10.57.13	37	100	7700	32.0 cm	15.6 Km/Hr	3200.0 mm/Km	3145	4.2	Good	26.267103	N	84.0334540	E	Normal
20/05/22	10.57.37	37	100	7800	25.0 cm	14.7 Km/Hr	2500.0 mm/Km	2512	3.44	Good	26.2275610	N	84.0327597	E	Normal
20/05/22	10.58.01	37	100	7900	19.0 cm	15.4 Km/Hr	1900.0 mm/Km	1970	2.77	Good	26.2282553	N	84.0322733	E	Normal
20/05/22	10.58.24	37	100	8000	23.0 cm	15.3 Km/Hr	2300.0 mm/Km	2332	3.22	Good	26.2285089	N	84.0311823	E	Normal
20/05/22	10.58.47	37	100	8100	24.0 cm	15.6 Km/Hr	2400.0 mm/Km	2422	3.33	Good	26.2289476	N	84.0302439	E	Normal
20/05/22	10.59.09	37	100	8200	25.0 cm	16.2 Km/Hr	2500.0 mm/Km	2512	3.44	Good	26.2291994	N	84.0293665	E	Normal
20/05/22	10.59.31	37	100	8300	25.0 cm	16.6 Km/Hr	2500.0 mm/Km	2512	3.44	Good	26.2293882	N	84.0283899	E	Normal
20/05/22	11.00.03	37	100	8400	22.0 cm	17.4 Km/Hr	2200.0 mm/Km	2241	3.11	Good	26.2295580	N	84.0272303	E	Normal
20/05/22	11.00.41	37	100	8500	28.0 cm	19.1 Km/Hr	2800.0 mm/Km	2784	3.77	Good	26.2299829	N	84.0263987	E	Breaker
20/05/22	11.01.04	37	100	8600	31.0 cm	15.7 Km/Hr	3100.0 mm/Km	3055	4.09	Good	26.2301397	N	84.0255899	E	CD
20/05/22	11.01.26	37	100	8700	29.0 cm	16.6 Km/Hr	2900.0 mm/Km	2874	3.88	Good	26.2305593	N	84.0248880	E	Normal

Name of work : Repair of Road from Gultihari to Sohagara

Name of customer : M/S KUNAL CONSTRUCTION

(R) Rural Road

Good	Average	Poor
< 4000	4001 - 5000	> 5000

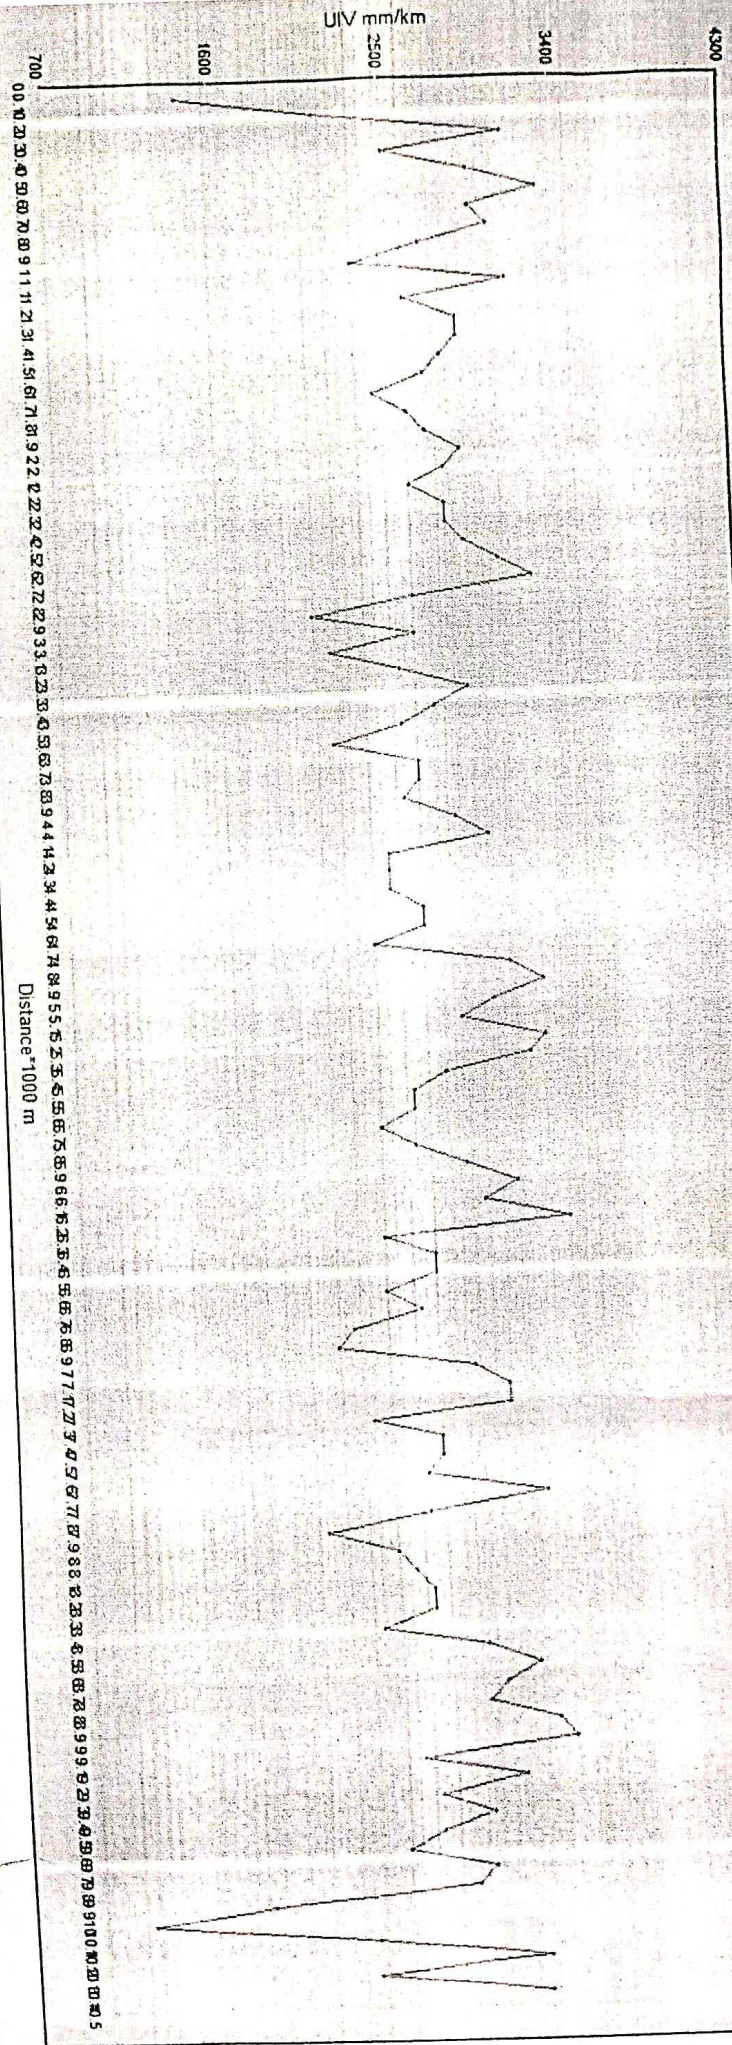
20/05/22	11/02/03	37	100	8800	28.0 cm	17.0 Km/Hr	2800.0 mm/Km	2784	3.77	Good	26.2314672	N	84.0239954	E	Breaker
20/05/22	11/02/45	37	100	8800	32.0 cm	18.4 Km/Hr	3200.0 mm/Km	3145	4.2	Good	26.232807	N	84.0238531	E	Normal
20/05/22	11/03/09	37	100	9000	33.0 cm	15.1 Km/Hr	3300.0 mm/Km	3296	4.31	Good	26.2329798	N	84.0231485	E	Normal
20/05/22	11/03/31	37	100	9100	24.0 cm	16.2 Km/Hr	2400.0 mm/Km	2422	3.33	Good	26.2338629	N	84.0230799	E	Normal
20/05/22	11/03/56	37	100	8200	30.0 cm	14.2 Km/Hr	3000.0 mm/Km	2964	3.99	Good	26.2345800	N	84.0229654	E	Normal
20/05/22	11/04/21	37	100	8300	25.0 cm	14.8 Km/Hr	2500.0 mm/Km	2512	3.44	Good	26.2346926	N	84.0218134	E	Normal
20/05/22	11/04/45	37	100	9400	28.0 cm	15.0 Km/Hr	2800.0 mm/Km	2784	3.77	Good	26.2350912	N	84.0208826	E	Normal
20/05/22	11/05/16	37	100	8500	26.0 cm	11.2 Km/Hr	2500.0 mm/Km	2512	3.44	Good	26.2352800	N	84.0206079	E	Normal
20/05/22	11/05/56	37	100	9600	23.0 cm	8.9 Km/Hr	2300.0 mm/Km	2332	3.22	Good	26.2352800	N	84.0206079	E	Normal
20/05/22	11/07/34	37	100	9700	28.0 cm	13.7 Km/Hr	2800.0 mm/Km	2784	3.77	Good	26.2352800	N	84.0206079	E	Normal
20/05/22	11/08/07	37	100	8600	27.0 cm	10.5 Km/Hr	2700.0 mm/Km	2693	3.66	Good	26.2352800	N	84.0206079	E	Normal
20/05/22	11/09/43	37	100	9500	15.0 cm	13.8 Km/Hr	1500.0 mm/Km	1608	2.31	Good	26.2371674	N	84.0168619	E	Normal
20/05/22	11/11/06	37	100	10000	8.0 cm	16.2 Km/Hr	800.0 mm/Km	976	1.48	Good	26.2374887	N	84.0159845	E	Normal
20/05/22	11/11/52	37	100	10100	21.0 cm	18.1 Km/Hr	2100.0 mm/Km	2151	2.99	Good	26.2378912	N	84.0150232	E	Normal
20/05/22	11/12/12	37	100	10200	31.0 cm	19.1 Km/Hr	3100.0 mm/Km	3055	4.09	Good	26.2378912	N	84.0150232	E	Normal
20/05/22	11/12/48	37	100	10300	21.0 cm	18.1 Km/Hr	2100.0 mm/Km	2151	2.99	Good	26.2378912	N	84.0150232	E	Normal
20/05/22	11/13/19	37	100	10400	31.0 cm	19.1 Km/Hr	3100.0 mm/Km	3055	4.09	Good	26.2378912	N	84.0150232	E	Normal

13-9-21
5-6

T.H.
13/09/21
A.A.

Handwritten signature

Name of Customer: M/S KUNAL CONSTRUCTION, Machine no: 19708, Road: Repair of Road from Gathani to Sahagara, Date: 20-05-22, Section No: 37, Equation: $Y=0.904X+252.3$



[Signature]
13/05/22

[Signature]
13/05/22
A.C

[Signature]
13/05/22

STANDARD FORMAT FOR ROADS QUARTELY STATEMENT

PIU Name :-

1st Quarter

1	Name of the Road	Repair of road from Gultani to Solagra		
2	Batch No.	RM/SI/SIW/19/0062		
3	Project ID	31406708029		
4	Total Length of Road (in Km)	11.00		
5	Length of Road to Meet Required Service Level [Completed Length] (in km) [1]	10.40		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	9960465.00		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	498023.00		
Compliance Criteria	Standard Job Description	Non-Compliance		Reduction Payment [6]=[3] / [1] * [2] * [4]
		Length Non-Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGE WAY)	0.0	60%	0.0
II	SHOULDERS AND EMBANKMENTS	0.0	10%	0.0
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0.0	15%	0.0
IV	SIGNAGE AND ROAD SAFETY	0.0	10%	0.0
V	VEGATAION	0.0	5%	0.0
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0.0
TO BE PAID FOR THE QUARTER / DEMAND (in Lakh) [6]				498023.00


Date of inspection by E/I or his agent prepared by Contractor's self Control unit

Name and Designation of person inspecting road


 30/06/22
 JRE
 (Md. Zahid)
 (Signature)

Date

Signature of person inspecting road


 30/06/22
 A-B


 15/9/22
 EXECUTIVE ENGINEER
 RWD, WORKS DIVISION
 SIWAN-2


 15/9/22

STANDARD FORMAT FOR ROADS QUARTELY STATEMENT

PIU Name :-

2nd Quarter

1	Name of the Road	Repair of road from Gulshan to Sakagra		
2	Batch No.	RM/SI/SIN/19/006		
3	Project ID	31406708029		
4	Total Length of Road (in Km)	11.00		
5	Length of Road to Meet Required Service Level [Completed Length] (in km) [1]	10.40		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	9960465 = 00		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	498023 = 00		
Compliance Criteria	Standard Job Description	Nnn-Compliance		Reduction Payment [6]=[3] / [1] * [2] * [4]
		Length Non-Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGE WAY)	0.0	60%	0.0
II	SHOULDERS AND EMBANMENTS	0.0	10%	0.0
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0.0	15%	0.0
IV	SIGNAGE AND ROAD SAFETY	0.0	10%	0.0
V	VEGATAION	0.0	5%	0.0
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0.0
TO BE PAID FOR THE QUARTER / DEMAND (in Lakh) [6]				498023 = 00

Date of inpection by E/I or his agent prepared by Contractor's self Control unit

Name and Designation of person inspecting road

31/06/22
JRE
(md. Zahid)
(Signature)

Date

Signature of person inspecting road

T.W.
30/06/22
A-B

EXECUTIVE ENGINEER
RWD, WORKS DIVISION
SIWAN-2

15/9/22

STANDARD FORMAT FOR ROADS QUARTELY STATEMENT


PIU Name :-

3rd Quarter

1	Name of the Road	Repair of road from Gulhani to Sahagra		
2	Batch No.	Km/SI/SIW/19/006		
3	Project ID	3406708029		
4	Total Length of Road (in Km)	11.00		
5	Length of Road to Meet Required Service Level [Completed Length] (in km) [1]	10.40		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	9960465.00		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	498023.00		
Compliance Criteria	Standard Job Description	Non-Compliance		Reduction Payment [6]=[3]/[1] * [2] * [4]
		Length Non-Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGE WAY)	0.0	60%	0.0
II	SHOULDERS AND EMBANMENTS	0.0	10%	0.0
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0.0	15%	0.0
IV	SIGNAGE AND ROAD SAFETY	0.0	10%	0.0
V	VEGETATION	0.0	5%	0.0
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0.0
TO BE PAID FOR THE QUARTER / DEMAND (in Lakh) [6]				498023.00

Date of inspection by E/I or his agent prepared by Contractor's self Control unit

Name and Designation of person inspecting road



30/06/22
JRE
(Md. Zahid)
(Signature)

Date

Signature of person inspecting road


30/06/22
A-E

EXECUTIVE ENGINEER
RWD, WORKS DIVISION
SIWAN-2


15/9/22

STANDARD FORMAT FOR ROADS QUARTELY STATEMENT

PIU Name :-

4th Quarter

1	Name of the Road	Repair of road from Gulshan to Sohagra		
2	Batch No.	RM/SI/SIW/19/0062		
3	Project ID	31406708029		
4	Total Length of Road (in Km)	11.00		
5	Length of Road to Meet Required Service Level [Completed Length] (in km) [1]	10.40		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	9960465 = 00		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	498023 = 00		
Compliance Criteria	Standard Job Description	Non-Compliance		Reduction Payment [6]=[3] / [1] * [2] * [4]
		Length Non-Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGE WAY)	0.0	60%	0.0
II	SHOULDERS AND EMBANKMENTS	0.0	10%	0.0
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0.0	15%	0.0
IV	SIGNAGE AND ROAD SAFETY	0.0	10%	0.0
V	VEGETATION	0.0	5%	0.0
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0.0
TO BE PAID FOR THE QUARTER / DEMAND (in Lakh) [6]				498023 = 00

Date of inspection by E/I or his agent prepared by Contractor's self Control unit

Name and Designation of person inspecting road

Date

Signature of person inspecting road

31/06/22
JRE
(md. Zahid)
(Signature)

T.W.
30/06/22
A-E

EXECUTIVE ENGINEER
RWD, WORKS DIVISION
SIWAN-2

15/9/22
