

कार्यपालक अभियंता, का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, सीतामढ़ी

पत्रांक 1728312 / दिनांक 13/09/2024

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, सीतामढ़ी।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव,
ग्रामीण कार्य विभाग,
बिहार, पटना।

विषय:-

शीर्ष बिहार नई अनुरक्षण नीति 2018 (MR 3054) अन्तर्गत अनुरक्षण मद में
आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपर्युक्त विषयक इस प्रमंडल अंतर्गत चल रहे नई अनुरक्षण नीति 2018 (MR 3054) में स्वीकृत योजनाओं के अनुरक्षण हेतु विभिन्न कार्यों के लिए संलग्न विवरणी अनुसार भुगतान हेतु आवंटन उपलब्ध कराने की कृपा की जाय।

अनु०:- यथोक्त।

विश्वासभाजन

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, सीतामढ़ी।

Requisition Format for Scheme Head-MR (3054) under Bihar Rural Road Maintenance Policy-2018

Name of Division: RWD Sitamarhi

S. No.	Name of Road work	Length (in KM)	Group No.	Project ID	Name of Contractor	Agreement Value (Lac)		Date of Completion		Date & Amount of Final Bill for Const. Work	1st Year Maintenance Cost Details (in Rs.)				Total	Remarks
						Const.	Maint. Cost	As per Agreement	Actual Date of Compl.		1st Quarter	2nd Quarter	3rd Quarter	4th Quarter		
1	Banspurhuda to Kachharpur	1.81	MR-N/19-20 Sitama rhi 03	31507902028	Sri Ashok Kumar Singh	55.24687	15.10248	06.05.21	30.09.2021	55.21252	75512	75512	0.00	0.00	151024	
2	Shurahi to Madhuban	2.36	MR-N/19-20 Sitama rhi 03	31507902048	Sri Ashok Kumar Singh	59.38575	19.77195	06.05.21	29.12.2020	59.36000	98859	98859	98859	98859	395436	
3	Madheshra to Shurahi Rahn	2.77	MR-N/19-20 Sitama rhi 03	31507902109	Sri Ashok Kumar Singh	73.96257	23.21672	06.05.21	18.11.2020	73.96257	116083	116083	116083	116083	464332	
Total		6.94				188.59519	58.09115			188.55509	290454	290454	214942.00	214942.00	1010792	

Executive Engineer
RWD (W) Division,
Sitamarhi
08.06.22
25/6/22

Requisition Format for Scheme Head-MR (3054) under Bihar Rural Road Maintenance Policy-2018


Name of Division:-RWD Sitamarhi

Sl. No	Name of Road word	Length (in KM)	Group No.	Project ID	Name of Contractor	Agreement Value (Lac)		Date of Completion		Date & Amount of Final Bill	2nd Year Maintenance Cost Details (in Rs.)				Total	Remarks
						Const.	Maint. Cost	As per Agreement	Actual Date of Compl.		1st Quarter	2nd Quarter	3rd Quarter	4th Quarter		
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17
1	Bhutahi to Madhuban	2.36	MR-N/19-20/Sitamarhi/03	31607902048	Sn Ashok Kumar Singh	59.38575	19.77195	06.05.21	29.12.2020	59.38000	98859	0	0	0	98859	
2	Madheshra to Bhutahi Rain	2.77	MR-N/19-20/Sitamarhi/03	31607902109	Sn Ashok Kumar Singh	73.96257	23.21672	06.05.21	18.11.2020	73.96257	116083	116083	0	0	232166	
	Total	5.13				133.34832	42.98867			133.34257	214942	116083	0.00	0.00	331025	

Executive Engineer
RWD (W) Division,
Sitamarhi

File : C:\Users\AMIT\Desktop\24052022.Xls. Section No. : 41. Egn : $Y = 0 * X^2 + 0.90 * X + 248.95$

Name of Customer : ASHOK KUMAR SINGH. Name of Work/ Road BHUTANI TO MADHUBAN, Lab Job number :

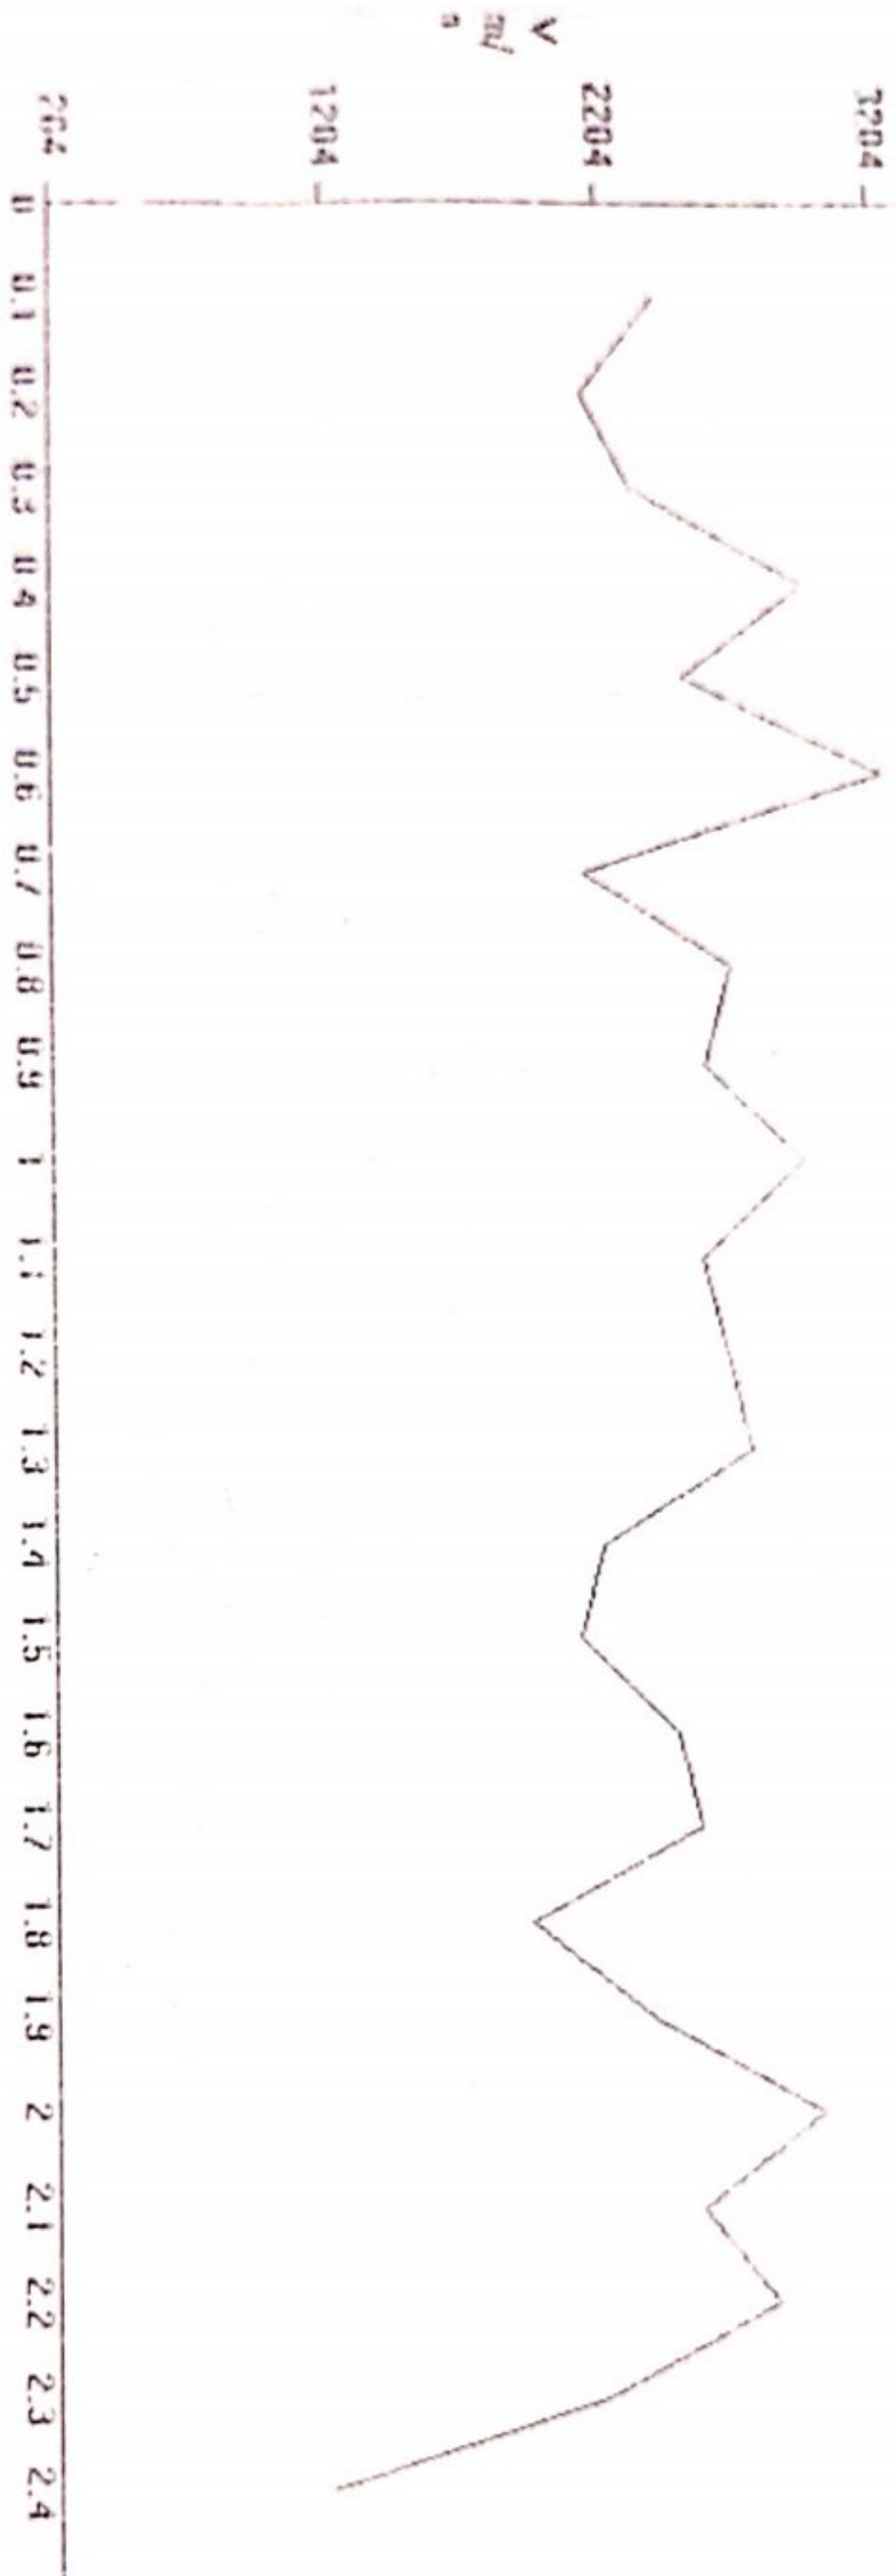

Distance * 1000 m

20/10/22
26165/022

26151/22
A

25.05.22
26151/22
A

ROAD NAME - BHUTAH TO MADHUBAN CONTRACTOR NAME - ASHOK KUMAR SINGH

Date	Time	Section	No.	Length	Bumps	Speed	OR	IRI\TEGORY	Latitude	ongitude	Event
24/5/22	19:57:0	41	in km	0.1	in mm	Rate	mm/km	mm/km	ROAD		
24/5/22	19:57:4	41	0.1	240	0	2400	2408 G	26.73884	85.55402	Normal	(R) RURAL ROAD
24/5/22	19:57:4	41	0.1	210	30.3	2100	2138 G	26.73957	85.55347	Normal	Good
24/5/22	19:57:4	41	0.1	230	30.3	2300	2318 G	26.74046	85.55354	Normal	Average
24/5/22	19:57:40	41	0.1	300	30.3	3000	2948 G	26.74126	85.55396	Normal	Poor
24/5/22	19:58:0	41	0.1	250	30.3	2500	2498 G	26.74206	85.55453	Normal	
24/5/22	19:58:15	41	0.1	330	30.3	3300	3218 G	26.74257	85.55527	Curve	
24/5/22	19:58:15	41	0.1	210	30.3	2100	2138 G	26.7429	85.55618	Curve	
24/5/22	19:58:50	41	0.1	270	30.3	2700	2678 G	26.74305	85.55719	Curve	
24/5/22	19:59:0	41	0.1	260	32.5	2600	2588 G	26.74379	85.55766	Normal	
24/5/22	19:59:0	41	0.1	300	30.3	3000	2948 G	26.7445	85.55822	Normal	
24/5/22	19:59:25	41	0.1	260	30.3	2600	2588 G	26.74533	85.55854	Normal	
24/5/22	19:59:25	41	0.1	270	31.2	2700	2678 G	26.74592	85.55911	Normal	
24/5/22	20:0:1	41	0.1	280	30.3	2800	2768 G	26.74585	85.56005	Normal	
24/5/22	20:0:1	41	0.1	220	30.3	2200	2228 G	26.74597	85.56074	Normal	
24/5/22	20:0:36	41	0.1	210	30.3	2100	2138 G	26.74585	85.56111	Curve	
24/5/22	20:1:0	41	0.1	250	30.3	2500	2498 G	26.74625	85.56153	Curve	
24/5/22	20:1:11	41	0.1	260	30.3	2600	2588 G	26.74666	85.56226	Curve	
24/5/22	20:1:47	41	0.1	190	20.2	1900	1958 G	26.74706	85.56271	Curve	
24/5/22	20:2:0	41	0.1	240	30.3	2400	2408 G	26.74683	85.56337	Normal	
24/5/22	20:2:22	41	0.1	310	20.2	3100	3038 G	26.74689	85.56436	Curve	
24/5/22	20:2:22	41	0.1	260	30.3	2600	2588 G	26.74691	85.5653	Normal	
24/5/22	20:3:0	41	0.1	290	30.3	2900	2858 G	26.74674	85.56625	Normal	
24/5/22	20:3:0	41	0.1	220	30.3	2200	2228 G	26.74655	85.56722	Normal	
24/5/22	20:3:32	41	0.6	170	30.3	3300	3218 G	26.74574	85.56736	Curve	

LENTH - 2.360 KM AVERAGE - 2569

MACHINE NO - 394

28/10/26
26/05/2022

26/15/22

26.74574
26.74574

RWD, Works Division Sitamarhi

1 Year (1st Quarter)

Government of India

Rural Works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From:- Bhutahi To Mdhuban
(Package No. MR-N/19-20/Sitamari/03)

Length of Road :- 2.360 Km

Period :- From :- 29.12.2020 to 28.03.2021

Inspector :- A.E. RWD Sub Division : Sonbarsa

To :-

Executive Engineer,
RWD, Works Division Sitamarhi.

Position :- A.E

No	Standard Of Work Item	work Unit	Unit Of Required	1	2	3	4	5	6	7	8	9	10	Comments
OM100	Sealed payment													No Pot Hole Found.
OM101	Pothole Patching	m ²	Nil	Nil										Not Surface Depression & Rut Patching
OM102	Surface Depression and Rut patching	M ³	Nil	Nil										No Crack Sealing found
OM103	Crack Sealing	Lm	Nil	Nil										No Crack sealing
	Surface Treatment													No loss of Aggregates (Surface Revealing) Found
OM104	(a) Loss of Aggregate (Surface Revealing)	m ²	Nil	Nil										No Bleeding / Flushing Required
	(b) Bleeding / Flushing	m ²	Nil	Nil										No Crocodile Cracking Found
	(c) Crocodile Cracking	m ²	Nil	Nil										No Edge Repair Required
105	Edge Repair	m ²	Nil	Nil										
106	Digouts	m ²	Nil	Nil										
107	Concrete pavement	M ³	N.A	N.A										
	Other activities													
OM200	Shoulder													
	Unsealed Shoulder													No Edge Drop-Off Required
	(a) Edge Drop - off	Lm	Nil	Nil										No Roughness, Scouring or Potholes Required
OM201	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil										No Holding Water Found
	(c) Holding water	Lm	Nil	Nil										
OM202	Embankment Repair	M ³	Nil	Nil										No Required
	Other activities (Rain Cuts)		N.A	N.A										No Required
OM300	Drainage including culverts major													No Required
OM301	Surface Drains & Verge	Lm	N.A	N.A										No Required
OM302	Culvert Cleaning	No	Nil	Nil										No Required
OM303	Culvert and pit Repair	M ³	Nil	Nil										No Required

2021/03/02
15/5/22
13.05.22
CE

Other activities (W)		M ²	Nil	Nil							Not R
No	Standard Of	Work Unit	1	2	in each kilometere						Comments
OM400	Vegetation	Unit			5	6	7	8	9	10	
	Grass Control										Not Required
OM401	(a)Roadside- General Tidy	Ha	Nil	Nil							Not Required
	(b)Clear near Safety sign, Kilometer posts and roadside furniture	HA	Nil	Nil							Not Required
	Tree and Shrub Management	No	Nil	Nil							Not Required
	Cutting Of Branches of trees	No	Nil	Nil							Not Required
OM402	Cutting Of Shrubs From Road Way	No	Nil	Nil							Not Required
	Other activities (Trimming of Grass)	M ²	Nil	Nil							Not Required
OM500	Safety Signage and Road										Not Required
OM501	Sign Maintenance	No	Nil	Nil							Not Required
OM502	Guard Stones	Lm	Nil	Nil							Not Required
OM503	Distance Stones	No	Nil	Nil							Not Required
OM504	Road Marking	M ²	Nil	Nil							Not Required
	Other activities										

Bidder Appendix

Executive Engineer
Works Division, Sitamarhi

20/11/2022
20/11/2022

20/11/2022

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT- 1 YEAR (1st Quarter)

PIU Name :-EE, RWD, WORKS DEPARTMENT, SITAMARHI

1	Name of the Road-	Bhutahi To Mdhuban		
2	Batch -	RM/SI/SIT/19/0003		
3	Project ID-	31607302048		
4	Total Length of Road (in KM)-	2.360 Km		
5	Length of Road to Meet Required Service Level [Complete Length](in KM) [1]	2.360 Km		
6	No. of Total Quarter (ie Months as a unit) in 5 Years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	0.98845		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	0.98845 (0.98845)		
	Standard Job Description	Non- Compliance		Reduction Payment [6] = [3] / [1] * [2] * [4]
		Length Non-Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGE WAY)	0	60%	0
II	SHOULDERS AND EMBANKMENTS	0	10%	0
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0	15%	0
IV	SIGNAGE AND ROAD SAFETY	0	10%	0
	VEGETATION	0	5%	0
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0.98845
TO BE PAID FOR THE QUARTER / DEMAND (in Lakh) [6]				0.98845

Date of inspection by E/I or his agent
Prepared by Contractor's self Control unit

Date

Signature of Person inspecting road

Name and Designation of Person inspecting road

(Signature)

Signature
15/05/22
AE
