

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, सिवान-2

पत्रांक.....6583150..... सिवान, दिनांक.....12-4-23-

प्रेषक,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, सिवान-2

सेवा में,

सचिव-सह-प्राधिकृत पदाधिकारी
बिहार ग्रामीण पथ विकास एजेन्सी
भूमि विकास बैंक भवन
बुद्ध मार्ग, पटना।

विषय:- योजना शीर्ष नई अनुरक्षण निति 2018 MR/3054 अन्तर्गत पथों में मरम्मत हेतु
अधियाचना के संबंध में।

महाशय,

उपर्युक्त विषयक प्रासंगिक पत्र के आलोक में कहना है कि योजना शीर्ष नई अनुरक्षण
निति 2018 MR/3054 अन्तर्गत संलग्न विहित प्रपत्र में 596.80500 लाख (पाँच करोड़ छानबे
लाख अस्सी हजार पाँच सौ) रुपये मात्र आवंटन देने की कृपा की जाय।

अनु0-अधियाचना पत्र, Bump Integrator Equipment Report की छाया प्रति,
एकरारनामा की छाया प्रति,

विश्वासभाजन

12/4/23
कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, सिवान-2
12/4/23

Requisition Format for Scheme Head - MR (3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division :- RVD, WORKS DIVISION, SIWAN-2

S.N.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (in Lakh)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Amount Alloted (in Lakh)	Up-to-date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks	
					Length (in Km)	Amount (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Year Routine Maintenance Maint. (in Lakh)											
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	
1	MR-N/22-23siwan-2/01	L03+T03 to Annaura (VR12)	31406702058	1999/02.05.22	3.700	198.53	119.39712	35.12117	18MBD of 2022-23/08.02.2023	30.10.23	05.04.23	Good	25mm	5.033	0.00	0.00	119.20500	Complete	
2		T02 Chitaur T02 to Salahpur	31406702048	1999/02.05.22	4.800	199.24	105.01567	49.40805	18MBD of 2022-23/08.02.2023	30.10.23	05.04.23	Good	25mm	5.032	0.00	0.00	105.10000	Complete	
3	MR-N/22-23siwan-2/02	PWD Road to Kharati Dalip	31406602031	1999/02.05.22	7.700	477.59	372.74867	99.13253	16MBD of 2022-23/07.01.2023	11.09.23	05.04.23	Good	25mm	5.032	0.00	0.00	372.50000	Complete	
Total																0.00	0.00	596.80500	

प्रमाणित किया जाता है कि पथ में कराये गये कार्य के सभी अवयववार 100 प्रतिशत कार्य का दर्ज मापी का सत्यापन संबंधित कनीय अभियंता 50 प्रतिशत मापी का सत्यापन संबंधित सहायक अभियंता एवं 10 प्रतिशत मापी का सत्यापन अद्योहस्ताक्षरी यथा कार्यपालक अभियंता द्वारा किया जा चुका है। कराया गया कार्य मानक एवं विशिष्टियों के अनुरूप है।

कनीय अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, सिवान-2

सहायक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, सिवान-2

प्रमुख लेखा परीक्षक
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, सिवान-2

कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, सिवान-2

कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, सिवान-2

FORM GFR-19-A
(See Government of India's Decision (I) below Rule-150)
Form of Utilisation Certificate up to 12th April 2023
NEW MAINTENANCE POLICY (2018)

PIU..... SLNo	Name of Scheme	Sanction No.& Date with Amount, (in Rs. Lacs)	Amount Received (in Rs. Lacs)	Particulars
1	Construction of Rural roads under NEW MAINTENANCE POLICY (2018)	24/19.03.2020 59/18.08.2020 78/29.10.2020 82/13.11.2020 86/11.12.2020 05/12.01.2021 17/26.02.2021 20/19.03.2021 26/15.04.2021 52/24.08.2021 58/27.10.2021 60/09.11.2021 64/06.12.2021 68/23.12.2021 02/03.01.2022 05/25.01.2022 10/21.02.2022 18/11.03.2022 49/27.04.2022 01/20.05.2022 22/08.08.2022 35/13.10.2022 32/03.03.2023 42/20.03.2023	309.44834 40.85500 127.93990 129.95438 140.17554 246.86987 257.50061 46.15519 70.50399 58.39236 177.05420 87.58854 1.27421 167.06400 614.19943 279.43486 11.26696 726.24067 29.31956 62.42914 272.11117 168.58187 604.61409 1.38703	Certified that out of Rs 4988.01999 lacs received during the years 2022-23 in favour of Ex. Engineer, RWD. Works Division, siwan-2 Bihar, a sum of Rs 4973.74128 Lacs has been utilized for the purpose of NEW MAINTENANCE POLICY-2018 Schemes as given in the margin for which it was sanctioned and that the balance of Rs 14.27871 lacs remaining unutilized at the end of the period under.
	Total :		4988.01999	

2. Certified that I have satisfied myself that the conditions on which the grants-in-aid was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.

Kind of Checks exercised :-

- Works have been supervised by Executive Engineer/Superintending Engineer.
- Periodical inspection has been conducted by Executive Engineer/ Superintending Engineer.
- Construction materials have been tested.
- Measurements have been recorded in the MBs and test check conducted by the Assistant Engineer/ Executive Engineer.
- All other codal formalities have been observed.


3. **Physical Progress achieved :-**

- Construction of Road works.
- Construction of CD works.


 DIVISIONAL ACCOUNT OFFICER
 RURAL WORKS DEPARTMENT
 WORKS DIVISION, SIWAN-2


 EXECUTIVE ENGINEER
 RURAL WORKS DEPARTMENT
 WORKS DIVISION, SIWAN-2
 12/4/23

Name of Customer: M K Enterprises Proprietor Manoj Kumar, Machine no: 19208, Road: PWD - Kharati Dalip, Date: 08-04-23, Section No: 137, Equation: $Y=0.904X+252.3$

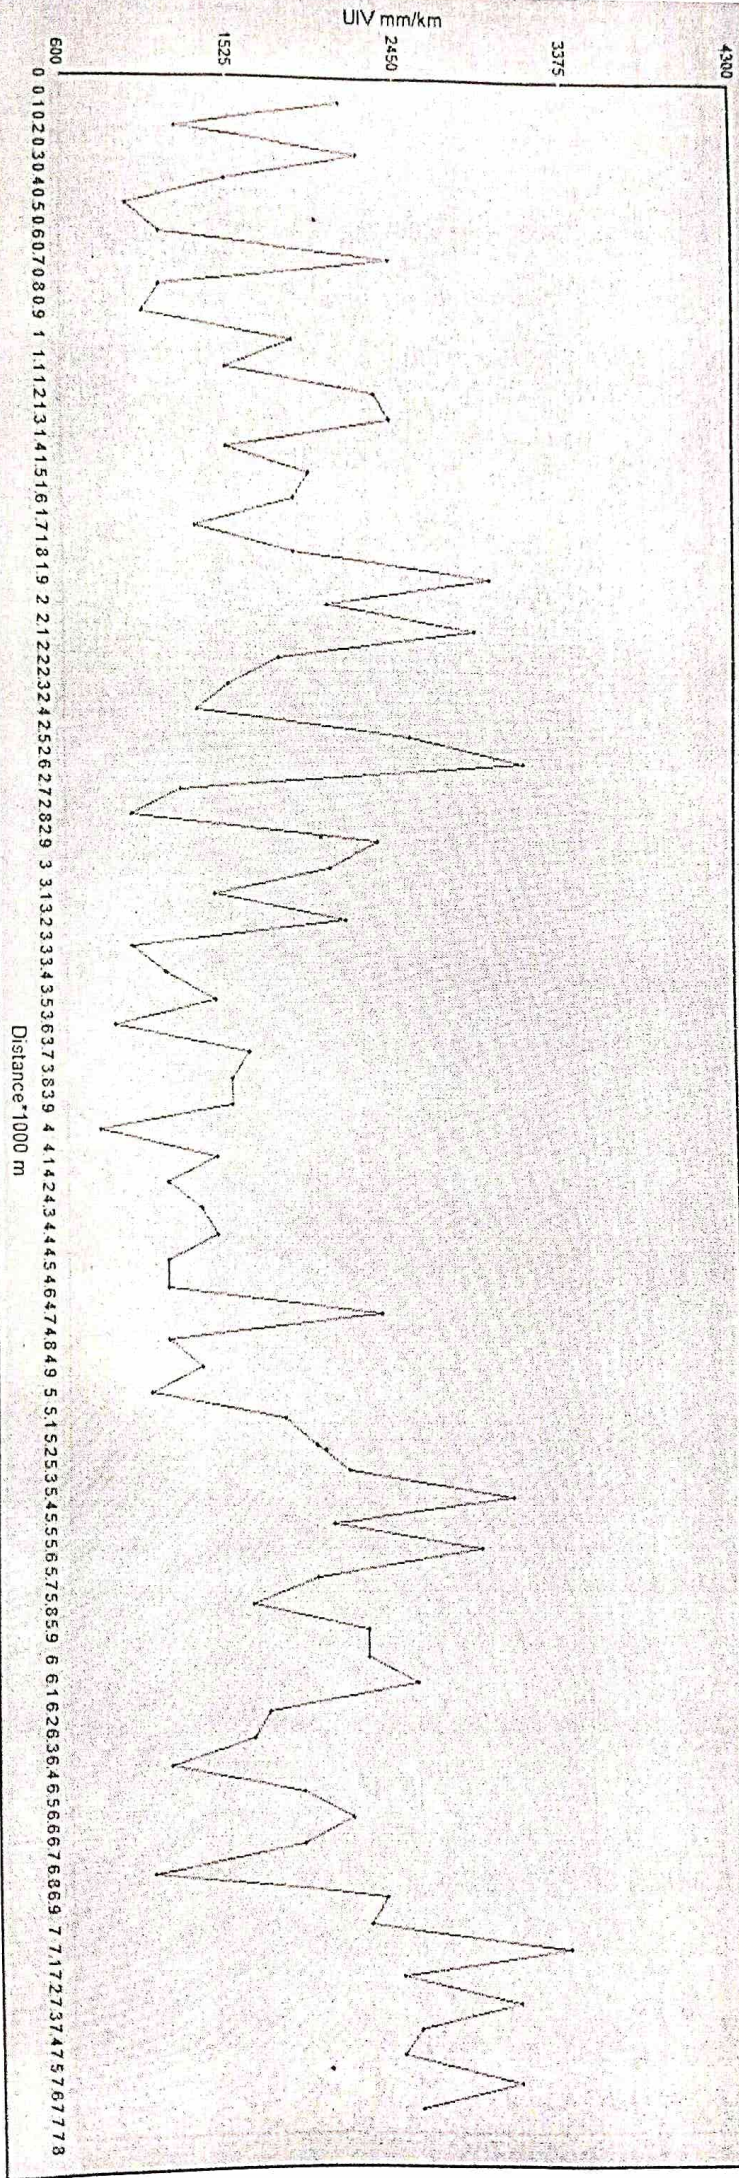

SAKSHI
08/04/23
JE

A.B.
08/04/23
A.E

08.04.23
Executive Engineer
Rural Work Department-2
Work Division Siwan-2

Name of work : PWD - Kharali Dalip

Name of customer : M K Enterprises Proprietor Manoj Kumar

(R) Rural Road

Good	Average	Poor
< 4000	4001 - 5000	> 5000

Date	Time	Test No	Distance(m)	Total Distance(m)	BUM/ft(cm)	Speed(Km/Hr)	Ull(mm/Km)	Corrected Ull (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks
08/04/23	19:24:45	137	100	100	21.0 cm	2.0 Km/Hr	2100.0 mm/Km	2151	2.99	Good	26.1639338	N	84.1919641	E	Normal
08/04/23	19:25:16	137	100	200	11.0 cm	11.2 Km/Hr	1100.0 mm/Km	1247	1.84	Good	26.1629438	N	84.1918955	E	Normal
08/04/23	19:25:48	137	100	300	22.0 cm	11.4 Km/Hr	2200.0 mm/Km	2241	3.11	Good	26.1620417	N	84.1919641	E	Normal
08/04/23	19:26:16	137	100	400	14.0 cm	12.6 Km/Hr	1400.0 mm/Km	1518	2.19	Good	26.1620531	N	84.1929407	E	Normal
08/04/23	19:26:40	137	100	500	8.0 cm	15.0 Km/Hr	800.0 mm/Km	976	1.48	Good	26.1616621	N	84.1936350	E	Normal
08/04/23	19:27:04	137	100	600	10.0 cm	15.3 Km/Hr	1000.0 mm/Km	1156	1.72	Good	26.1607885	N	84.1939936	E	Normal
08/04/23	19:27:41	137	100	700	24.0 cm	9.6 Km/Hr	2400.0 mm/Km	2422	3.33	Good	26.1598883	N	84.1944208	E	Normal
08/04/23	19:28:01	137	100	800	10.0 cm	18.1 Km/Hr	1000.0 mm/Km	1156	1.72	Good	26.1590910	N	84.1948938	E	Normal
08/04/23	19:28:23	137	100	900	9.0 cm	16.5 Km/Hr	900.0 mm/Km	1066	1.6	Good	26.1581755	N	84.1951380	E	Normal
08/04/23	19:28:47	137	100	1000	18.0 cm	15.0 Km/Hr	1800.0 mm/Km	1880	2.65	Good	26.1573095	N	84.1953440	E	Normal
08/04/23	19:29:10	137	100	1100	14.0 cm	15.3 Km/Hr	1400.0 mm/Km	1518	2.19	Good	26.1564589	N	84.1955881	E	Normal
08/04/23	19:29:33	137	100	1200	23.0 cm	15.7 Km/Hr	2300.0 mm/Km	2332	3.22	Good	26.1556444	N	84.1956419	E	Normal
08/04/23	19:29:51	137	100	1300	24.0 cm	19.4 Km/Hr	2400.0 mm/Km	2422	3.33	Good	26.1548433	N	84.1963205	E	Normal
08/04/23	19:30:07	137	100	1400	14.0 cm	22.5 Km/Hr	1400.0 mm/Km	1518	2.19	Good	26.1539850	N	84.1966639	E	Normal
08/04/23	19:30:23	137	100	1500	19.0 cm	23.4 Km/Hr	1900.0 mm/Km	1970	2.77	Good	26.1530771	N	84.1969538	E	Normal
08/04/23	19:30:39	137	100	1600	18.0 cm	22.0 Km/Hr	1800.0 mm/Km	1880	2.65	Good	26.1524096	N	84.1975260	E	Normal
08/04/23	19:30:53	137	100	1700	12.0 cm	25.4 Km/Hr	1200.0 mm/Km	1337	1.96	Good	26.1515150	N	84.1976099	E	Normal
08/04/23	19:31:07	137	100	1800	18.0 cm	25.4 Km/Hr	1800.0 mm/Km	1880	2.65	Good	26.1506186	N	84.1977549	E	Normal
08/04/23	19:31:25	137	100	1900	30.0 cm	21.1 Km/Hr	3000.0 mm/Km	2964	3.99	Good	26.1500082	N	84.1973658	E	Normal
08/04/23	19:31:56	137	100	2000	20.0 cm	12.0 Km/Hr	2000.0 mm/Km	2060	2.88	Good	26.1501398	N	84.1963587	E	Normal
08/04/23	19:32:18	137	100	2100	29.0 cm	16.0 Km/Hr	2900.0 mm/Km	2874	3.88	Good	26.1502295	N	84.1953592	E	Normal

SHRIS
08/04/23
JE

ABV
08/04/23
A.T

Executive Engineer
Rural Road Department
Work Division Siwan-2

Name of work		: PWD - Kharati Dalip													
Name of customer		: M K Enterprises Proprietor Manoj Kumar													
(R) Rural Road															
Good				Average				Poor							
< 4000				4001 - 5000				> 5000							
08/04/23	19.32.34	137	100	2200	17.0 cm	22.2 Km/Hr	1700.0 mm/Km	1789	2.54	Good	26.1503057	N	84.1943627	E	Normal
08/04/23	19.32.50	137	100	2300	14.0 cm	22.2 Km/Hr	1400.0 mm/Km	1518	2.19	Good	26.1503992	N	84.1933603	E	Normal
08/04/23	19.33.04	137	100	2400	12.0 cm	25.4 Km/Hr	1200.0 mm/Km	1337	1.96	Good	26.1504812	N	84.1923638	E	Normal
08/04/23	19.33.19	137	100	2500	25.0 cm	23.8 Km/Hr	2500.0 mm/Km	2512	3.44	Good	26.1505765	N	84.1913767	E	Normal
08/04/23	19.33.41	137	100	2600	32.0 cm	16.5 Km/Hr	3200.0 mm/Km	3145	4.2	Good	26.1506641	N	84.1904764	E	Normal
08/04/23	19.33.56	137	100	2700	11.0 cm	24.4 Km/Hr	1100.0 mm/Km	1247	1.84	Good	26.1496267	N	84.1900721	E	Normal
08/04/23	19.34.08	137	100	2800	8.0 cm	28.5 Km/Hr	800.0 mm/Km	976	1.48	Good	26.1487970	N	84.1897669	E	Normal
08/04/23	19.34.29	137	100	2900	23.0 cm	17.8 Km/Hr	2300.0 mm/Km	2332	3.22	Good	26.1481943	N	84.1891642	E	Normal
08/04/23	19.34.51	137	100	3000	20.0 cm	16.2 Km/Hr	2000.0 mm/Km	2060	2.88	Good	26.1479578	N	84.1882181	E	Normal
08/04/23	19.35.06	137	100	3100	13.0 cm	23.8 Km/Hr	1300.0 mm/Km	1428	2.08	Good	26.1476374	N	84.1873560	E	Normal
08/04/23	19.35.21	137	100	3200	21.0 cm	23.4 Km/Hr	2100.0 mm/Km	2151	2.99	Good	26.1474333	N	84.1865549	E	Normal
08/04/23	19.35.36	137	100	3300	8.0 cm	24.6 Km/Hr	800.0 mm/Km	976	1.48	Good	26.1464453	N	84.1863947	E	Normal
08/04/23	19.35.51	137	100	3400	10.0 cm	23.4 Km/Hr	1000.0 mm/Km	1156	1.72	Good	26.1462774	N	84.1855478	E	Normal
08/04/23	19.36.06	137	100	3500	13.0 cm	24.6 Km/Hr	1300.0 mm/Km	1428	2.08	Good	26.1464453	N	84.1845255	E	Normal
08/04/23	19.36.30	137	100	3600	7.0 cm	15.1 Km/Hr	700.0 mm/Km	885	1.35	Good	26.1467905	N	84.1834955	E	Normal
08/04/23	19.36.46	137	100	3700	15.0 cm	22.0 Km/Hr	1500.0 mm/Km	1608	2.31	Good	26.1467905	N	84.1825495	E	Normal
08/04/23	19.37.01	137	100	3800	14.0 cm	23.8 Km/Hr	1400.0 mm/Km	1518	2.19	Good	26.1470137	N	84.1815577	E	Normal
08/04/23	19.37.18	137	100	3900	14.0 cm	21.1 Km/Hr	1400.0 mm/Km	1518	2.19	Good	26.1473722	N	84.1805498	E	Normal
08/04/23	19.37.34	137	100	4000	6.0 cm	21.8 Km/Hr	600.0 mm/Km	795	1.23	Good	26.1476605	N	84.1798334	E	Normal
08/04/23	19.37.51	137	100	4100	13.0 cm	22.2 Km/Hr	1300.0 mm/Km	1428	2.08	Good	26.1483946	N	84.1789713	E	Normal
08/04/23	19.38.07	137	100	4200	10.0 cm	22.2 Km/Hr	1000.0 mm/Km	1156	1.72	Good	26.1487932	N	84.1781397	E	Normal
08/04/23	19.38.22	137	100	4300	12.0 cm	23.8 Km/Hr	1200.0 mm/Km	1337	1.96	Good	26.1491270	N	84.1772776	E	Normal

SAVITRI
08/04/23
JE

AS
08/04/23
A.C

Executive Engineer
Rural Work Department
Rural Division Swan-2

Name of work : PWD - Kharali Dalip															
Name of customer : M K Enterprises Proprietor Manoj Kumar															
(R) Rural Road															
Good				Average				Poor							
< 4000				4001 - 5000				> 6000							
08/04/23	19.39.38	137	100	4400	13.0 cm	22.9 Km/Hr	1300.0 mm/Km	1428	2.08	Good	26.1494509	N	84.1762552	E	Normal
08/04/23	19.38.53	137	100	4500	10.0 cm	22.7 Km/Hr	1000.0 mm/Km	1156	1.72	Good	26.1497812	N	84.1752939	E	Normal
08/04/23	19.38.10	137	100	4600	10.0 cm	22.2 Km/Hr	1000.0 mm/Km	1156	1.72	Good	26.1499605	N	84.1743226	E	Normal
08/04/23	19.39.26	137	100	4700	23.0 cm	22.0 Km/Hr	2300.0 mm/Km	2332	3.22	Good	26.1498919	N	84.1733103	E	Normal
08/04/23	19.39.41	137	100	4800	10.0 cm	23.9 Km/Hr	1000.0 mm/Km	1156	1.72	Good	26.1497164	N	84.1722956	E	Normal
08/04/23	19.39.55	137	100	4900	12.0 cm	25.4 Km/Hr	1200.0 mm/Km	1337	1.96	Good	26.1498136	N	84.1713724	E	Normal
08/04/23	19.40.09	137	100	5000	9.0 cm	25.6 Km/Hr	900.0 mm/Km	1066	1.6	Good	26.1496530	N	84.1703119	E	Normal
08/04/23	19.40.23	137	100	5100	17.0 cm	25.2 Km/Hr	1700.0 mm/Km	1789	2.54	Good	26.1494436	N	84.1693659	E	Normal
08/04/23	19.40.39	137	100	5200	19.0 cm	22.2 Km/Hr	1900.0 mm/Km	1970	2.77	Good	26.1493006	N	84.1683893	E	Normal
08/04/23	19.40.56	137	100	5300	21.0 cm	21.8 Km/Hr	2100.0 mm/Km	2151	2.99	Good	26.1495191	N	84.1674814	E	Normal
08/04/23	19.41.21	137	100	5400	31.0 cm	14.8 Km/Hr	3100.0 mm/Km	3055	4.09	Good	26.1498823	N	84.1665354	E	Normal
08/04/23	19.41.41	137	100	5500	20.0 cm	17.1 Km/Hr	2000.0 mm/Km	2060	2.88	Good	26.1498019	N	84.1655970	E	Normal
08/04/23	19.42.04	137	100	5600	29.0 cm	16.0 Km/Hr	2900.0 mm/Km	2874	3.88	Good	26.1491098	N	84.1647806	E	Normal
08/04/23	19.42.26	137	100	5700	19.0 cm	16.5 Km/Hr	1900.0 mm/Km	1970	2.77	Good	26.1490774	N	84.1638193	E	Normal
08/04/23	19.42.43	137	100	5800	15.0 cm	20.0 Km/Hr	1500.0 mm/Km	1608	2.31	Good	26.1489801	N	84.1629724	E	Normal
08/04/23	19.43.00	137	100	5900	22.0 cm	21.3 Km/Hr	2200.0 mm/Km	2241	3.11	Good	26.1484461	N	84.1620111	E	Normal
08/04/23	19.43.18	137	100	6000	22.0 cm	21.2 Km/Hr	2200.0 mm/Km	2241	3.11	Good	26.1482153	N	84.1610498	E	Normal
08/04/23	19.43.36	137	100	6100	25.0 cm	19.0 Km/Hr	2500.0 mm/Km	2512	3.44	Good	26.1482592	N	84.1600580	E	Normal
08/04/23	19.43.52	137	100	6200	16.0 cm	22.5 Km/Hr	1600.0 mm/Km	1699	2.42	Good	26.1482668	N	84.1590662	E	Normal
08/04/23	19.44.07	137	100	6300	15.0 cm	23.8 Km/Hr	1500.0 mm/Km	1608	2.31	Good	26.1484556	N	84.1580896	E	Normal
08/04/23	19.44.21	137	100	6400	10.0 cm	25.2 Km/Hr	1000.0 mm/Km	1156	1.72	Good	26.1485777	N	84.1571588	E	Normal
08/04/23	19.44.36	137	100	6500	18.0 cm	25.2 Km/Hr	1800.0 mm/Km	1880	2.65	Good	26.1487188	N	84.1560526	E	Normal

MA/23
08/04/23
JTC

AW
08/04/23
A.T

Executive Engineer
Rural Ward Department
Shakti Division Siwan-2

Name of work		: PWD - Kharati Dalip													
Name of customer :		M K Enterprises Proprietor Manoj Kumar													
(R)Rural Road															
Good		Average										Poor			
< 4000		4001 - 5000										> 5000			
08/04/23	19.44.51	137	100	6600	21.0 cm	24.4 Km/Hr	2100.0 mm/Km	2151	2.99	Good	26.1486902	N	84.1551142	E	Normal
08/04/23	19.45.05	137	100	6700	18.0 cm	24.7 Km/Hr	1800.0 mm/Km	1880	2.65	Good	26.1488733	N	84.1540842	E	Normal
08/04/23	19.45.19	137	100	6800	9.0 cm	25.4 Km/Hr	900.0 mm/Km	1066	1.6	Good	26.1491098	N	84.1530924	E	Normal
08/04/23	19.45.33	137	100	6900	23.0 cm	25.9 Km/Hr	2300.0 mm/Km	2332	3.22	Good	26.1492891	N	84.1521692	E	Normal
08/04/23	19.45.47	137	100	7000	22.0 cm	24.9 Km/Hr	2200.0 mm/Km	2241	3.11	Good	26.1496592	N	84.1512079	E	Normal
08/04/23	19.46.29	137	100	7100	34.0 cm	8.6 Km/Hr	3400.0 mm/Km	3326	4.42	Good	26.1505537	N	84.1508341	E	Normal
08/04/23	19.46.48	137	100	7200	24.0 cm	18.0 Km/Hr	2400.0 mm/Km	2422	3.33	Good	26.1513567	N	84.1505518	E	Normal
08/04/23	19.47.17	137	100	7300	31.0 cm	12.6 Km/Hr	3100.0 mm/Km	3055	4.09	Good	26.1517096	N	84.1496439	E	Normal
08/04/23	19.48.01	137	100	7400	25.0 cm	8.5 Km/Hr	2500.0 mm/Km	2512	3.44	Good	26.1520967	N	84.1486673	E	Normal
08/04/23	19.48.40	137	100	7500	24.0 cm	18.0 Km/Hr	2400.0 mm/Km	2422	3.33	Good	26.1513567	N	84.1505518	E	Normal
08/04/23	19.49.15	137	100	7600	31.0 cm	12.6 Km/Hr	3100.0 mm/Km	3055	4.09	Good	26.1517096	N	84.1496439	E	Normal
08/04/23	19.49.51	137	100	7700	25.0 cm	8.5 Km/Hr	2500.0 mm/Km	2512	3.44	Good	26.1520967	N	84.1486673	E	Normal

14/11/23
08/04/23
SE

AB
08/04/23
A.E

Executive Engineer
Rural Ward Department
Mook Division Swarn-2
8.11.23
