

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, सिवान-2

पत्रांक.....6843अनु..... सिवान, दिनांक.....17-4-23..

प्रेषक,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, सिवान-2

सेवा में,

सचिव-सह-प्राधिकृत पदाधिकारी
बिहार ग्रामीण पथ विकास एजेन्सी
भूमि विकास बैंक भवन
बुद्ध मार्ग, पटना।

विषय:- योजना शीर्ष नई अनुरक्षण निति 2018 MR/3054 अन्तर्गत पथों में मरम्मत हेतु
अधियाचना के संबंध में।

महाशय,

उपर्युक्त विषयक प्रासंगिक पत्र के आलोक में कहना है कि योजना शीर्ष नई अनुरक्षण
निति 2018 MR/3054 अन्तर्गत संलग्न विहित प्रपत्र में 185.55188 लाख (एक करोड़ पचासी
लाख पचपन हजार एक सौ अठ्ठासी) रुपये मात्र आवंटन देने की कृपा की जाय।

अनु0-अधियाचना पत्र, Bump Integrator Equipment Report की छाया प्रति,
एकरारनामा की छाया प्रति,

विश्वासभाजन


कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, सिवान-2


17.4.23

Requisition Format for Scheme Head - MR (3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division :- RWD, WORKS DIVISION, SIWAN-2

S.N.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (in Lakh)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Amount Alloted (in Lakh)	Up-to-date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (in Km)	Amount (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Year Routine Maintenance (in Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	MR-N/20-2/01	Sakara to Hussainganj	NEA220001350	1605/29.05.20	15.100	521.2351	280.07154	129.9216	214MBD of 2021-22/08.02.2023	02.06.22	12.04.23	Good	25mm	5.032	0.00	0.00	185.55188	Complete
Total															0.00	0.00	185.55188	

प्रमाणित किया जाता है कि पथ में कराये गये कार्य के सभी अवयववार 100 प्रतिशत कार्य का दर्ज मापी का सत्यापन संबंधित कर्मीय अभियंता 50 प्रतिशत मापी का सत्यापन संबंधित सहायक अभियंता एवं 10 प्रतिशत मापी का सत्यापन अद्योहस्ताक्षरी यथा कार्यपालक अभियंता द्वारा किया जा चुका है। कराया गया कार्य मानक एवं विशिष्टियों के अनुरूप है।

कमीय अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, सिवान-2

सहायक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, सिवान-2

प्रमुखीय सेवा प्रदाता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, सिवान-2

कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, सिवान-2

17.4.23

FORM GFR 19-A
(See Government of India's Decision (I) below Rule-150)
Form of Utilisation Certificate up to 17th April 2023
NEW MAINTENANCE POLICY (2018)

Name of Scheme	Sanction No.& Date with Amount, (in Rs. Laacs)	Amount Received (in Rs. Laacs)	Particulars
Construction of Rural roads under NEW MAINTENANCE POLICY (2018)	24/19.03.2020	309.44834	Certified that out of Rs 4988.01999 laacs received during the years 2022-23 in favour of Ex. Engineer, RWD, Works Division, Siwan-2 Bihar, a sum of Rs 4973.74128 Laacs has been utilized for the purpose of NEW MAINTENANCE POLICY-2018 Schemes as given in the margin for which it was sanctioned and that the balance of Rs 505.98371 laacs remaining unutilized at the end of the period under.
	59/18.08.2020	40.85500	
	78/29.10.2020	127.93990	
	82/13.11.2020	129.95438	
	86/11.12.2020	140.17554	
	05/12.01.2021	246.86987	
	17/26.02.2021	257.50061	
	20/19.03.2021	46.15519	
	26/15.04.2021	70.50399	
	52/24.08.2021	58.39236	
	58/27.10.2021	177.05420	
	60/09.11.2021	87.58854	
	64/06.12.2021	1.27421	
	68/23.12.2021	167.06400	
	02/03.01.2022	614.19943	
	05/25.01.2022	279.43486	
	10/21.02.2022	11.26696	
	18/11.03.2022	726.24067	
	49/27.04.2022	29.31956	
	01/20.05.2022	62.42914	
	22/08.08.2022	272.11117	
	35/13.10.2022	168.58187	
	32/03.03.2023	604.61409	
	42/20.03.2023	1.38703	
	63/13.04.2023	491.70500	
Total :		5479.72499	

2. Certified that I have satisfied myself that the conditions on which the grants-in-aid was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.

Kind of Checks exercised :-


- Works have been supervised by Executive Engineer/Superintending Engineer.
- Periodical inspection has been conducted by Executive Engineer/ Superintending Engineer.
- Construction materials have been tested.
- Measurements have been recorded in the MBs and test check conducted by the Assistant Engineer/ Executive Engineer.
- All other codal formalities have been observed.

3. **Physical Progress achieved :-**

- Construction of Road works.
- Construction of CD works.


DIVISIONAL ACCOUNT OFFICER
RURAL WORKS DEPARTMENT
WORKS DIVISION, SIWAN-2

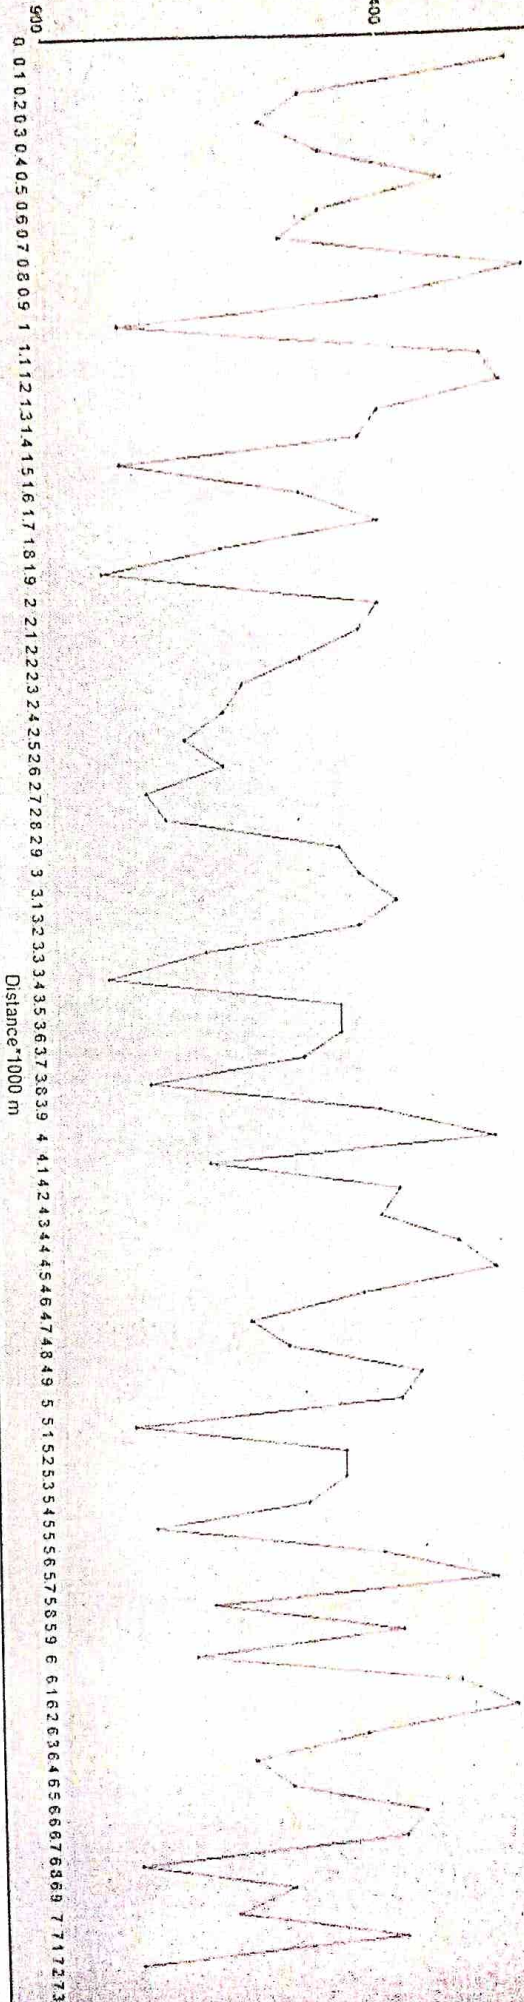

EXECUTIVE ENGINEER
RURAL WORKS DEPARTMENT
WORKS DIVISION, SIWAN-2


17.4.23

3900

Name of Customer: Arun Kumar Jaiswal, Machine no: 19208, Road: Sakara - Hussainganj, Date: 13-04-23, Section No: 138, Equation: $Y = -0.904X + 257.3$

UIV mm/km
2400



[Signature]
13/04/2023
JE

[Signature]
13/04/2023
AE

Executive Engineer
Rural Work Department
Work Division Sivan-2

[Signature]
13.4.23

Name of work : Sakara - Hussainganj

Name of customer : Arun Kumar Jaiswal

(R)Rural Road

Good	Average	Poor
< 4000	4001 - 5000	> 5000

Date	Time	Test No	Distance(m)	Total Distance(m)	Bump(m)	Speed(km/h)	Ull(mmm/km)	Corrected Ull (mm/km)	IRI	Status	Latitude	Direction	Longitude	Direction 1	Remarks
13/04/23	10:24:02	138	100	100	30.0 cm	0.8 Km/Hr	3000.0 mm/km	2964	3.99	Good	26.1503678	N	84.2729554	E	Normal
13/04/23	10:24:22	138	100	200	20.0 cm	17.5 Km/Hr	2000.0 mm/km	2060	2.88	Good	26.1510420	N	84.2728357	E	Normal
13/04/23	10:24:43	138	100	300	18.0 cm	17.2 Km/Hr	1800.0 mm/km	1880	2.65	Good	26.1522226	N	84.2728357	E	Normal
13/04/23	10:25:17	138	100	400	21.0 cm	10.8 Km/Hr	2100.0 mm/km	2151	2.99	Good	26.1530371	N	84.2731104	E	Normal
13/04/23	10:25:46	138	100	500	27.0 cm	12.2 Km/Hr	2700.0 mm/km	2683	3.66	Good	26.1538820	N	84.2732782	E	Normal
13/04/23	10:26:07	138	100	600	21.0 cm	16.5 Km/Hr	2100.0 mm/km	2151	2.99	Good	26.1548681	N	84.2741022	E	Normal
13/04/23	10:26:30	138	100	700	19.0 cm	15.7 Km/Hr	1900.0 mm/km	1970	2.77	Good	26.1551123	N	84.2745600	E	Normal
13/04/23	10:26:54	138	100	800	31.0 cm	15.1 Km/Hr	3100.0 mm/km	3055	4.09	Good	26.1555471	N	84.2751627	E	Normal
13/04/23	10:27:15	138	100	900	24.0 cm	14.5 Km/Hr	2400.0 mm/km	2422	3.33	Good	26.1552572	N	84.2757502	E	Normal
13/04/23	10:27:46	138	100	1000	11.0 cm	12.9 Km/Hr	1100.0 mm/km	1247	1.84	Good	26.1544733	N	84.2759104	E	Normal
13/04/23	10:28:06	138	100	1100	29.0 cm	16.8 Km/Hr	2900.0 mm/km	2874	3.88	Good	26.1536760	N	84.2764673	E	Normal
13/04/23	10:28:41	138	100	1200	30.0 cm	10.5 Km/Hr	3000.0 mm/km	2964	3.99	Good	26.1533937	N	84.2772303	E	Normal
13/04/23	10:29:12	138	100	1300	24.0 cm	11.8 Km/Hr	2400.0 mm/km	2422	3.33	Good	26.1529551	N	84.2778482	E	Normal
13/04/23	10:29:35	138	100	1400	23.0 cm	15.5 Km/Hr	2300.0 mm/km	2332	3.22	Good	26.1537447	N	84.2787502	E	Normal
13/04/23	10:30:02	138	100	1500	11.0 cm	12.9 Km/Hr	1100.0 mm/km	1247	1.84	Good	26.1544733	N	84.2797174	E	Normal
13/04/23	10:30:22	138	100	1600	20.0 cm	18.0 Km/Hr	2000.0 mm/km	2060	2.88	Good	26.1533422	N	84.2804346	E	Normal
13/04/23	10:30:40	138	100	1700	24.0 cm	19.4 Km/Hr	2400.0 mm/km	2422	3.33	Good	26.1528902	N	84.2815638	E	Normal
13/04/23	10:30:56	138	100	1800	16.0 cm	22.5 Km/Hr	1600.0 mm/km	1699	2.42	Good	26.1526937	N	84.2823877	E	Normal
13/04/23	10:31:11	138	100	1900	10.0 cm	25.2 Km/Hr	1000.0 mm/km	1156	1.72	Good	26.1525278	N	84.2834787	E	Normal
13/04/23	10:31:37	138	100	2000	24.0 cm	13.9 Km/Hr	2400.0 mm/km	2422	3.33	Good	26.1523886	N	84.2843409	E	Normal
13/04/23	10:32:03	138	100	2100	23.0 cm	13.5 Km/Hr	2300.0 mm/km	2332	3.22	Good	26.1521120	N	84.2843409	E	Normal

13/04/2023
DE

13/04/2023
AF

Executive Engineer
Rural Ward Department
Work Division Sharda

Name of work : Sakara - Hussainganj

Name of customer : Anun Kumar Jaiswal

(R) Rural Road

Good	Average	Poor
< 4000	4001 - 5000	> 5000

13/04/23	10.32.26	138	100	2200	20.0 cm	15.7 km/Hr	2000.0 mm/Km	2060	2.88	Good	26.1513251	11	84.2852411	E	Normal
13/04/23	10.32.56	138	100	2300	17.0 cm	12.3 km/Hr	1700.0 mm/Km	1789	2.54	Good	26.1517229	N	84.2862229	E	Normal
13/04/23	10.33.17	138	100	2400	16.0 cm	17.2 km/Hr	1600.0 mm/Km	1699	2.42	Good	26.1513795	11	84.2871103	E	Normal
13/04/23	10.33.32	138	100	2500	14.0 cm	23.4 km/Hr	1400.0 mm/Km	1518	2.19	Good	26.1505345	11	84.2866552	E	Normal
13/04/23	10.33.46	135	100	2600	16.0 cm	24.9 km/Hr	1600.0 mm/Km	1699	2.42	Good	26.1496420	N	84.2865068	E	Normal
13/04/23	10.34.00	138	100	2700	12.0 cm	27.0 km/Hr	1200.0 mm/Km	1337	1.96	Good	26.1488425	N	84.2863332	E	Normal
13/04/23	10.34.15	138	100	2800	13.0 cm	24.0 km/Hr	1300.0 mm/Km	1428	2.08	Good	26.1479005	N	84.2865678	E	Normal
13/04/23	10.34.32	138	100	2900	22.0 cm	21.3 km/Hr	2200.0 mm/Km	2241	3.11	Good	26.1474295	N	84.2873697	E	Normal
13/04/23	10.34.53	138	100	3000	23.0 cm	17.5 km/Hr	2300.0 mm/Km	2332	3.22	Good	26.1467466	N	84.2877741	E	Normal
13/04/23	10.35.37	138	100	3100	25.0 cm	8.1 km/Hr	2500.0 mm/Km	2512	3.44	Good	26.1464453	N	84.2882237	E	Normal
13/04/23	10.38.00	138	100	3200	23.0 cm	2.5 km/Hr	2300.0 mm/Km	2332	3.22	Good	26.1462984	N	84.2947626	E	Normal
13/04/23	10.38.33	135	100	3300	15.0 cm	11.1 km/Hr	1500.0 mm/Km	1608	2.31	Good	26.1463232	N	84.2957697	E	Normal
13/04/23	10.38.56	135	100	3400	10.0 cm	15.2 km/Hr	1000.0 mm/Km	1156	1.72	Good	26.1466856	N	84.2965021	E	Normal
13/04/23	10.39.18	138	100	3500	22.0 cm	16.2 km/Hr	2200.0 mm/Km	2241	3.11	Good	26.1470919	N	84.2970896	E	Normal
13/04/23	10.39.39	138	100	3600	22.0 cm	16.8 km/Hr	2200.0 mm/Km	2241	3.11	Good	26.1466684	N	84.2982569	E	Normal
13/04/23	10.40.03	138	100	3700	20.0 cm	15.4 km/Hr	2000.0 mm/Km	2060	2.88	Good	26.1468267	N	84.2989740	E	Normal
13/04/23	10.40.24	138	100	3800	12.0 cm	17.4 km/Hr	1200.0 mm/Km	1337	1.96	Good	26.1477022	N	84.2992182	E	Normal
13/04/23	10.40.48	138	100	3900	24.0 cm	14.8 km/Hr	2400.0 mm/Km	2422	3.33	Good	26.1481695	N	84.2997751	E	Normal
13/04/23	10.41.27	138	100	4000	30.0 cm	9.3 km/Hr	3000.0 mm/Km	2964	3.99	Good	26.1478929	N	84.3014154	E	Normal
13/04/23	10.42.10	138	100	4100	15.0 cm	8.0 km/Hr	1500.0 mm/Km	1608	2.31	Good	26.1476336	N	84.3028040	E	Normal
13/04/23	10.42.39	138	100	4200	25.0 cm	12.4 km/Hr	2500.0 mm/Km	2512	3.44	Good	26.1476946	N	84.3041010	E	Normal
13/04/23	10.43.21	138	100	4300	24.0 cm	8.6 km/Hr	2400.0 mm/Km	2422	3.33	Good	26.1468954	N	84.3055963	E	Normal

13/04/2023

13/04/2023

Executive Engineer
Rural Work Department
Work Division Siwan-2

Name of work : Sakata - Hussainigani

Name of customer : Alun Kumar Jaiswal

(R) Rural Road

Good	Average	Poor
< 4000	4001 - 5000	> 5000

13/04/23	10.44.02	138	100	4400	28.0 cm	8.9 km/hr	2800.0 mm/km	2784	3.77	Good	26.1464128	N	84.3069010	E	Normal
13/04/23	10.49.53	138	100	4500	30.0 cm	1.0 km/hr	3000.0 mm/km	2984	3.90	Good	26.1450129	N	84.3133325	E	Normal
13/04/23	10.50.28	138	100	4600	23.0 cm	10.2 km/hr	2300.0 mm/km	2332	3.22	Good	26.1446943	N	84.3142939	E	Normal
13/04/23	10.51.02	138	100	4700	17.0 cm	10.1 km/hr	1700.0 mm/km	1789	2.54	Good	26.1442460	N	84.3151026	E	Normal
13/04/23	10.51.23	138	100	4800	19.0 cm	17.1 km/hr	1900.0 mm/km	1970	2.77	Good	26.1438894	N	84.3169334	E	Normal
13/04/23	10.51.54	138	100	4900	25.0 cm	11.5 km/hr	2500.0 mm/km	2512	3.55	Good	26.1441259	N	84.3169107	E	Normal
13/04/23	10.52.25	138	100	5000	25.0 cm	11.5 km/hr	2500.0 mm/km	2512	3.44	Good	26.1438894	N	84.3172558	E	Normal
13/04/23	10.53.02	138	100	5100	11.0 cm	9.8 km/hr	1100.0 mm/km	1247	1.84	Good	26.1436892	N	84.3188791	E	Normal
13/04/23	10.53.49	138	100	5200	22.0 cm	16.2 km/hr	2200.0 mm/km	2241	3.11	Good	26.1470919	N	84.2970886	E	Normal
13/04/23	10.54.19	138	100	5300	22.0 cm	16.8 km/hr	2200.0 mm/km	2241	3.11	Good	26.1466894	N	84.2982559	E	Normal
13/04/23	10.54.53	138	100	5400	20.0 cm	15.4 km/hr	2000.0 mm/km	2060	2.88	Good	26.1468267	N	84.2989740	E	Normal
13/04/23	10.55.20	138	100	5500	12.0 cm	17.4 km/hr	1200.0 mm/km	1337	1.96	Good	26.1477022	N	84.2992182	E	Normal
13/04/23	10.55.48	138	100	5600	24.0 cm	14.8 km/hr	2400.0 mm/km	2422	3.33	Good	26.1481695	N	84.3014154	E	Normal
13/04/23	10.56.07	138	100	5700	30.0 cm	9.3 km/hr	3000.0 mm/km	2984	3.99	Good	26.1478929	N	84.3028040	E	Normal
13/04/23	10.56.45	138	100	5800	15.0 cm	8.0 km/hr	1500.0 mm/km	1608	2.31	Good	26.1476336	N	84.3041010	E	Normal
13/04/23	10.57.14	138	100	5900	25.0 cm	12.4 km/hr	2500.0 mm/km	2512	3.44	Good	26.1475946	N	84.3055963	E	Normal
13/04/23	10.57.51	138	100	6000	14.0 cm	8.6 km/hr	1400.0 mm/km	1518	2.19	Good	26.1468954	N	84.3069010	E	Normal
13/04/23	10.58.16	138	100	6100	28.0 cm	8.9 km/hr	2800.0 mm/km	2784	3.77	Good	26.1464128	N	84.3133326	E	Normal
13/04/23	10.58.50	138	100	6200	31.0 cm	1.0 km/hr	3100.0 mm/km	3055	4.09	Good	26.1450129	N	84.3142939	E	Normal
13/04/23	10.59.17	138	100	6300	23.0 cm	10.2 km/hr	2300.0 mm/km	2332	3.22	Good	26.1446843	N	84.3151026	E	Normal
13/04/23	10.59.47	138	100	6400	17.0 cm	10.1 km/hr	1700.0 mm/km	1789	2.54	Good	26.1442480	N	84.3169334	E	Normal
13/04/23	11.00.18	138	100	6500	19.0 cm	17.1 km/hr	1900.0 mm/km	1970	2.77	Good	26.1438894	N	84.3169334	E	Normal

13/04/2023
JE

13/04/2023
A-E

Executive Engineer
Rural Road Department
Work Division Sivan-2

Name of work : Sakara - Hussaingari

Name of customer : Arun Kumar Jaiswal

(R)Rural Road

Good

Average

Poor

< 4000

4001 - 5000

> 5000

13/04/23	11.00.55	138	100	6600	26.0 cm	11.5 Km/Hr	2500.0 mm/Km	2603	3.55	Good	26.1441259	N	84.3169107	E	Normal
13/04/23	11.01.25	138	100	6700	25.0 cm	11.5 Km/Hr	2500.0 mm/Km	2512	3.44	Good	26.1438894	N	84.3178566	E	Normal
13/04/23	11.02.14	138	100	6800	11.0 cm	9.8 Km/Hr	1100.0 mm/Km	1247	1.84	Good	26.1435892	N	84.3168791	E	Normal
13/04/23	11.02.45	138	100	6900	19.0 cm	17.1 Km/Hr	1900.0 mm/Km	1970	2.77	Good	26.1438894	N	84.3160334	E	Normal
13/04/23	11.03.07	138	100	7000	16.0 cm	11.5 Km/Hr	1600.0 mm/Km	1699	2.42	Good	26.1441259	N	84.3169107	E	Normal
13/04/23	11.03.51	138	100	7100	23.0 cm	11.5 Km/Hr	2500.0 mm/Km	2512	3.44	Good	26.1438894	N	84.3178566	E	Normal
13/04/23	10.04.12	138	100	7200	11.0 cm	9.8 Km/Hr	1100.0 mm/Km	1247	1.84	Good	26.1435892	N	84.3168791	E	Normal

13/04/2023
DE

13/04/2023
AE

Executive Engineer
Rural Work Department
Work Division Swara
