

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्यप्रमंडल, चकिया, (पूर्वी चम्पारण),

पत्रांक: 620/अनु0/ चकिया, दिनांक: 12/04/2023

प्रेषक

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, चकिया।

सेवामे,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव
बिहार ग्रामीण पथ विकास एजेंसी,
ग्रामीण कार्य विभाग, बिहार, पटना।

विषय- विभाग के नई अनुरक्षण नीति-2018 M.R (3054) योजना के अन्तर्गत पंचवर्षीय अनुरक्षण कार्य के लिए निधि उपलब्ध कराने के संबंध में।

प्रसंग- अभियंता प्रमुख, ग्रा0का0वि0, बिहार, पटना के पत्रांक-मु0अ0-4(मु0)
3054-04-229/2021-1135 (अनु0)/पटना, दिनांक-09.03.2022

महाशय,

उपर्युक्त विषयक प्रासंगिक पत्र में दिये निर्देश के आलोक में नई अनुरक्षण नीति-2018 अन्तर्गत पथों का अनुरक्षण की राशि के आवंटन हेतु विहित प्रपत्र में अंकित कर आवश्यक कार्रवाई हेतु समर्पित किया जाता है।

अतः M.R (3054) नई अनुरक्षण नीति-2018 (Package No.RM/EA/CHA/20/0012) योजनान्तर्गत अनुरक्षण हेतु अधियाचना प्रपत्र में दशाये गये अधियाचित राशि उपलब्ध कराने की कृपा की जाय। कार्य का निरीक्षण किया गया, कार्य संतोषप्रद है। उक्त पथ में ए0टी0आर0 लंबित नहीं है।

अनु0:- 1. अधियाचना प्रपत्र।

2. Signed Hard Copy and of recorded IRI is enclosed
3. Standard Format for Roads Quarterly Statement

विश्वनाथभाजन,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल-चकिया।

STANDRAD FORMAT FOR ROADS QUARTERLY STATEMENT 8th Quarter)

PIU Name :- RWD, WD, CHAKIA

1	Name of the Road -	Kotwa Kalyanpur Through Road near Daupur Bariya		
2	Batch No. -	RM/EA/CHA/20/0012		
3	Project ID -	31708202100		
4	Total Length of Road (In KM) -	8.365		
5	Length of Road to Meet Required Service Level [Completed Length] (in KM) [1]	8.365		
6	No. of Total Quarter (ie 3 Months as a unit) In 5 Years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	120.49740		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	6.02487		
Compliance Criteria	Standard Job Description	Non- Compliance		Reduction Payment [6] = [3] / [1] * [2] * [4]
		Length Non-Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGE WAY)	0	60%	0
II	SHOULDERS AND EMBANMENTS	0	10%	0
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0	15%	0
IV	SIGNAGE AND ROAD SAFETY	0	10%	0
V	VEGETATION	0	5%	0
TOTAL PAYMENT REDUCTION FOR THE QUATRER (in Lakh) [5]				0
TO BE PAID FOR THE QUARTER / DEMAND (in Lakh) [6]				6.02487

Date of Inpection by E/ I or his agent
Prepared by Contractor's self Control unit

Name and Designation of Person inspecting road

Date

Signature of Person inspecting road

(Signature)

Certify by E/I [Signature] Date

Requisition Formet for Scheme Head-MR-(3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

2 Year (8th Quarter)

RWD, Works Division Chakia

Government Of Bihar

OM01

Rural Works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

To:- Executive Engineer
RWD, Works Division Chakia

Position :- A.E

Date:-

Road From:- Kotwa Kalyanpur Through Road near Dawpur - Baniya
(Package No.RMEA/CHA/20.0012)

Length of Road :- 8.365 Km

Period :- From - 08.11.2022 To 07.02.2023

Inspector :- A.E RWD Sub Division : Kalyanpur

No	Standard Of Work Item Name	Work Unit	Unit Of Required in each Kilometer										Comments
			1	2	3	4	5	6	7	8	9	10	
OM100	Sealed payment	m ²	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	No Pot Hole Found.
OM101	Pothole Patching	m ³	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	No Surface Depression & Rut Patching Found
OM102	Surface Depression and Rut patching	Lm	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	No Crack sealing Found
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	No Loss Of Aggregates (Surface Ravelling) Found
OM104	Surface Treatment	m ²	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	No Bleeding/ Flushing Required
	(a) Loss of Aggregate (Surface Ravelling)	m ²	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	No Bleeding/ Flushing Required
	(b) Bleeding / Flushing	m ²	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	No Crocodile Cracking Found
	(c) Crocodile Cracking	m ²	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	No Edge Repair Required
105	Edge Repair	m ²	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	N.A	N.A	
106	Dipouts	m ³	N.A	N.A	N.A	N.A	N.A	N.A	N.A	N.A			
107	Concrete pavement												
	Other activities												
OM200	Shoulder												No Edge Drop-Off Required
	Unsealed Shoulder	Lm	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Not Required
OM201	(a) Edge Drop-off	Lm	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	No Holding Water Found
	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil	Nil	Nil	Nil	Nil	Nil	12.43	8.69		
	(c) Holding water	M ³	11.36	21.98	14.67	12.35	13.39	16.75	15.23	N.A	N.A	N.A	Not Required
OM202	Embankment Repair	M ³	N.A	N.A	N.A	N.A	N.A	N.A	N.A	N.A	N.A	N.A	
	Other activities (Rain Cuts)												
OM300	Drainage including culverts major	Lm	N.A	N.A	N.A	N.A	N.A	N.A	N.A	N.A	N.A	N.A	Not Required
OM301	Surface Drains & Verge	No	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Not Required
OM302	Culvert Cleaning	M ³	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Not Required
OM303	Culvert and pit Repair	M ²	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Not Required
	Other activities(Whirlw washing)												

ना के अन्तर्गत पंचवर्षीय (सह)

No	standard Of Work Item	Work	Unit	1	2	3	4	5	6	7	8	9	10	Comments
OM400	Vegetation													
	Grass Control													
OM401	(a) Roadside- General Tidy													
	(b) Clear near Safety signs, kilometer posts and roadside furniture													
		Ha												Not Required
		Ha												Not Required
OM402	Tree and Shrub Management:													
	Cutting Of Branches Of Trees	No												Not Required
	Cutting Of Shrubs From Road Way	No												Not Required
	Other activities (Trimming of Grass)	M ²												Not Required
OM500	Safety Signage and Road													
	Signs Maintenance	No												Not Required
OM501	Guard Stones	Lm												Not Required
OM502	Distance Stones	No												Not Required
OM503	Road Marking	M ²												Not Required
OM504	Other activities													

Execution Engineer,
Works Division, Chakia

11/04/23

11/04/23

Bidder
Appendix

Name of work : Kotwakalyanpur Through Road near Dawpur - Bariya

Name of customer : Prabhat Kumar

(R) Rural Road

Date	Time	Test No	Distance(m)	Total Distance(m)	BUMP(cm)	Speed(Km/Hr)	Ul(mm/Km)	Corrected Ul (mm/Km)	IRI	Status	Poor			Direction1	Remarks	
											Average		Direction			Longitude
											Good < 4000	4001 - 5000				
											> 5000					
19/02/23	10:37:21	48	0	0	0.0 cm	0.0 Km/Hr	0.0 mm/Km	205	0.37	Good	26.5535727	N	84.9210291	E	Normal	
19/02/23	10:38:06	48	100	100	23.0 cm	16.7 Km/Hr	2300.0 mm/Km	2337	3.22	Good	26.4739875	N	84.9355784	E	Normal	
19/02/23	10:38:31	48	100	200	21.0 cm	14.2 Km/Hr	2100.0 mm/Km	2152	2.99	Good	26.4733648	N	84.9363261	E	Normal	
19/02/23	10:38:52	48	100	300	22.0 cm	17.1 Km/Hr	2200.0 mm/Km	2244	3.11	Good	26.4728231	N	84.9379893	E	Normal	
19/02/23	10:39:13	48	100	400	22.0 cm	17.1 Km/Hr	2200.0 mm/Km	2244	3.11	Good	26.4723597	N	84.9383784	E	Normal	
19/02/23	10:39:44	48	100	500	25.0 cm	12.1 Km/Hr	2500.0 mm/Km	2622	3.45	Good	26.4707212	N	84.9382334	E	Normal	
19/02/23	10:40:03	48	100	600	26.0 cm	18.9 Km/Hr	2600.0 mm/Km	2615	3.56	Good	26.4698592	N	84.9380198	E	Normal	
19/02/23	10:40:26	48	100	700	20.0 cm	13.7 Km/Hr	2000.0 mm/Km	2059	2.88	Good	26.4690561	N	84.9376994	E	Normal	
19/02/23	10:40:37	48	100	800	21.0 cm	32.0 Km/Hr	2100.0 mm/Km	2152	2.99	Good	26.4681578	N	84.9374171	E	Normal	
19/02/23	10:40:48	48	100	900	26.0 cm	31.5 Km/Hr	2600.0 mm/Km	2615	3.56	Good	26.4674044	N	84.9371577	E	Normal	
19/02/23	10:40:59	48	100	1000	29.0 cm	32.4 Km/Hr	2900.0 mm/Km	2893	3.9	Good	26.4669447	N	84.9371577	E	Normal	
19/02/23	10:41:08	48	100	1100	20.0 cm	40.3 Km/Hr	2000.0 mm/Km	2059	2.88	Good	26.4653406	N	84.9368144	E	Normal	
19/02/23	10:41:16	48	100	1200	20.0 cm	43.2 Km/Hr	2000.0 mm/Km	2059	2.88	Good	26.4644461	N	84.9365084	E	Normal	
19/02/23	10:41:26	48	100	1300	20.0 cm	37.8 Km/Hr	2000.0 mm/Km	2059	2.88	Good	26.4636412	N	84.9364939	E	Normal	
19/02/23	10:41:43	48	100	1400	28.0 cm	21.3 Km/Hr	2800.0 mm/Km	2800	3.79	Good	26.4627695	N	84.9363642	E	Normal	
19/02/23	10:41:54	48	100	1500	29.0 cm	30.9 Km/Hr	2900.0 mm/Km	2893	3.9	Good	26.4617643	N	84.9363642	E	Normal	
19/02/23	10:42:07	48	100	1600	29.0 cm	27.3 Km/Hr	2900.0 mm/Km	2893	3.9	Good	26.4612150	N	84.9371577	E	Normal	
19/02/23	10:42:19	48	100	1700	26.0 cm	30.0 Km/Hr	2600.0 mm/Km	2615	3.56	Good	26.4605036	N	84.9370814	E	Normal	
19/02/23	10:42:30	48	100	1800	24.0 cm	31.8 Km/Hr	2400.0 mm/Km	2430	3.34	Good	26.4595957	N	84.9366847	E	Normal	
19/02/23	10:42:41	48	100	1900	24.0 cm	34.9 Km/Hr	2400.0 mm/Km	2430	3.34	Good	26.4589281	N	84.9361964	E	Normal	
19/02/23	10:42:51	48	100	2000	29.0 cm	35.6 Km/Hr	2900.0 mm/Km	2893	3.9	Good	26.4589281	N	84.9361964	E	Normal	

Name of work : Kotwakalyanpur Through Road near Dawpur - Baniya

Name of customer : Prabhat Kumar

(R) Rural Road

		Good		Average		Poor									
		< 4000		4001 - 5000		> 5000									
19/02/23	10:43:00	48	100	2100	20.0 cm	38.1 Km/Hr	2000.0 mm/Km	2059	2.88	Good	26.4575363	N	84.9557254	E	Normal
19/02/23	10:43:10	48	100	2200	22.0 cm	38.0 Km/Hr	2200.0 mm/Km	2244	3.11	Good	26.4571124	N	84.9554437	E	Normal
19/02/23	10:43:50	48	100	2300	21.0 cm	29.4 Km/Hr	2100.0 mm/Km	2152	2.99	Good	26.4567450	N	84.9547843	E	Normal
19/02/23	10:43:50	48	100	2300	30.0 cm	12.8 Km/Hr	3000.0 mm/Km	2686	4.01	Good	26.4562208	N	84.9541780	E	Normal
19/02/23	10:44:17	48	100	2400	23.0 cm	22.0 Km/Hr	2300.0 mm/Km	2237	3.22	Good	26.4558908	N	84.9535642	E	Normal
19/02/23	10:44:33	48	100	2500	24.0 cm	31.2 Km/Hr	2400.0 mm/Km	2430	3.34	Good	26.4557156	N	84.9529623	E	Normal
19/02/23	10:44:44	48	100	2600	27.0 cm	34.9 Km/Hr	2700.0 mm/Km	2708	3.68	Good	26.4554729	N	84.9523577	E	Normal
19/02/23	10:44:55	48	100	2700	25.0 cm	34.2 Km/Hr	2500.0 mm/Km	2522	3.45	Good	26.4551554	N	84.9517511	E	Normal
19/02/23	10:45:05	48	100	2800	25.0 cm	25.4 Km/Hr	2500.0 mm/Km	2522	3.45	Good	26.4549105	N	84.9511579	E	Normal
19/02/23	10:45:20	48	100	2900	26.0 cm	18.4 Km/Hr	2600.0 mm/Km	2615	3.56	Good	26.4546733	N	84.9505554	E	Normal
19/02/23	10:45:16	48	100	3000	29.0 cm	13.6 Km/Hr	2900.0 mm/Km	2893	3.9	Good	26.4542202	N	84.9499559	E	Normal
19/02/23	10:47:54	48	100	3100	29.0 cm	18.6 Km/Hr	2900.0 mm/Km	2893	3.9	Good	26.4537715	N	84.9493533	E	Normal
19/02/23	10:48:12	48	100	3200	20.0 cm	11.0 Km/Hr	2000.0 mm/Km	2059	2.88	Good	26.4535554	N	84.9487241	E	Normal
19/02/23	10:48:35	48	100	3300	20.0 cm	30.0 Km/Hr	2000.0 mm/Km	2059	2.88	Good	26.4533507	N	84.9481080	E	Normal
19/02/23	10:48:47	48	100	3400	21.0 cm	29.7 Km/Hr	2100.0 mm/Km	2152	2.99	Good	26.4531401	N	84.9474923	E	Normal
19/02/23	10:48:59	48	100	3500	22.0 cm	34.2 Km/Hr	2200.0 mm/Km	2244	3.11	Good	26.45277401	N	84.9468783	E	Normal
19/02/23	10:49:09	48	100	3600	22.0 cm	33.8 Km/Hr	2200.0 mm/Km	2244	3.11	Good	26.4525330	N	84.9462649	E	Normal
19/02/23	10:49:20	48	100	3700	24.0 cm	35.2 Km/Hr	2400.0 mm/Km	2430	3.34	Good	26.45231093	N	84.9456535	E	Normal
19/02/23	10:49:30	48	100	3800	20.0 cm	36.7 Km/Hr	2000.0 mm/Km	2059	2.88	Good	26.4520932	N	84.9450415	E	Normal
19/02/23	10:49:40	48	100	3900	20.0 cm	36.7 Km/Hr	2000.0 mm/Km	2059	2.88	Good	26.45187303	N	84.9444294	E	Normal
19/02/23	10:49:50	48	100	4000	19.0 cm	39.2 Km/Hr	1900.0 mm/Km	1956	2.76	Good	26.45165363	N	84.9438179	E	Normal
19/02/23	10:49:59	48	100	4100	25.0 cm	32.0 Km/Hr	2500.0 mm/Km	2522	3.45	Good	26.4514363	N	84.9432064	E	Normal
19/02/23	10:50:10	48	100	4200											

Name of work : Kolwakalyanpur Through Road near Dawpur - Bariya

Name of customer : Prabhat Kumar

(R) Rural Road

		Good		Average		Poor									
		< 4000		4001 - 5000		> 5000									
19/02/23	10:50:22	48	100	4300	29.0 cm	31.2 Km/Hr	2900.0 mm/Km	2893	3.9	Good	26.3332579	N	84.9572611	E	Normal
19/02/23	10:50:39	48	100	4400	29.0 cm	21.2 Km/Hr	2900.0 mm/Km	2893	3.9	Good	26.3824301	N	84.9574273	E	Normal
19/02/23	10:50:59	48	100	4500	23.0 cm	18.0 Km/Hr	2300.0 mm/Km	2337	3.22	Good	26.3619094	N	84.9568379	E	Normal
19/02/23	10:51:19	48	100	4600	28.0 cm	17.4 Km/Hr	2800.0 mm/Km	2800	3.79	Good	26.3815527	N	84.9590540	E	Normal
19/02/23	10:51:30	48	100	4700	20.0 cm	34.5 Km/Hr	2000.0 mm/Km	2059	2.88	Good	26.3866772	N	84.9593440	E	Normal
19/02/23	10:51:46	48	100	4800	26.0 cm	22.2 Km/Hr	2600.0 mm/Km	2615	3.56	Good	26.3798342	N	84.9591609	E	Normal
19/02/23	10:52:03	48	100	4900	26.0 cm	21.8 Km/Hr	2600.0 mm/Km	2615	3.56	Good	26.3787355	N	84.9589252	E	Normal
19/02/23	10:52:20	48	100	5000	29.0 cm	20.7 Km/Hr	2900.0 mm/Km	2893	3.9	Good	26.3779020	N	84.9583674	E	Normal
19/02/23	10:52:36	48	100	5100	25.0 cm	23.1 Km/Hr	2500.0 mm/Km	2522	3.45	Good	26.3770933	N	84.9579783	E	Normal
19/02/23	10:52:52	48	100	5200	29.0 cm	22.0 Km/Hr	2900.0 mm/Km	2893	3.9	Good	26.3751282	N	84.9576197	E	Normal
19/02/23	10:53:10	48	100	5300	30.0 cm	20.4 Km/Hr	3000.0 mm/Km	2986	4.01	Good	26.3753672	N	84.9575663	E	Normal
19/02/23	10:53:27	48	100	5400	28.0 cm	21.2 Km/Hr	2800.0 mm/Km	2800	3.79	Good	26.3745527	N	84.9574366	E	Normal
19/02/23	10:53:44	48	100	5500	29.0 cm	21.1 Km/Hr	2900.0 mm/Km	2893	3.9	Good	26.376906	N	84.9572764	E	Normal
19/02/23	10:54:01	48	100	5600	30.0 cm	21.2 Km/Hr	3000.0 mm/Km	2886	4.01	Good	26.3725130	N	84.9570170	E	Normal
19/02/23	10:54:17	48	100	5700	30.0 cm	22.5 Km/Hr	3000.0 mm/Km	2886	4.01	Good	26.3710851	N	84.9568034	E	Normal
19/02/23	10:54:34	48	100	5800	25.0 cm	19.8 Km/Hr	2500.0 mm/Km	2522	3.45	Good	26.370906	N	84.9565440	E	Normal
19/02/23	10:54:44	48	100	5900	20.0 cm	34.5 Km/Hr	2000.0 mm/Km	2059	2.88	Good	26.3704443	N	84.9563685	E	Normal
19/02/23	10:55:33	48	100	6000	21.0 cm	28.2 Km/Hr	2100.0 mm/Km	2152	2.99	Good	26.3690310	N	84.9562006	E	Normal
19/02/23	10:55:59	48	100	6100	23.0 cm	13.8 Km/Hr	2300.0 mm/Km	2337	3.22	Good	26.4739675	N	84.9355784	E	Normal
19/02/23	10:56:51	48	100	6200	21.0 cm	17.0 Km/Hr	2100.0 mm/Km	2152	2.99	Good	26.4733648	N	84.9363261	E	Normal
19/02/23	10:56:05	48	100	6300	25.0 cm	25.4 Km/Hr	2500.0 mm/Km	2522	3.45	Good	26.4728231	N	84.9368933	E	Normal
19/02/23	10:56:19	48	100	6400	22.0 cm	26.7 Km/Hr	2200.0 mm/Km	2244	3.11	Good	26.4723597	N	84.9375893	E	Normal

Name of customer :	Prabhat Kumar
--------------------	---------------

(R)Rural Road


Good				Average				Poor							
< 4000				4001 - 5000				> 5000							
19/02/23	10:56:35	48	100	6500	26.0 cm	22.5 Km/Hr	2600.0 mm/Km	26:15	3.56	Good	26:47:16:68	N	84.9383784	E	Normal
19/02/23	10:56:55	48	100	6600	25.0 cm	18.2 Km/Hr	2500.0 mm/Km	25:22	3.45	Good	26:47:02:12	N	84.9382334	E	Normal
19/02/23	10:57:16	48	100	6700	24.0 cm	16.6 Km/Hr	2400.0 mm/Km	24:30	3.34	Good	26:46:58:32	N	84.9380198	E	Normal
19/02/23	10:57:55	48	100	6800	24.0 cm	19.6 Km/Hr	2400.0 mm/Km	24:30	3.34	Good	26:48:05:51	N	84.9376994	E	Normal
19/02/23	10:58:15	48	100	6900	31.0 cm	17.4 Km/Hr	3100.0 mm/Km	30:79	4.12	Good	26:48:01:58	N	84.9374171	E	Normal
19/02/23	10:58:40	48	100	7000	29.0 cm	15.0 Km/Hr	2900.0 mm/Km	28:33	3.9	Good	26:46:74:44	N	84.9371577	E	Normal
19/02/23	10:59:02	48	100	7100	23.0 cm	15.8 Km/Hr	2300.0 mm/Km	23:37	3.22	Good	26:46:53:47	N	84.9371577	E	Normal
19/02/23	10:59:33	48	100	7200	32.0 cm	11.5 Km/Hr	3200.0 mm/Km	31:71	4.23	Good	26:46:53:06	N	84.9368144	E	Normal
19/02/23	11:00:17	48	100	7300	24.0 cm	17.2 Km/Hr	2400.0 mm/Km	24:30	3.34	Good	26:46:35:12	N	84.9364939	E	Normal
19/02/23	11:00:40	48	100	7400	30.0 cm	15.6 Km/Hr	3000.0 mm/Km	29:56	4.01	Good	26:46:27:55	N	84.9363642	E	Normal
19/02/23	11:01:09	48	100	7500	29.0 cm	12.6 Km/Hr	2900.0 mm/Km	28:33	3.9	Good	26:46:17:54	N	84.9363642	E	Normal
19/02/23	11:01:33	48	100	7600	21.0 cm	14.8 Km/Hr	2100.0 mm/Km	21:52	2.99	Good	26:46:12:50	N	84.9371577	E	Normal
19/02/23	11:01:56	48	100	7700	21.0 cm	15.5 Km/Hr	2100.0 mm/Km	21:52	2.99	Good	26:46:03:06	N	84.9370814	E	Normal
19/02/23	11:02:18	48	100	7800	30.0 cm	16.3 Km/Hr	3000.0 mm/Km	29:56	4.01	Good	26:45:59:57	N	84.9366847	E	Normal
19/02/23	11:02:33	48	100	7900	23.0 cm	22.9 Km/Hr	2300.0 mm/Km	23:37	3.22	Good	26:45:52:51	N	84.9361964	E	Normal
19/02/23	11:02:52	48	100	8000	23.0 cm	19.6 Km/Hr	2300.0 mm/Km	23:37	3.22	Good	26:45:73:53	N	84.9357234	E	Normal
19/02/23	11:03:05	48	100	8100	23.0 cm	25.7 Km/Hr	2300.0 mm/Km	23:37	3.22	Good	26:45:71:04	N	84.9354487	E	Normal
19/02/23	11:03:19	48	100	8200	22.0 cm	26.2 Km/Hr	2200.0 mm/Km	22:44	3.11	Good	26:45:50:48	N	84.9347849	E	Normal
19/02/23	11:03:32	48	100	8300	30.0 cm	26.7 Km/Hr	3000.0 mm/Km	29:56	4.01	Good	26:45:52:08	N	84.9341670	E	Normal
19/02/23	11:03:45	48	100	8400	26.0 cm	30.0 Km/Hr	2600.0 mm/Km	26:15	3.56	Good	26:45:55:08	N	84.9335542	E	Normal

12/11/23

~~11104123~~ AE

Executive Engineer
R.W.D. Works Division
Gnakia

Name of Customer: Prabhat Kumar, Machine no: 19191, Road: Kotwakalyanpur Through Road near Dampur - Bariya, Date: 19-02-23, Section No: 48, Equation: $Y = 0.927 X + 204.8$

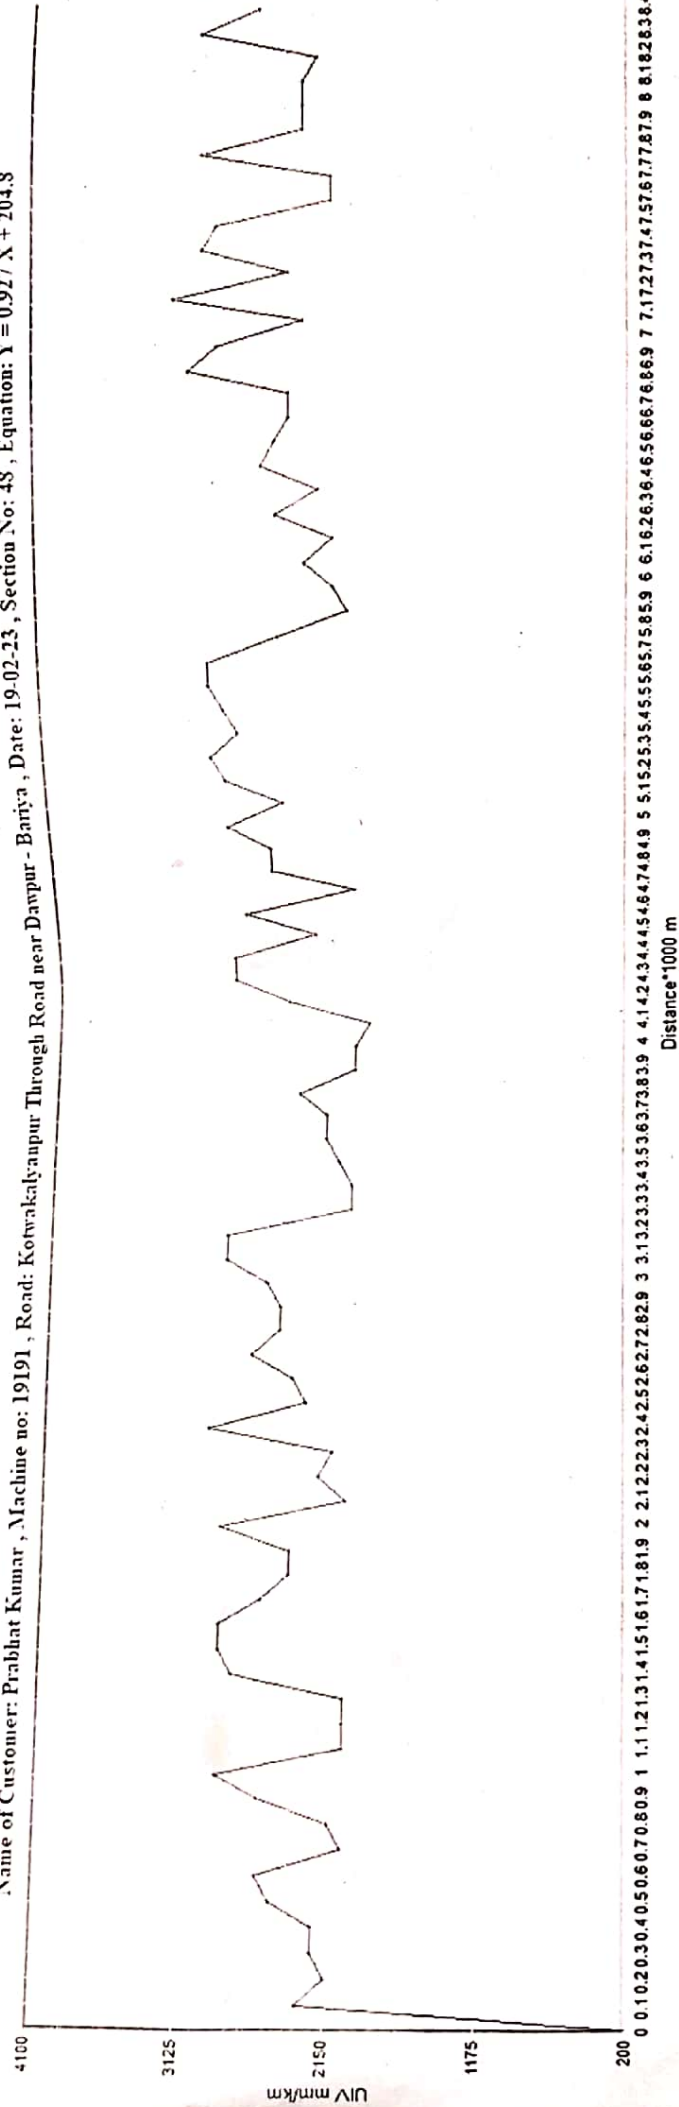

18/11/23
17/11/23
72.

11/04/23
AC

[Signature]
Executive Engineer
Executive Works Division
R.W.D. Chhabra
