

कार्यालय
कार्यपालक अभियंता, ग्रामीण कार्य विभाग
कार्य प्रमंडल, दलसिंहसराय, समस्तीपुर

पत्रांक 482(म/क) दलसिंहसराय / दिनांक 1.7.4.2023

प्रेषक, कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, दलसिंहसराय

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी,
सचिव -सह- प्राधिकृत पदाधिकारी, बिहार
ग्रामीण पथ विकास एजेंसी पटना।

विषय- **New Maintenance Policy 2018** योजनान्तर्गत पथ में आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपरोक्त विषय के संबंध में कहना है कि **New Maintenance Policy 2018** योजनान्तर्गत चल रहे पथ के निर्माणधीन कार्य के विरुद्ध चल रहे योजनाओं का भुगतान हेतु मो0- 482.79770 लाख की आवश्यकता है। अधियाचना का निर्माण कार्य विशिष्टियों के अनुरूप है तथा कार्य संतोषप्रद है।

अतः अनुरोध है कि अधियाचना पत्र के आधार पर आवंटन हेतु मो0- 482.79770 लाख उपलब्ध कराने की कृपा की जाय।

अनु0- 1) अधियाचना प्रपत्र।

2) 19ए फॉर्म।

विश्वासभाजन

[Signature] 104123

कार्यपालक अभियंता

ग्रामीण कार्य विभाग

[Signature] कार्य प्रमंडल, दलसिंहसराय

FROM GFR-19-A

(See Govt. of India's decision(i) below rule 150)

Form of Utilisation Certificate upto April.-2023

New Maintenance Policy 2018(MR New)

PIU:- RWD Works Division Dalsinghsarai

Sl No	Name of Scheme	Sanction No. & Date with Amount (in Rs. Lakh)	Amount Received (in Lakh)	Particulars
1	2	3	4	5
1	New Maintenance Policy 2018 (MR New)	3173.65743	3173.65743	Certified that out of Rs-3173.65743 Lakh received till date in favour of Executive Engineer, RWD Works Division Dalsinghsarai a Sum of Rs-3158.22155 Lakh has been utilized for the New Maintenance Policy 2018(MR New) Scheme as given in the margine for which it was Sanctioned and that the Balance of Rs-15.43588 Lakh remaining unutilized at the end of period under the time of completion
		3173.65743	3173.65743	

2. Certified that I have satisfied myself that the conditions on which the grants-in-aid was

Kind of Checks Exercised:-


- (i) Workers have been supervised by Executive Engineer/ Superintending Engineer
- (ii) Periodical inspection has been conducted by Executive Engineer/ Superintending Engineer
- (iii) Construction materials have been tested
- (iv) Measurments have been recorded in the MB's and test check conducted by the
- (v) All other codal formalities have overserved

3. Physical Progress Achieved

- (i) Construction of Road Works
- (ii) Construction of CD Works


Sr.DAO

Rural Works Department,
Works Division Dalsinghsarai


Executive Engineer


Rural Works Department,
Works Division Dalsinghsarai

Rural Works Department, Works Division Dalsinghsarai
Requisition Format for Scheme Head - MR (3054) Under Bihar Rural Road maintenance Policy 2018
(Initial Rectification and Surface Renewal)


Name of Division : PU(Dalsinghsarai)

Sl No	Package no	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (in Lac)		Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allotted Amount (1 Lac)	up to date expenditure as per MIS (in Lac)	Requisition Against work done (in lac)	Remarks
					Length (in Km)	Amount (in Lac)	Initial Rectification with Surface Renewal (in lac)	5 years Routine Maintenance (in lac)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	2	NH - Barabati	32010402018	1424/26.03.22	3.700	167.64000	125.70591	42.80071	MBD 01/22-23 17.02.23	16.11.23	-	2908	25mm	5.10%	0.00000	0.00000	113.13532	
2	2	NH 28 To Sileampur Tak	3201041895697	1424/26.03.22	3.500	161.63000	123.21568	39.63455	MBD 01/22-23 17.02.23	16.11.23	-	3333	25mm	5.10%	0.00000	0.00000	110.89411	
3	2	Haringhpur Kalixati Path - unedpur Harpur Bhandi	32010402004	1424/26.03.22	4.500	217.78000	159.07204	50.78354	MBD 03/22-23 28.02.23	27.11.23	-	3279	25mm	5.10%	0.00000	0.00000	127.25763	
4	2	Kalixati path laly Chowk - Chandauli Mizepur R. o Path	32010402005	1424/26.03.22	4.840	225.76000	164.38830	55.10699	MBD 03/22-23 28.02.23	27.11.23	-	3216	25mm	5.10%	0.00000	0.00000	131.51064	
TOTAL					16.540	772.810	572.882	188.236							0.00000	0.00000	482.79770	

- Signed Hard Copy and Soft Copy (in Excel) of recorded IRI is enclosed.
- Up-to date Physical Progress has been uploaded in MIS.

Sr Divisional Account Officer
Rural Works Department,
Works Division Dalsinghsarai

Executive Engineer
Rural Works Department,
Works Division Dalsinghsarai

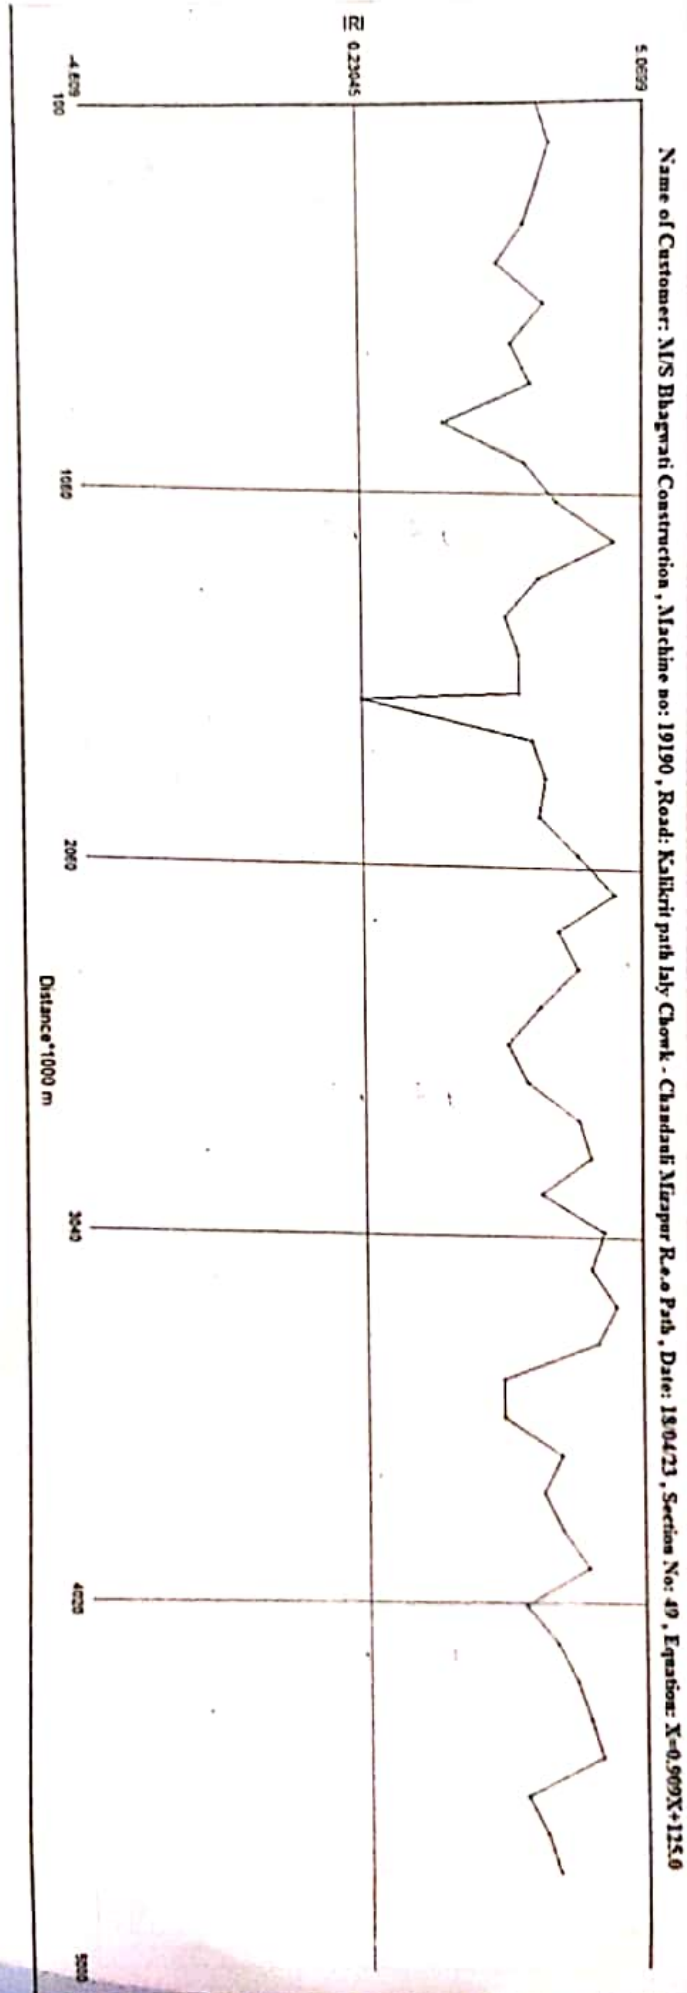

18/04/23
18/04/23
18/04/23

18/04/23
18/04/23
18/04/23

18/04/23
18/04/23
18/04/23

Name of the work: Kalikrit path laly Chowk - Chandauli Mizapur R.e.o Path

Date	Time	Test No	Distance (meter)	Total Distance (meter)	BUMP (cm)	Speed (Km/Hr)	UI (mm/Km)	Corrected UI (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks
18/04/2023	10:54:16	49	100	100	25.0 cm	11.7 Km/Hr	2500.0 mm/Km	2397.5	3.3	Good	25.7995	N	85.697423	E	Normal
18/04/2023	10:54:41	49	100	200	27.0 cm	14.2 Km/Hr	2700.0 mm/Km	2579.3	3.52	Good	25.79952	N	85.697319	E	Normal
18/04/2023	10:55:03	49	100	300	25.0 cm	16.0 Km/Hr	2500.0 mm/Km	2397.5	3.3	Good	25.79916	N	85.696219	E	Normal
18/04/2023	10:55:21	49	100	400	23.0 cm	20.4 Km/Hr	2300.0 mm/Km	2215.7	3.07	Good	25.79843	N	85.694101	E	Normal
18/04/2023	10:55:39	49	100	500	19.0 cm	19.6 Km/Hr	1900.0 mm/Km	1852.1	2.62	Good	25.79826	N	85.693373	E	Normal
18/04/2023	10:55:54	49	100	600	26.0 cm	24.3 Km/Hr	2600.0 mm/Km	2488.4	3.41	Good	25.79826	N	85.692643	E	Normal
18/04/2023	10:56:12	49	100	700	21.0 cm	19.8 Km/Hr	2100.0 mm/Km	2033.9	2.85	Good	25.79816	N	85.692284	E	Normal
18/04/2023	10:56:32	49	100	800	24.0 cm	17.4 Km/Hr	2400.0 mm/Km	2306.6	3.19	Good	25.79775	N	85.691478	E	Normal
18/04/2023	10:56:49	49	100	900	11.0 cm	21.1 Km/Hr	1100.0 mm/Km	1124.9	1.68	Good	25.79763	N	85.691105	E	Normal
18/04/2023	10:57:56	49	100	1000	23.0 cm	17.9 Km/Hr	2300.0 mm/Km	2215.7	3.07	Good	25.79728	N	85.690529	E	Normal
18/04/2023	10:58:21	49	100	1100	28.0 cm	14.2 Km/Hr	2800.0 mm/Km	2670.2	3.63	Good	25.79744	N	85.689227	E	Normal
18/04/2023	10:58:54	49	100	1200	37.0 cm	11.3 Km/Hr	3700.0 mm/Km	3488.3	3.61	Good	25.79801	N	85.688129	E	Normal
18/04/2023	10:59:21	49	100	1300	25.0 cm	13.0 Km/Hr	2500.0 mm/Km	2397.5	3.3	Good	25.79856	N	85.687184	E	Normal
18/04/2023	10:59:49	49	100	1400	20.0 cm	12.8 Km/Hr	2000.0 mm/Km	1943	2.73	Good	25.79875	N	85.686859	E	Normal
18/04/2023	11:00:19	49	100	1500	22.0 cm	12.0 Km/Hr	2200.0 mm/Km	2124.8	2.96	Good	25.71845	N	85.903063	E	Normal
18/04/2023	11:00:50	49	100	1600	22.0 cm	11.9 Km/Hr	2200.0 mm/Km	2124.8	2.96	Good	25.79897	N	85.685953	E	Normal
18/04/2023	11:01:53	49	100	1700	24.0 cm	13.5 Km/Hr	2400.0 mm/Km	2306.6	3.19	Good	25.8001	N	85.683259	E	Normal
18/04/2023	11:02:20	49	100	1800	26.0 cm	13.7 Km/Hr	2600.0 mm/Km	2488.4	3.41	Good	25.80014	N	85.68299	E	Normal
18/04/2023	11:02:49	49	100	1900	25.0 cm	12.4 Km/Hr	2500.0 mm/Km	2397.5	3.3	Good	25.8004	N	85.682151	E	Normal
18/04/2023	11:03:36	49	100	2000	31.0 cm	17.6 Km/Hr	3100.0 mm/Km	2942.9	3.96	Good	25.80156	N	85.680626	E	Normal
18/04/2023	11:04:16	49	100	2100	37.0 cm	18.9 Km/Hr	3700.0 mm/Km	3488.3	3.61	Good	25.80172	N	85.680523	E	Normal
18/04/2023	11:04:50	49	100	2200	28.0 cm	10.8 Km/Hr	2800.0 mm/Km	2670.2	3.63	Good	25.80229	N	85.679892	E	Normal
18/04/2023	11:11:27	49	100	2300	31.0 cm	10.8 Km/Hr	3100.0 mm/Km	2942.9	3.96	Good	25.80279	N	85.679353	E	Normal
18/04/2023	11:11:59	49	100	2400	25.0 cm	11.3 Km/Hr	2500.0 mm/Km	2397.5	3.3	Good	25.80317	N	85.679135	E	Normal
18/04/2023	11:12:41	49	100	2500	20.0 cm	18.4 Km/Hr	2000.0 mm/Km	1943	2.73	Good	25.80378	N	85.678007	E	Normal
18/04/2023	11:13:36	49	100	2600	23.0 cm	16.7 Km/Hr	2300.0 mm/Km	2215.7	3.07	Good	25.80373	N	85.677884	E	Normal
18/04/2023	11:14:20	49	100	2700	31.0 cm	18.0 Km/Hr	3100.0 mm/Km	2942.9	3.96	Good	25.80481	N	85.675709	E	Normal
18/04/2023	11:14:51	49	100	2800	33.0 cm	12.0 Km/Hr	3300.0 mm/Km	3124.7	3.18	Good	25.8052	N	85.674828	E	Normal
18/04/2023	11:15:27	49	100	2900	25.0 cm	19.9 Km/Hr	2500.0 mm/Km	2397.5	3.3	Good	25.80539	N	85.674127	E	Normal
18/04/2023	11:15:57	49	100	3000	35.0 cm	11.7 Km/Hr	3500.0 mm/Km	3306.5	3.39	Good	25.80606	N	85.672965	E	Normal
18/04/2023	11:16:28	49	100	3100	33.0 cm	11.5 Km/Hr	3300.0 mm/Km	3124.7	3.18	Good	25.80666	N	85.671984	E	Normal

18/04/2023	11:17:03	49	100	3200	37.0 cm	10.4 Km/Hr	3700.0 mm/Km	3488.3	3.61	Good	25.80722	N	85.671099	E	Normal
18/04/2023	11:17:34	49	100	3300	34.0 cm	11.5 Km/Hr	3400.0 mm/Km	3215.6	3.29	Good	25.80735	N	85.670338	E	Normal
18/04/2023	11:18:04	49	100	3400	19.0 cm	11.8 Km/Hr	1900.0 mm/Km	1852.1	2.62	Good	25.80841	N	85.668701	E	Normal
18/04/2023	11:18:27	49	100	3500	19.0 cm	15.2 Km/Hr	1900.0 mm/Km	1852.1	2.62	Good	25.80843	N	85.667577	E	Normal
18/04/2023	11:18:50	49	100	3600	28.0 cm	16.2 Km/Hr	2800.0 mm/Km	2670.2	3.63	Good	25.80847	N	85.666653	E	Normal
18/04/2023	11:19:10	49	100	3700	25.0 cm	17.5 Km/Hr	2500.0 mm/Km	2397.5	3.3	Good	25.80913	N	85.665401	E	Normal
18/04/2023	11:19:31	49	100	3800	28.0 cm	17.2 Km/Hr	2800.0 mm/Km	2670.2	3.63	Good	25.80971	N	85.663861	E	Normal
18/04/2023	11:20:03	49	100	3900	32.0 cm	16.5 Km/Hr	3200.0 mm/Km	3033.8	3.07	Good	25.8089	N	85.662742	E	Normal
18/04/2023	11:20:53	49	100	4000	22.0 cm	13.1 Km/Hr	2200.0 mm/Km	2124.8	2.96	Good	25.8086	N	85.661368	E	Normal
18/04/2023	11:21:11	49	100	4100	27.0 cm	10.5 Km/Hr	2700.0 mm/Km	2579.3	3.52	Good	25.80741	N	85.661207	E	Normal
18/04/2023	11:21:59	49	100	4200	30.0 cm	11.6 Km/Hr	3000.0 mm/Km	2852	3.85	Good	25.80868	N	85.660025	E	Normal
18/04/2023	11:22:06	49	100	4300	32.0 cm	36.5 Km/Hr	3200.0 mm/Km	3033.8	3.07	Good	25.80874	N	85.658805	E	Normal
18/04/2023	11:22:49	49	100	4400	34.0 cm	11.9 Km/Hr	3400.0 mm/Km	3215.6	3.29	Good	25.80954	N	85.657807	E	Normal
18/04/2023	11:23:00	49	100	4500	22.0 cm	16.5 Km/Hr	2200.0 mm/Km	2124.8	2.96	Good	25.80909	N	85.657651	E	Normal
18/04/2023	11:23:40	49	100	4600	25.0 cm	15.1 Km/Hr	2500.0 mm/Km	2397.5	3.3	Good	25.80899	N	85.657158	E	Normal
18/04/2023	11:24:59	49	100	4700	37.0 cm	10.0 Km/Hr	3700.0 mm/Km	2579.3	3.52	Good	25.80929	N	85.656034	E	Normal
18/04/2023	11:25:52	49	100	4700	27.0 cm	10.0 Km/Hr	2700.0 mm/Km	2579.3	2.52	Good	25.80929	N	85.656034	E	Normal
18/04/2023	11:25:52	49	100	4700	17.0 cm	10.0 Km/Hr	1700.0 mm/Km	2579.3	2.52	Good	25.80929	N	85.656034	E	Normal

18/04/23
18/04/23

18/04/23
18/04/23

18/04/23
18/04/23

IRI Value 3216
Machine ID 19190
