

कार्यालय कार्यपालक अभियंता ग्राहीण कार्य विभाग, कार्य प्रमण्डल, धमदाहा

पत्रांक...568.../ दिनांक...18/4/23...

प्रेषक,

कार्यपालक अभियंता,
ग्राहीण कार्य विभाग,
कार्य प्रमण्डल धमदाहा।

सेवा में,

सचिव—सह—शक्ति प्रदत्त पदाधिकारी,
बी0आर0आर0डी0ए0,
बुद्ध मार्ग, पटना।

विषय :- MR3054-NEW गद में राशि अधियाचना के संबंध में।
महाशय,

उपर्युक्त विषय के संबंध में कहना है कि MR3054-NEW अंतर्गत योजनाओं में राशि की आवश्यकता है

अतः अनुरोध है कि अधियाचित राशि आवंटित करने की कृपा की जाय।

अनु0 :- (1) अधियाचना की प्रति
(2) Copy of BUMP REPORT

विश्वासभाजन

निम्नलिखित
कार्यपालक अभियंता,
ग्राहीण कार्य विभाग,
कार्य प्रमण्डल धमदाहा,
18/4/23

RESIDENTIAL ENGINEER RWD WORKS DIVISION DHAMDHAHA																		
Sl No	Package No	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date	Administrative Approval		Agreement Amount (In Lakh)		Agreement No. & Date	Date of Completion as per Agreement	Actual date of Completion	Value OF IRI(in mm/km)	Thickness of Bitumen Layer (in MM)	Value Bitumen Content In Percent	Previous Total Allocated Amount (in Lakh)	up-to date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (in (In Lakh)	Amount of Rectification with Surface Renewal (In Lakh)	Initial	5 Year Routine Maintenance (In Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	MR-N22-23 Dharmdaha/18	SARITA PMGSY ROAD KURIYA TOLA TO HARIZAN TOLA	21105312010	762/27.07.2022	1.749	89.436	66.89754	29.85988	48MBD/2022 23/12.12.2022 ²	11.09.2023		2844.5	25mmmsdbc	5.0sdbc	0.00000	66.75000		
2	MR-N22-23 Dharmdaha/15	BHOTIYA PMGSY ROAD TO DHANUK MANDAL TOLA	21105313002	762/27.07.2022	2.100	115.900	93.04714	29.41833	50MBD/2022 23/22.12.2022 ²	21.09.2023		3265.38	25mmmsdbc	5.0sdbc	0.00000	92.75000		
TOTAL RS																		
(RS-ONR CRORE FIFTY NINE LAKH FIFTY THOUSAND ONLY)																		
159.94468 59.27821 0.00000 159.50000																		

1 SIGNED HARD COPY & SOFT COPY (IN EXCEL) OF RECORDED IRI IS ENCLOSED
2 UP-TO-DATE PHYSICAL PROGRESS HAS BEEN UPLOADED IN MIS

SR DIVISIONAL ACCOUNTS OFFICER,
RURAL WORKS DEPARTMENT
WORKS DIVISION, DHAMDAHA, PURNEA

EXECUTIVE ENGINEER
RURAL WORKS DEPARTMENT
WORKS DIVISION, DHAMDAHA, PURNEA

18/4/23

Lab Job number :66(RWD DHAMDAHA)

Date :14-04-23

Name of Customer :NISHA KUMARI

Name of Work/ Road :BHOTIYA PMGSY ROAD TO DHANUK TOLA

Sr.no	Location of Corrected U.I test(in km) value(mm/km)	Road catagory
-------	---	---------------

20	0.1	3069 G
21	0.2	2183 G
22	0.3	3856 G
23	0.4	2773 G
24	0.5	3364 G
25	0.6	3265 G
26	0.7	3364 G
27	0.8	3069 G
28	0.9	3265 G
29	1	2773 G
30	1.1	3561 G
31	1.2	3856 G
32	1.3	3364 G
33	1.4	2970 G
34	1.5	2872 G
35	1.6	3265 G
36	1.7	3462 G
37	1.8	2773 G
38	1.9	3954 G
39	2	3856 G
40	2.1	3659 G
AVERAGE		3265.38


Executive Engineer
 Rural Works Department
 Works Division Dhamdaha (Purnea)

M. Prasad S. S.
 17-04-23
 J.B.
 Borla Kothi


 18/4/23
 @2

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	UIV	TEGORY ROAD	IRI	Latitude	ongitude	Event
14/4/23	15:17:36	92	0.1	260	0	2600	3069 G		4.11	25.83849	87.20185	Normal
14/4/23	15:18:0	92	0.1	170	10.1	1700	2183 G		3.03	25.83938	87.20177	Normal
14/4/23	15:18:11	92	0.1	340	20.2	3400	3856 G		5.03	25.84021	87.20189	Normal
14/4/23	15:18:11	92	0.1	230	20.2	2300	2773 G		3.75	25.84116	87.20192	Normal
14/4/23	15:18:46	92	0.1	290	20.2	2900	3364 G		4.46	25.84206	87.202	Normal
14/4/23	15:19:0	92	0.1	280	10.1	2800	3265 G		4.34	25.84295	87.20214	Normal
14/4/23	15:19:22	92	0.1	290	20.2	2900	3364 G		4.46	25.84383	87.20232	Normal
14/4/23	15:19:22	92	0.1	260	10.1	2600	3069 G		4.11	25.84438	87.20173	Normal
14/4/23	15:20:0	92	0.1	280	10.1	2800	3265 G		4.34	25.84492	87.20226	Normal
14/4/23	15:20:0	92	0.1	230	20.2	2300	2773 G		3.75	25.84513	87.20323	Normal
14/4/23	15:20:32	92	0.1	310	20.2	3100	3561 G		4.69	25.84567	87.20394	Normal
14/4/23	15:21:0	92	0.1	340	20.2	3400	3856 G		5.03	25.84645	87.20441	Normal
14/4/23	15:21:7	92	0.1	290	10.1	2900	3364 G		4.46	25.84724	87.20487	Normal
14/4/23	15:21:7	92	0.1	250	10.1	2500	2970 G		3.99	25.84804	87.20534	Normal
14/4/23	15:21:43	92	0.1	240	20.2	2400	2872 G		3.87	25.84884	87.20562	Normal
14/4/23	15:22:0	92	0.1	280	20.2	2800	3265 G		4.34	25.84975	87.20564	Normal
14/4/23	15:22:18	92	0.1	300	20.2	3000	3462 G		4.57	25.85064	87.20552	Normal
14/4/23	15:22:18	92	0.1	230	20.2	2300	2773 G		3.75	25.85154	87.20559	Normal
14/4/23	15:23:0	92	0.1	350	20.2	3500	3954 G		5.15	25.85237	87.20588	Normal
14/4/23	15:23:0	92	0.1	340	20.2	3400	3856 G		5.03	25.85326	87.20586	Normal
14/4/23	15:23:28	92	0.1	320	20.2	3200	3659 G		4.8	25.85413	87.20562	Normal
							AVERAGE					
							3265.38					

$$Y = 0 * X^2 + 0.984 * X + 510.70$$

$$X = 3300$$

$$Y = 3757$$

(R) RURAL ROAD


Good Average Poor
 <4000 4001-5000 >5001

Signature
Executive Engineer
 Rural Works Department
 Works Division Dhamdaha (Pune)

Signature
 18/4/23

Signature
 17-04-23
 J. B. Borhara Kethi

File :H:\15041033.Xls, Section No.:92, Eqn : $Y = 0 * X^2 + 0.984 * X + 510.70$
 Name of Customer :NISHA KUMARI, Name of Work/ Road :BHOTIYA PMGSY ROAD TO DHANUK TOLA, Lab Job

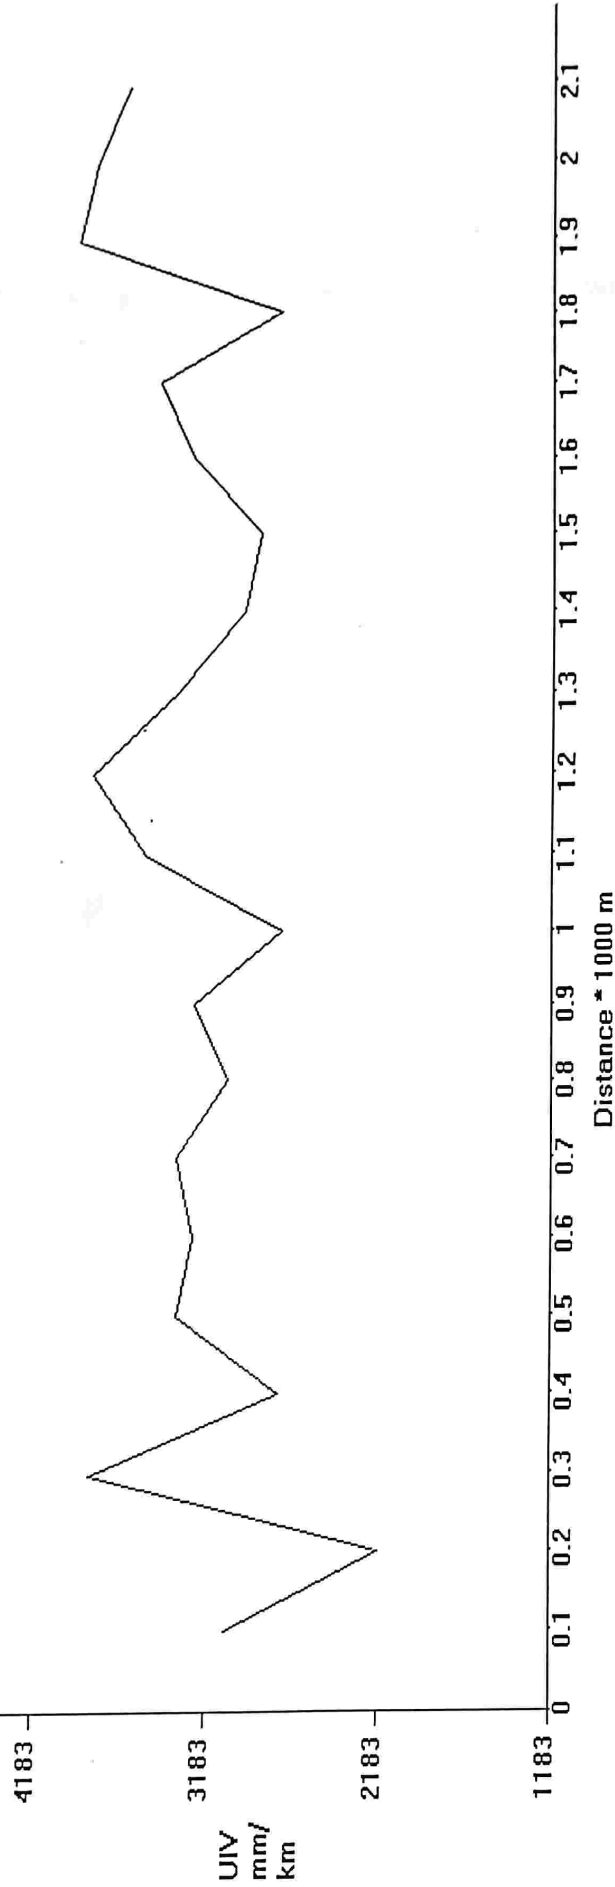

M. S. D. S. S.
 17-04-23
 J. B. B. S. S. S.

[Signature]
 18/11/23


[Signature]
Executive Engineer
 Rural Works Department
 Works Division Chanddaha (Purnea)

कार्यपालक अभियंता का कार्यालय

ग्रामीण कार्य विभाग, कार्य प्रमण्डल, धमदाहा

Email. ID- eerwddhamdaha@gmail.com

प्रमाणित किया जाता है कि BHOTIYA PMGSY ROAD TO DHANUK MANDAL TOLA का सभी अवयवों की जाँच शत-प्रतिशत कनीय अभियंता द्वारा किया गया है। सहायक अभियंता द्वारा सभी अवयवों की 50% से अधिक जाँच किया गया है। अधोहस्ताक्षरी द्वारा 10% अवयवों की जाँच की गई है।


17-04-23.

कनीय अभियंता,
बड़हरा कोठी


सहायक अभियंता,
ग्रामीण कार्य विभाग,
कार्य अवर प्रमण्डल, बड़हरा कोठी


कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, धमदाहा

Lab Job number :65(RWD DHAMDAHA)

Date :14-04-23

Name of Customer :PREM KUMAR

Name of Work/ Road :SARITA PMGSY ROAD TO KURIYA TOLA

Sr.no	Location of Corrected U.I test(in km) value(mm/km)	Road catagory
2	0.1	2970 G
3	0.2	3364 G
4	0.3	3069 G
5	0.4	2773 G
6	0.5	2872 G
7	0.6	2577 G
8	0.7	3069 G
9	0.8	2970 G
10	0.9	2577 G
11	1	3167 G
12	1.1	2675 G
13	1.2	2773 G
14	1.3	2872 G
15	1.4	2970 G
16	1.5	2773 G
17	1.6	2675 G
18	1.7	2380 G
19	1.8	2675 G
AVERAGE		2844.5

M. Jha
14/4/23
JE

[Signature]
14/04/2023
(AE)

[Signature]
Executive Engineer
Rural Works Department
Works Division Dhamdaha (Purnea)

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	UUV	TEGORY ROAD	IRI	Latitude .ongitude	Event
14/4/23	10:55:0	90	0.1	250	0	2500		2970 G	3.99	25.84033	87.2499 Normal
14/4/23	10:55:35	90	0.1	290	10.1	2900		3364 G	4.46	25.84025	87.25094 Normal
14/4/23	10:55:35	90	0.1	260	20.2	2600		3069 G	4.11	25.84039	87.25187 Normal
14/4/23	10:56:0	90	0.1	230	30.3	2300		2773 G	3.75	25.84054	87.25283 Normal
14/4/23	10:56:10	90	0.1	240	30.3	2400		2872 G	3.87	25.84077	87.25372 Normal
14/4/23	10:56:10	90	0.1	210	30.3	2100		2577 G	3.51	25.84107	87.25463 Normal
14/4/23	10:56:46	90	0.1	260	20.2	2600		3069 G	4.11	25.84129	87.25557 Normal
14/4/23	10:57:0	90	0.1	250	20.2	2500		2970 G	3.99	25.84142	87.25658 Normal
14/4/23	10:57:0	90	0.1	210	30.3	2100		2577 G	3.51	25.84151	87.25749 Normal
14/4/23	10:57:21	90	0.1	270	30.3	2700		3167 G	4.22	25.84159	87.2585 Normal
14/4/23	10:57:21	90	0.1	220	30.3	2200		2675 G	3.63	25.84188	87.25943 Normal
14/4/23	10:57:21	90	0.1	230	20.2	2300		2773 G	3.75	25.84225	87.2603 Normal
14/4/23	10:58:0	90	0.1	240	10.1	2400		2872 G	3.87	25.84265	87.26109 Normal
14/4/23	10:58:0	90	0.1	250	30.3	2500		2970 G	3.99	25.84303	87.26204 Normal
14/4/23	10:58:31	90	0.1	230	30.3	2300		2773 G	3.75	25.84316	87.26301 Normal
14/4/23	10:58:31	90	0.1	220	30.3	2200		2675 G	3.63	25.84316	87.26396 Normal
14/4/23	10:59:7	90	0.1	190	10.1	1900		2380 G	3.27	25.8432	87.26502 Normal
14/4/23	10:59:7	90	0.1	220	10.1	2200		2675 G	3.63	25.8433	87.26593 Normal
AVERAGE									2844.5		

$$Y = 0 * X^2 + 0.984 * X + 510.70$$

$$X = 3300$$

$$Y = 3757$$


(R) RURAL ROAD
 Good <4000
 Average 4001-5000
 Poor >5001

[Signature]
 Executive Engineer
 Rural Works Department
 Works Division Dhamdaha (Purnea)

[Signature]
 14/04/2023
 CTE

[Signature]
 14/4/23
 5E

File :H:\15041033.Xls, Section No.:90, Eqn : $Y = 0 * X^2 + 0.984 * X + 510.70$
 Name of Customer :PREM KUMAR, Name of Work/ Road :SARITA PMGSY ROAD TO KURIYA TOLA, Lab Job

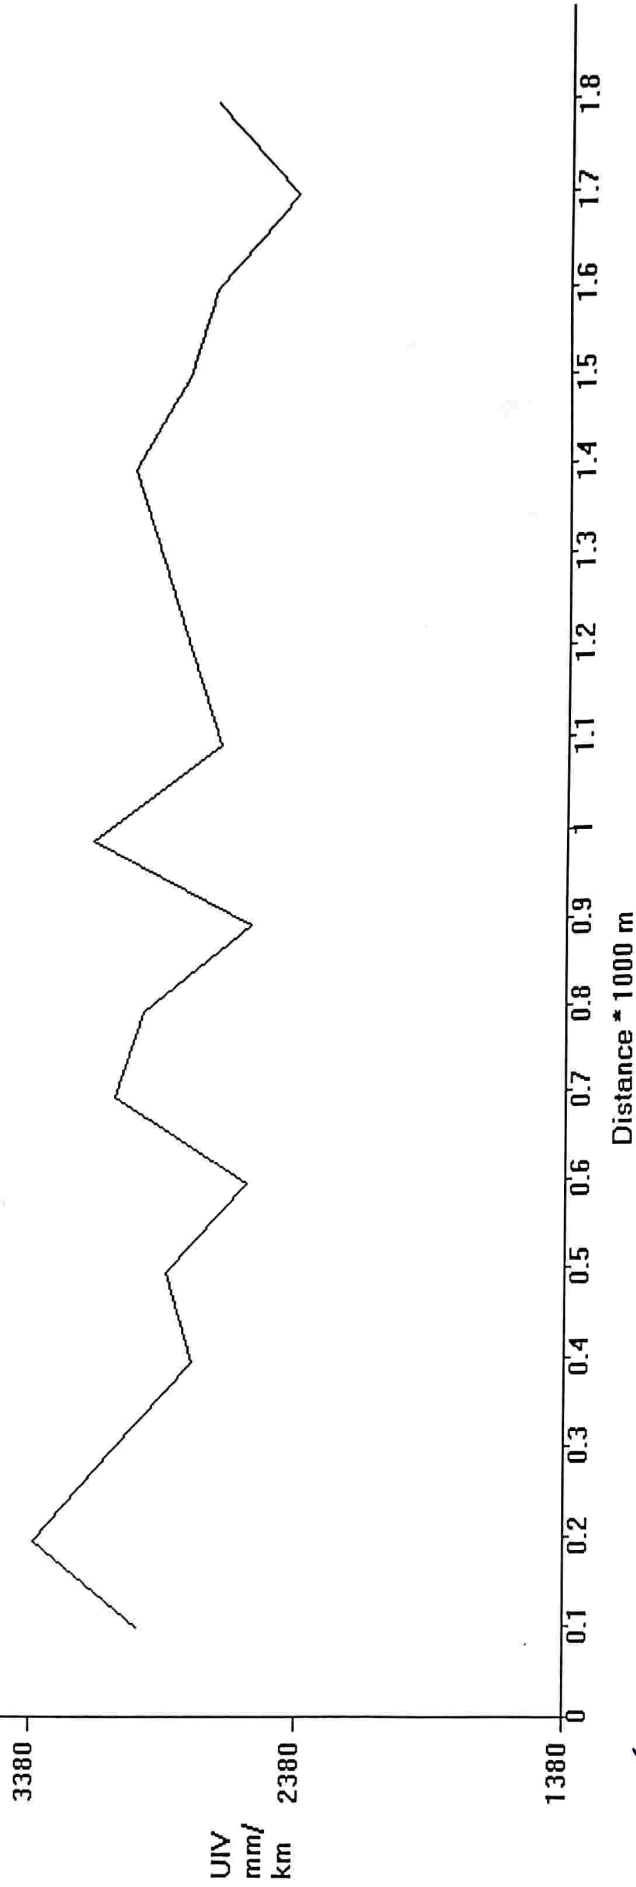

[Signature]
Executive Engineer
 Rural Works Department
 Works Division Chanddaha (Purnea)

[Signature]
 14/10/2023
 (10)

[Signature]
 14/11/23
 SC

कार्यपालक अभियंता, का कार्यालय ग्रामीण कार्य विभाग, कार्य प्रमण्डल, धमदाहा

Email. ID- eervddhamdaha@gmail.com

प्रमाणित किया जाता है कि SARITA PMGSY ROAD TO KURIYA का सभी अवयवों की जाँच शत-प्रतिशत कनीय अभियंता द्वारा किया गया है। सहायक अभियंता द्वारा सभी अवयवों की 50% से अधिक जाँच किया गया है। अधोहस्ताक्षरी द्वारा 10% अवयवों की जाँच की गई है।

(Signature)
8/4/23

कनीय अभियंता,
धमदाहा

(Signature)
सहायक अभियंता,
ग्रामीण कार्य विभाग

कार्य प्रमण्डल, धमदाहा

(Signature)
कार्यपालक अभियंता

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, धमदाहा
